

Archived: Tuesday, September 22, 2026 12:21:52 PM
From: [Medina, Steven](#)
Sent: Fri, 18 Sep 2026 21:03:28
To: ndickel@aqmd.gov
Cc: [Huber, Rachelle](#)
Subject: Case No. 6177-4 Stipulated Order for Abatement – Well Drilling Update
Importance: Normal
Sensitivity: None
Attachments:          2026-09-
[CCLF_GCCS Expan Weekly Well Install Notification Map_V1.0.pdf](#)

Good afternoon,

In accordance with Condition 15(c) of the Stipulated Order, below is the up-to-date construction summary for the Chiquita Canyon Landfill 2026 GCCS Expansion Master Plan Project.

During 09/14/2026 to 09/18/2026, Chiquita completed the installation of one (1) vertical LFG extraction well. The total count of vertical LFG extraction wells installed from December 6, 2023 (the start date of the GCCS Master Expansion) through today is three hundred thirty-nine (339).

The wells scheduled for drilling during the week of 09/21/2026 to 09/25/2026 are as follows (subject to change):

Rig (Continuum): CV-2604, CV-2668, CV-2673, CV-2674S/D, CV-2678S/D

Well installation locations scheduled for drilling next week are subject to change due to rig downtime, weather, and/or safety conditions.

Regards,



STEVEN Medina, E.I.T.

Project Professional

smedina@scsengineers.com


O: 858-583-7746

M: 858-204-4342

3900 Kilroy Airport Way, Suite #300

Long Beach, CA 90806



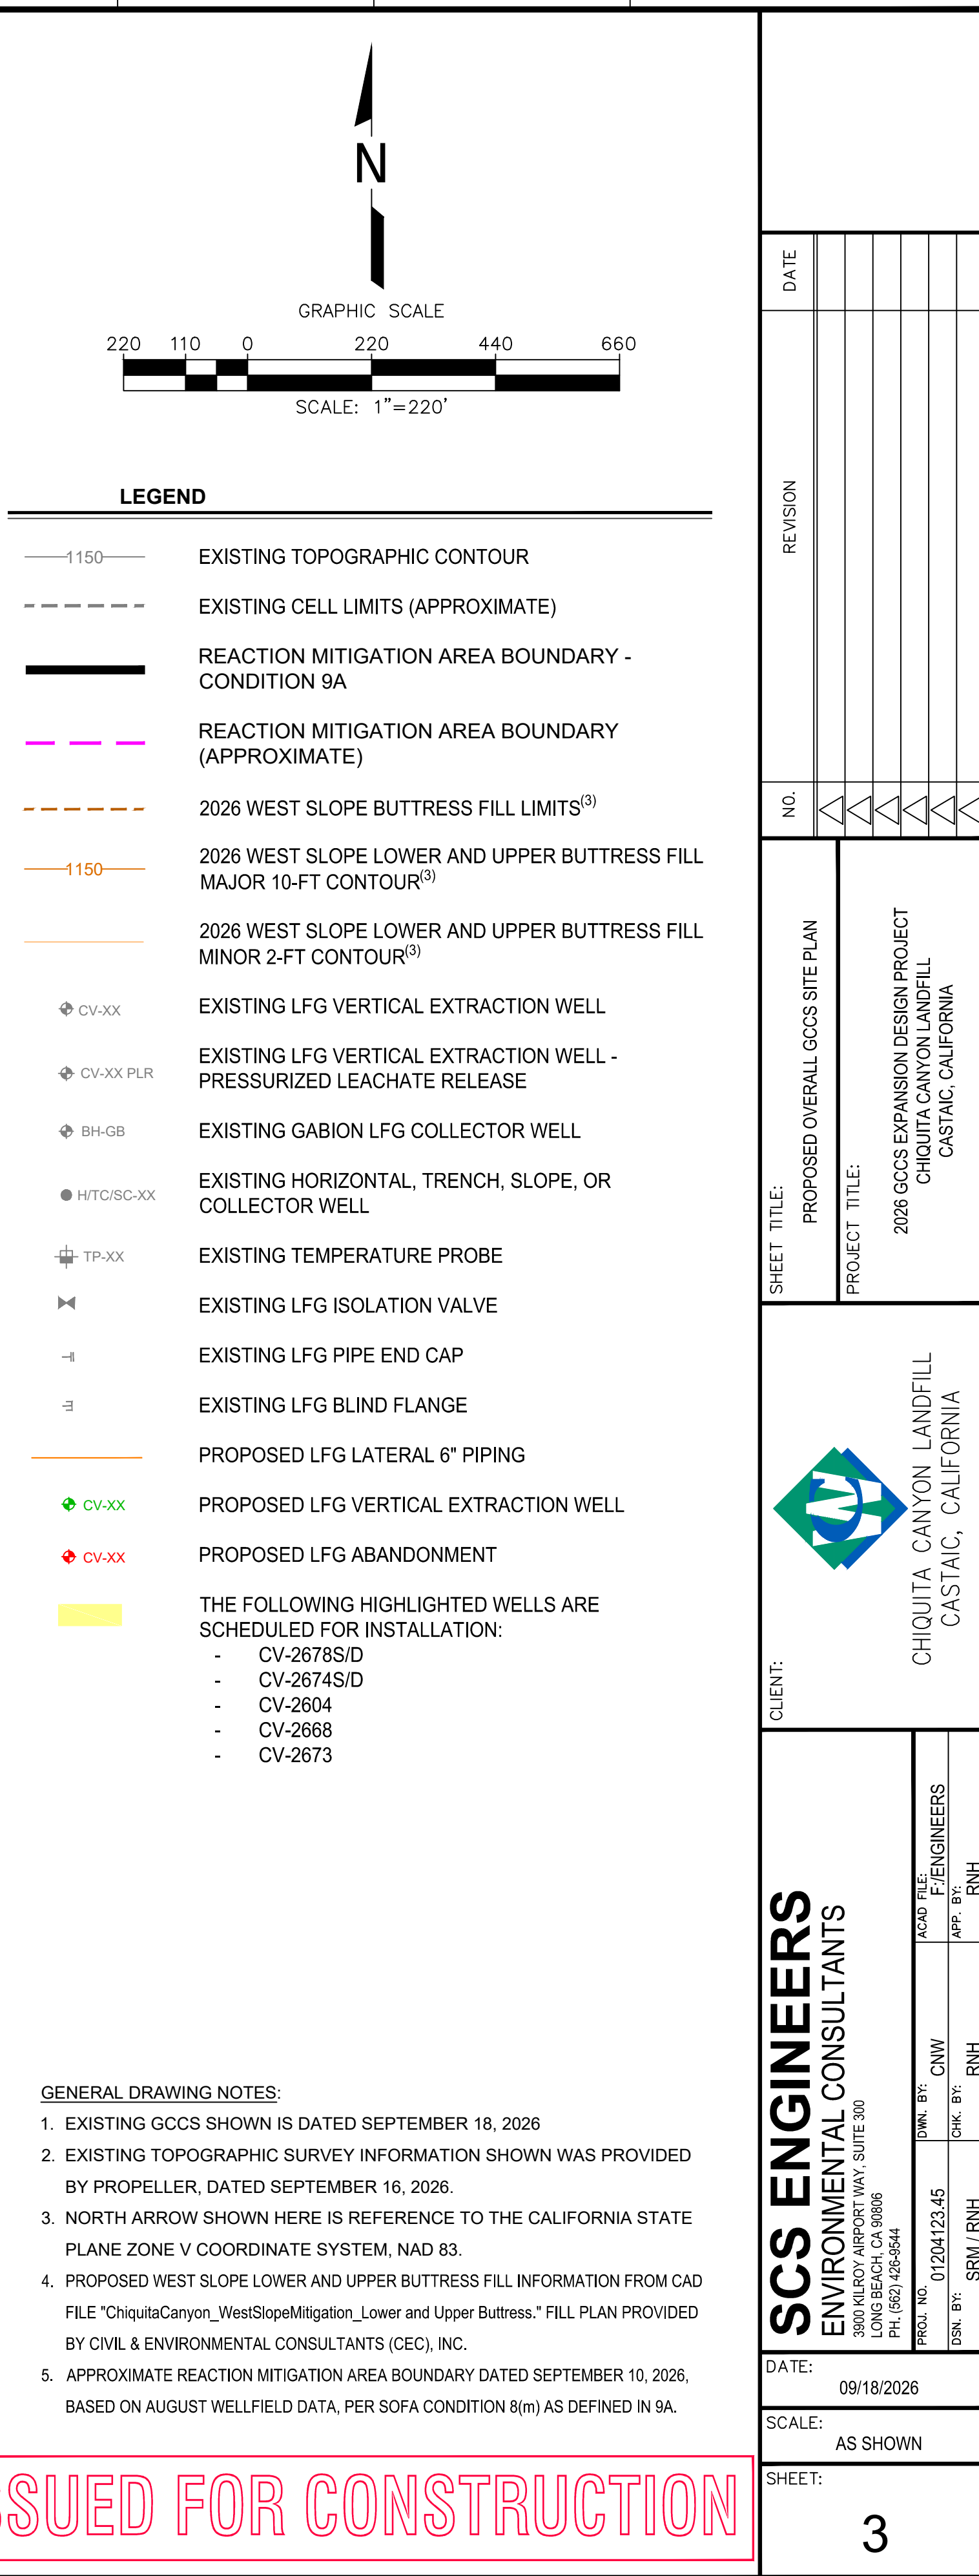

3
