

**Archived:** Thursday, October 16, 2025 10:46:41 AM  
**From:** [Medina, Steven](#)  
**Sent:** Friday, October 10, 2025 11:44:43 AM  
**To:** [bchen@aqmd.gov](mailto:bchen@aqmd.gov)  
**Cc:** [Han, Jessie](#)  
**Subject:** Re: Case No. 6177-4 Stipulated Order for Abatement – Well Drilling Update  
**Importance:** Normal  
**Sensitivity:** None  
[image.png](#) [Outlook-myxdcuf3.png](#) [Outlook-oduaynce.png](#) [Outlook-spy4csyp.png](#) [Outlook-uyzruysj.png](#)  
**Attachments:** [2025 CCLF GCCS Expan Master Plan\\_Proposed LFG Extraction Well and Temp Probe Map\\_2025-10-10.pdf](#)

---

[EXTERNAL SENDER: Use caution with links/attachments]

---

All,

In accordance with Condition 15(c) of the Stipulated Order, below is the up-to-date construction summary for the Chiquita Canyon Landfill 2025 GCCS Expansion Master Plan Project.

**As of 10/06/2025 to 10/10/2025 - Installation of LFG vertical extraction wells included:**

1. CV-2520
2. CV-2521
3. CV-2522
4. CV-2535
5. CV-2539

During 10/06/2025 to 10/10/2025, Chiquita completed the installation of five (5) vertical LFG extraction wells. The total count of vertical LFG extraction wells installed from December 6, 2023 (the start date of the GCCS Master Expansion) through today is three hundred five (305).

During 10/06/2025 to 10/10/2025, Chiquita completed the installation of zero (0) temperature probes. The total count of temperature probes installed from February 26th, 2024 (the start date of the temperature probe installations) through today is thirty-seven (37).

**The wells and temperature probes scheduled for drilling during the week of 10/13/2025 to 10/17/2025 are as follows (subject to change):**

**Rig (Continuum):** CV-2537, CV-2538, CV-2571, CV-2572, CV-2575

**Temperature Probe Rig (Boart Longyear):** Drilling of the temperature probes will resume upon completion of the Soil Vapor Extraction (SVE) well drilling and installation. Drilling of the SVE wells is now scheduled to begin on Monday, October 13, following a delay due to the mobilization of the drill rig from the previously planned start date of October 8.

Regards,

**STEVEN** Ruben Medina, **E.I.T.**

Staff Professional

**SCS Engineers**


3900 Kilroy Airport Way, Suite 300

Long Beach, CA 90806  
858-204-4342 (c)  
[SMedina@scsengineers.com](mailto:SMedina@scsengineers.com)

**Driven by Client Success**  
[www.scsengineers.com](http://www.scsengineers.com)





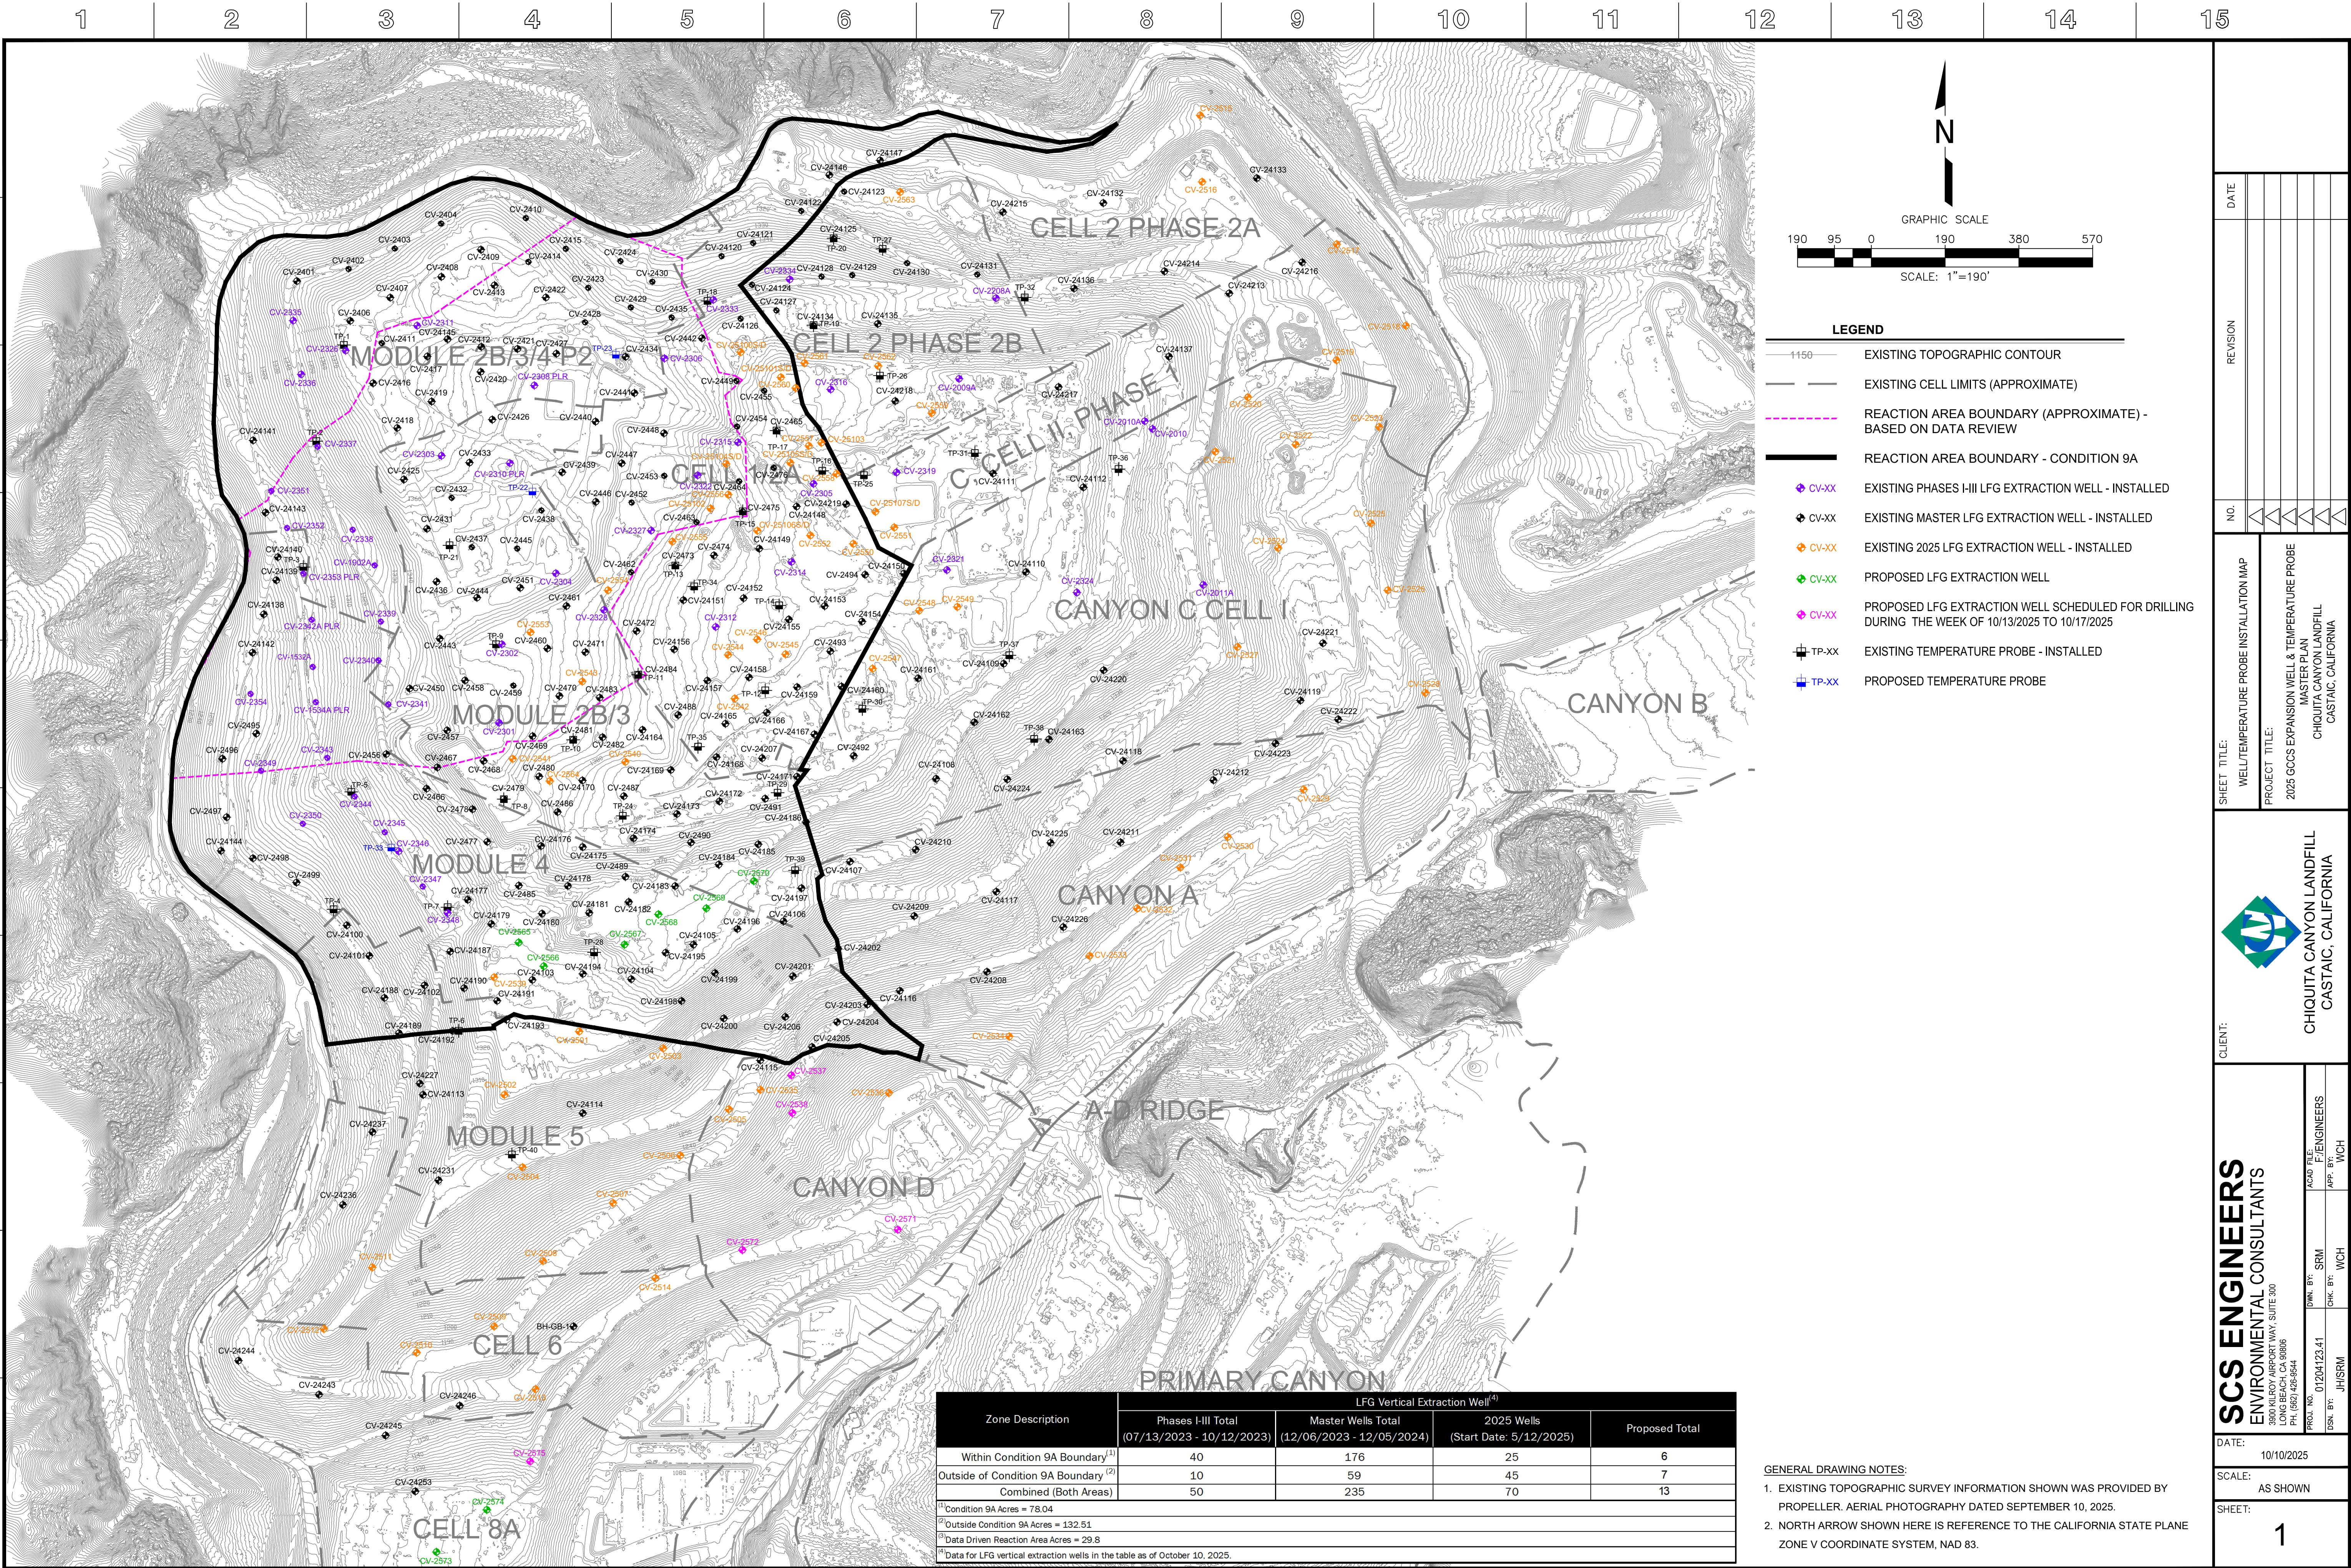

SCS ENGINEERS  
ENVIRONMENTAL CONSULTANTS  
15000 W. ORANGE AVE., SUITE 300  
LONG BEACH, CA 90806  
PH: (562) 426-9544

ACAD FILE: SRM

APP. BY: WCH

CHK. BY: WCH

JHSRM

C:\Users\5160sr\Desktop\2025 CCLF GCCS Expan Master Plan\_Proposed LFG Extraction Well and Temp Probe Map\_2025-10-10.dwg Oct 10, 2025 - 8:40am By: srmcdon
