20 de octubre de 2026
Archivo No. 01204123.42, Tarea 10

Baitong Chen, Ingeniero de la Calidad del Aire, bchen@aqmd.gov
Nathaniel Dickel, Ingeniero Sénior de la Calidad del Aire, ndickel@aqmd.gov
Christina Ojeda, Inspectora de la Calidad del Aire, cojeda@aqmd.gov
Distrito de Gestión de la Calidad del Aire de la Costa Sur
21865 East Copley Drive
Diamond Bar, CA 91765-4182

Asunto: Informe Mensual de Septiembre de 2026 de la Orden de Depuración Estipulada Modificada (Caso No. 6177-4), Vertedero de Chiquita Canyon (Código de Centro 119219), Castaic, California

A Quien Corresponda:

SCS Engineers (SCS), en nombre de Chiquita Canyon, LLC (Chiquita), mediante el presente le proporciona al Distrito de Gestión de la Calidad del Aire de la Costa Sur (SCAQMD) un informe mensual según la Orden de Depuración Estipulada Modificada (SOFA) (Caso No. 6177-4). La SOFA se aprobó inicialmente el 6 de septiembre de 2023 y se modificó posteriormente el 17 de enero de 2024, el 21 de marzo de 2024, el 24 de abril de 2024, el 27 de agosto de 2024, el 13 de noviembre de 2024, el 16 de abril de 2025, el 24 de junio de 2025, el 9 de diciembre de 2025 y el 4 de junio de 2026.

Este informe abarca el período mensual de septiembre de 2026. Según la Condición No. 8, el informe mensual de septiembre de 2026 debe entregarse el día 20 del mes o el siguiente día hábil, que es el martes 20 de octubre de 2026.

ANTECEDENTES

El Vertedero de Chiquita Canyon (CCL) es un vertedero/centro de disposición de desechos sólidos ubicado en 29201 Henry Mayo Dr., Castaic, California, 91384 (SCAQMD Centro No. 119219). Con relación al vertedero, Chiquita opera un sistema de recolección y control de biogás.

En 2023, CCL comenzó a experimentar mayores niveles de azufre total reducido y de óxidos de azufre, en un supuesto incumplimiento de su permiso del Título V.[1] Además, CCL comenzó a estar sujeto a reclamos de olores del público y el SCAQMD le emitió Avisos de Violaciones. Las condiciones en CCL indican que el vertedero está pasando por un evento de vertedero de temperaturas elevadas (ETLF). El 6 de septiembre de 2023, se celebró una audiencia ante la Junta de Audiencias de SCAQMD para aprobar la SOFA que incluye numerosas medidas para mitigar las emisiones resultantes de las condiciones del ETLF del vertedero. La SOFA fue aprobada el 6 de septiembre de 2023. Desde ese momento, la SOFA se modificó el 17 de enero de 2024, el 21 de marzo de 2024, el 24 de abril de 2024, el 27 de agosto de 2024, el 13 de noviembre de 2024, el 16 de abril de 2025, el 24 de junio de 2025, el 9 de diciembre de 2025,

[1] CCL operó bajo una Variación de Emergencia Ex Parte (aprobada el 8 de febrero de 2023), una Variación Interina (aprobada el 15 de febrero de 2023 y emitida como final el 7 de marzo de 2023) y una Variación Regular (aprobada el 3 de mayo de 2023 y emitida como final el 16 de mayo de 2023). La Variación Regular terminó el 6 de septiembre de 2023, la fecha efectiva de la SOFA inicial. La SOFA se modificó el 17 de enero de 2024, el 21 de marzo de 2024, el 24 de abril de 2024, el 27 de agosto de 2024, el 13 de noviembre de 2024, el 16 de abril de 2025, el 24 de junio de 2025, el 9 de diciembre de 2025 y el 4 de junio de 2026.

y el 4 de junio de 2026, después de las audiencias ante la Junta de Audiencias del SCAQMD. Este informe mensual sigue las condiciones aprobadas de la SOFA modificada por última vez el 4 de junio de 2026, según corresponda.

La Condición No. 8 de la SOFA requiere que se presenten informes mensuales por e-mail a Baitong Chen, Nathaniel Dickel y Christina Ojeda del SCAQMD, que incluyan la siguiente información:

A. *Las mediciones de compuestos de azufre de biogás y los análisis de laboratorio con la hora y fecha de cada medición o toma de muestra, identificadas en la Condición No. 5.*

B. *Los registros y cálculos de biogás identificados en la Condición No. 7 en un formato de planilla de cálculo en Microsoft Excel. Si los registros de biogás indican que algún equipo de combustión/control de biogás (antorchas u oxidantes térmicos) está fuera de línea por un período que excede los 7 días calendario consecutivos o por más de 15 días calendario en cualquier mes calendario, el Demandado deberá informarlo proporcionando una descripción detallada de los motivos por los que el equipo estuvo fuera de línea (rotura del equipo, mantenimiento, construcción, si hubo suficiente redundancia de control de biogás para controlar el biogás recolectado, etc.).*

C. *El análisis integrado de la muestra de la superficie del vertedero y las lecturas de los monitoreos de la superficie del vertedero identificados en las Condiciones No. 9 y 10, en un formato de planilla de cálculo en Microsoft Excel. Los mapas de vigilancia aérea, las mediciones de las inspecciones de campo de seguimiento con las fechas/horas asociadas, la causa de las excedencias, cualquier acción correctiva realizada y la documentación (fecha, hora, razonamiento) de las inspecciones de campo no realizadas debido a la falta de accesibilidad o a condiciones peligrosas identificadas en la Condición 77.*

D. ***[Reservado; Consulte el Apéndice 1].***

E. ***[Reservado; Consulte el Apéndice 1].***

F. ***[Reservado; Consulte el Apéndice 1].***

G. *Todas las mediciones de temperaturas de cabezales de pozos, de sondas de temperatura y de concentraciones de CO de los pozos que requieren datos analíticos, mediciones de concentración de H2 de los pozos que requieren datos analíticos, mediciones de CH4, mediciones de O2, mediciones de CO2, relaciones de CH4:CO2, análisis de laboratorio y lecturas de tubos Draeger de biogás del mes pasado en formato de hoja de cálculo en Microsoft Excel.* ***Desde el informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá dejar de incluir esta información en los informes mensuales, excepto todos los análisis de laboratorio del biogás del mes anterior, que el Demandado continuará proporcionando en un formato de planilla en Microsoft Excel.***

H. *Un mapa gráfico que muestra la ubicación de cada pozo que excede la temperatura (por encima de los 145 grados Fahrenheit), cada pozo con excedencias de CO (por encima de los 1,000 ppmv y menores o iguales a 1,500 ppmv, por encima de los 1,500 ppmv y menores o iguales a 2,000 ppmv y por encima de los 2,000 ppmv) y estratificación de los rangos de temperatura durante ese mes, que incluye una descripción de las medidas de remediación tomadas para tratar o reducir temperaturas de pozos de gas.* ***A partir del informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá quitar estos datos de los informes mensuales.***

I. *Todos los pozos verticales de biogás impactados con líquidos, según la Condición No. 17, incluyendo una descripción de las medidas de remediación tomadas para tratar o reducir líquidos en pozos de biogás.*

J. ***Desde el informe presentado el 20 de octubre de 2026, actualizaciones de la investigación sobre la disponibilidad, la viabilidad y la factibilidad de los equipos de control de SOx post combustión, que incluyen actualizaciones sobre la investigación, el informe y el posterior diseño y progreso de la instalación y los plazos, en cumplimiento con la Condición 3(c).***

K. Un informe resumido de las mejoras implementadas en el sistema de recolección de biogás por el Demandado más allá de los agregados al sistema de recolección de biogás requeridos según la Condición No. 15 y 8(m).

L. Un registro de inspecciones y reparaciones de cubiertas del vertedero e inspecciones de cubiertas geosintéticas, en cumplimiento con la Condición No. 30 y los puntos de conexión, las costuras y los sellos de la cubierta geosintética, conforme a la Condición 97.

M. *Cualquier agregado posterior al sistema de recolección de biogás, según la Condición No. 15; un mapa del pozo de extracción vertical actualizado detallando todos los pozos existentes de extracción vertical que están operando de forma completamente funcional y los pozos de extracción vertical agregados dentro del mes; un mapa que muestre una superposición de los pozos completamente operativos y de las cuadrículas de monitoreo de la superficie del vertedero, y los contornos de las áreas demarcadas como exentas en el Anexo A adjunto, conforme a la Condición 15(b); copias de los registros de pozos conforme a obra (en lo relacionado a las instalaciones y actualizaciones en las profundidades de los pozos) de extracción vertical completados dentro del mes; y un mapa o plano actualizado de la infraestructura de recolección y transporte de biogás conforme a obra, actualizado con respecto a cualquier modificación sustancial en los cabezales principales del sistema de recolección y control de biogás, con los límites de la Zona de* ***Mitigación*** *de Reacciones;* ***una tabla en formato Microsoft Excel que detalle los códigos de identificación de los pozos de extracción vertical, las fechas de instalación, la profundidad de la perforación deseada y/o requerida en cumplimiento con la Condición 15(b), la profundidad de perforación alcanzada, si el pozo tiene una bomba de desagote y, hasta donde sea posible, las lecturas de los niveles de líquido más recientes (fecha, hora, valores); y un mapa que muestre el campo de pozos según el plano, con indicación visual de los pozos que están y que no están en las profundidades deseadas.***

N. Cualquier agregado posterior al sistema de condensado de biogás o de recolección de lixiviados, como sumideros/bombas de desagüe u otros trabajos de desagote realizados según las pautas para desagote y el plan de implementación conforme a la Condición No. 18.

O. Actualizaciones sobre la adquisición e instalación de cubiertas geosintéticas conforme a la Condición No. 31, incluyendo los cambios requeridos o aprobados por la Agencia de Cumplimiento Local.

P. Actualizaciones sobre el trabajo de excavación en el vertedero sujeto a la Regla 1150, incluyendo las ubicaciones de las excavaciones (identificadas en los mapas gráficos del vertedero) y características de los residuos excavados/expuestos (saturados, semisecos, secos, tipo e intensidad de olor, etc.). Los trabajos de excavación que ocurren conforme a una exención como lo indican la Regla 1150(c)(3) o la Regla 1150(c)(2) del AQMD de la Costa Sur que se realizan en esta Área de ***Mitigación*** *de Reacciones también deben incluirse en estas actualizaciones.*

Q. Actualizaciones sobre los lixiviados, que incluyen:

- *i. Registros de temperatura de lixiviados conforme a la Condición No. 27(a);*
- *ii. Registro diario de los hallazgos de las inspecciones y actividades de contención conforme a la Condición 27(b);*
- *iii. Registro semanal de filtraciones y acumulación de lixiviados conforme a la Condición 27(c);*
- *iv. Cantidad de lixiviados medidos y nombre de la empresa y dirección física relacionados de los centros de disposición/tratamiento fuera del sitio que reciben lixiviados generados por el vertedero, conforme a la Condición 27(d); y*
- *v. Una lista de todas las instalaciones de almacenamiento y tratamiento de líquidos peligrosos y no peligrosos que se hayan contactado y el estado actual de cada una de las instalaciones, incluyendo la capacidad disponible, contratada y utilizada, para recibir líquidos del vertedero peligrosos y no peligrosos; y*
- *vi. Una actualización sobre la cantidad de tanques en cada grupo de tanques de lixiviados; la cantidad total de tanques de lixiviados tratados; la cantidad total mensual y en lo que va del año de líquido recogido; la cantidad total mensual y en lo que va del año de líquido tratado; y la cantidad total mensual y en lo que va del año de lixiviados de filtraciones, acumulaciones o estancamientos recogidos.*

R. *Análisis diarios de la composición de los gases del vertedero, que incluyen CH4%, concentración de CO (ppm), CO2% y O2%, registrados por un analizador en tiempo real y/o muestras tomadas en las entradas de los equipos de control (TOx, Antorchas y equipos de control adicionales llevados al sitio para que hagan combustión con el biogás)* ***en formato de planilla de cálculo en Microsoft Excel.*** *Los análisis serán realizados por un analizador aprobado por el AQMD de la Costa Sur para CH4, CO2 u O2, y analizados conforme al Método 10 de la EPA de EE.UU. o el Método ALT-144 para CO. La solicitud de aprobación deberá incluir la presentación de las especificaciones de los analizadores.* ***A partir del informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá quitar estos datos de los informes mensuales.***

S. *Actualizaciones sobre la adquisición de equipos necesarios para construir la Antorcha No. 4 conforme a la Condición No. 74.*

T. Los registros de las temperaturas operativas (por minuto) y los tipos de combustible piloto/combustible complementario e índices de uso (por hora), hasta donde se conozcan los datos, de cada antorcha de biogás y oxidante térmico del último mes, en un formato de planilla de cálculo en Microsoft Excel. A partir del informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá quitar estos datos de los informes mensuales.

Conforme a la Condición 7(d), estos informes mensuales también deben incluir lo siguiente:

> ***El Demandado deberá mantener un registro de la siguiente información y proporcionarle estos registros al AQMD de la Costa Sur conforme a la Condición No. 8:***
>
> ***a. El flujo de biogás por hora y por día incinerado, en pies cúbicos estándar, en cada antorcha (antorchas No. 1 y No. 2 bajo el Permiso G73696, A/N 645450; antorcha No. 3 bajo A/N 624296), el oxidante térmico/las antorchas y cualquier otro equipo usado para quemar o controlar biogás en las instalaciones, como también la cantidad total de biogás incinerado en las instalaciones;***
> ***b. El flujo diario de biogás no quemado en antorchas, en pies cúbicos estándar, si corresponde; y***
> ***c. Los resultados de las lecturas de azufre, las tomas de muestras y los análisis calculados como H2S con la hora y fecha en la que se tomó cada medición o en la que se tomó cada muestra; y***
> ***d. Los resultados de las calificaciones diarias del calor del gas, con la hora y fecha de cada muestra tomada, la ubicación de la toma de muestra y el tipo del gas del que se tomaron muestras (ej. biogás, mezcla de vapores de biogás y lixiviados).***

Conforme a la Condición No. 29, estos informes mensuales también deben incluir lo siguiente:

> *El Demandado deberá asegurarse de contar con la capacidad adecuada de lixiviados del vertedero y de condensado de biogás (en base a los informes de producción y recolección de líquidos, conforme a la Condición 8) para acumular en el sitio y/o disponer de los líquidos/lixiviados recogidos en un centro o centros apropiados.*

Conforme a la Condición No. 35, estos informes mensuales también deben incluir lo siguiente:

> ***El Demandado debe proporcionar actualizaciones sobre todos los procedimientos operativos estándar (SOPs) y cualquier otro documento de Control de Calidad y Aseguramiento de la Calidad (QA/QC) presentado al AQMD de la Costa Sur el 19 de enero de 2024 que describa la operación y el mantenimiento de todos los instrumentos utilizados en las estaciones de monitoreo de aire y/o en las estaciones de monitoreo mejoradas especificadas en la Condición No. 34***

(si hubiera) y un registro de calibración y actividades de mantenimiento realizadas en los monitores en los informes mensuales conforme a la Condición No. 8.

Conforme a la Condición 31, estos informes mensuales también deben incluir lo siguiente:

El Demandado deberá incluir actualizaciones sobre la adquisición e instalación de la cubierta geosintética en los informes mensuales conforme a la Condición No. 8.

Conforme a la Condición No. 42(w), estos informes mensuales también deben incluir lo siguiente, en la parte relevante:

Si el Demandado recibe un Aviso de Infracción por Molestias de la Regla 402 del AQMD de la Costa Sur durante la excavación o un olor distinto (nivel 3 o superior según la Escala de Olor a continuación) resultante de la excavación en o pasando la línea de la propiedad, el Demandado deberá, conforme a su Plan de Salud y Seguridad, tomar muestras de la calidad del aire del ambiente dentro de las 2 horas desde que se recibe el Aviso de Infracción por Molestias de la Regla 402 o cuando se detecta un olor distinto (nivel 3 o superior) en o pasando la línea de la propiedad y analizar los TOC y los TOCs especiados de la siguiente manera:

Escala de Olor	*Descripción de la Intensidad del Olor*
0	*No se detectó olor*
1	*Se detectó un olor muy leve*
2	*Se detectó un olor leve, distinguible*
3	*Olor moderado, muy distinguible*
4	*Olor fuerte, muy distinguible, irritable*
5	*Olor muy fuerte, muy distinguible, abrumador*

i. Se deben tomar muestras en los siguientes lugares: inmediatamente a barlovento del sitio de la excavación, inmediatamente a sotavento del sitio de la excavación, dentro de las 3 pulgadas de la cara de trabajo de la excavación expuesta, si la seguridad lo permite, y en la línea de la propiedad a sotavento o en otros lugares aprobados por escrito por el AQMD de la Costa Sur. Si se considera inseguro, el Demandado deberá documentar la fecha y las condiciones que no permiten el cumplimiento de esta condición. Deberán presentarse registros de estas condiciones en el siguiente informe mensual, conforme a la Condición 8.

Conforme a la Condición No. 42(x), estos informes mensuales también deben incluir lo siguiente, en la parte relevante:

Durante la excavación, deberán tomarse muestras de los TOC y de los TOC especiados en el aire ambiental por lo menos una vez entre las 6:00 am y las 11:00 am y por lo menos una vez entre las 2:00 pm y las 6:00 pm, según el Plan de Salud y Seguridad del Demandado y los siguientes requerimientos:

i. Se deben tomar muestras en los siguientes lugares: inmediatamente a barlovento del sitio de la excavación, inmediatamente a sotavento del sitio de la excavación, dentro de las 3 pulgadas de la cara de trabajo de la excavación expuesta, si la seguridad lo permite, y en la línea de la propiedad a sotavento o en otros lugares aprobados por escrito por el AQMD de la Costa Sur. Si se considera inseguro, el Demandado deberá documentar la fecha y las condiciones que no permiten

el cumplimiento de esta condición. Deberán presentarse registros de estas condiciones en el siguiente informe mensual, conforme a la Condición 8.

Conforme a la Condición No. 55(g), estos informes mensuales también deben incluir lo siguiente:

El Demandado mantiene registros de muestras/resultados de análisis de condensados para demostrar que el líquido no es peligroso, mantiene registros de flujos de inyección de condensados diarios (galones por día) y proporciona estos registros en el informe mensual conforme a la Condición No. 8.

Conforme a la Condición No. 63, estos informes mensuales también deben incluir lo siguiente:

El Demandado deberá proporcionarle a más tardar el 12 de junio de 2026 al AQMD de la Costa Sur un esquema del sistema de tratamiento de lixiviados actual y el sistema de almacenamiento de lixiviados, que incluyen de forma enunciativa más no limitativa, conexiones, líneas de flujo, depósitos de tratamiento, tanques de aireación, tanques de almacenamiento y grupos de tanques, líneas de ventilación que se dirigen a los equipos de control, equipos de control, líneas que se dirigen hacia los tanques de lixiviados y entre tanques de lixiviados, tanques que están conectados y no conectados a las líneas de ventilación de vacío y los equipos y las ubicaciones de carga/descarga de camiones cisterna de lixiviados. El Demandado debe proporcionar un esquema revisado en los informes mensuales de la Condición 8 después de todo mes durante el cual el Demandado haya completado cualquier cambio o modificación en el sistema de tratamiento de lixiviados y/o sistema de almacenamiento de lixiviados, que se reflejaría en el esquema.

Conforme a la Condición No. 68, estos informes mensuales también deben incluir lo siguiente:

El Demandado deberá instalar, a más tardar el 15 de junio de 2024, medidores de presión diferencial con rangos apropiados, con una resolución de por lo menos 0.01 pulgadas de columna de agua o un indicador de presión aprobado de otra manera por escrito por el AQMD de la Costa Sur, en cada tanque de almacenamiento de lixiviados. El Demandado deberá monitorear y registrar la presión diferencial diaria de cada tanque de lixiviados, el número de identificación del tanque, la fecha y hora de la lectura y el personal que realizó la lectura. Las lecturas de las presiones que indiquen el menor valor del medidor o el mayor valor del medidor deberán informarse utilizando dígitos significativos hasta las centésimas, como "<= [valor más bajo en el medidor] (ej. <= -0.50 pulgadas de columna de agua)" y ">= [valor más alto en el medidor] (ej. >= 0.50 pulgadas de columna de agua)", respectivamente. Los tanques deberán mantenerse bajo presión negativa, según lo demuestren las lecturas de la presión diferencial. Las lecturas de cero y presión positiva no demuestran una presión negativa. Los medidores de presión deben calibrarse en cumplimiento con las especificaciones del fabricante y el programa de calibración. El Demandado deberá informar todas las lecturas en el informe mensual, conforme a la Condición No. 8.

Conforme a la Condición No. 72, estos informes mensuales también deben incluir lo siguiente:

El Demandado deberá realizar la toma de muestras y análisis, las pruebas, la instalación y el monitoreo del sistema de recolección y tanques de almacenamiento de lixiviados y condensados de biogás, como se especifica a continuación:

A. Por lo menos cada seis meses, realizar pruebas para tomar muestras y analizar el flujo de vapor en las tuberías utilizadas para ventilar los tanques de almacenamiento de lixiviados y los tanques de condensado de biogás y dirigir los vapores al sistema de control de biogás. Las pruebas deberán incluir por lo menos los siguientes puntos y los resultados de estas pruebas deben proporcionarse en el informe mensual, en cumplimiento con la Condición No. 8:

- *i. índice de flujo de vapores de tanques de lixiviados ventilados,*
- *ii. índice de flujo de vapores de tanques de condensados ventilados,*

iii. *temperatura del vapor,*
iv. *concentraciones de orgánicos especiados (incluyen, de forma enunciativa más no limitativa, Contaminantes del Aire Carcinogénicos y Tóxicos de la Tabla 1 de la Regla 1150.1),*
v. *los compuestos de azufre total como H2S y compuestos de azufre especiados, y*
vi. *analizar en cada uno de los lugares indicados a continuación:*
    1. *Las ventilaciones o los colectores de los tanques que sean representativos de un set de tanques;*
    2. *El cabezal/colector de cada parque de tanques de lixiviados o colector que incluye el Parque de Tanques No. 7, el Parque de Tanques No. 9, el Colector del Perímetro Norte, el Nuevo Colector del Perímetro Este, el Colector LC, los tanques de almacenamiento de condensado de biogás y cualquier otro futuro parque de tanques o colectores, realizando las pruebas flujo arriba de la conexión de la tubería al Sistema de Recolección y Transporte de LFG donde el biogás pueda afectar los resultados; y*
    3. *La entrada de la(s) antorcha(s) antes de la combustión.*

B. *Deberá presentarse un protocolo de pruebas de origen al AQMD de la Costa Sur antes del 17 de mayo de 2024, a menos que el AQMD de la Costa Sur apruebe otra cosa por escrito. Las pruebas deberán realizarse dentro de los 45 días desde que se recibe la aprobación escrita del protocolo de prueba de origen por parte del AQMD de la Costa Sur y deberán presentarse los resultados finales en un formato de informe de prueba de origen dentro de los 30 días desde que se realizan las pruebas, a menos que el AQMD de la Costa Sur apruebe otra cosa por escrito.*
C. *[Completado]*
D. *[Completado]*
    i. *[Completado]*
E. *[Completado]*
    i. *[Reservado]*

Conforme a la Condición No. 77, en la parte relevante, estos informes mensuales también deben incluir lo siguiente:

El Demandado deberá realizar una vigilancia aérea por toda la superficie del ***Cañón Principal todas las semanas****, empleando un dron equipado con sensores con un nivel de detección mínimo de 1 ppmv de metano y conforme a OTM-51. Si alguna lectura de la vigilancia aérea llega o excede los 200 ppmv de metano, el Demandado deberá realizar inspecciones de campo de seguimiento para monitorear las emisiones superficiales en el suelo, según los procedimientos de OTM-51 y el Método 21 de la EPA de EE.UU., a menos que el Demandado no pueda monitorear las ubicaciones en cuestión debido a que no se puede acceder o a condiciones peligrosas para un técnico. La inspección de seguimiento debe realizarse dentro de las 2 horas desde que se toma conocimiento de las excedencias en las vigilancias aéreas. Si se descubre o se confirma una excedencia de 500 ppmv de metano durante la inspección de seguimiento, el Demandado deberá implementar acciones correctivas dentro de los 2 días calendario, que incluyan, de forma enunciativa más no limitativa, mantenimiento o reparación de la cubierta geosintética, mantenimiento o reparación de la cubierta del vertedero, ajustes de vacío del campo de pozos y mantenimiento o reparación de tuberías/componentes de gases. El Demandado deberá desarrollar 1) un mapa geoespacial de metano interpolado, con códigos de colores, que exhiba los resultados del valor absoluto de las lecturas de metano, 2) un mapa geoespacial de metano interpolado, con códigos de colores, que exhiba el cambio en las lecturas de metano, comparadas con la vigilancia aérea previa, 3) un mapa que exhiba las coordenadas de la geoubicación con los picos de metano locales y verificación del pico de seguimiento en tierra y 4) un mapa que exhiba la ruta de vuelo del dron. El mapa de metano pico local (mapa No. 3) debe incluir una leyenda en colores para diferenciar las ubicaciones que muestren las lecturas de metano de 1) < 200 ppmv, 2) ≥ 200 y < 500 ppmv, 3) ≥ 500 y < 1,000 ppmv, 4) ≥1,000 y < 2,000 ppmv, 5) ≥2,000 y < 5,000 ppmv y 6) ≥ 5000 ppmv o según lo apruebe de otra manera por escrito el AQMD de la Costa Sur. Los mapas interpolados que exhiban el valor absoluto (mapa No. 1) y el cambio en las lecturas de metano (mapa No. 2) deben incluir una leyenda de los colores, para diferenciar la*

magnitud de la lectura determinada por el Demandado o como lo solicite el AQMD de la Costa Sur de otra manera. Los mapas, las mediciones y las ubicaciones de las inspecciones de campo de seguimiento con las fechas/horas asociadas, las causas de las excedencias (500 ppmv de metano o más), cualquier acción correctiva realizada y la documentación (fecha, hora, justificación) de las inspecciones de campo no realizadas debido a que no se puede acceder al lugar o a condiciones peligrosas, deberán entregarse en el informe mensual siguiente conforme a la Condición 8(c). Deben proporcionarse al AQMD de la Costa Sur los datos crudos que se utilizaron para crear cualquiera de los documentos arriba indicados, dentro de los 5 días hábiles desde la solicitud.

Conforme a la Condición No. 80, estos informes mensuales también deben incluir lo siguiente:

Cuando se traigan o se operen en el sitio equipos con permiso de Varios Lugares del AQMD de la Costa Sur o equipos con permiso del Registro de Equipos Portátiles a Nivel Estatal (PERP) de CARB, el Demandado deberá:

a. *Informar al AQMD de la Costa Sur por escrito la fecha y hora en la que se trajeron los equipos a las instalaciones en el informe mensual correspondiente según la Condición No. 8 e incluir una copia de los permisos en los varios lugares y/o los permisos de PERP en el informe mensual correspondiente según la Condición No. 8.*
b. *Mantener un registro diario que incluya la siguiente información para cada unidad de permiso: número de permiso y/o número de registración, número de solicitud (si corresponde), ubicación de los equipos y hora de inicio y fin de la operación de los equipos (según corresponda). El Demandado deberá presentar el registro diario en el informe mensual correspondiente según la Condición No. 8.*
c. *Informar al AQMD de la Costa Sur por escrito la fecha y hora en la que se retiró el equipo del lugar, en el informe mensual correspondiente, según la Condición No. 8.*

Conforme a la Condición No. 104, estos informes mensuales también deben incluir lo siguiente:

El Demandado deberá contratar a John Zink y/o a otra empresa de diseño o instalación de equipos de combustión de biogás apropiada para que ayude a diseñar e instalar un sistema o varios sistemas de combustible complementarios (gas natural o propano), para que la operación pueda enriquecer el biogás, la mezcla de vapores de biogás/lixiviados y/o vapor de lixiviados controlados en las antorchas de biogás (antorchas 1, 2, 3, 4 y/o 5 como corresponda). El sistema debe diseñarse e instalarse de forma de asegurar que pueda enriquecerse el biogás, la mezcla de vapores de biogás/lixiviados y/o los vapores de lixiviados con poco contenido de metano, para permitir el funcionamiento continuo de las antorchas, el mantenimiento de la llama en los quemadores de las antorchas, un control suficiente del gas recogido y el mantenimiento de la temperatura de la pila de antorchas por encima de los 1400 grados Fahrenheit. El sistema debe ser utilizado por el Demandado, según la necesidad. Los sistemas deben incluir un registrador de flujo de combustible complementario y los registros de combustible deben presentarse en el informe mensual, en cumplimiento con la Condición 8(t). El Demandado deberá completar el diseño y la instalación, conforme a los siguientes plazos:

a. *Para el 31 de julio de 2026, proporcionar una confirmación escrita de los fabricantes existentes de las Antorchas 1, 2 y 3 sobre el contenido de metano mínimo en el biogás necesario para asegurar la eficiencia de destrucción del metano y de los NMOC, conforme a los requerimientos reglamentarios. El contenido mínimo más alto de estas tres antorchas debe proporcionar el contenido mínimo requerido para la Condición 106(c) a continuación.*
b. *Para el 31 de julio de 2026, proporcionar documentación escrita de un instalador calificado indicando los plazos propuestos (lo más rápido posible) para instalar sistemas de combustible complementarios.*

c. *Si los datos recopilados por el Demandado dan como resultado un contenido de metano semanal promedio en el gas combinado que se dirige a las Antorchas 1, 2 y 3 dentro de 2.5 puntos porcentuales del contenido mínimo requerido conforme a la Condición 104(a), el Demandado deberá comenzar la instalación de los sistemas complementarios de combustible según los plazos establecidos en la Condición 104(b).*

Podrán permitirse extensiones a los programas propuestos, si lo aprueba el AQMD de la Costa Sur por escrito.

Sección A - Mediciones de Compuestos de Azufre LFG Durante el Período del Informe

Las mediciones de compuestos de azufre LFG y los análisis de laboratorio con la hora y fecha de cada medición o toma de muestra, como se identifican en la Condición No. 5.

Condición No. 5: El Demandado deberá tomar muestras, analizar y registrar los compuestos de azufre y la calificación del calor del gas para el vapor combinado de biogás/lixiviados que:

1. *Hacen combustión en cada antorcha (medidos en el lugar de toma de muestra FL-150 que es representativo del gas que hace combustión en las antorchas bajo el Permiso G73696, A/N 645450; A/N 624296),*

2. *Hacen combustión en el oxidante térmico/las antorchas y*

3. Hacen combustión en cualquier otro equipo de control de biogás que opera en el sitio. Las muestras y los análisis deben completarse por lo menos una vez al día utilizando el Método 307-91 del AQMD de la Costa Sur para compuestos de azufre totales como H2S y por lo menos una vez al día para contenido de metano utilizando instrumentos de campo, que pueden convertirse a una clasificación de calor del gas (BTU/scf). Además, el Demandado deberá tomar muestras, analizar y registrar los compuestos de azufre de biogás y los compuestos orgánicos de especiación encontrados en el biogás crudo, previo al tratamiento y previo al control, tomado de la Zona de Mitigación de Reacciones (como se define en la Condición 9(a)) por lo menos una vez por mes calendario, para compuestos de azufre total como H2S utilizando el Método 307-91 del AQMD de la Costa Sur y para compuestos orgánicos de especiación utilizando el Método TO-15 de la Agencia de Protección Ambiental de EE.UU. (EPA).

a. Registrar el análisis del Método 307-91 del AQMD de la Costa Sur al recibir el informe de los análisis de laboratorio y documentar la hora y fecha en la que se realizó la medición o toma de muestra y debe llevar las iniciales del personal que realizó la medición o la toma de muestra.

b. Las lecturas y los análisis de compuestos de azufre deben ser reportados al AQMD de la Costa Sur conforme a la Condición No. 8.

i. Las bolsas de Tedlar usadas para la toma de muestras y análisis del Método 307-91 no deben contener microgotas ni residuos.

4. [Reservado; Consulte el Apéndice 1]

Se han implementado los requerimientos revisados establecidos en la Condición 5 de la SOFA, modificada el 4 de junio de 2026, y se tratan en este informe que abarca septiembre de 2026.

Los análisis de laboratorio realizados y los informes correspondientes recibidos para el período de informe de septiembre de 2026, como lo requiere la Condición 5 modificada, se presentan en el **Adjunto A**. Las muestras de FL-1995 (Antorcha 1), FL-2009 (Antorcha 2) y FL-2023 (Antorcha 3) son representativas del biogás que combustiona en las antorchas bajo el Permiso G73696 (A/N 645450; A/N 624296), en los oxidantes térmicos (TOx) y en cualquier otro equipo de LFG que opera en el sitio. Las muestras de Entrada de Zeeco (Zeeco 1 y 6 en la Estación Sur de Zeeco; Zeeco 7), Parnel y Hero son de biogás (LFG) crudo, previo al tratamiento y previo al control, tomado de la Zona de Mitigación de Reacciones. Este informe incluye datos analíticos de muestras tomadas entre el 1 de septiembre de 2026 y el 30 de septiembre de 2026. Las muestras de las bolsas de Tedlar fueron tomadas y analizadas utilizando el Método 307.91 de SCAQMD para observar la presencia de ácido sulfhídrico, compuestos de azufre reducido, monóxido de carbono (CO), gases permanentes (metano, dióxido de carbono, oxígeno y nitrógeno) y compuestos orgánicos de especiación. Se toman muestras de los compuestos orgánicos de especiación utilizando el Método TO-15 de EPA. Se tomaron muestras de FL-2009 y de las unidades TOx Hero, Parnel, Estación Sur de Zeeco y Zeeco 7 para el análisis TO-15 el 1 de septiembre de 2026 (informados el 30 de septiembre de 2026).

En la siguiente tabla se proporciona un resumen de los análisis de laboratorio de azufre de LFG, que abarca el período de septiembre de 2026, como corresponde.

Date Sampled	Permanent Flare Station				Zeeco Inlet TOx (Reaction Area)			Zeeco South Station TOx (Reaction Area)			Parnel TOx (Reaction Area)			Hero TOx (Reaction Area)		
	Lab Analysis (ppmv)				Lab Analysis (ppmv)			Lab Analysis (ppmv)			Lab Analysis (ppmv)			Lab Analysis (ppmv)		
	Flare	H2S	DMS	TRS	H2S	DMS	TRS	H2S	DMS	TRS	H2S	DMS	TRS	H2S	DMS	TRS
09/01/26	FL-2009	187	305	631.9	133	744	1224.9	155	249	529.4	291	1155	2106.8	239	1291	2134.3
09/02/26	FL-1995	177	313	630.5	145	731	1234.2	144	238	496.8	299	1261	2290.2	241	1342	2207.9
09/03/26	FL-2009	183	325	650.5	130	694	1139.5	145	165	395.1	275	1050	1920.1	220	1226	2013.4
09/04/26	FL-2009	245	280	644.2	149	916	1482.9	155	235	509.4	265	1195	2122.0	212	1238	2038.9
09/05/26	FL-1995	36	51	108.4	139	883	1389.9	181	285	583.9	291	1206	2163.7	249	1442	2370.6
09/06/26	FL-1995	187	357	699.0				210	373	741.1	164	940	1564.6	159	960	1542.1
09/07/26	FL-1995	127	290	520.8				213	480	926.5	156	855	1420.2	132	848	1326.7
09/08/26	FL-1995	192	269	570.7	126	826	1305.3	161	299	587.5	245	1065	1886.5	181	1149	1838.2
09/09/26	FL-2009	217	449	858.4	143	731	1220.2	145	292	575.3	182	987	1668.0	161	1011	1613.3
09/10/26	FL-2009	214	484	917.3				188	284	605.1	219	907	1595.0	166	1169	1844.8
09/11/26	FL-1995	200	420	801.0	121	811	1260.9	160	248	528.7	258	1083	1911.4	151	1105	1738.7
09/12/26	FL-2009	206	274	600.3	102	705	1089.8	143	170	381.1	271	1105	1958.3	175	1216	1945.0
09/13/26	FL-2009	191	278	587.5	125	784	1240.2	134	202	417.5	273	1130	2008.6	146	1036	1646.6
09/14/26	FL-2009	188	260	556.4	90	691	1071.3	146	148	354.5	234	919	1637.6	163	1119	1789.3
09/15/26	FL-2009	207	328	677.7	127	701	1138.9	146	170	388.2				172	1285	2046.2
09/16/26	FL-2009	190	282	597.8	124	941	1485.7	149	333	626.5				186	1218	1961.6
09/17/26	FL-2009	194	251	559.4	122	683	1113.2	155	167	394.7	249	1009	1780.8	160	1171	1855.4
09/18/26	FL-2009	177	376	710.4	160	688	1177.6	218	121	402.5	182	1141	1861.9	166	1044	1644.4
09/19/26	FL-2009	168	285	569.6	120	644	1056.3	132	156	352.9	94	1111	1541.4	165	956	1536.7
09/20/26	FL-2009	142	364	658.2	130	628	1061.0	144	169	388.4	186	1087	1814.6	177	1023	1648.6
09/21/26	FL-2009	202	351	712.8	135	674	1115.6	137	152	358.0	171	914	1533.1	209	1105	1813.3
09/22/26	FL-2009	194	278	599.9	151	667	1143.8	139	137	343.6	172	958	1617.1	166	931	1504.0
09/23/26	FL-2009	192	298	609.2	157	656	1114.9	111	176	353.7	168	924	1556.6	145	815	1308.9
09/24/26	FL-2009	185	276	582.0	164	712	1221.0	122	202	405.8	149	958	1581.5	145	889	1421.3
09/25/26	FL-2009	203	296	639.7	158	721	1236.1	104	228	429.3				198	1024	1680.0
09/26/26	FL-2009	194	280	592.5	161	716	1190.0	119	312	537.3				195	960	1569.7
09/27/26	FL-2009	182	237	527.2	165	663	1139.7	136	223	430.4	168	790	1365.6	220	1012	1676.4
09/28/26	FL-2009	175	320	636.2	165	777	1298.2	159	226	472.1				186	959	1569.9
09/29/26	FL-1995	128	385	662.5	118	793	1258.0	172	224	475.3				212	1122	1879.5
09/30/26	FL-1995	142	379	674.1	153	831	1374.4	171	211	463.5				223	1218	2035.2

*Flare 1 is FL-1995, Flare 2 is FL-2009, and Flare 3 is FL-2023
Notes:
Draeger Tube readings no longer required as of June 4, 2026 SOFA revision.
Zeeco TOx No. 7 was offline on 9/6/26 to 9/7/26 due to restart failure after routine meter cleaning and on 9/10/26 to prepare surface for TOx stack.
Parnel TOx ran intermittently between 9/15/26 and 9/30/26 due to flame failure; please note that as of 9/30/26, Parnel TOx will be used as an emergency backup device, so it will continue to operate intermittently.

Los análisis de laboratorio resumidos arriba están incluidos en el **Adjunto A** y en el **Adjunto F.**

Sección B - Registros y Cálculos de LFG

Los registros y cálculos de biogás identificados en la Condición No. 7 en un formato de planilla de cálculo en Microsoft Excel. Si los registros de biogás indican que algún equipo de combustión/control de biogás (antorchas u oxidantes térmicos) está fuera de línea por un período que excede los 7 días calendario consecutivos o por más de 15 días calendario en cualquier mes calendario, el Demandado deberá informarlo proporcionando una descripción detallada de los motivos por los que el equipo estuvo fuera de línea (rotura del equipo, mantenimiento, construcción, si hubo suficiente redundancia de control de biogás para controlar el biogás recolectado, etc.).

Condición No. 7: El Demandado deberá mantener un registro de la siguiente información y proporcionarle estos registros al AQMD de la Costa Sur conforme a la Condición No. 8:

a. El flujo de biogás por hora y por día incinerado, en pies cúbicos estándar, en cada antorcha (antorchas No. 1 y No. 2 bajo el Permiso G73696, A/N 645450; antorcha No. 3 bajo A/N 624296), el oxidante térmico/las antorchas y cualquier otro equipo usado para quemar o controlar biogás en las instalaciones, como también la cantidad total de biogás incinerado en las instalaciones;

b. El flujo diario de biogás no quemado en antorchas, en pies cúbicos estándar, si corresponde; y

c. Los resultados de las lecturas de azufre, las tomas de muestras y los análisis calculados como H2S con la hora y fecha en la que se tomó cada medición o en la que se tomó cada muestra; y

d. Los resultados de las calificaciones diarias del calor del gas, con la hora y fecha de cada muestra tomada, la ubicación de la toma de muestra y el tipo de gas del que se tomaron muestras (ej. biogás, mezcla de vapores de biogás y lixiviados).

Se han implementado los requerimientos revisados establecidos en la Condición 7 de la SOFA, modificada el 4 de junio de 2026, y se tratan en este informe que abarca septiembre de 2026.

Para el período de septiembre de 2026, los análisis de laboratorio arriba mencionados requeridos por la Condición 7(c) están incluidos en el **Adjunto A** y los cálculos están disponibles en el **Adjunto B**.

Conforme a la Condición 7(a), los índices de flujo de cada antorcha como pies cúbicos estándar (scf) por minuto, scf por hora y scf por día se indican en las tablas de los cálculos y el flujo por hora y por día de LFG incinerado para los TOx Zeeco (que ahora incluyen los nuevos dispositivos Zeeco 1 y Zeeco 6, además del Zeeco 7 existente), el TOx Parnel y el TOx Hero están disponibles en el **Adjunto B**.

Conforme a la Condición 7(b), el flujo diario de LFG sin quemar se encuentra en el **Adjunto B**. La Planta de Ameresco estuvo fuera de línea todo el mes y cada una de las antorchas experimentó períodos de inactividad en varios días; no hubo días que incluyeran excesos de emisiones de LFG no quemado, como se muestra en el **Adjunto B**. La Planta de Ameresco ha estado fuera de línea desde el 31 de enero de 2024, ya que Ameresco determina la disposición correcta

de su condensado. Ningún equipo de combustión/control de biogás estuvo fuera de línea por un período que exceda los 7 días calendario consecutivos ni por más de 15 días calendario en septiembre de 2026.

Sección C - Monitoreo de las Emisiones en la Superficie

El análisis integrado de la muestra de la superficie del vertedero y las lecturas de los monitoreos de la superficie del vertedero identificados en las Condiciones No. 9 y 10, en un formato de planilla de cálculo en Microsoft Excel.

Condición No. 9: El Demandado deberá tomar muestras integradas de la superficie del vertedero para analizarlas en toda la Zona de Mitigación de Reacciones (como se define en la Condición 9(a)) por lo menos tres veces al mes, en intervalos de no más de una vez cada 7 días (a menos que se conduzcan otros eventos de monitoreo que excedan las tres veces por mes) y además en todo el resto del vertedero, por lo menos cuatro veces por trimestre, como se especifica en la Regla 1150.1, Adjunto A 2.0. En el caso de que el Demandado no pueda tomar muestras en áreas o cuadrículas específicas de la superficie del vertedero debido a que no son accesibles o a condiciones peligrosas para un técnico, el Demandado deberá documentar la fecha y las condiciones que no permiten la toma de muestras en las áreas o cuadrículas específicas. La documentación deberá ser suficiente para demostrar la inaccesibilidad o las condiciones peligrosas y podrá incluir pronósticos climáticos y mediciones de lluvias reales o fotografías y/o videos que exhiban las condiciones del sitio que no permitan que se realicen estas actividades de toma de muestras en cada área o cuadrícula específica afectada.

a. *La "Zona de Mitigación de Reacciones" deberá definirse inicialmente con los límites de las Celdas 1/2A, 2B/3, 4 y el Módulo 2B/3/4 P2. El límite de la Zona de Mitigación de Reacciones deberá modificarse para incluir además todas las cuadrículas de las superficies del vertedero identificadas en 9(b) que estén fuera de las celdas dentro de los módulos/las celdas indicadas arriba. El Demandado deberá transmitirle al AQMD de la Costa Sur [att.: Baitong Chen, bchen@aqmd.gov; Nathaniel Dickel, ndickel@aqmd.gov; Christina Ojeda, cojeda@aqmd.gov]: el mapa revisado que exhiba claramente los cambios propuestos en los límites y muestre la nueva Zona de Mitigación de Reacciones.*

b. *El Demandado revisará los datos aplicables para determinar el alcance y el límite de la Zona de Mitigación de Reacciones. El Demandado considerará la revisión de este límite de la Zona de Mitigación de Reacciones determinado por datos con la frecuencia que sea apropiada, pero deberá tomar una determinación sobre el límite de la Zona de Mitigación de Reacciones determinado por datos y la Zona de Mitigación de Reacciones de la Condición 9(a) por lo menos una vez por mes. La*

determinación debe realizarse mediante la revisión de los parámetros a continuación, que indican que hay reacción:

1. *Temperaturas de los pozos verticales de biogás (mayores a 160 grados Fahrenheit),*
2. *Mediciones de sondas de temperatura (mayores a 170 grados Fahrenheit por más de 3 semanas en cualquier profundidad),*
3. *Calidad del biogás y relación metano-CO2 (niveles de metano de menos del 30 por ciento junto con relaciones de metano-CO2 menores a 1.0),*
4. *Concentración de monóxido de carbono en el biogás (mayor a 1,500 ppm), hasta donde se mide,*
5. *Concentración de hidrógeno en el biogás (mayor al 2 por ciento en volumen), hasta donde se mide,*
6. *Asentamiento del vertedero (18 pulgadas o más dentro de un período de 60 días),*
7. *Liberaciones de lixiviados presurizados.*

Condición No. 10: El Demandado deberá realizar un monitoreo instantáneo de la superficie del vertedero en toda la Zona de Mitigación de Reacciones (como se define en la Condición 9(a)) por lo menos tres veces al mes, en intervalos de no más de una vez cada 7 días (a menos que se conduzcan otros eventos de monitoreo que excedan las tres veces por mes) y además en todo el resto del vertedero, por lo menos cuatro veces por trimestre, como se especifica en la Regla 1150.1, Adjunto A 3.0, comenzando a más tardar siete (7) días después de emitida esta Orden. En el caso de que el Demandado no pueda monitorear en áreas o cuadrículas específicas de la superficie del vertedero debido a que no son accesibles o a condiciones peligrosas para un técnico, el Demandado deberá documentar la fecha y las condiciones que no permiten el monitoreo de las áreas o cuadrículas específicas.

Se han implementado los requerimientos revisados establecidos en la Condición 9 de la SOFA, modificada el 4 de junio de 2026, y se tratan en este informe que abarca septiembre de 2026.

- La toma de muestras integrada de la superficie del vertedero de septiembre se completó el 8, 9, 14, 15, 16, 17, 18, 28 y 29 de septiembre de 2026, dando como resultado excesos el 8, 9, 14 y 29 de septiembre de 2026.
    - El 16 de septiembre de 2026 se completaron la Acción Correctiva de 10 días y el monitoreo de seguimiento para los excesos del 8 y 9 de septiembre de 2026 y se obtuvieron lecturas en cumplimiento.
    - El 21 de septiembre de 2026 se completaron la Acción Correctiva de 10 días y el monitoreo de seguimiento para los excesos del 14 de septiembre de 2026 y se obtuvieron lecturas en cumplimiento.
    - El 8 de octubre de 2026 se completaron la Acción Correctiva de 10 días y el monitoreo de seguimiento para la excedencia del 29 de septiembre de 2026 y se obtuvieron lecturas en cumplimiento.

- El monitoreo instantáneo de la superficie del vertedero de septiembre se condujo el 1, 2, 3, 9, 10 y 21 de septiembre de 2026, dando como resultado excesos el 1, 2, 9, 10 y 21 de septiembre de 2026.
    - El 11 de septiembre de 2026 se completaron la Acción Correctiva de 10 días y el monitoreo de seguimiento para los excesos del 1 y 2 de septiembre de 2026 y se obtuvieron lecturas en cumplimiento.
    - El 16 de septiembre de 2026 se completaron la Acción Correctiva de 10 días y el monitoreo de seguimiento para los excesos del 9 y 10 de septiembre de 2026, y se obtuvieron lecturas en cumplimiento.
    - El 28 de septiembre de 2026 se completaron la Acción Correctiva de 10 días y el monitoreo de seguimiento para los excesos del 21 de septiembre de 2026 y se obtuvieron lecturas en cumplimiento.
    - Los eventos de remonitoreo de 1 mes para las excedencias del 17, 18 y 24 de agosto y 1 y 2 de septiembre de 2026 se realizaron el 16, 21 y 28 de septiembre de 2026 e indicaron lecturas en cumplimiento.

El análisis de las muestras integradas de la superficie del vertedero y las lecturas del monitoreo de la superficie del vertedero se incluyen en el **Adjunto C-1**.

Incluir en el informe mensual de la Condición 8 los tres (3) mapas de vigilancia aérea, las mediciones y las ubicaciones de las inspecciones de campo de seguimiento con las fechas/horas asociadas, la causa de las excedencias (500 ppmv de metano o superior), cualquier acción correctiva realizada y la documentación (fecha, hora, razonamiento) de las inspecciones de campo no realizadas debido a la falta de accesibilidad o a condiciones peligrosas identificadas en la Condición 77.

Se están implementando los requerimientos revisados establecidos en la Condición 77 de la SOFA, modificada el 4 de junio de 2026, y se tratan en este informe que abarca septiembre de 2026.

El contratista de Chiquita realizó una vigilancia aérea semanal sobre la superficie del Cañón Principal el 1, 9, 16, 22 y 30 de septiembre y el 1 de octubre de 2026, empleando un dron equipado con sensores con un nivel de detección mínimo de 1 ppmv de metano y conforme a OTM-51. Si una lectura alcanzó o excedió los 200 ppmv de metano, el consultor condujo inspecciones de seguimiento de campo para monitorear las emisiones de la superficie sobre el suelo, conforme a los procedimientos de OTM-51 y al Método 21 de la EPA de EE.UU. Si se descubrió o se confirmó alguna excedencia de 500 ppmv de metano durante la inspección de seguimiento, Chiquita implementó acciones correctivas conforme a la Condición 77. El **Apéndice C-2** incluye: una narrativa que analiza las lecturas registradas en septiembre; mapas geoespaciales de metano interpolado, con códigos de colores, que exhiben los resultados con los valores absolutos de las lecturas de metano; mapas geoespaciales de metano interpolado, con códigos de colores, que exhiben el cambio en las lecturas de metano comparadas con la vigilancia aérea previa; mapas que exhiben las coordenadas de la geoubicación con picos de metano locales y verificación de picos de seguimiento en el suelo; un mapa que exhibe la ruta de vuelo del dron; registros de las inspecciones de campo de seguimiento con mediciones y ubicaciones de las mediciones con las fechas y horas asociadas; y un cuadro que describe

las causas de las excedencias de 500 ppm de metano o mayores, como también las acciones correctivas realizadas para las lecturas registradas en septiembre de 2026.

Sección D - Temperaturas de Entrada de LFGTS

> *El Demandado deberá monitorear y registrar la temperatura del biogás por lo menos una vez al día en la entrada del Sistema de Tratamiento de Biogás. La temperatura de biogás no debe exceder los 145 °F.*

Se monitorearon las temperaturas de entrada del Sistema de Tratamiento de Biogás (LFGTS) conforme a la Condición 3(a) y han estado por debajo de los 145 °F. Las temperaturas de entrada diarias de los depósitos se registran manualmente y están disponibles en el **Adjunto D**.

Sección E - Reservada; modificada según la modificación de la SOFA del 4 de junio de 2026

Sección F - Reservada; modificada según la modificación de la SOFA del 4 de junio de 2026

Sección G - Mediciones de Temperatura y de Gas en el Cabezal del Pozo

> Todas las mediciones de temperatura de cabezales de pozos, de sondas de temperatura y de concentraciones de CO de los pozos que requieren datos analíticos, mediciones de concentración de H2 de los pozos que requieren datos analíticos, mediciones de CH4, mediciones de O2, mediciones de CO2, relaciones de CH4:CO2, análisis de laboratorio y lecturas de tubos Draeger de biogás del mes pasado en formato de hoja de cálculo en Microsoft Excel. Desde el informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá dejar de incluir esta información en los informes mensuales, excepto todos los análisis de laboratorio del biogás del mes anterior, que el Demandado continuará proporcionando en un formato de planilla en Microsoft Excel.

Las lecturas de temperatura del cabezal del pozo, de la sonda de temperatura, de CO, H2, CH4, O2, CO2 requeridas con las relaciones de CH4:CO2 del último mes se incluyen en el **Adjunto E**. Los análisis de laboratorio del último mes están incluidos en el **Adjunto A** y en el **Adjunto F**, respectivamente.

Se instalaron las 20 sondas de monitoreo de temperatura originales (TP-1 a TP-20) y otras 20 sondas de monitoreo de temperatura adicionales (TP-21 a TP-40) y están operativas desde febrero de 2026. Los datos promedio diarios de las sondas de temperatura del último mes están incluidos en el **Adjunto E**.

Chiquita presentó una solicitud de aprobación escrita del AQMD de la Costa Sur para dejar de incluir esta información en sus informes mensuales de la Condición 8, como lo autoriza la Condición 8(g). El AQMD de la Costa Sur ya puede acceder a la información a través de las plataformas eTools y RMC de SCS y SCS previamente le proporcionó a la agencia instrucciones para que pueda acceder a la información de forma independiente en cualquier momento. Mientras esté pendiente la aprobación por escrito, Chiquita continuará incluyendo la información necesaria en sus informes mensuales.

Sección H - Mapa Gráfico

> Un mapa gráfico que muestre la ubicación de cada pozo con excedencias de temperatura (por encima de los 145 grados Fahrenheit), mediciones de CO de cada pozo (por encima de los 1,000 ppmv y menor o igual a 1,500 ppmv, por encima de los 1,500 ppmv y menor o igual a 2,000 ppmv y por encima de los

2,000 ppmv) y estratificación de los rangos de temperatura durante ese mes, que incluye una descripción de las medidas de remediación tomadas para tratar o reducir las temperaturas de los pozos y las concentraciones de gas. A partir del informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá quitar estos datos de los informes mensuales.

Se incluyen mapas gráficos con la información previamente mencionada en el **Adjunto G**. Chiquita continúa implementando medidas correctivas para extraer de forma consistente biogás y lixiviados de pozos que exhiben temperaturas elevadas dentro de la Zona de Mitigación de Reacciones para facilitar la remoción de calor acumulado de la masa de desechos.

Chiquita presentó una solicitud de aprobación escrita del AQMD de la Costa Sur para dejar de incluir esta información en sus informes mensuales de la Condición 8, como lo autoriza la Condición 8(h). El AQMD de la Costa Sur ya puede acceder a la información a través de las plataformas eTools y RMC de SCS y SCS previamente le proporcionó a la agencia instrucciones para que pueda acceder a la información de forma independiente en cualquier momento. Mientras esté pendiente la aprobación por escrito, Chiquita continuará incluyendo la información necesaria en sus informes mensuales.

Sección I - Estado de los Pozos Verticales de Biogás Impactados con Líquidos

Todos los pozos verticales de biogás impactados con líquidos, según la Condición No. 17, incluyendo una descripción de las medidas de remediación tomadas para tratar o reducir líquidos en pozos de biogás.

Condición No. 17: El Demandado deberá desagotar inmediatamente los pozos que son impactados con líquidos lo máximo posible y deberá tomar medidas proactivas para remover otros líquidos de la Zona de Mitigación de Reacciones, para limitar la gravedad de la reacción y su propagación. Esto deberá lograrse mediante la instalación de sumideros/bombas de desagüe en por lo menos el 60 por ciento de los pozos verticales de extracción de biogás en la Zona de Mitigación de Reacciones (como se define en la Condición 9(a)) que sean capaces de extraer líquidos antes del 15 de marzo de 2024, a menos que se determine que no es viable, según la Condición No. 17(a) indicada a continuación. El Demandado deberá proporcionar actualizaciones en los informes mensuales, conforme a la Condición No. 8.

a. En el caso de que el Demandado determine que la instalación de pozos de desagote que sean capaces de extraer líquidos sea inviable, el Demandado deberá proporcionar una justificación y un razonamiento detallados en el informe mensual presentado conforme a la Condición No. 8 y deberá continuar con la implementación de las pautas para desagotes en cumplimiento con la Condición No. 18, para remover líquidos lo máximo posible.

En septiembre de 2026, Chiquita continuó la instalación y operación de bombas en pozos de extracción vertical para desagotar pozos afectados por líquidos de forma expeditiva. Al 1 de octubre de 2026, Chiquita había completado la instalación y estaba operando 193 bombas en pozos verticales de extracción. Este número no incluye las bombas adicionales que operan en sumideros perimetrales. Chiquita además continuó limpiando y realizando el mantenimiento de las bombas ya instaladas.

Sección J - Estado de la Investigación de Sistemas de Tratamiento de Compuestos de Azufre Alternativos

Desde el informe presentado el 20 de octubre de 2026, actualizaciones de la investigación sobre la disponibilidad, la viabilidad y la factibilidad de los equipos de control de SOx post combustión, que incluyen actualizaciones sobre la investigación, el informe y el posterior diseño y progreso de la instalación y los plazos, en cumplimiento con la Condición 3(c).

El sitio no tiene actualizaciones sobre el diseño previo a la combustión y está trabajando en el diseño post combustión.

Sección K - Mejoras Implementadas por SCS

Un informe resumido de las mejoras implementadas en el sistema de recolección de biogás por el Demandado más allá de los agregados al sistema de recolección de biogás requeridos según la Condición No. 15 y 8(m).

Además de la instalación de la bomba, Chiquita comenzó a perforar pozos nuevos y de reemplazo y continuó la expansión de los cabezales y los laterales y la infraestructura de recolección de lixiviados en septiembre de 2026 incluyendo la optimización de las unidades TOx. En el mes de septiembre de 2026, el Sitio perforó e instaló 6 pozos de LFG nuevos.

Sección L - Inspecciones de Cubiertas del Sistema de Recolección de LFG

Un registro de inspecciones de cubiertas del vertedero e inspecciones de las cubiertas geosintéticas, conforme a la Condición No. 30.

> *Condición No. 30: El Demandado deberá inspeccionar visualmente la cubierta del vertedero y las cubiertas geosintéticas en y alrededor de la Zona de Mitigación de Reacciones (como se define en la Condición 9(a)) en cada día operativo y deberá reparar inmediatamente cualquier problema identificado en la cubierta, que podrá incluir agregar y esparcir tierra limpia, humedecer, volver a compactar el área dañada y reparar o volver a sellar la cubierta geosintética. Las reparaciones de la cubierta geosintética que incluyen el agregado de material para sumar o reemplazar la cubierta existente deben realizarse utilizando un EVOH, o si no hay EVOH disponible y la reparación se realiza dentro o antes de los tres meses desde la fecha en la que el DTSC aprueba el EVOH, una geomembrana de HDPE. El EVOH o la geomembrana de HDPE deben tener un espesor de por lo menos 60 milésimas de pulgada, con costuras continuas y soldada de forma continua a la geomembrana de HDPE de 30 milésimas de pulgada existente. Todas las acciones de reparación y corrección en la cubierta del vertedero y la reparación intermedia de la cubierta geosintética se realizarán de inmediato y a más tardar dos horas después de que se identifiquen durante la inspección, si lo permite la seguridad. Deberá programarse inmediatamente la reparación permanente de la cubierta geosintética y deberá hacerse lo antes posible después de la identificación del problema en la cubierta. El Demandado deberá mantener un registro que demuestre que ha tratado todos los daños de la cubierta del vertedero o en la cubierta geosintética, que incluya la fecha en la que se identificó el daño, la acción tomada para reparar el daño y la hora a la que se completó la reparación. Los resultados de la inspección diaria y el registro de reparaciones requerido por esta condición deben incluirse en los informes mensuales requeridos conforme a la Condición No. 8.*

Se realizaron y registraron las inspecciones de rutina y las reparaciones, según la necesidad, en las cubiertas del vertedero y en las cubiertas geosintéticas durante todo el mes de septiembre de 2026. Los resultados de las inspecciones diarias y de los registros de reparaciones se proporcionan en el **Adjunto H**.

Sección M - Posteriores Agregados al Sistema de Recolección de LFG

Cualquier agregado posterior al sistema de recolección de biogás, según la Condición No. 15; un mapa del pozo de extracción vertical actualizado detallando todos los pozos existentes de extracción vertical que están operando de forma completamente funcional y los pozos de extracción vertical agregados dentro del mes; un mapa que muestre una superposición de los pozos completamente operativos y de las cuadrículas de monitoreo de la superficie del vertedero, y los contornos de las áreas demarcadas como exentas en el Anexo A adjunto, conforme a la Condición 15(b); copias de los registros de pozos conforme a obra (en lo relacionado a las instalaciones y actualizaciones en las profundidades de los pozos) de extracción vertical completados dentro del mes; y un mapa o plano actualizado de la infraestructura de recolección y transporte de biogás conforme a obra, actualizado con respecto a cualquier modificación sustancial en los cabezales principales del sistema de recolección y control de biogás, con los límites de la Zona de Mitigación de Reacciones; una tabla en formato Microsoft Excel que detalle los códigos de identificación de los pozos de extracción vertical, las fechas de instalación, la profundidad de la perforación deseada y/o requerida en cumplimiento con la Condición 15(b), la profundidad de perforación alcanzada, si el pozo tiene una bomba de desagote y, hasta donde sea posible, las lecturas de los niveles de líquido más recientes (fecha, hora, valores); y un mapa que muestre el campo de pozos según el plano, con indicación visual de los pozos que están y que no están en las profundidades deseadas.

> *Condición No. 15: El Demandado deberá continuar evaluando e instalando, según la necesidad, pozos verticales de extracción doble, para recolectar tanto biogás como lixiviados. Los agregados posteriores al campo de pozos deben ser documentados en los informes mensuales, conforme a la Condición 8. Al instalar pozos adicionales, el Demandado deberá asegurarse de que cumplen con todas las condiciones del permiso para sistemas de recolección de biogás actualmente operativos del Demandado. Al instalar otros pozos conforme a esta Condición, el Demandado además deberá tomar las siguientes medidas: (…)*
>
> *(d): Después de la instalación de todos los pozos en cumplimiento con la Condición 15(b), el Demandado deberá informarle por escrito al AQMD de la Costa Sur [atn.: Baitong Chen, Ingeniero de la Calidad del Aire, (bchen@aqmd.gov); Nathaniel Dickel, Ingeniero Sénior de la Calidad del Aire, (ndickel@aqmd.gov), y Christina Ojeda, Inspectora de la Calidad del Aire, (cojeda@aqmd.gov)] por lo menos una (1) semana antes cuando se vaya a instalar otro pozo o conjunto de pozos y sus tuberías asociadas. Deberán proporcionarse al AQMD de la Costa Sur en este aviso anticipado, el volumen de recolección de gas estimado, las profundidades de los pozos, las longitudes de las tuberías, los diámetros y los diseños, hasta donde se conozcan. Deben proporcionarse actualizaciones en el diseño y el programa en el informe mensual, en cumplimiento con la Condición No. 8(m); (…)*

En el mes de septiembre de 2026 se instalaron pozos nuevos de extracción vertical de LFG dentro o fuera de la Zona de Mitigación de Reacciones 9(a). En el **Adjunto I** se incluyen un mapa de todos los pozos funcionales instalados, cuadrículas de monitoreo de la superficie y los contornos de las áreas demarcadas como exentas. Se está presentando una planilla de cálculo en Excel rotulada 'Liquid Level Report – CCL September 2026' (Informe sobre el Nivel de Líquido - CCL septiembre de 2026) junto a este informe. Los posteriores agregados al sistema serán documentados en estos informes mensuales. Chiquita ha completado la instalación de un total de 252 pozos dentro de la Zona Reactiva inicial definida en la Condición 9(a), al 30 de septiembre de 2026, llevando la cantidad total de pozos instalados dentro de la Zona Reactiva 9(a) a una cantidad mayor a la densidad requerida de tres (3) pozos por acre (equivalente al 107%).

> *Condición No. 15(o): El Demandado deberá determinar todos los meses si alguno de los pozos de recolección de biogás existentes en la Zona de Mitigación de Reacciones (definida en la Condición 9(a)), que no se pudieron perforar e instalar a la profundidad del pozo deseada (generalmente aproximadamente 30 pies por encima del revestimiento inferior), puede ampliarse a una mayor profundidad o perforarse para alcanzar la profundidad deseada inicialmente o si pueden perforarse cerca pozos de reemplazo nuevos para alcanzar la profundidad deseada inicialmente. Esta determinación deberá incluir una evaluación de las condiciones del pozo/perforación de biogás, los datos del flujo de líquidos/lixiviados del vertedero, los datos de liberación de líquidos/lixiviados presurizados y los datos del biogás,*

los datos de la temperatura del cabezal del pozo, los datos de las sondas de temperatura y cualquier otro parámetro adicional que sea necesario. El Demandado deberá informar sobre la determinación mensual, junto con cualquier evidencia y razonamiento que respalde la determinación, como parte del informe mensual conforme a la Condición No. 8, comenzando con el informe presentado en octubre de 2024 que abarca datos de septiembre de 2024.

Chiquita revisó los datos de los niveles de líquidos de septiembre de 2026 de los pozos instalados dentro de la Zona Reactiva inicial 9(a) definida en la Condición 9(a) para determinar si alguno de los pozos que acaban de instalarse podría ampliarse a mayores profundidades. Se determinó que todos los pozos dentro de la Zona Reactiva inicial definida en la Condición 9(a) continúan siendo funcionales, con flujo de gas y líquido que indica que las perforaciones de los pozos están intactas. En base a los datos sobre los lixiviados, los datos de las sondas de monitoreo de temperatura y los datos de monitoreo de biogás, que incluyen datos de la temperatura, todos los pozos que están en la Zona Reactiva inicial definida en la Condición 9(a) se mantuvieron productivos. Mientras que los niveles de lixiviados dentro de los pozos se han reducido, ninguno de los pozos dentro de la Zona Reactiva inicial definida en la Condición 9(a) se había desagotado hasta un nivel que indique que los pozos más profundos eran necesarios para continuar extrayendo líquidos y biogás más profundos. Además, los niveles de líquido informados en el Informe de Niveles de Líquido reflejan niveles de líquidos dentro de los pozos individuales y no necesariamente son representativos de los niveles de líquido dentro del vertedero.

En el **Adjunto I** se proporciona un plano conforme a obra actualizado de la infraestructura de recolección y transporte de biogás. El plano conforme a obra adjunto muestra las ubicaciones de los pozos instalados al 30 de septiembre de 2026.

Sección N - Agregados al Sistema de Recolección de Condensado de LFG o Lixiviados

Cualquier agregado posterior al sistema de condensado de biogás o de recolección de lixiviados, como sumideros/bombas de desagüe u otros trabajos de desagote realizados según las pautas para desagote y el plan de implementación conforme a la Condición No. 18.

Condición No. 18(i). El Demandado deberá implementar las pautas de desagote revisadas, presentadas el 7 de junio de 2024. En el caso de que el AQMD de la Costa Sur proporcione algún comentario sobre las pautas de desagote revisadas o sobre cualquier pauta de desagote revisada posterior, el Demandado deberá incorporar los comentarios del AQMD de la Costa Sur y presentar al AQMD de la Costa Sur otras pautas de desagote revisadas o deberá proporcionar una justificación detallada indicando por qué no incorpora comentarios dentro de los 15 días desde que recibe los comentarios. Las pautas revisadas para el desagote deben implementarse al ser presentadas al AQMD de la Costa Sur. Las pautas para el desagüe de la Zona de Mitigación de Reacciones y los procedimientos de implementación propuestos deberán ser implementados hasta el máximo posible si el centro del Demandado está encontrando faltas en la capacidad y/o en la disposición de los tanques de lixiviados. Si existiera algún conflicto entre cualquier condición o requerimiento de esta Orden y de cualquier parte de las Pautas para el Desagote aprobadas por el AQMD de la Costa Sur, tendrá precedencia esta Orden sobre las Pautas para el Desagote aprobadas y el Demandado deberá presentar al AQMD de la Costa Sur las Pautas para el Desagote revisadas que resuelvan el conflicto para la aprobación escrita final.

Chiquita está implementando las pautas para el desagote revisadas presentadas al SCAQMD el 7 de junio de 2024, en cumplimiento con la Condición 18(i) de la SOFA, modificada el 4 de junio de 2026. Además, al 1 de octubre de 2026, Chiquita completó la instalación y estaba operando 193 bombas en pozos verticales de extracción. Este número no incluye las bombas adicionales que operan en sumideros perimetrales.

Chiquita también continuó limpiando y realizando el mantenimiento de las bombas que ya se habían instalado, para ayudar a que el sistema continúe funcionando de forma continua.

Sección O - Actualizaciones sobre la Cubierta Geosintética

Actualizaciones sobre la adquisición e instalación de cubiertas geosintéticas conforme a la Condición No. 31, incluyendo los cambios requeridos o aprobados por la Agencia de Cumplimiento Local.

Condición No. 31: El Demandado deberá incluir actualizaciones sobre la adquisición e instalación de la cubierta geosintética en los informes mensuales conforme a la Condición 8.

Al 31 de diciembre de 2024, Chiquita había instalado aproximadamente 44.6 acres de la cubierta geosintética original en el Vertedero, que completa la obra asociada al Objetivo 2A-1 de la Orden de Cumplimiento de la LEA emitida el 6 de junio de 2024. Además, al 3 de enero de 2025, se instalaron aproximadamente 1.3 acres de cubierta de geosintética sobre la zona de disposición, conforme al plan de trabajo de drenaje del talud oeste. El Informe de Terminación Final del Objetivo 2A-1 (Ex Medida de Mitigación #2A) se presentó el 17 de enero de 2025. La LEA, junto con el Departamento de Reciclaje y Recuperación de Recursos de California (CalRecycle), aprobó condicionalmente el Informe de Terminación Final el 9 de abril de 2025, con la condición de que Chiquita presentara un Plan de Operaciones y Mantenimiento. Chiquita presentó un Plan de Operaciones y Mantenimiento a la LEA el 9 de mayo de 2025 y un Plan de Operaciones y Mantenimiento modificado el 3 de octubre de 2025.

Además, al 2 de octubre de 2026, Chiquita había instalado aproximadamente 4,168,230 pies cuadrados de cubierta de geomembrana de EVOH/HDPE de 60 milésimas de pulgada, marrón. Chiquita también continuó realizando amplias reparaciones y detallando la cubierta de geomembrana de HDPE de 30 milésimas de pulgada existente utilizando la geomembrana de EVOH/HDPE de 60 milésimas de pulgada, que incluyó la fabricación de botas, parches, soldaduras por extrusión, costuras nuevas y colocación de bolsas de arena, según la necesidad.

Sección P - Actualizaciones de la Obra de Excavación del Vertedero Sujeta a la Regla 1150

Actualizaciones sobre el trabajo de excavación en el vertedero sujeto a la Regla 1150, incluyendo las ubicaciones de las excavaciones (identificadas en los mapas gráficos del vertedero) y características de los residuos excavados/expuestos (saturados, semisecos, secos, tipo e intensidad de olor, etc.). Los trabajos de excavación que ocurren conforme a una exención como lo indican la Regla 1150(c)(3) o la Regla 1150(c)(2) del AQMD de la Costa Sur que se realizan en la Zona de Mitigación de Reacciones también deben incluirse en estas actualizaciones.

Chiquita no realizó ninguna obra relacionada con el proyecto previo de excavación de la pendiente oeste o con el proyecto de terminación del drenaje del talud. Chiquita realizó una obra de excavación el 3 y 4 de septiembre de 2026 a lo largo de la calle de transporte principal del Vertedero para construir una zanja interceptora prevista para proporcionar una mayor infraestructura de recolección de biogás y lixiviados, como se describe en el aviso de excavación de la Regla 1150 de Chiquita, presentado al AQMD de la Costa Sur el 9 de septiembre de 2026. Chiquita también realizó obras de excavación del 30 de septiembre al 2 de octubre de 2026 en la zona del Parque de Tanques 10 para construir una zanja interceptora de lixiviados, como se describe en el aviso de excavación de la Regla 1150 de Chiquita presentado al AQMD de la Costa Sur el 7 de octubre de 2026.

.

Sección Q - Actualizaciones sobre los Lixiviados

Actualizaciones sobre los lixiviados, que incluyen:

Condición No. 27: El Demandado deberá realizar las siguientes acciones e informarlas al AQMD de la Costa Sur [Baitong Chen, Ingeniero de la Calidad del Aire, (bchen@aqmd.gov); Nathaniel Dickel, Ingeniero Sénior de la Calidad del Aire, (ndickel@aqmd.gov), y Christina Ojeda, Inspectora de la Calidad del Aire, (cojeda@aqmd.gov)] en el informe de cada mes presentado conforme a la Condición No. 8 comenzando con el informe que debe presentarse el 19 de febrero de 2024:

i. Registros de temperatura de lixiviados conforme a la Condición No. 27(a);

a. Medir y registrar la temperatura de lixiviados dentro de todos los tubos de lixiviados de 6 pulgadas que ingresan a los tanques de fractura en el sitio y en la cañería que va hacia los tanques de todos los parques de tanques. Las mediciones de temperatura informadas deben incluir un mapa que indique claramente las ubicaciones de monitoreo de temperatura y los resultados informados deben indicar claramente qué tanques o parques de tanques están flujo abajo de la ubicación de monitoreo que recibe los lixiviados medidos;

Los datos de las temperaturas de los lixiviados de los tubos de lixiviados que ingresan a los tanques de fractura en el sitio y a los tanques de todos los parques de tanques se tomaron el 29 de septiembre de 2026 y se incluyen en el **Adjunto J**.

ii. Registro diario de los hallazgos de las inspecciones y actividades de contención conforme a la Condición 27(b);

b. El Demandado debe contar con personal específico o con un contratista que conduzca y documente las inspecciones dos veces cada día calendario, una vez a la mañana, completando la inspección antes de las 10 am y una vez a la tarde, comenzando la inspección a partir de la 1 pm como muy temprano. Las inspecciones deben comenzar con la superficie de las pendientes occidental y norte de la Zona de Mitigación de Reacciones para filtraciones y acumulación de líquidos/lixiviados y además deberá consistir en una inspección de los canales de aguas pluviales de las instalaciones y las cuencas de aguas pluviales de las instalaciones. El Demandado deberá mantener registros de cada inspección, que incluyan los detalles de las filtraciones y acumulaciones de lixiviados, incluyendo las ubicaciones (identificadas en los mapas gráficos del vertedero con la cuadrícula del vertedero correspondiente y las coordenadas de GPS), el momento en que se descubrieron, la duración estimada de la presencia de lixiviados en esos lugares, las características del lixiviado (cantidad estimada en galones, alcance del área impactada en pies cuadrados, tipo de olor e intensidad), el nivel de saturación de lixiviados de los suelos en los alrededores (con líquido libre estancado, saturados, semisecos y secos) y sistemas o medidas de contención adicionales desplegados para dirigir, recolectar y contener los lixiviados expuestos y evitar una mayor exposición de los lixiviados;

i. En el caso de que dos semanas de inspecciones diarias realizadas dos veces al día demuestren que no hay filtración o acumulación de líquidos/lixiviados expuestos, el Demandado podrá reducir la frecuencia de las inspecciones a una vez al día. Si después de otras dos semanas de inspecciones diarias no se observan filtraciones o acumulación de líquidos/lixiviados expuestas, el Demandado podrá reducir la frecuencia de las inspecciones a un día por medio durante la semana operativa (es decir, tres veces por semana operativa). Si en

algún momento las inspecciones demuestran filtración o acumulación de líquidos/lixiviados expuestas, la frecuencia de las inspecciones deberá volver a inspecciones de dos veces al día. Las filtraciones o acumulaciones de líquidos/lixiviados cubiertas con membrana, u otra solución temporal a la filtración o acumulación en curso, que requiera intervención continua para exponer y recoger/bombear los líquidos mediante camión de vacío, deberán considerarse filtraciones o acumulaciones de líquidos/lixiviados expuestos y darán como resultado la inelegibilidad de esta frecuencia reducida en las inspecciones.

ii. *Todas las semanas, el personal del Demandado o el contratista deberá llevar a cabo y documentar una inspección ampliada sobre toda la zona del Cañón Principal para observar si hay filtraciones o acumulaciones de líquidos/lixiviados. En el caso de que dos semanas de inspecciones semanales demuestren que no hay filtración o acumulación de líquidos/lixiviados expuestos, el Demandado podrá reducir la frecuencia de las inspecciones a una semana por medio. Si en algún momento las inspecciones demuestran filtración o acumulación de líquidos/lixiviados expuestas, la frecuencia de las inspecciones deberá volver a ser de una vez por semana.*

iii. Registro semanal de filtraciones y acumulación de lixiviados conforme a la Condición 27(c);

c. Todas las semanas, compile e informe los detalles de los registros de inspección de esa semana calendario requeridos bajo la Condición 27(b). El Demandado además deberá informar sobre cualquier otra filtración o acumulación de líquidos/lixiviados que se encuentren, además de las condiciones indicadas en la Condición 27(b) y deberá informar todas las filtraciones y acumulaciones de lixiviados del vertedero que se descubra que han ocurrido en un lugar más de una vez dentro de la semana calendario, incluyendo las ubicaciones (identificadas en los mapas gráficos del vertedero), la duración estimada de la presencia de lixiviados en esos lugares, las características del lixiviado (cantidad estimada, alcance del área impactada, tipo de olor e intensidad), la saturación de lixiviados de los suelos en los alrededores (con líquido libre estancado, saturados, semisecos y secos), sistemas o medidas de contención desplegados para dirigir, recolectar y contener los lixiviados expuestos y evitar una mayor exposición de los lixiviados y soluciones propuestas para resolver las filtraciones o acumulaciones en curso (si corresponde). Antes del 23 de enero de 2024, el Demandado deberá entregarle al AQMD de la Costa Sur [Baitong Chen, Ingeniero de la Calidad del Aire, (bchen@aqmd.gov); Nathaniel Dickel, Ingeniero Sénior de la Calidad del Aire, (ndickel@aqmd.gov), y Christina Ojeda, Inspectora de la Calidad del Aire, (cojeda@aqmd.gov)], el primer informe semanal y deberá presentar otro informe semanal cada 7 días calendario posteriormente;

Los registros diarios de los hallazgos de las inspecciones y las actividades de contención, como también los informes semanales de filtraciones y acumulación de lixiviados requeridos por las Condiciones 27(b) y 27(c) están incluidos en el **Adjunto K**.

iv. Cantidad de lixiviados medidos y nombre de la empresa y dirección física relacionados de los centros de disposición/tratamiento fuera del sitio que reciben lixiviados generados por el vertedero, conforme a la Condición 27(d); y

d. Mida y registre las cantidades de lixiviados enviados fuera del sitio para su disposición/tratamiento durante la semana previa por todo el tiempo en el que se transporte todo el lixiviado fuera del sitio para su disposición. Los registros deben incluir el nombre de la empresa asociada

y la dirección física relacionados de los centros de disposición/tratamiento fuera del sitio que reciben lixiviados generados por el vertedero. Si el Demandado comienza un tratamiento en el sitio, deberá registrar todas las semanas las cantidades de lixiviados tomados y los lixiviados tratados en el sitio. El Demandado deberá reportar esta información en los informes mensuales, conforme a la Condición No. 8(c). El Demandado deberá presentar copias de los manifiestos al AQMD de la Costa Sur dentro de las tres semanas desde su solicitud.

La cantidad de lixiviados que se envía fuera del sitio para su disposición/tratamiento, el nombre de la empresa asociada y la dirección física de los centros de disposición/tratamiento fuera del sitio están incluidos en el **Adjunto L**. Chiquita comenzó a tratar lixiviados en el sitio en febrero de 2024. Los detalles sobre la cantidad de lixiviados tratados en el sitio también están incluidos en el **Adjunto L**. Chiquita está proporcionando esta información a su mejor saber y entender; esta información se encuentra sujeta a cambios en base a mayores revisiones y verificaciones.

v. Una lista de todas las instalaciones de almacenamiento y tratamiento de líquidos peligrosos y no peligrosos que se hayan contactado y el estado actual de cada una de las instalaciones, incluyendo la capacidad disponible, contratada y utilizada, para recibir líquidos del vertedero peligrosos y no peligrosos.

El cuadro a continuación proporciona una lista de cada una de las instalaciones de almacenamiento y tratamiento de líquidos peligrosos y no peligrosos contratadas y sus respectivas capacidades contratadas y máximas disponibles al 30 de septiembre de 2026. La capacidad disponible la establece el centro de almacenamiento y tratamiento y fluctúa día a día, sujeta a cambios y ajustes de las instalaciones. Chiquita utiliza toda la capacidad disponible por las instalaciones hasta el punto en que haya líquidos disponibles para disposición y hasta el punto en que sea viable para las instalaciones que lo reciben.

Nombre de las Instalaciones	Peligroso/No Peligroso*	Capacidad Contratada	Capacidad Máxima Disponible
Avalon**	No Peligroso	150,000 galones/día durante la semana (50,000 gal/día el sábado)	150,000 gal/día durante la semana (50,000 gal/día el sábado)
East Valley Remediation	No Peligroso	8 camiones/día (aprox. 45,000 galones/día); 6 días/semana	8 camiones/día (aprox. 45,000 galones/día); 6 días/semana
Clean Harbors – UT	Peligroso	2 camiones/día (aprox. 10,000 galones/día); 5 días/semana	2 camiones/día (aprox. 10,000 galones/día); 5 días/semana
Clean Harbors – NE***	Peligroso	4 camiones/día (aprox. 20,000 galones/día); 5 días/semana	4 camiones/día (aprox. 20,000 galones/día); 5 días/semana
Clean Harbors – TX****	Peligroso	3 vagones/semana (aprox. 60,000 galones/semana)	3 vagones/semana (aprox. 60,000 galones/semana)
Durham – Arizona	No Peligroso	Aprox. 80,000 galones/día 5 días/semana	Aprox. 80,000 galones/día 5 días/semana
Crystal Clean Wyoming	No Peligroso	7 vagones/semana (aprox. 140,000 galones/semana)	7 vagones/semana (aprox. 140,000 galones/semana)
Crystal Clean Bakersfield	No Peligroso	Aprox. 90,000 galones/día 6 días/semana	Aprox. 90,000 galones/día 6 días/semana

Nombre de las Instalaciones	Peligroso/No Peligroso*	Capacidad Contratada	Capacidad Máxima Disponible
Industrial Recycling, Baja	No Peligroso	10 camiones/día (aprox. 50,000 galones/día); 5 días/semana	10 camiones/día (aprox. 50,000 galones/día); 5 días/semana
ReWorld Advanced Processing	No Peligroso	3 vagones/ día (aprox. 60,000 galones/día); 5 días/semana	3 vagones/ día (aprox. 60,000 galones/día); 5 días/semana
Midway Environmental Services, Inc.	No Peligroso	3 vagones/ día (aprox. 60,000 galones/día); 6 días/semana	3 vagones/ día (aprox. 60,000 galones/día); 6 días/semana

* El 1 de septiembre de 2026, el DTSC aprobó la solicitud de Chiquita de tratar todos los líquidos característicamente peligrosos en el sitio. Por este motivo, a partir de septiembre, Chiquita comenzó a tratar todo el líquido característicamente peligroso en el sitio antes de su envío fuera del sitio. Chiquita actualmente anticipa que todos los líquidos enviados fuera del sitio serán característicamente no peligrosos después del tratamiento.

**Avalon Environmental Services (Avalon) continúa bajo contrato, pero debido a las contradicciones en las asignaciones de las agencias, entre los Distritos Sanitarios del Condado de LA, Obras Públicas y Planificación Regional, Avalon no ha podido aceptar envíos de lixiviados no peligrosos tratados de Chiquita de forma consistente por varios meses. Por lo tanto, la aceptación diaria total de Avalon continúa siendo significativamente reducida.

***Como se indicó previamente, Chiquita se enteró por Clean Harbors que Clean Harbors - Nebraska puede recibir y transferir líquido a Clean Harbors - Arkansas sin el conocimiento o la aprobación de Chiquita.

vi. Una actualización sobre la cantidad de tanques en cada grupo de tanques de lixiviados; la cantidad total de tanques de lixiviados tratados; la cantidad total mensual y en lo que va del año de líquido recogido; la cantidad total mensual y en lo que va del año de líquido tratado; y la cantidad total mensual y en lo que va del año de lixiviados de filtraciones, acumulaciones o estancamientos recogidos.

Según las Condiciones 8(q) y 53 de la Orden Estipulada, Chiquita proporciona la siguiente actualización para el mes de septiembre de 2026. Chiquita proporciona esta información a su mejor saber y entender; esta información se encuentra sujeta a cambios en base a mayores revisiones y verificaciones.

- **Cantidad de tanques en cada grupo de tanques de lixiviados.** Hubo aproximadamente 252 tanques de fraccionamiento de lixiviados en el Vertedero de Chiquita Canyon al 30 de septiembre de 2026, de la siguiente manera:

  Colector de Tanque de Cubierta Superior No. 1: 0
  Colector del Perímetro Este No. 2: 0
  Colector LC No. 4: 1
  Colector del Perímetro Norte No. 6: 0
  Parque de Tanques No. 7: 25
  Parque de Tanques No. 9: 0
  Cañón D No. 10: 37
  Parque de Tanques No. 13: 153
  Cañón Principal: 13
  Área de preparación, no está en uso: 22
  Necesita Reparación: 1

- **Cantidad total de tanques de lixiviados tratados.** Chiquita trató 351 tanques en septiembre de 2026. Chiquita trató 2,638 tanques desde el 17 de febrero de 2024 (el inicio del tratamiento) hasta el 31 de diciembre de 2024, 3,249 tanques desde el 1 de enero de 2025 hasta el 31 de diciembre de 2025 y 2,135 tanques desde el 1 de enero hasta el 30 de septiembre de 2026.

- **Cantidad total de líquidos recolectados mensualmente y en lo que va del año.** Chiquita estima que recogió aproximadamente 8,186,895 galones de líquido en septiembre de 2026 (sin contar el condensado de las antorchas). Chiquita estima que recogió aproximadamente 62,576,218 galones desde el 1 de enero de 2024 hasta el 31 de diciembre de 2024 (sin contar condensado de las antorchas), aproximadamente 101,384,450 galones del 1 de enero de 2025 al 31 de diciembre de 2025 y aproximadamente 77,200,894 galones desde el 1 de enero hasta el 30 de septiembre de 2026.

- **Cantidad total de líquidos tratados mensualmente y en lo que va del año.** Asumiendo 17,000 galones por tanque, Chiquita trató aproximadamente 5,969,993 galones en septiembre de 2026. Chiquita estima que trató aproximadamente 46,368,981 galones desde el 17 de febrero de 2024 (el inicio del tratamiento) hasta el 31 de diciembre de 2024, aproximadamente 54,795,437 galones desde el 1 de enero de 2025 hasta el 31 de diciembre de 2025 y aproximadamente 41,574,377 galones desde el 1 de enero hasta el 30 de septiembre de 2026.

- **Cantidad total mensual y en lo que va del año de filtraciones**, acumulaciones o encharcamientos de los lixiviados recolectados. Chiquita estima que se observaron y/o recogieron aproximadamente 70 galones de filtraciones, acumulaciones o encharcamientos de lixiviados en septiembre de 2026. Estas filtraciones se corrigieron como se describió en los informes semanales de inspecciones de lixiviados presentados en conformidad con la Condición 27(c) de la SOFA. El estimativo en lo que va del año desde el primer trimestre de 2024 hasta el 31 de diciembre de 2024 fue de aproximadamente 175,051 galones. El estimativo en lo que va del año desde el 1 de enero de 2025 hasta el 31 de diciembre de 2025 fue menor a 185 galones, incluyendo la filtración de 1-5 galones observada en la Cuadrícula 60. El estimativo en lo que va del año para el período del 1 de enero al 30 de septiembre de 2026 fue de 526,634 galones, que incluyeron el líquido extraído de la zona de contención asociada a la filtración informada previamente a lo largo de la pendiente oeste del vertedero. Para tratar esta filtración y en cumplimiento con la Carta de la Orden de Trabajo: RE: Obra Adicional Requerida por la UAO para Realizar Mejoras en el Talud Oeste, con fecha 17 de marzo de 2026, Chiquita completó el Proyecto de Apuntalamiento del Talud Oeste pero continúa realizando obras auxiliares a lo largo del talud oeste. Estos números se basan en las inspecciones de filtraciones/acumulaciones de lixiviados que realiza Chiquita dos veces al día y en los estimativos registrados de la cantidad de galones de filtraciones/acumulaciones

de lixiviados, como también en estimativos de aguas pluviales y lixiviados bombeados del canal de aguas pluviales represados durante eventos de tormenta a principios de este año. Esto sobreestima la cantidad de lixiviados observados y/o recogidos porque incluye estos eventos informados previamente donde las filtraciones de lixiviados ingresaron al canal y entraron en contacto con las aguas pluviales. Se debe tener en cuenta que el volumen de cualquier filtración/acumulación de lixiviados que se recoge también se captura en los totales arriba indicados, porque esos líquidos se transfieren a los tanques de fractura para su eventual disposición. También se debe tener en cuenta que Chiquita continúa informando fugas/derrames de lixiviados por separado, conforme a la Condición 27(e) de la Orden Estipulada.

Sección R - Capacidad Adecuada

Actualizaciones sobre la capacidad adecuada:

Condición No. 29. El Demandado deberá asegurarse de contar con la capacidad adecuada de lixiviados del vertedero y de condensado de biogás (en base a los informes de producción y recolección de líquidos, conforme a la Condición 8) para acumular en el sitio y/o disponer de los líquidos/lixiviados recogidos en un centro o centros apropiados.

Como se demostró arriba en la Sección Q, Chiquita cuenta con una capacidad adecuada para acumular en el sitio y/o disponer de los líquidos/lixiviados/condensados recogidos en instalaciones apropiadas.

Sección S - Datos de las Estaciones de Monitoreo

Actualizaciones sobre las estaciones de monitoreo de aire:

Condición No. 35. El Demandado debe proporcionar actualizaciones sobre todos los procedimientos operativos estándar (SOPs) y cualquier otro documento de Control de Calidad y Aseguramiento de la Calidad (QA/QC) presentado al AQMD de la Costa Sur el 19 de enero de 2024 que describa la operación y el mantenimiento de todos los instrumentos utilizados en las estaciones de monitoreo de aire y/o en las estaciones de monitoreo mejoradas especificadas en la Condición No. 34 (si hubiera) y un registro de calibración y actividades de mantenimiento realizadas en los monitores en los informes mensuales conforme a la Condición No. 8. (...)

No hubo actualizaciones ni cambios en los SOPs ni en otros documentos de QA/QC de Monitoreo del Aire durante el período de los informes. En septiembre de 2026 no hubo eventos de mantenimiento que hayan requerido planillas de datos de campo.

Sección T - Toma de Muestras de Carbono Orgánico Total (TOC) Durante Eventos de Molestias y Excavaciones

Conforme a la Condición No. 42(w), estos informes mensuales deben incluir lo siguiente:

Condición No. 42(w). Si el Demandado recibe un Aviso de Infracción por Molestias de la Regla 402 del AQMD de la Costa Sur durante la excavación o un olor distinto (nivel 3 o superior según la Escala de Olor a continuación) resultante de la excavación en o pasando la línea de la propiedad, el Demandado deberá, conforme a su Plan de Salud y Seguridad, tomar muestras de la calidad del aire del ambiente dentro de las 2 horas desde que se recibe el Aviso de Infracción por Molestias de la Regla 402 o cuando se detecta un olor distinto (nivel 3 o superior) en o pasando la línea de la propiedad y analizar los TOC y los TOCs especiados de la siguiente manera:

Escala de Olor	*Descripción de la Intensidad del Olor*
0	*No se detectó olor*
1	*Se detectó un olor muy leve*
2	*Se detectó un olor leve, distinguible*
3	*Olor moderado, muy distinguible*
4	*Olor fuerte, muy distinguible, irritable*
5	*Olor muy fuerte, muy distinguible, abrumador*

ii. Se deben tomar muestras en los siguientes lugares: inmediatamente a barlovento del sitio de la excavación, inmediatamente a sotavento del sitio de la excavación, dentro de las 3 pulgadas de la cara de trabajo de la excavación expuesta, si la seguridad lo permite, y en la línea de la propiedad a sotavento o en otros lugares aprobados por escrito por el AQMD de la Costa Sur. Si se considera inseguro, el Demandado deberá documentar la fecha y las condiciones que no permiten el cumplimiento de esta condición. Deberán presentarse registros de estas condiciones en el siguiente informe mensual, conforme a la Condición 8.

Durante el mes de septiembre de 2026, se realizó el monitoreo de la Condición 42(w) el 3 y 4 de septiembre de 2026.

Conforme a la Condición No. 42(x), estos informes mensuales también deben incluir lo siguiente:

Condición No. 42(x). Durante la excavación, deberán tomarse muestras de los TOC y de los TOC especiados en el aire ambiental por lo menos una vez entre las 6:00 am y las 11:00 am y por lo menos una vez entre las 2:00 pm y las 6:00 pm, según el Plan de Salud y Seguridad del Demandado y los siguientes requerimientos:

i. Se deben tomar muestras en los siguientes lugares: inmediatamente a barlovento del sitio de la excavación, inmediatamente a sotavento del sitio de la excavación, dentro de las 3 pulgadas de la cara de trabajo de la excavación expuesta, si la seguridad lo permite, y en la línea de la propiedad a sotavento o en otros lugares aprobados por escrito por el AQMD de la Costa Sur. Si se considera inseguro, el Demandado deberá documentar la fecha y las condiciones que no permiten el cumplimiento de esta condición. Deberán presentarse registros de estas condiciones en el siguiente informe mensual, conforme a la Condición 8.

Durante el mes de septiembre de 2026, se realizó el monitoreo de la Condición 42(x) el 3 y 4 de septiembre de 2026.

Los resultados de estos eventos de monitoreo se incluyen como

Sección U - Muestreo/Análisis de Condensados

Resultados de los registros de tomas de muestras/análisis de condensados:

Condición No. 55(g). El Demandado mantiene registros de muestras/resultados de análisis de condensados para demostrar que el líquido no es peligroso, mantiene registros de flujos de inyección de condensados diarios (galones por día) y proporciona estos registros en el informe mensual conforme a la Condición No. 8.

La inyección de condensados se registra en la estación de antorchas, pero actualmente está desconectada hasta que se analicen los condensados y se confirme que son no peligrosos. Por lo tanto, los flujos de inyección de condensados para septiembre de 2026 son de cero.

Sección V - Información de los Registros de Presión/Flujo de los Tanques de Lixiviados

Condición No. 68. El Demandado deberá instalar, a más tardar el 15 de junio de 2024, medidores de presión diferencial con rangos apropiados, con una resolución de por lo menos 0.01 pulgadas de columna de agua o un indicador de presión aprobado de otra manera por escrito por el AQMD de la Costa Sur, en cada tanque de almacenamiento de lixiviados. El Demandado deberá monitorear y registrar la presión diferencial diaria de cada tanque de lixiviados, el número de identificación del tanque, la fecha y hora de la lectura y el personal que realizó la lectura. Las lecturas de las presiones que indiquen el menor valor del medidor o el mayor valor del medidor deberán informarse utilizando dígitos significativos hasta las centésimas, como "<= [valor más bajo en el medidor] (ej. <= -0.50 pulgadas de columna de agua)" y ">= [valor más alto en el medidor] (ej. >= 0.50 pulgadas de columna de agua)", respectivamente. Los tanques deberán mantenerse bajo presión negativa, según lo demuestren las lecturas de la presión diferencial. Las lecturas de cero y presión positiva no demuestran una presión negativa. Los medidores de presión deben calibrarse en cumplimiento con las especificaciones del fabricante y el programa de calibración. El Demandado deberá informar todas las lecturas en el informe mensual, conforme a la Condición No. 8.

Como lo indica la Condición 68, Chiquita completó la instalación de medidores de presión diferencial en cada tanque de almacenamiento de lixiviados el 10 de julio de 2024, después de su solicitud de extensión del 12 de junio de 2024 y la posterior documentación de las demoras del fabricante para entregar los medidores de presión en el sitio. Después de la instalación, Chiquita experimentó complicaciones con respecto a la implementación. Como resultado, los registros comenzaron el 28 de agosto de 2024. Las lecturas del mes de septiembre de 2026 se incluyen como **Adjunto M**.

Condición No. 72. El Demandado deberá realizar la toma de muestras y análisis, las pruebas, la instalación y el monitoreo del sistema de recolección y tanques de almacenamiento de lixiviados y condensados de biogás, como se especifica a continuación:

A. Por lo menos cada seis meses, realizar pruebas para tomar muestras y analizar el flujo de vapor en las tuberías utilizadas para ventilar los tanques de almacenamiento de lixiviados y los tanques de condensado de biogás y dirigir los vapores al sistema de control de biogás. Las pruebas deberán incluir por lo menos los siguientes puntos y los resultados de estas pruebas deben proporcionarse en el informe mensual, en cumplimiento con la Condición No. 8:

- *i. índice de flujo de vapores de tanques de lixiviados ventilados,*
- *ii. índice de flujo de vapores de tanques de condensados ventilados,*
- *iii. temperatura del vapor,*
- *iv. concentraciones de orgánicos especiados (incluyen, de forma enunciativa más no limitativa, Contaminantes del Aire Carcinogénicos y Tóxicos de la Tabla 1 de la Regla 1150.1),*
- *v. los compuestos de azufre total como H2S y compuestos de azufre especiados, y*
- *vi. analizar en cada uno de los lugares indicados a continuación:*
  1. *Las ventilaciones o los colectores de los tanques que sean representativos de un set de tanques;*
  2. *El cabezal/colector de cada parque de tanques de lixiviados o colector que incluye el Parque de Tanques No. 7, el Parque de Tanques No. 9, el Colector del Perímetro Norte, el Nuevo Colector del Perímetro Este, el Colector LC, los tanques de almacenamiento de condensado de biogás y cualquier otro futuro parque de tanques o colectores, realizando las pruebas flujo arriba de la conexión de la tubería al Sistema de Recolección y Transporte de LFG donde el biogás*

pueda afectar los resultados; y

3. *La entrada de la(s) antorcha(s) antes de la combustión.*

B. *Deberá presentarse un protocolo de pruebas de origen al AQMD de la Costa Sur antes del 17 de mayo de 2024, a menos que el AQMD de la Costa Sur apruebe otra cosa por escrito. Las pruebas deberán realizarse dentro de los 45 días desde que se recibe la aprobación escrita del protocolo de prueba de origen por parte del AQMD de la Costa Sur y deberán presentarse los resultados finales en un formato de informe de prueba de origen dentro de los 30 días desde que se realizan las pruebas, a menos que el AQMD de la Costa Sur apruebe otra cosa por escrito.*

C. *[Completado].*

Se presentó al AQMD de la Costa Sur un *Plan de las Pruebas de Origen para la Toma de Muestras de Lixiviados y de Vapores Condensados* en nombre de Chiquita el 12 de julio de 2024, conforme a la Condición No. 72(b). El protocolo de la prueba de origen se presentó originalmente el 17 de mayo de 2024, pero fue revisado y reenviado el 12 de julio de 2024 para tratar dudas planteadas por el AQMD de la Costa Sur. El plan modificado fue aprobado el 6 de septiembre de 2024 y la prueba de origen se realizó el 17 de octubre de 2024. El informe final de la prueba de origen se presentó al AQMD de la Costa Sur el 15 de noviembre de 2024. La prueba de origen más reciente para el primer trimestre de 2026 la completó Montrose Environmental el 30 de marzo de 2026 y se informó al AQMD de la Costa Sur el 28 de abril de 2026. Se presentó una prueba de origen modificada al AQMD de la Costa Sur el 29 de junio de 2026. SCS recibió comentarios del AQMD de la Costa Sur el 23 de julio de 2026. SCS y Montrose revisaron el protocolo en respuesta a los comentarios del AQMD de la Costa Sur y presentaron un protocolo revisado el 30 de julio de 2026. SCS recibió los comentarios adicionales del AQMD de la Costa Sur el 2 de septiembre de 2026. SCS y Montrose revisaron en mayor profundidad el protocolo en respuesta a los comentarios adicionales del AQMD de la Costa Sur y presentaron un protocolo revisado el 9 de septiembre de 2026. SCS recibió los comentarios del AQMD de la Costa Sur el 16 de septiembre de 2026. SCS y Onterris revisaron el protocolo en respuesta a los comentarios del AQMD de la Costa Sur y presentaron un protocolo revisado el 28 de septiembre de 2026.

Sección W - Lecturas de la Composición del Biogás

Condición No. 8(r). Análisis diarios de la composición de los gases del vertedero, que incluyen CH4%, concentración de CO (ppm), CO2% y O2%, registrados por un analizador en tiempo real y/o muestras tomadas en las entradas de los equipos de control (TOx, Antorchas y equipos de control adicionales llevados al sitio para que hagan combustión con el biogás) en forma de Planilla de Cálculo en Microsoft Excel. Los análisis serán realizados por un analizador aprobado por el AQMD de la Costa Sur para CH4, CO2 u O2, y analizados conforme al Método 10 de la EPA de EE.UU. o el Método ALT-144 para CO. La solicitud de aprobación deberá incluir la presentación de las especificaciones de los analizadores. A partir del informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá quitar estos datos de los informes mensuales.

A partir del 28 de agosto de 2024, se solicitaron análisis adicionales para los TOx y las antorchas y los gases permanentes (CO2, O2 y N2) fueron analizados utilizando el método D1946 de ASTM y de CO utilizando el método de la EPA ALT-144. Los resultados analíticos están incluidos en el **Adjunto A**.

Chiquita presentó una solicitud de aprobación escrita del AQMD de la Costa Sur para dejar de incluir esta información en sus informes mensuales de la Condición 8, como lo autoriza la Condición 8(r). El AQMD de la Costa Sur ya puede acceder a la información a través de las plataformas eTools y RMC de SCS y SCS previamente le proporcionó a la agencia instrucciones para que pueda acceder a la información de forma independiente en cualquier momento. Mientras esté pendiente la aprobación por escrito, Chiquita continuará incluyendo la información necesaria en sus informes mensuales.

Sección X - Progreso de la Construcción de la Antorcha No. 4

Condición No. 74. El Demandado deberá acelerar la adquisición de los equipos necesarios para construir la Antorcha No. 4 lo máximo posible mientras que sea viable, de forma que la Antorcha No. 4 esté lista para ser construida y puesta en funcionamiento lo antes posible después de que el Demandado reciba todos los permisos y otras aprobaciones necesarios. El Demandado deberá proporcionar actualizaciones sobre la adquisición de estos equipos en el informe mensual conforme a la Condición 8(s).

Chiquita y SCS Engineers presentaron al AQMD el permiso para la Antorcha 4 en octubre de 2023). Chiquita y SCS Engineers iniciaron la adquisición de la Antorcha 4 a John Zink en enero de 2025.

El Sitio actualmente está avanzando para sacar los permisos, realizar las evaluaciones geotécnicas y diseñar los refinamientos asociados a la Antorcha 4. Además, se están evaluando modificaciones en la Antorcha 4 original para tratar los requerimientos actuales del sitio. John Zink entregó la Antorcha 4 y el módulo soplador al Sitio en julio de 2026. A septiembre de 2026, el Sitio continúa desarrollando el diseño de la Antorcha 4.

Sección Y - Seguimiento de Equipos en Varias Ubicaciones

Condición No. 80. Cuando se traigan o se operen en el sitio equipos con permiso de Varios Lugares del AQMD de la Costa Sur o equipos con permiso del Registro de Equipos Portátiles a Nivel Estatal (PERP) de CARB, el Demandado deberá:

a. *Informar al AQMD de la Costa Sur por escrito la fecha y hora en la que se trajeron los equipos a las instalaciones en el informe mensual correspondiente según la Condición No. 8 e incluir una copia de los permisos en los varios lugares y/o los permisos de PERP en el informe mensual correspondiente según la Condición No. 8.*

b. *Mantener un registro diario que incluya la siguiente información para cada unidad de permiso: número de permiso y/o número de registración, número de solicitud (si corresponde), ubicación de los equipos y hora de inicio y fin de la operación de los equipos (según corresponda). El Demandado deberá presentar el registro diario en el informe mensual correspondiente según la Condición No. 8.*

c. *Informar al AQMD de la Costa Sur por escrito la fecha y hora en la que se retiró el equipo del lugar, en el informe mensual correspondiente, según la Condición No. 8.*

El registro PERP para septiembre de 2026 y copias de los permisos relevantes, si corresponde, se proporcionan como **Adjunto N**.

Sección Z - Inspecciones Semanales de la Cubierta Geosintética

Condición No. 97. El Demandado debe inspeccionar visualmente todos los puntos de conexión, costuras y sellos de las cubiertas geosintéticas en y alrededor de la Zona de Mitigación de Reacciones (como la define la Condición No. 9(a)) por lo menos una vez cada siete (7) días calendario y deberá reparar inmediatamente cualquier problema identificado en la cubierta. El Demandado deberá mantener un registro que demuestre que completó cada inspección y que trató cualquier problema con cualquier punto de conexión, costura o sello de la cubierta geosintética, incluyendo la fecha en la que se identificó el problema, la acción tomada para reparar el daño y la hora en la que se completó la reparación. Los resultados de la inspección y el registro de reparaciones requerido por esta condición deben incluirse en los informes mensuales requeridos conforme a la Condición No. 8.

Chiquita inspecciona visualmente todos los puntos de conexión, las costuras y los sellos de la cubierta geosintética por lo menos una vez cada siete (7) días calendario, repara inmediatamente los problemas identificados en las cubiertas y mantiene un registro que demuestra que se completaron estas inspecciones y reparaciones, conforme a la Condición 97. Los registros semanales que detallan la inspección visual de los puntos de conexión, las costuras y los sellos de la cubierta geosintética en y alrededor de la Zona de Mitigación de Reacciones y las reparaciones de septiembre de 2026 se incluyen como **Adjunto O**.

Sección AA - Registros de Temperaturas Operativas y Tipos de Combustible Piloto/Combustible Complementario e Índices de Uso

Condición No. 104. El Demandado deberá contratar a John Zink y/o a otra empresa de diseño o instalación de equipos de combustión de biogás apropiada para que ayude a diseñar e instalar un sistema o varios sistemas de combustible complementarios (gas natural o propano), para que la operación pueda enriquecer el biogás, la mezcla de vapores de biogás/lixiviados y/o vapor de lixiviados controlados en las antorchas de biogás (antorchas 1, 2, 3, 4 y/o 5 como corresponda). El sistema debe diseñarse e instalarse de forma de asegurar que pueda enriquecerse el biogás, la mezcla de vapores de biogás/lixiviados y/o los vapores de lixiviados con poco contenido de metano, para permitir el funcionamiento continuo de las antorchas, el mantenimiento de la llama en los quemadores de las antorchas, un control suficiente del gas recogido y el mantenimiento de la temperatura de la pila de antorchas por encima de los 1400 grados Fahrenheit. El sistema debe ser utilizado por el Demandado, según la necesidad. Los sistemas deben incluir un registrador de flujo de combustible complementario y los registros de combustible deben presentarse en el informe mensual, en cumplimiento con la Condición 8(t). El Demandado deberá completar el diseño y la instalación, conforme a los siguientes plazos:

a. *Para el 31 de julio de 2026, proporcionar una confirmación escrita de los fabricantes existentes de las Antorchas 1, 2 y 3 sobre el contenido de metano mínimo en el biogás necesario para asegurar la eficiencia de destrucción del metano y de los NMOC, conforme a los requerimientos reglamentarios. El contenido mínimo más alto de estas tres antorchas debe proporcionar el contenido mínimo requerido para la Condición 106(c) a continuación.*
b. *Para el 31 de julio de 2026, proporcionar documentación escrita de un instalador calificado indicando los plazos propuestos (lo más rápido posible) para instalar sistemas de combustible complementarios.*
c. *Si los datos recopilados por el Demandado dan como resultado un contenido de metano semanal promedio en el gas combinado que se dirige a las Antorchas 1, 2 y 3 dentro de 2.5 puntos porcentuales del contenido mínimo requerido conforme a la Condición 104(a), el Demandado deberá comenzar la instalación de los sistemas complementarios de combustible según los plazos establecidos en la Condición 104(b).*

Podrán permitirse extensiones a los programas propuestos, si lo aprueba el AQMD de la Costa Sur por escrito.

Conforme a los requerimientos revisados establecidos en la Condición 104 de la SOFA, modificada el 4 de junio de 2026, el Sitio proporcionó antes del 31 de julio de 2026 una confirmación escrita de los fabricantes de las Antorchas 1, 2 y 3 sobre la concentración mínima necesaria de metano de biogás para lograr eficiencias de destrucción de metano y NMOC consistentes con los requerimientos regulatorios aplicables. El Sitio ha coordinado con un fabricante externo el programa de diseño, fabricación e instalación y entregó los plazos del proyecto al AQMD de la Costa Sur por e-mail el 9 de septiembre de 2026. La instalación de los sistemas de combustible complementarios y medidores de flujo asociados de las unidades TOx Zeeco 1, Zeeco 6, Zeeco 7, Parnel y Hero se completó el 12 de octubre de 2026.

Sección BB - Esquemas del Sistema de Tratamiento y Almacenamiento de Lixiviados

Condición No. 63. A más tardar el 12 de junio de 2026, el Demandado deberá proporcionarle al AQMD de la Costa Sur un esquema del sistema de tratamiento de lixiviados actual y el sistema de almacenamiento de lixiviados, que incluyen de forma enunciativa más no limitativa, conexiones, líneas de flujo, depósitos de tratamiento, tanques de aireación, tanques de almacenamiento y grupos de tanques, líneas de ventilación que se dirigen a los equipos de control, equipos de control, líneas que se dirigen hacia los tanques de lixiviados y entre tanques de lixiviados, tanques que están conectados y no conectados a las líneas de ventilación de vacío y los equipos y las ubicaciones de carga/descarga de camiones cisterna de lixiviados. El Demandado debe proporcionar un esquema revisado en los informes mensuales de la Condición 8 después de todo mes durante el cual el Demandado haya completado cualquier cambio o modificación en el sistema de tratamiento de lixiviados y/o sistema de almacenamiento de lixiviados, que se reflejaría en el esquema.

El esquema actualizado del sistema de tratamiento de lixiviados actual y del sistema de almacenamiento de lixiviados se incluye en el plano conforme a obra más reciente, con fecha 21 de septiembre de 2026, en el **Adjunto P**.

Sección CC - Registros de Temperaturas Operativas y Tipos de Combustible Piloto/Combustible Complementario

Condición No. 8(t). Los registros de las temperaturas operativas (por minuto) y los tipos de combustible piloto/combustible complementario e índices de uso (por hora), hasta donde se conozcan los datos, de cada antorcha de biogás y oxidante térmico del último mes, en un formato de planilla de cálculo en Microsoft Excel. A partir del informe presentado el 20 de octubre de 2026, si el AQMD de la Costa Sur aprueba por escrito una solicitud del Demandado, el Demandado podrá quitar estos datos de los informes mensuales.

Se están presentando los registros de la temperatura operativa, por minuto para cada dispositivo, en una hoja de cálculo en Excel con el título "CCL Chart Recorder Data – September 2026" (Datos del Registrador Gráfico de CCL – septiembre de 2026) junto a este informe.

Chiquita presentó una solicitud de aprobación escrita del AQMD de la Costa Sur para dejar de incluir esta información en sus informes mensuales de la Condición 8, como lo autoriza la Condición 8(t). El AQMD de la Costa Sur ya puede acceder a la información a través de las plataformas eTools y RMC de SCS y SCS previamente le proporcionó a la agencia instrucciones para que pueda acceder a la información de forma independiente en cualquier momento. Mientras esté pendiente la aprobación por escrito, Chiquita continuará incluyendo la información necesaria en sus informes mensuales.

Sección DD - Flujo de Biogás

Condición 7(d). El Demandado deberá mantener un registro de la siguiente información y proporcionarle estos registros al AQMD de la Costa Sur conforme a la Condición No. 8:

a. *El flujo de biogás por hora y por día incinerado, en pies cúbicos estándar, en cada antorcha (antorchas No. 1 y No. 2 bajo el Permiso G73696, A/N 645450; antorcha No. 3 bajo A/N 624296), el oxidante térmico/las antorchas y cualquier otro equipo usado para quemar o controlar biogás en las instalaciones, como también la cantidad total de biogás incinerado en las instalaciones;*
b. *El flujo diario de biogás no quemado en antorchas, en pies cúbicos estándar, si corresponde; y*
c. *Los resultados de las lecturas de azufre, las tomas de muestras y los análisis calculados como H2S con la hora y fecha en la que se tomó cada medición o en la que se tomó cada muestra; y*
d. *Los resultados de las calificaciones diarias del calor del gas, con la hora y fecha de cada muestra tomada, la ubicación de la toma de muestra y el tipo del gas del que se tomaron muestras (ej. biogás, mezcla de vapores de biogás y lixiviados).*

Los registros de los datos del flujo, las lecturas de azufre y las clasificaciones diarias del calor del gas se adjuntan en el **Apéndice A** y **Apéndice B**.

CIERRE

Si tiene preguntas o si necesita más información, por favor, comuníquese con Cornelius Fong de SCS Field Services llamando al (562) 743-7895 o con Gabrielle Stephens de SCS llamando al (562) 355-6510.

Atentamente,

Chuck Rainey
Profesional del Proyecto
SCS Engineers

Gabrielle F. Stephens
Vicepresidente
SCS Engineers

GFS/PSS

cc: Cornelius Fong, SCS Engineers
Kevin Green, Chiquita Canyon
Dylan Smith, Chiquita Canyon
William Haley, Chiquita Canyon
Tessa Lenz, Chiquita Canyon

Adjuntos

Attachment A

Lab Analyses from the Reporting Period

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 1, 2026
Date Received: September 1, 2026
Date Analyzed: September 1, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22446-10	22446-11	22446-12	22446-13	22446-14
Sample I.D.:	Zeeco South	Hero Inlet	FL-2009 Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	8.49	4.36	6.77	3.35	9.03
Nitrogen	34.62	23.25	33.03	18.24	40.41
Methane	23.83	11.32	23.69	18.31	11.54
Carbon Dioxide	28.93	49.05	32.58	52.22	31.90
Hydrogen	1.47	6.95	2.10	5.29	3.37
		(Concentration in ppmv)			
Carbon Monoxide	185	937	310	1062	463
		(Concentration in %v, by component)			
TNMHC	0.303	0.994	0.239	0.652	0.547
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	266.0	189.9	261.6	237.4	157.6
BTU/ft3 (Wet @ 0.25636 psia)	261.4	186.6	257.0	233.3	154.9
BTU/lb (Dry @60F, 14.696 psia)	3365	2142	3274	2696	1888

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon. The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported. Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 1, 2026
Date Received: September 1, 2026
Date Analyzed: September 1, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	8.49	8.49	8.49	0.00
Nitrogen	Zeeco South	34.64	34.60	34.62	0.12
Methane	Zeeco South	23.92	23.74	23.83	0.76
Carbon Dioxide	Zeeco South	28.94	28.91	28.93	0.10
Hydrogen	Zeeco South	1.46	1.47	1.47	0.68
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	183	186	185	1.4
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.303	0.304	0.303	0.10

Five Tedlar bag samples, laboratory numbers 22446-(10-14), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.46%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 1, 2026
Date Received: September 1, 2026
Date Analyzed: September 1, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22446-10	22446-11	22446-12	22446-13	22446-14
Sample I.D.:	Zeeco South	Hero Inlet	FL-2009 Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	155	239	187	291	133
Carbonyl sulfide	0.49	<1.60	0.52	<1.60	<1.20
Methyl mercaptan	94.5	501	111	557	277
Ethyl mercaptan	1.33	5.67	1.39	5.40	3.19
Dimethyl sulfide	249	1291	305	1155	744
Carbon disulfide	<0.40	<1.60	<0.40	<1.60	<1.20
i-Propyl mercaptan	1.47	2.84	1.86	3.76	1.88
t-Butyl mercaptan	<0.40	<1.60	<0.40	<1.60	<1.20
n-Propyl mercaptan	3.43	16.7	3.99	15.1	9.74
s-Butyl mercaptan	4.63	18.1	5.47	19.2	11.3
i-Butyl mercaptan	<0.40	<1.60	<1.60	<1.60	<1.20
Dimethyl disulfide	2.83	4.86	1.80	5.89	5.79
Tetrahydrothiophene	2.98	12.9	2.44	8.96	7.10
Unidentified sulfurs	10.6	38.0	10.0	39.9	25.7
	(Concentration in ppmv, as H_2S)				
Total Sulfur	529.43	2134.25	631.88	2106.79	1224.93

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 1, 2026
Date Received: September 1, 2026
Date Analyzed: September 1, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	154	156	155	1.7
	Hero Inlet	240	238	239	0.75
	FL-2009 Inlet	187	186	187	0.47
	Parnel Inlet	284	297	291	4.7
	Zeeco Inlet	131	134	133	2.5
Carbonyl sulfide	Zeeco South	0.47	0.50	0.49	6.2
	Hero Inlet	<1.60	<1.60	---	---
	FL-2009 Inlet	0.53	0.50	0.52	5.8
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	93.1	95.8	94.5	2.8
	Hero Inlet	501	500	501	0.21
	FL-2009 Inlet	112	110	111	1.8
	Parnel Inlet	545	569	557	4.3
	Zeeco Inlet	276	278	277	0.80
Ethyl mercaptan	Zeeco South	1.33	1.32	1.33	0.75
	Hero Inlet	5.59	5.74	5.67	2.6
	FL-2009 Inlet	1.40	1.38	1.39	1.4
	Parnel Inlet	5.38	5.41	5.40	0.56
	Zeeco Inlet	3.13	3.24	3.19	3.5
Dimethyl sulfide	Zeeco South	248	251	249	1.3
	Hero Inlet	1289	1293	1291	0.29
	FL-2009 Inlet	307	304	305	0.86
	Parnel Inlet	1132	1178	1155	4.0
	Zeeco Inlet	740	749	744	1.2
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.48	1.45	1.47	2.0
	Hero Inlet	2.87	2.80	2.84	2.5
	FL-2009 Inlet	1.89	1.83	1.86	3.2
	Parnel Inlet	3.73	3.79	3.76	1.6
	Zeeco Inlet	1.91	1.84	1.88	3.7

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	3.37	3.48	3.43	3.2
	Hero Inlet	16.6	16.7	16.7	0.48
	FL-2009 Inlet	4.00	3.97	3.99	0.75
	Parnel Inlet	14.8	15.5	15.1	4.6
	Zeeco Inlet	9.60	9.88	9.74	2.9
s-Butyl mercaptan	Zeeco South	4.60	4.65	4.63	1.1
	Hero Inlet	17.9	18.2	18.1	1.3
	FL-2009 Inlet	5.56	5.37	5.47	3.5
	Parnel Inlet	18.9	19.4	19.2	2.6
	Zeeco Inlet	11.3	11.3	11.3	0.09
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	FL-2009 Inlet	<1.60	<0.40	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	2.83	2.82	2.83	0.35
	Hero Inlet	4.86	4.86	4.86	0.00
	FL-2009 Inlet	1.80	1.80	1.80	0.00
	Parnel Inlet	5.82	5.96	5.89	2.4
	Zeeco Inlet	5.72	5.86	5.79	2.4
Tetrahydrothiophene	Zeeco South	2.94	3.02	2.98	2.7
	Hero Inlet	13.0	12.8	12.9	1.3
	FL-2009 Inlet	2.48	2.40	2.44	3.3
	Parnel Inlet	8.86	9.06	8.96	2.2
	Zeeco Inlet	7.08	7.11	7.10	0.42
Unidentified sulfurs	Zeeco South	10.6	10.6	10.6	0.09
	Hero Inlet	38.6	37.4	38.0	3.4
	FL-2009 Inlet	10.1	9.91	10.0	2.2
	Parnel Inlet	39.5	40.2	39.9	1.7
	Zeeco Inlet	25.3	26.1	25.7	2.9

Five Tedlar bag samples, laboratory numbers 22446-(10-14), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.1%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277

LABORATORY ANALYSIS REPORT **specialized air assessment laboratory**
atmaa.com

TO-15 Component Analysis in Tedlar Bag Sample, by GC/MS Method EPA TO-15

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Received: September 1, 2026
Date Analyzed: September 1, 2026

AtmAA Lab No.:	22446-10	22446-11	22446-12	22446-13	22446-14
Sample ID:	Zeeco South	Hero Inlet	FL-2009 Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentations in ppmv)*				
Freon 12	<1.50	<1.50	<1.50	<1.50	<1.50
Chloromethane	<1.90	<1.90	<1.90	<1.90	<1.90
Freon 114	<1.10	<1.10	<1.10	<1.10	<1.10
Vinyl Chloride	<1.50	<1.50	<1.50	<1.50	<1.50
1,3-Butadiene	<1.80	<1.80	<1.80	<1.80	<1.80
Bromomethane	<1.90	<1.90	<1.90	<1.90	<1.90
Chloroethane	<1.50	<1.50	<1.50	<1.50	<1.50
Acetone	161	662	150	514	346
Freon 11	<1.40	<1.40	<1.40	<1.40	<1.40
Isopropyl Alcohol	79.8	193	70.7	86.6	125
1,1-Dichloroethene	<1.90	<1.90	<1.90	<1.90	<1.90
Methylene Chloride	<2.20	<2.20	<2.20	<2.20	<2.20
Carbon Disulfide	<1.30	<1.30	<1.30	<1.30	<1.30
Freon 113	<1.00	<1.00	<1.00	<1.00	<1.00
trans-1,2-Dichloroethene	<1.90	<1.90	<1.90	<1.90	<1.90
1,1-Dichloroethane	<1.90	<1.90	<1.90	<1.90	<1.90
MTBE	<2.10	<2.10	<2.10	<2.10	<2.10
Vinyl Acetate	<2.60	<2.60	<2.60	<2.60	<2.60
2-Butanone	135	554	133	431	288
cis-1,2-Dichloroethene	<1.90	<1.90	<1.90	<1.90	<1.90
n-Hexane	<2.20	<2.20	<2.20	<2.20	<2.20
Chloroform	<1.60	<1.60	<1.60	<1.60	<1.60
Ethyl Acetate	<2.10	<2.10	<2.10	<2.10	<2.10
Tetrahydrofuran	120	503	102	363	274
1,2-Dichloroethane	<1.90	<1.90	<1.90	<1.90	<1.90
1,1,1-Trichloroethane	<1.40	<1.40	<1.40	<1.40	<1.40
Benzene	75.3	360	86.4	336	188
Carbon Tetrachloride	<1.20	<1.20	<1.20	<1.20	<1.20
Cyclohexane	<2.20	<2.20	<2.20	<2.20	<2.20
1,2-Dichloropropane	<1.70	<1.70	<1.70	<1.70	<1.70
Bromodichloromethane	<1.20	<1.20	<1.20	<1.20	<1.20
Trichloroethene	<1.40	<1.40	<1.40	<1.40	<1.40
1,4-Dioxane	<2.10	<2.10	<2.10	<2.10	<2.10
n-Heptane	2.13	6.14	2.63	5.02	4.16
cis-1,3-Dichloropropene	<1.70	<1.70	<1.70	<1.70	<1.70
4-Methyl-2-pentanone	7.07	26.2	8.40	16.0	13.1
trans-1,3-Dichloropropene	<1.70	<1.70	<1.70	<1.70	<1.70
1,1-2-Trichloroethane	<1.40	<1.40	<1.40	<1.40	<1.40
Toluene	12.8	42.2	15.7	35.9	22.6
2-Hexanone	2.10	8.66	<1.90	5.80	4.67
Dibromochloromethane	<0.90	<0.90	<0.90	<0.90	<0.90
1,2-Dibromoethane	<1.00	<1.00	<1.00	<1.00	<1.00
Tetrachloroethene	<1.10	<1.10	<1.10	<1.10	<1.10
Chlorobenzene	<1.70	<1.70	<1.70	<1.70	<1.70
Ethylbenzene	6.87	26.7	7.06	19.0	14.00
m,p-Xylene	6.87	21.5	7.75	15.9	12.00
Bromoform	<0.80	<0.80	<0.80	<0.80	<0.80
Styrene	<1.80	<1.80	<1.80	<1.80	<1.80
1,1,2,2-Tetrachloroethane	<1.10	<1.10	<1.10	<1.10	<1.10
o-Xylene	2.60	7.87	2.68	5.59	4.47
Benzyl Chloride	<1.40	<1.40	<1.40	<1.40	<1.40
4-Ethyl Toluene	2.45	9.31	1.94	5.96	5.20
1,3,5-Trimethyl Benzene	<1.60	1.82	<1.60	<1.60	<1.60
1,2,4-Trimethyl Benzene	<1.60	2.04	<1.60	<1.60	<1.60
1,3-Dichlorobenzene	<1.30	<1.30	<1.30	<1.30	<1.30
1,4-Dichlorobenzene	<1.30	1.31	<1.30	<1.30	<1.30
1,2-Dichlorobenzene	<1.30	<1.30	<1.30	<1.30	<1.30
1,2,4-Trichlorobenzene	<4.10	<4.10	<4.10	<4.10	<4.10
Hexachlorobutadiene	<2.90	<2.90	<2.90	<2.90	<2.90

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Received: September 1, 2026
Date Analyzed: September 1, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Freon-12	Parnel Inlet	<1.50	<1.50	---	---
Chloromethane	Parnel Inlet	<1.90	<1.90	---	---
Freon 114	Parnel Inlet	<1.10	<1.10	---	---
Vinyl Chloride	Parnel Inlet	<1.50	<1.50	---	---
1,3-Butadiene	Parnel Inlet	<1.80	<1.80	---	---
Bromomethane	Parnel Inlet	<1.90	<1.90	---	---
Chloroethane	Parnel Inlet	<1.50	<1.50	---	---
Acetone	Parnel Inlet	513	514	514	0.19
Freon 11	Parnel Inlet	<1.40	<1.40	---	---
Isopropyl Alcohol	Parnel Inlet	85.8	87.4	86.6	1.8
1,1-Dichloroethene	Parnel Inlet	<1.90	<1.90	---	---
Methylene Chloride	Parnel Inlet	<2.20	<2.20	---	---
Carbon Disulfide	Parnel Inlet	<1.30	<1.30	---	---
Freon 113	Parnel Inlet	<1.00	<1.00	---	---
trans-1,2-Dichloroethene	Parnel Inlet	<1.90	<1.90	---	---
1,1-Dichloroethane	Parnel Inlet	<1.90	<1.90	---	---
MTBE	Parnel Inlet	<2.10	<2.10	---	---
Vinyl Acetate	Parnel Inlet	<2.60	<2.60	---	---
2-Butanone	Parnel Inlet	428	433	431	1.2
cis-1,2-Dichloroethene	Parnel Inlet	<1.90	<1.90	---	---
n-Hexane	Parnel Inlet	<2.20	<2.20	---	---
Chloroform	Parnel Inlet	<1.60	<1.60	---	---
Ethyl Acetate	Parnel Inlet	<2.10	<2.10	---	---
Tetrahydrofuran	Parnel Inlet	356	369	363	3.6
1,2-Dichloroethane	Parnel Inlet	<1.90	<1.90	---	---

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
1,1,1-Trichloroethane	Parnel Inlet	<1.40	<1.40	---	---
Benzene	Parnel Inlet	334	338	336	1.2
Carbon Tetrachloride	Parnel Inlet	<1.20	<1.20	---	---
Cyclohexane	Parnel Inlet	<2.20	<2.20	---	---
1,2-Dichloropropane	Parnel Inlet	<1.70	<1.70	---	---
Bromodichloromethane	Parnel Inlet	<1.20	<1.20	---	---
Trichloroethene	Parnel Inlet	<1.40	<1.40	---	---
1,4-Dioxane	Parnel Inlet	<2.10	<2.10	---	---
n-Heptane	Parnel Inlet	5.20	4.83	5.02	7.4
cis-1,3-Dichloropropene	Parnel Inlet	<1.70	<1.70	---	---
4-Methyl-2-pentanone	Parnel Inlet	15.5	16.5	16.0	6.3
trans-1,3-Dichloropropene	Parnel Inlet	<1.70	<1.70	---	---
1,1-2-Trichloroethane	Parnel Inlet	<1.40	<1.40	---	---
Toluene	Parnel Inlet	35.6	36.2	35.9	1.7
2-Hexanone	Parnel Inlet	5.50	6.09	5.80	10
Dibromochloromethane	Parnel Inlet	<0.90	<0.90	---	---
1,2-Dibromoethane	Parnel Inlet	<1.00	<1.00	---	---
Tetrachloroethene	Parnel Inlet	<1.10	<1.10	---	---
Chlorobenzene	Parnel Inlet	<1.70	<1.70	---	---
Ethylbenzene	Parnel Inlet	18.4	19.5	19.0	5.8
m,p-Xylene	Parnel Inlet	15.3	16.4	15.9	6.9
Bromoform	Parnel Inlet	<0.80	<0.80	---	---
Styrene	Parnel Inlet	<1.80	<1.80	---	---
1,1,2,2-Tetrachloroethane	Parnel Inlet	<1.10	<1.10	---	---
o-Xylene	Parnel Inlet	5.31	5.87	5.59	10

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Benzyl Chloride	Parnel Inlet	<1.40	<1.40	---	---
4-Ethyl Toluene	Parnel Inlet	5.58	6.33	5.96	13
1,3,5-Trimethyl Benzene	Parnel Inlet	<1.60	<1.60	---	---
1,2,4-Trimethyl Benzene	Parnel Inlet	<1.60	<1.60	---	---
1,3-Dichlorobenzene	Parnel Inlet	<1.30	<1.30	---	---
1,4-Dichlorobenzene	Parnel Inlet	<1.30	<1.30	---	---
1,2-Dichlorobenzene	Parnel Inlet	<1.30	<1.30	---	---
1,2,4-Trichlorobenzene	Parnel Inlet	<4.10	<4.10	---	---
Hexachlorobutadiene	Parnel Inlet	<2.90	<2.90	---	---

Five Tedlar bag samples, laboratory numbers 22446-(10-14), were analyzed for TO-15 components, by GC/MS. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 5.3%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)* Brandon Rodriguez	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA ALT--144	HHV (3588)	VOCs (TO-15)		Special Remarks
Zeeco South Station	LFG	22446-10	9-1-26	8:50am	X	X	X	X	X		
Hero Inlet	LFG	-11	9-1-26	7:50am	X	X	X	X	X		
FL-2009 Inlet	LFG	-12	9-1-26	7:35am	X	X	X	X	X		
Parnel Inlet	LFG	-13	9-1-26	8:05am	X	X	X	X	X		
Zeeco Inlet		-14	9-1-26	8:25am							

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
Sandra Reese	9-1-26	8:55 AM	Sandra Reese	9/1/26	905
Relinquished by: *(Signature)* Sandra Reese	Date 9/1/26	Time 1029	Received by: *(Signature)*	Date	Time
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date 9/1/26	Time 10:29

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	Company: SCS Engineers	AtmAA Inc.
Street Address: 3900 Kilroy Airport Way Suite 300	Street Address: 3900 Kilroy Airport Way Suite 300	5107 Douglas Fir Rd.
City/State/Zip: Long Beach / CA / 90806	City/State/Zip: Long Beach / CA / 90806	Calabasas, CA 91302
Telephone No.: 562-743-7895 /562-335-0002	Project Manager: Cornelius Fong	TEL: (818) 223-3277
Fax No.:	Email Address: CFong@scsengineers.com	Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 2, 2026
Date Received: September 2, 2026
Date Analyzed: September 2, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22456-4	22456-5	22456-6	22456-7	22456-8
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	8.48	5.25	3.60	2.64	8.18
Nitrogen	34.76	28.02	19.98	14.95	37.67
Methane	23.80	25.98	11.80	18.17	13.11
Carbon Dioxide	29.19	35.84	51.37	54.69	35.25
Hydrogen	1.52	2.31	7.58	5.84	3.85
		(Concentration in ppmv)			
Carbon Monoxide	182	332	897	1101	455
		(Concentration in %v, by component)			
TNMHC	0.295	0.244	0.977	0.639	0.567
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	264.2	288.0	197.2	239.2	173.4
BTU/ft3 (Wet @ 0.25636 psia)	259.6	283.0	193.8	235.0	170.4
BTU/lb (Dry @60F, 14.696 psia)	3340	3587	2214	2693	2069

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 2, 2026
Date Received: September 2, 2026
Date Analyzed: September 2, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	8.46	8.50	8.48	0.47
Nitrogen	Zeeco South	34.85	34.67	34.76	0.52
Methane	Zeeco South	23.84	23.76	23.80	0.34
Carbon Dioxide	Zeeco South	29.17	29.21	29.19	0.14
Hydrogen	Zeeco South	1.51	1.52	1.52	0.66
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	181	184	182	1.4
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.294	0.296	0.295	0.52

Five Tedlar bag samples, laboratory numbers 22456-(4-8), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.58%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 2, 2026
Date Received: September 2, 2026
Date Analyzed: September 2, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22456-4	22456-5	22456-6	22456-7	22456-8
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	144	177	241	299	145
Carbonyl sulfide	0.47	0.46	<1.60	<1.60	<1.20
Methyl mercaptan	85.5	114	524	627	286
Ethyl mercaptan	1.12	1.37	5.90	5.90	3.15
Dimethyl sulfide	238	313	1342	1261	731
Carbon disulfide	<0.40	<0.40	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.28	1.69	2.87	3.81	1.92
t-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
n-Propyl mercaptan	3.17	3.81	17.0	16.3	9.55
s-Butyl mercaptan	4.13	5.09	18.3	19.7	11.0
i-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
Dimethyl disulfide	2.78	1.58	4.50	5.14	6.04
Tetrahydrothiophene	2.78	2.29	12.8	9.53	6.84
Unidentified sulfurs	10.2	8.05	35.6	36.9	27.5
	(Concentration in ppmv, as H_2S)				
Total Sulfur	496.75	630.45	2207.92	2290.15	1234.23

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 2, 2026
Date Received: September 2, 2026
Date Analyzed: September 2, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	143	145	144	1.2
	FL-1995 Inlet	181	174	177	3.6
	Hero Inlet	243	239	241	1.9
	Parnel Inlet	299	300	299	0.24
	Zeeco Inlet	145	145	145	0.46
Carbonyl sulfide	Zeeco South	0.47	0.46	0.47	2.2
	FL-1995 Inlet	0.45	0.46	0.46	2.2
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	84.8	86.2	85.5	1.6
	FL-1995 Inlet	116	111	114	3.9
	Hero Inlet	529	518	524	2.0
	Parnel Inlet	629	626	627	0.48
	Zeeco Inlet	287	285	286	0.68
Ethyl mercaptan	Zeeco South	1.09	1.15	1.12	5.4
	FL-1995 Inlet	1.39	1.35	1.37	2.9
	Hero Inlet	5.97	5.83	5.90	2.4
	Parnel Inlet	5.93	5.87	5.90	1.0
	Zeeco Inlet	3.07	3.23	3.15	5.1
Dimethyl sulfide	Zeeco South	234	243	238	4.2
	FL-1995 Inlet	320	307	313	4.1
	Hero Inlet	1353	1330	1342	1.7
	Parnel Inlet	1267	1255	1261	0.94
	Zeeco Inlet	740	722	731	2.5
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.28	1.28	1.28	0.00
	FL-1995 Inlet	1.64	1.73	1.69	5.3
	Hero Inlet	2.90	2.83	2.87	2.4
	Parnel Inlet	3.83	3.78	3.81	1.3
	Zeeco Inlet	1.90	1.94	1.92	2.1

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	3.15	3.18	3.17	0.95
	FL-1995 Inlet	3.77	3.84	3.81	1.8
	Hero Inlet	17.1	16.8	17.0	1.83
	Parnel Inlet	16.4	16.3	16.3	0.24
	Zeeco Inlet	9.67	9.43	9.55	2.5
s-Butyl mercaptan	Zeeco South	4.06	4.20	4.13	3.4
	FL-1995 Inlet	5.10	5.08	5.09	0.39
	Hero Inlet	18.6	18.0	18.3	3.2
	Parnel Inlet	19.6	19.8	19.7	1.1
	Zeeco Inlet	11.1	11.0	11.0	0.72
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	2.76	2.80	2.78	1.4
	FL-1995 Inlet	1.58	1.58	1.58	0.00
	Hero Inlet	4.57	4.42	4.50	3.3
	Parnel Inlet	5.10	5.18	5.14	1.6
	Zeeco Inlet	5.96	6.11	6.04	2.5
Tetrahydrothiophene	Zeeco South	2.78	2.77	2.78	0.36
	FL-1995 Inlet	2.30	2.28	2.29	0.87
	Hero Inlet	13.3	12.4	12.8	6.9
	Parnel Inlet	9.58	9.47	9.53	1.2
	Zeeco Inlet	6.73	6.95	6.84	3.2
Unidentified sulfurs	Zeeco South	10.2	10.3	10.2	0.98
	FL-1995 Inlet	8.08	8.02	8.05	0.75
	Hero Inlet	36.0	35.2	35.6	2.2
	Parnel Inlet	37.1	36.6	36.9	1.3
	Zeeco Inlet	27.9	27.2	27.5	2.2

Five Tedlar bag samples, laboratory numbers 22456-(4-8), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.0%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: *(Signature)* Branden Rodriguez	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22456-4	9/2/26	8:35am	X	X	X	X			
FL-~~2005~~ 1995 Inlet	LFG	-5	9/2/26	7:25am	X	X	X	X			
Hero Inlet	LFG	-6	9/2/26	7:40am	X	X	X	X			
Parnel Inlet	LFG	-7	9/2/26	7:50am	X	X	X	X			
Zeeco Inlet	LFG	-8	9/2/26	8:15am	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9-2-26	2:50pm	**Received by: *(Signature)***	9/2/26	8:50
Relinquished by: *(Signature)*	9/2/26	952	**Received by: *(Signature)***		
Relinquished by: *(Signature)*			**Received for Laboratory by: *(Signature)***	9/2/26	9:52

Company Info:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach / CA / 90806
Telephone No.: 562-743-7895 /562-335-0002
Fax No.:

Send Report to:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach / CA / 90806
Project Manager: Cornelius Fong
Email Address: CFong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 3, 2026
Date Received: September 3, 2026
Date Analyzed: September 3, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22466-9	22466-10	22466-11	22466-12	22466-13
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components			*(Concentration in %v)*		
Oxygen	7.88	4.59	4.33	3.56	8.49
Nitrogen	32.60	26.48	23.49	18.74	39.17
Methane	27.02	27.10	10.93	18.51	13.03
Carbon Dioxide	30.22	37.35	49.93	50.98	33.69
Hydrogen	1.14	2.32	7.07	5.08	3.41
			(Concentration in ppmv)		
Carbon Monoxide	155	348	924	934	446
			(Concentration in %v, by component)		
TNMHC	0.237	0.260	0.954	0.565	0.520
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	290.2	299.1	182.6	235.3	169.8
BTU/ft3 (Wet @ 0.25636 psia)	285.2	293.9	179.4	231.2	166.9
BTU/lb (Dry @60F, 14.696 psia)	3694	3716	2053	2687	2034

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 3, 2026
Date Received: September 3, 2026
Date Analyzed: September 3, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	8.00	7.75	7.88	3.2
Nitrogen	Zeeco South	32.99	32.21	32.60	2.4
Methane	Zeeco South	26.78	27.25	27.02	1.7
Carbon Dioxide	Zeeco South	29.96	30.48	30.22	1.7
Hydrogen	Zeeco South	1.14	1.14	1.14	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	157	153	155	2.9
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.237	0.237	0.237	0.20

Five Tedlar bag samples, laboratory numbers 22466-(9-13), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 1.7%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 3, 2026
Date Received: September 3, 2026
Date Analyzed: September 3, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22466-9	22466-10	22466-11	22466-12	22466-13
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	145	183	220	275	130
Carbonyl sulfide	0.47	0.49	<1.60	<1.60	<1.20
Methyl mercaptan	65.0	114	469	513	254
Ethyl mercaptan	0.98	1.36	5.30	4.88	2.87
Dimethyl sulfide	165	325	1226	1050	694
Carbon disulfide	<0.40	<0.40	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.28	1.76	2.70	3.54	1.72
t-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.38	3.91	15.6	13.7	8.55
s-Butyl mercaptan	3.52	5.28	17.0	16.7	9.84
i-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
Dimethyl disulfide	1.47	1.81	4.92	4.73	5.00
Tetrahydrothiophene	2.06	2.37	12.0	7.09	6.18
Unidentified sulfurs	6.45	9.74	36.2	26.9	22.1
	(Concentration in ppmv, as H_2S)				
Total Sulfur	395.05	650.54	2013.42	1920.06	1139.51

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 3, 2026
Date Received: September 3, 2026
Date Analyzed: September 3, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	150	141	145	6.4
	FL-2009 Inlet	185	181	183	2.2
	Hero Inlet	220	221	220	0.32
	Parnel Inlet	277	273	275	1.4
	Zeeco Inlet	129	131	130	1.8
Carbonyl sulfide	Zeeco South	0.48	0.46	0.47	4.3
	FL-2009 Inlet	0.49	0.48	0.49	2.1
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	66.2	63.7	65.0	3.8
	FL-2009 Inlet	114	114	114	0.54
	Hero Inlet	467	470	469	0.55
	Parnel Inlet	513	512	513	0.16
	Zeeco Inlet	256	252	254	1.6
Ethyl mercaptan	Zeeco South	0.96	0.99	0.98	3.1
	FL-2009 Inlet	1.38	1.33	1.36	3.7
	Hero Inlet	5.28	5.32	5.30	0.75
	Parnel Inlet	4.87	4.89	4.88	0.41
	Zeeco Inlet	2.87	2.86	2.87	0.35
Dimethyl sulfide	Zeeco South	166	163	165	1.6
	FL-2009 Inlet	323	327	325	1.4
	Hero Inlet	1222	1230	1226	0.70
	Parnel Inlet	1050	1049	1050	0.14
	Zeeco Inlet	712	676	694	5.1
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.26	1.30	1.28	3.1
	FL-2009 Inlet	1.78	1.73	1.76	2.8
	Hero Inlet	2.67	2.72	2.70	1.9
	Parnel Inlet	3.47	3.60	3.54	3.7
	Zeeco Inlet	1.71	1.73	1.72	1.2

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.35	2.40	2.38	2.1
	FL-2009 Inlet	3.94	3.87	3.91	1.8
	Hero Inlet	15.5	15.6	15.6	0.64
	Parnel Inlet	13.7	13.7	13.7	0.22
	Zeeco Inlet	8.50	8.59	8.55	1.1
s-Butyl mercaptan	Zeeco South	3.48	3.55	3.52	2.0
	FL-2009 Inlet	5.34	5.21	5.28	2.5
	Hero Inlet	16.9	17.0	17.0	0.41
	Parnel Inlet	16.7	16.7	16.7	0.30
	Zeeco Inlet	9.79	9.89	9.84	1.0
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	1.46	1.48	1.47	1.4
	FL-2009 Inlet	1.81	1.80	1.81	0.55
	Hero Inlet	4.93	4.90	4.92	0.61
	Parnel Inlet	4.73	4.73	4.73	0.00
	Zeeco Inlet	5.03	4.97	5.00	1.2
Tetrahydrothiophene	Zeeco South	1.92	2.19	2.06	13
	FL-2009 Inlet	2.34	2.39	2.37	2.1
	Hero Inlet	12.1	11.9	12.0	1.3
	Parnel Inlet	7.03	7.14	7.09	1.6
	Zeeco Inlet	6.24	6.11	6.18	2.1
Unidentified sulfurs	Zeeco South	6.48	6.41	6.45	1.1
	FL-2009 Inlet	9.81	9.67	9.74	1.4
	Hero Inlet	37.0	35.4	36.2	4.4
	Parnel Inlet	26.9	26.8	26.9	0.48
	Zeeco Inlet	22.9	21.4	22.1	7.0

Five Tedlar bag samples, laboratory numbers 22466-(9-13), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.0%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)* Barden Rodriguez	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22466-9	9.3.26	8:05am	X	X	X	X			
FL-2009 Inlet	LFG	-10	9.3.26	7:10am	X	X	X	X			
Hero Inlet	LFG	-11	9.3.26	7:25am	X	X	X	X			
Parnel Inlet	LFG	-12	9.3.26	7:35am	X	X	X	X			
Zeeco Inlet	LFG	-13	9.3.26	7:45am	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9.3.26	8:38am	**Received by:** *(Signature)*	9.3.26	8:38
Relinquished by: *(Signature)*	9-3-26	9:45am	**Received by:** *(Signature)*		
Relinquished by: *(Signature)*			**Received for Laboratory by:** *(Signature)*	9/3/26	9:55

Company Info:		Send Report to:		Analytical Laboratory
Company:	SCS Engineers	**Company:**	SCS Engineers	AtmAA Inc.
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300	5107 Douglas Fir Rd.
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806	Calabasas, CA 91302
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong	TEL: (818) 223-3277
Fax No.:		**Email Address:**	CFong@scsengineers.com	Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 4, 2026
Date Received: September 4, 2026
Date Analyzed: September 4, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22476-3	22476-4	22476-5	22476-6	22476-7
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components			*(Concentration in %v)*		
Oxygen	5.95	2.88	4.50	3.26	5.80
Nitrogen	30.39	18.67	23.68	17.60	29.81
Methane	15.80	32.35	10.54	17.08	15.51
Carbon Dioxide	41.22	41.68	48.33	53.53	40.52
Hydrogen	1.28	2.57	7.20	6.15	3.85
			(Concentration in ppmv)		
Carbon Monoxide	129	375	858	1017	546
			(Concentration in %v, by component)		
TNMHC	0.317	0.248	1.007	0.714	0.588
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	188.0	352.6	183.7	228.9	204.1
BTU/ft3 (Wet @ 0.25636 psia)	184.7	346.4	180.5	224.9	200.6
BTU/lb (Dry @60F, 14.696 psia)	2156	4393	2074	2588	2392

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 4, 2026
Date Received: September 4, 2026
Date Analyzed: September 4, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	5.99	5.90	5.95	1.5
Nitrogen	Zeeco South	30.42	30.35	30.39	0.23
Methane	Zeeco South	15.86	15.74	15.80	0.76
Carbon Dioxide	Zeeco South	41.22	41.22	41.22	0.00
Hydrogen	Zeeco South	1.27	1.28	1.28	0.78
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	130	128	129	2.0
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.317	0.316	0.317	0.22

Five Tedlar bag samples, laboratory numbers 22476-(3-7), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.78%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 4, 2026
Date Received: September 4, 2026
Date Analyzed: September 4, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22476-3	22476-4	22476-5	22476-6	22476-7
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	155	245	212	265	149
Carbonyl sulfide	0.46	0.60	<1.60	<1.60	<1.20
Methyl mercaptan	88.0	96.5	492	554	335
Ethyl mercaptan	1.14	1.14	5.42	5.31	3.47
Dimethyl sulfide	235	280	1238	1195	916
Carbon disulfide	<0.40	<0.40	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.29	2.06	2.56	3.29	2.08
t-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.88	3.16	15.7	15.2	10.9
s-Butyl mercaptan	3.97	4.70	16.7	17.9	12.8
i-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
Dimethyl disulfide	4.30	1.12	4.30	9.31	8.44
Tetrahydrothiophene	2.62	1.77	12.5	9.19	6.69
Unidentified sulfurs	11.0	7.10	35.0	38.9	29.7
	(Concentration in ppmv, as H_2S)				
Total Sulfur	509.37	644.15	2038.88	2122.01	1482.92

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 4, 2026
Date Received: September 4, 2026
Date Analyzed: September 4, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	152	158	155	3.8
	FL-2009 Inlet	250	240	245	3.8
	Hero Inlet	212	212	212	0.09
	Parnel Inlet	259	271	265	4.5
	Zeeco Inlet	151	147	149	2.3
Carbonyl sulfide	Zeeco South	0.47	0.45	0.46	4.3
	FL-2009 Inlet	0.61	0.59	0.60	3.3
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	86.7	89.2	88.0	2.8
	FL-2009 Inlet	98.1	95.0	96.5	3.3
	Hero Inlet	491	493	492	0.41
	Parnel Inlet	547	560	554	2.4
	Zeeco Inlet	337	333	335	1.2
Ethyl mercaptan	Zeeco South	1.12	1.16	1.14	3.5
	FL-2009 Inlet	1.14	1.14	1.14	0.00
	Hero Inlet	5.36	5.48	5.42	2.2
	Parnel Inlet	5.31	5.31	5.31	0.00
	Zeeco Inlet	3.51	3.42	3.47	2.6
Dimethyl sulfide	Zeeco South	232	237	235	2.0
	FL-2009 Inlet	285	274	280	4.0
	Hero Inlet	1233	1244	1238	0.90
	Parnel Inlet	1182	1208	1195	2.1
	Zeeco Inlet	911	921	916	1.2
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.26	1.31	1.29	3.9
	FL-2009 Inlet	2.06	2.06	2.06	0.00
	Hero Inlet	2.62	2.50	2.56	4.7
	Parnel Inlet	3.26	3.32	3.29	1.8
	Zeeco Inlet	2.05	2.11	2.08	2.9

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.86	2.90	2.88	1.4
	FL-2009 Inlet	3.23	3.08	3.16	4.8
	Hero Inlet	15.7	15.6	15.7	0.26
	Parnel Inlet	15.1	15.3	15.2	1.4
	Zeeco Inlet	11.0	10.8	10.9	1.7
s-Butyl mercaptan	Zeeco South	3.95	3.98	3.97	0.76
	FL-2009 Inlet	4.75	4.65	4.70	2.1
	Hero Inlet	16.8	16.6	16.7	1.0
	Parnel Inlet	17.6	18.2	17.9	3.1
	Zeeco Inlet	13.0	12.5	12.8	4.4
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	4.22	4.38	4.30	3.7
	FL-2009 Inlet	1.13	1.10	1.12	2.7
	Hero Inlet	4.29	4.31	4.30	0.47
	Parnel Inlet	9.21	9.40	9.31	2.0
	Zeeco Inlet	8.56	8.32	8.44	2.8
Tetrahydrothiophene	Zeeco South	2.53	2.71	2.62	6.9
	FL-2009 Inlet	1.80	1.74	1.77	3.4
	Hero Inlet	12.4	12.6	12.5	1.4
	Parnel Inlet	9.21	9.17	9.19	0.44
	Zeeco Inlet	6.91	6.46	6.69	6.7
Unidentified sulfurs	Zeeco South	11.1	10.9	11.0	1.9
	FL-2009 Inlet	7.15	7.05	7.10	1.4
	Hero Inlet	34.2	35.8	35.0	4.7
	Parnel Inlet	39.3	38.6	38.9	1.9
	Zeeco Inlet	30.5	29.0	29.7	5.0

Five Tedlar bag samples, laboratory numbers 22476-(3-7), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.5%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: *(Signature)* Branden Rodriguez	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22476-3	9.4.26	9:40am	X	X	X	X			
FL-2009 Inlet	LFG	-4	9.4.26	7:25am	X	X	X	X			
Hero Inlet	LFG	-5	9.4.26	7:40am	X	X	X	X			
Parnel Inlet	LFG	-6	9.4.26	8:00am	X	X	X	X			
Zeeco Inlet	LFG	-7	9.4.26	8:25am	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9-4-26	8:50		9/4/26	8:50
Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9.4.26	9:45		9/4/26	10:29
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date	Time

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach / CA / 90806	**City/State/Zip:** Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895 /562-335-0002	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:	**Email Address:** CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 5, 2026
Date Received: September 5, 2026
Date Analyzed: September 7, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22486-1	22486-2	22486-3	22486-4	22486-5
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	6.40	18.46	4.35	3.86	6.92
Nitrogen	27.46	67.25	22.90	19.17	33.81
Methane	28.74	6.22	11.23	17.16	15.75
Carbon Dioxide	34.43	7.56	51.14	51.00	38.91
Hydrogen	1.47	0.45	7.31	5.65	3.28
		(Concentration in ppmv)			
Carbon Monoxide	189	73.2	911	989	529
		(Concentration in %v, by component)			
TNMHC	0.255	0.047	0.986	0.559	0.378
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	310.8	66.5	185.5	221.1	187.9
BTU/ft3 (Wet @ 0.25636 psia)	305.4	65.4	182.3	217.3	184.6
BTU/lb (Dry @60F, 14.696 psia)	3911	865	2083	2526	2226

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 5, 2026
Date Received: September 5, 2026
Date Analyzed: September 7, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.39	6.40	6.40	0.16
Nitrogen	Zeeco South	27.40	27.51	27.46	0.40
Methane	Zeeco South	28.73	28.75	28.74	0.07
Carbon Dioxide	Zeeco South	34.50	34.36	34.43	0.41
Hydrogen	Zeeco South	1.47	1.47	1.47	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	189	189	189	0.11
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.258	0.253	0.255	1.7

Five Tedlar bag samples, laboratory numbers 22486-(1-5), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.41%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: September 30, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 5, 2026
Date Received: September 5, 2026
Date Analyzed: September 5, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22486-1	22486-2	22486-3	22486-4	22486-5
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	181	35.9	249	291	139
Carbonyl sulfide	0.46	<0.40	<1.60	<1.60	<1.60
Methyl mercaptan	89.0	15.9	572	586	312
Ethyl mercaptan	1.20	<0.40	6.24	5.52	3.30
Dimethyl sulfide	285	51.2	1442	1206	883
Carbon disulfide	<0.40	<0.40	<1.60	<1.60	<1.60
i-Propyl mercaptan	1.49	0.46	2.90	3.42	1.99
t-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.60
n-Propyl mercaptan	3.29	0.72	18.2	14.6	9.54
s-Butyl mercaptan	4.43	1.09	19.5	16.5	10.4
i-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.60
Dimethyl disulfide	3.66	0.41	4.87	6.54	6.25
Tetrahydrothiophene	2.35	0.65	14.1	6.55	4.10
Unidentified sulfurs	8.31	1.68	38.1	20.5	14.1
	(Concentration in ppmv, as H_2S)				
Total Sulfur	583.85	108.39	2370.56	2163.67	1389.87

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 5, 2026
Date Received: September 5, 2026
Date Analyzed: September 5, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	186	175	181	6.2
	FL-1995 Inlet	35.7	36.1	35.9	1.1
	Hero Inlet	250	247	249	1.0
	Parnel Inlet	291	292	291	0.37
	Zeeco Inlet	136	141	139	3.7
Carbonyl sulfide	Zeeco South	0.46	0.45	0.46	2.2
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.60	<1.60	---	---
Methyl mercaptan	Zeeco South	90.7	87.4	89.0	3.7
	FL-1995 Inlet	15.7	16.1	15.9	2.4
	Hero Inlet	570	574	572	0.66
	Parnel Inlet	582	591	586	1.6
	Zeeco Inlet	307	317	312	3.3
Ethyl mercaptan	Zeeco South	1.25	1.14	1.20	9.2
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	6.16	6.31	6.24	2.4
	Parnel Inlet	5.49	5.54	5.52	0.91
	Zeeco Inlet	3.36	3.24	3.30	3.6
Dimethyl sulfide	Zeeco South	287	283	285	1.6
	FL-1995 Inlet	50.5	51.9	51.2	2.8
	Hero Inlet	1431	1452	1442	1.5
	Parnel Inlet	1199	1213	1206	1.2
	Zeeco Inlet	884	882	883	0.26
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.60	<1.60	---	---
i-Propyl mercaptan	Zeeco South	1.54	1.43	1.49	7.4
	FL-1995 Inlet	0.43	0.49	0.46	13
	Hero Inlet	2.87	2.93	2.90	2.1
	Parnel Inlet	3.35	3.48	3.42	3.8
	Zeeco Inlet	2.01	1.97	1.99	2.0



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.60	<1.60	---	---
n-Propyl mercaptan	Zeeco South	3.38	3.19	3.29	5.8
	FL-1995 Inlet	0.70	0.73	0.72	4.2
	Hero Inlet	18.0	18.4	18.2	2.5
	Parnel Inlet	14.4	14.8	14.6	3.0
	Zeeco Inlet	9.50	9.57	9.54	0.73
s-Butyl mercaptan	Zeeco South	4.51	4.34	4.43	3.8
	FL-1995 Inlet	1.06	1.12	1.09	5.5
	Hero Inlet	19.4	19.7	19.5	1.6
	Parnel Inlet	16.3	16.7	16.5	2.2
	Zeeco Inlet	10.4	10.4	10.4	0.29
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.60	<1.60	---	---
Dimethyl disulfide	Zeeco South	3.74	3.58	3.66	4.4
	FL-1995 Inlet	0.41	0.40	0.41	2.5
	Hero Inlet	4.78	4.96	4.87	3.7
	Parnel Inlet	6.46	6.62	6.54	2.4
	Zeeco Inlet	6.26	6.23	6.25	0.48
Tetrahydrothiophene	Zeeco South	2.39	2.30	2.35	3.8
	FL-1995 Inlet	0.65	0.65	0.65	0.00
	Hero Inlet	13.9	14.3	14.1	2.9
	Parnel Inlet	6.26	6.83	6.55	8.7
	Zeeco Inlet	4.15	4.04	4.10	2.7
Unidentified sulfurs	Zeeco South	8.52	8.10	8.31	5.1
	FL-1995 Inlet	1.78	1.58	1.68	12
	Hero Inlet	37.0	39.1	38.1	5.6
	Parnel Inlet	20.3	20.8	20.5	2.5
	Zeeco Inlet	14.0	14.1	14.1	0.78

Five Tedlar bag samples, laboratory numbers 22486-(1-5), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 3.3%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: *(Signature)*	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22486-1	9/5/26	8:20 AM	X	X	X	X			
FL-2009 Inlet	LFG	-2	9/5/26	8:10 AM	X	X	X	X			
Hero Inlet	LFG	-3	9/5/26	7:35 AM	X	X	X	X			
Parnel Inlet	LFG	-4	9/5/26	7:45	X	X	X	X			
Zeeco Inlet	LFG	-5	9/5/26	7:30 AM	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9/5/26	9:30	**Received by:** *(Signature)*	9.5.26	9:40
Relinquished by: *(Signature)*	9/5/26	10:11	**Received by:** *(Signature)*	Date	Time
Relinquished by: *(Signature)*	Date	Time	**Received for Laboratory by:** *(Signature)*	9/5/26	10:11

Company Info:		Send Report to:	
Company:	SCS Engineers	**Company:**	SCS Engineers
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong
Fax No.:		**Email Address:**	CFong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 6, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22506-6	22506-7	22506-8	22506-9
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet
Components		*(Concentration in %v)*		
Oxygen	3.87	3.90	7.11	6.50
Nitrogen	20.15	24.09	33.43	30.51
Methane	31.07	27.56	10.42	13.13
Carbon Dioxide	40.69	38.54	39.76	41.33
Hydrogen	1.55	2.60	5.13	4.08
		(Concentration in ppmv)		
Carbon Monoxide	246	355	644	683
		(Concentration in %v, by component)		
TNMHC	0.271	0.289	0.687	0.603
		BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	339.6	309.6	158.9	180.3
BTU/ft3 (Wet @ 0.25636 psia)	333.7	304.2	156.1	177.2
BTU/lb (Dry @60F, 14.696 psia)	4186	3837	1847	2087

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon. The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported. Actual analysis results are reported on a "wet" basis.

B Fung

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 6, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	3.88	3.85	3.87	0.78
Nitrogen	Zeeco South	20.12	20.18	20.15	0.30
Methane	Zeeco South	31.03	31.11	31.07	0.26
Carbon Dioxide	Zeeco South	40.61	40.77	40.69	0.39
Hydrogen	Zeeco South	1.56	1.54	1.55	1.29
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	248	245	246	1.1
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.270	0.273	0.271	1.2

Four Tedlar bag samples, laboratory numbers 22506-(6-9), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.76%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 6, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22506-6	22506-7	22506-8	22506-9
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	210	187	159	164
Carbonyl sulfide	0.48	0.48	<1.60	<1.60
Methyl mercaptan	133	127	354	384
Ethyl mercaptan	1.59	1.33	3.98	3.59
Dimethyl sulfide	373	357	960	940
Carbon disulfide	<0.40	<0.40	<1.60	<1.60
i-Propyl mercaptan	1.95	1.73	1.91	2.12
t-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60
n-Propyl mercaptan	4.54	3.86	10.8	10.5
s-Butyl mercaptan	6.76	5.21	11.8	12.4
i-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60
Dimethyl disulfide	<0.40	1.86	5.83	8.52
Tetrahydrothiophene	2.31	2.69	8.48	7.42
Unidentified sulfurs	8.20	8.66	20.6	23.2
	(Concentration in ppmv, as H_2S)			
Total Sulfur	741.10	698.98	1542.13	1564.58

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 6, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	208	212	210	1.8
	FL-1995 Inlet	187	187	187	0.07
	Hero Inlet	162	156	159	4.2
	Parnel Inlet	165	163	164	1.2
Carbonyl sulfide	Zeeco South	0.47	0.48	0.48	2.1
	FL-1995 Inlet	0.47	0.48	0.48	2.1
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
Methyl mercaptan	Zeeco South	132	133	133	0.83
	FL-1995 Inlet	128	126	127	1.5
	Hero Inlet	363	345	354	4.9
	Parnel Inlet	386	383	384	0.91
Ethyl mercaptan	Zeeco South	1.59	1.59	1.59	0.00
	FL-1995 Inlet	1.33	1.32	1.33	0.75
	Hero Inlet	4.00	3.96	3.98	1.0
	Parnel Inlet	3.60	3.58	3.59	0.56
Dimethyl sulfide	Zeeco South	376	369	373	1.9
	FL-1995 Inlet	363	352	357	3.2
	Hero Inlet	978	942	960	3.8
	Parnel Inlet	953	926	940	2.9
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
i-Propyl mercaptan	Zeeco South	1.96	1.94	1.95	1.0
	FL-1995 Inlet	1.76	1.69	1.73	4.1
	Hero Inlet	1.97	1.84	1.91	6.8
	Parnel Inlet	2.15	2.09	2.12	2.8
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	4.57	4.50	4.54	1.5
	FL-1995 Inlet	3.90	3.81	3.86	2.3
	Hero Inlet	10.9	10.7	10.8	1.6
	Parnel Inlet	10.6	10.3	10.5	2.8
s-Butyl mercaptan	Zeeco South	6.82	6.69	6.76	1.9
	FL-1995 Inlet	5.29	5.13	5.21	3.1
	Hero Inlet	11.9	11.6	11.8	2.3
	Parnel Inlet	12.4	12.4	12.4	0.24
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
Dimethyl disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	1.88	1.83	1.86	2.7
	Hero Inlet	5.91	5.75	5.83	2.7
	Parnel Inlet	8.58	8.46	8.52	1.4
Tetrahydrothiophene	Zeeco South	2.33	2.28	2.31	2.2
	FL-1995 Inlet	2.80	2.58	2.69	8.2
	Hero Inlet	8.69	8.27	8.48	5.0
	Parnel Inlet	7.40	7.43	7.42	0.40
Unidentified sulfurs	Zeeco South	8.32	8.08	8.20	2.9
	FL-1995 Inlet	8.68	8.63	8.66	0.58
	Hero Inlet	21.1	20.1	20.6	4.9
	Parnel Inlet	22.7	23.7	23.2	4.2

Four Tedlar bag samples, laboratory numbers 22506-(6-9), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 2.4%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22506-6	09.06.26	3:40 PM	X	X	X	X			
FL-2009 Inlet	LFG	-7	09.06.26	3:30 PM	X	X	X	X			
Hero Inlet	LFG	-8	09.06.26	3:55 PM	X	X	X	X			
Parnel Inlet	LFG	-9	09.06.26	4:05 PM	X	X	X	X			
~~Zeeco Inlet~~	LFG		09.06.26		X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/7/26	9:20 am		9/7/26	9:20 am
Relinquished by: *(Signature)*	**Date**	**Time**	**Received by:** *(Signature)*	**Date**	**Time**
	9/7/26	9:36 am		9/7/26	9:20
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by:** *(Signature)*	**Date**	**Time**
	9/7/26	10:10		9/7/26	10:10

Company Info:		Send Report to:		Analytical Laboratory
Company:	SCS Engineers	**Company:**	SCS Engineers	**AtmAA Inc.**
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:		**Email Address:**	CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 7, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22506-10	22506-11	22506-12	22506-13
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet
Components		*(Concentration in %v)*		
Oxygen	4.37	4.07	7.11	6.42
Nitrogen	21.38	24.75	32.82	29.27
Methane	28.15	27.28	10.47	12.73
Carbon Dioxide	41.09	38.12	41.20	42.38
Hydrogen	2.11	2.69	5.54	5.32
		(Concentration in ppmv)		
Carbon Monoxide	315	355	665	707
		(Concentration in %v, by component)		
TNMHC	0.245	0.195	0.505	0.445
		BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	309.1	300.7	147.0	169.1
BTU/ft3 (Wet @ 0.25636 psia)	303.7	295.5	144.4	166.2
BTU/lb (Dry @60F, 14.696 psia)	3778	3744	1714	1974

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 7, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	4.41	4.33	4.37	1.8
Nitrogen	Zeeco South	21.53	21.23	21.38	1.4
Methane	Zeeco South	28.09	28.20	28.15	0.39
Carbon Dioxide	Zeeco South	41.03	41.14	41.09	0.27
Hydrogen	Zeeco South	2.14	2.08	2.11	2.8
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	315	316	315	0.37
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.242	0.248	0.245	2.2

Four Tedlar bag samples, laboratory numbers 22506-(10-13), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 1.3%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 7, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22506-10	22506-11	22506-12	22506-13
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	213	127	132	156
Carbonyl sulfide	0.44	0.45	<1.60	<1.60
Methyl mercaptan	217	89.6	318	377
Ethyl mercaptan	2.00	0.94	3.38	3.23
Dimethyl sulfide	480	290	848	855
Carbon disulfide	<0.40	<0.40	<1.60	<1.60
i-Propyl mercaptan	1.68	1.16	1.51	1.76
t-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60
n-Propyl mercaptan	4.49	2.55	7.75	7.71
s-Butyl mercaptan	4.71	2.55	6.16	6.46
i-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60
Dimethyl disulfide	<0.40	2.37	2.08	3.90
Tetrahydrothiophene	0.80	0.54	1.67	1.38
Unidentified sulfurs	2.19	1.30	3.51	3.52
	(Concentration in ppmv, as H_2S)			
Total Sulfur	926.53	520.81	1326.65	1420.24

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 7, 2026
Date Received: September 7, 2026
Date Analyzed: September 7, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	209	217	213	3.7
	FL-1995 Inlet	128	126	127	1.8
	Hero Inlet	130	134	132	2.9
	Parnel Inlet	156	156	156	0.22
Carbonyl sulfide	Zeeco South	0.43	0.45	0.44	4.5
	FL-1995 Inlet	0.46	0.44	0.45	4.4
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
Methyl mercaptan	Zeeco South	217	218	217	0.40
	FL-1995 Inlet	90.1	89.1	89.6	1.1
	Hero Inlet	311	326	318	4.8
	Parnel Inlet	375	379	377	0.83
Ethyl mercaptan	Zeeco South	1.98	2.02	2.00	2.0
	FL-1995 Inlet	0.94	0.94	0.94	0.00
	Hero Inlet	3.30	3.46	3.38	4.7
	Parnel Inlet	3.18	3.28	3.23	3.1
Dimethyl sulfide	Zeeco South	484	475	480	1.7
	FL-1995 Inlet	292	287	290	1.7
	Hero Inlet	836	860	848	2.8
	Parnel Inlet	847	864	855	2.1
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
i-Propyl mercaptan	Zeeco South	1.66	1.69	1.68	1.8
	FL-1995 Inlet	1.17	1.15	1.16	1.7
	Hero Inlet	1.45	1.57	1.51	7.9
	Parnel Inlet	1.75	1.76	1.76	0.57
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	4.33	4.65	4.49	7.1
	FL-1995 Inlet	2.57	2.53	2.55	1.6
	Hero Inlet	7.69	7.80	7.75	1.4
	Parnel Inlet	7.53	7.88	7.71	4.5
s-Butyl mercaptan	Zeeco South	4.55	4.87	4.71	6.8
	FL-1995 Inlet	2.53	2.57	2.55	1.6
	Hero Inlet	6.03	6.28	6.16	4.1
	Parnel Inlet	6.36	6.56	6.46	3.1
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
Dimethyl disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	2.36	2.37	2.37	0.42
	Hero Inlet	1.97	2.18	2.08	10
	Parnel Inlet	3.81	3.99	3.90	4.6
Tetrahydrothiophene	Zeeco South	0.78	0.83	0.80	6.2
	FL-1995 Inlet	0.51	0.56	0.54	9.3
	Hero Inlet	1.62	1.72	1.67	6.0
	Parnel Inlet	1.35	1.40	1.38	3.6
Unidentified sulfurs	Zeeco South	2.09	2.28	2.19	8.7
	FL-1995 Inlet	1.28	1.31	1.30	2.3
	Hero Inlet	3.65	3.36	3.51	8.3
	Parnel Inlet	3.43	3.61	3.52	5.1

Four Tedlar bag samples, laboratory numbers 22506-(10-13), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 3.6%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: *(Signature)*	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22506-10	9/7/26	8:50 Am	X	X	X	X			
FL-1995 inlet ~~FL-2009 Inlet~~	LFG	-11	9/7/26	9:00 Am	X	X	X	X			
Hero Inlet	LFG	-12	9/7/26	8:20 Am	X	X	X	X			
Parnel Inlet	LFG	-13	9/7/26	8:30 Am	X	X	X	X			
Zeeco Inlet	LFG				X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9/7/26		**Received by:** *(Signature)*	9/7/26	9:30
Relinquished by: *(Signature)*	9/7/26	18:10	**Received by:** *(Signature)*		
Relinquished by: *(Signature)*			**Received for Laboratory by:** *(Signature)*	9/7/26	10:10

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach / CA / 90806	**City/State/Zip:** Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895 /562-335-0002	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:	**Email Address:** CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 8, 2026
Date Received: September 8, 2026
Date Analyzed: September 8, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22516-12	22516-13	22516-14	22516-15	22516-16
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	6.26	3.26	5.52	3.97	7.01
Nitrogen	27.59	22.61	28.01	21.66	33.39
Methane	26.58	30.19	9.70	16.28	15.05
Carbon Dioxide	33.75	38.98	45.56	49.03	37.12
Hydrogen	1.76	2.33	6.55	5.58	3.36
		(Concentration in ppmv)			
Carbon Monoxide	229	330	846	925	446
		(Concentration in %v, by component)			
TNMHC	0.312	0.250	0.901	0.785	0.533
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	300.2	332.1	166.1	224.1	194.3
BTU/ft3 (Wet @ 0.25636 psia)	294.9	326.3	163.2	220.2	190.9
BTU/lb (Dry @60F, 14.696 psia)	3757	4149	1889	2562	2302

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 8, 2026
Date Received: September 8, 2026
Date Analyzed: September 8, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.27	6.24	6.26	0.48
Nitrogen	Zeeco South	27.55	27.62	27.59	0.25
Methane	Zeeco South	26.52	26.63	26.58	0.41
Carbon Dioxide	Zeeco South	33.74	33.76	33.75	0.06
Hydrogen	Zeeco South	1.73	1.79	1.76	3.4
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	228	230	229	0.86
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.314	0.310	0.312	1.3

Five Tedlar bag samples, laboratory numbers 22516-(12-16), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.97%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 8, 2026
Date Received: September 8, 2026
Date Analyzed: September 8, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22516-12	22516-13	22516-14	22516-15	22516-16
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	161	192	181	245	126
Carbonyl sulfide	0.48	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	97.4	91.4	420	479	283
Ethyl mercaptan	1.21	1.01	4.68	4.77	2.92
Dimethyl sulfide	299	269	1149	1065	826
Carbon disulfide	<0.40	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.49	1.71	2.20	3.01	2.01
t-Butyl mercaptan	<0.40	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	3.39	2.82	14.4	13.7	8.94
s-Butyl mercaptan	4.42	4.10	14.9	16.6	11.2
i-Butyl mercaptan	<0.40	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	3.16	1.20	4.61	6.31	6.62
Tetrahydrothiophene	2.55	1.70	11.2	8.82	6.23
Unidentified sulfurs	9.95	4.86	32.5	38.1	25.7
	(Concentration in ppmv, as H_2S)				
Total Sulfur	587.52	570.68	1838.17	1886.49	1305.30

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 8, 2026
Date Received: September 8, 2026
Date Analyzed: September 8, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	161	162	161	0.72
	FL-1995 Inlet	189	195	192	2.7
	Hero Inlet	182	179	181	1.7
	Parnel Inlet	252	238	245	5.6
	Zeeco Inlet	130	122	126	7.1
Carbonyl sulfide	Zeeco South	0.48	0.47	0.48	2.1
	FL-1995 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	97.4	97.4	97.4	0.04
	FL-1995 Inlet	91.0	91.7	91.4	0.74
	Hero Inlet	421	419	420	0.59
	Parnel Inlet	487	470	479	3.4
	Zeeco Inlet	292	274	283	6.1
Ethyl mercaptan	Zeeco South	1.20	1.22	1.21	1.7
	FL-1995 Inlet	1.01	1.00	1.01	1.0
	Hero Inlet	4.67	4.69	4.68	0.43
	Parnel Inlet	4.84	4.70	4.77	2.9
	Zeeco Inlet	2.93	2.91	2.92	0.68
Dimethyl sulfide	Zeeco South	297	301	299	1.4
	FL-1995 Inlet	269	269	269	0.06
	Hero Inlet	1150	1147	1149	0.25
	Parnel Inlet	1078	1051	1065	2.5
	Zeeco Inlet	852	800	826	6.4
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.50	1.47	1.49	2.0
	FL-1995 Inlet	1.74	1.67	1.71	4.1
	Hero Inlet	2.16	2.24	2.20	3.6
	Parnel Inlet	3.01	3.00	3.01	0.33
	Zeeco Inlet	1.95	2.07	2.01	6.0



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	3.28	3.49	3.39	6.2
	FL-1995 Inlet	2.83	2.81	2.82	0.71
	Hero Inlet	14.4	14.4	14.4	0.14
	Parnel Inlet	13.8	13.5	13.7	2.4
	Zeeco Inlet	9.24	8.64	8.94	6.7
s-Butyl mercaptan	Zeeco South	4.39	4.45	4.42	1.4
	FL-1995 Inlet	4.15	4.05	4.10	2.4
	Hero Inlet	14.8	14.9	14.9	0.27
	Parnel Inlet	16.8	16.5	16.6	2.1
	Zeeco Inlet	11.4	11.0	11.2	3.6
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	3.12	3.19	3.16	2.2
	FL-1995 Inlet	1.18	1.22	1.20	3.3
	Hero Inlet	4.61	4.61	4.61	0.00
	Parnel Inlet	6.37	6.25	6.31	1.9
	Zeeco Inlet	6.90	6.33	6.62	8.6
Tetrahydrothiophene	Zeeco South	2.56	2.54	2.55	0.78
	FL-1995 Inlet	1.74	1.66	1.70	4.7
	Hero Inlet	11.1	11.2	11.2	1.2
	Parnel Inlet	8.86	8.77	8.82	1.0
	Zeeco Inlet	6.19	6.26	6.23	1.1
Unidentified sulfurs	Zeeco South	9.83	10.1	10.0	2.4
	FL-1995 Inlet	4.84	4.87	4.86	0.62
	Hero Inlet	32.7	32.2	32.5	1.7
	Parnel Inlet	37.4	38.8	38.1	3.7
	Zeeco Inlet	26.9	24.6	25.7	8.9

Five Tedlar bag samples, laboratory numbers 22516-(12-16), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.6%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)* Brandon Rodriguez	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22516-12	9-8-26	8:40am	X	X	X	X			
FL ~~2009~~ 1995 Inlet	LFG	-13	9-8-26	7:10am	X	X	X	X			
Hero Inlet	LFG	-14	9-8-26	7:30am	X	X	X	X			
Parnel Inlet	LFG	-15	9-8-26	7:55am	X	X	X	X			
Zeeco Inlet	LFG	-16	9-8-26	8:20am	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9-8-26	9:11am	Ruben G	9/8/26	9:11
Relinquished by: *(Signature)* Ruben G	**Date** 9/8/26	**Time** 10:29	**Received by: *(Signature)***	**Date**	**Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by: *(Signature)***	**Date** 9/8/26	**Time** 10:29

Company Info:		Send Report to:		Analytical Laboratory
Company:	SCS Engineers	**Company:**	SCS Engineers	**AtmAA Inc.**
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:		**Email Address:**	CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 9, 2026
Date Received: September 9, 2026
Date Analyzed: September 9, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22526-4	22526-5	22526-6	22526-7	22526-8
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	6.84	3.82	6.11	5.86	7.60
Nitrogen	30.05	24.77	31.42	29.52	35.99
Methane	25.65	26.89	10.58	13.67	14.72
Carbon Dioxide	32.76	39.22	42.48	42.87	35.44
Hydrogen	1.50	2.88	5.70	5.24	3.02
		(Concentration in ppmv)			
Carbon Monoxide	166	410	775	816	470
		(Concentration in %v, by component)			
TNMHC	0.322	0.338	0.864	0.770	0.559
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	287.4	303.1	169.6	193.9	189.2
BTU/ft3 (Wet @ 0.25636 psia)	282.4	297.8	166.6	190.6	185.9
BTU/lb (Dry @60F, 14.696 psia)	3594	3742	1954	2255	2252

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 9, 2026
Date Received: September 9, 2026
Date Analyzed: September 9, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.85	6.83	6.84	0.29
Nitrogen	Zeeco South	30.04	30.05	30.05	0.03
Methane	Zeeco South	25.66	25.64	25.65	0.08
Carbon Dioxide	Zeeco South	32.64	32.87	32.76	0.70
Hydrogen	Zeeco South	1.50	1.50	1.50	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	167	165	166	0.96
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.322	0.321	0.322	0.52

Five Tedlar bag samples, laboratory numbers 22526-(4-8), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.37%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 9, 2026
Date Received: September 9, 2026
Date Analyzed: September 9, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22526-4	22526-5	22526-6	22526-7	22526-8
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	145	217	161	182	143
Carbonyl sulfide	0.41	0.51	<1.60	<1.60	<1.20
Methyl mercaptan	107	161	352	396	283
Ethyl mercaptan	1.25	1.64	4.07	3.96	2.83
Dimethyl sulfide	292	449	1011	987	731
Carbon disulfide	<0.40	<0.40	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.27	1.98	2.07	2.42	2.05
t-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
n-Propyl mercaptan	3.26	4.64	12.7	12.3	8.14
s-Butyl mercaptan	4.29	6.10	13.4	14.4	10.3
i-Butyl mercaptan	<0.40	<0.40	<1.60	<1.60	<1.20
Dimethyl disulfide	3.99	1.65	5.61	10.6	5.83
Tetrahydrothiophene	2.73	2.98	10.1	8.58	5.47
Unidentified sulfurs	10.1	10.7	35.1	40.2	22.4
	(Concentration in ppmv, as H_2S)				
Total Sulfur	575.31	858.35	1613.25	1668.02	1220.20

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 9, 2026
Date Received: September 9, 2026
Date Analyzed: September 9, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	143	147	145	2.3
	FL-2009 Inlet	217	216	217	0.44
	Hero Inlet	162	160	161	0.89
	Parnel Inlet	183	181	182	1.3
	Zeeco Inlet	140	147	143	5.1
Carbonyl sulfide	Zeeco South	0.41	<0.40	---	---
	FL-2009 Inlet	0.51	0.51	0.51	0.00
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	106	109	107	3.3
	FL-2009 Inlet	161	160	161	0.57
	Hero Inlet	353	351	352	0.61
	Parnel Inlet	398	393	396	1.4
	Zeeco Inlet	278	287	283	3.0
Ethyl mercaptan	Zeeco South	1.22	1.28	1.25	4.8
	FL-2009 Inlet	1.65	1.62	1.64	1.8
	Hero Inlet	4.12	4.02	4.07	2.5
	Parnel Inlet	4.04	3.88	3.96	4.0
	Zeeco Inlet	2.76	2.90	2.83	5.1
Dimethyl sulfide	Zeeco South	288	295	292	2.4
	FL-2009 Inlet	452	446	449	1.1
	Hero Inlet	1016	1006	1011	1.0
	Parnel Inlet	993	982	987	1.0
	Zeeco Inlet	717	746	731	3.9
Carbon disulfide	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.27	1.27	1.27	0.00
	FL-2009 Inlet	1.98	1.98	1.98	0.00
	Hero Inlet	2.05	2.08	2.07	1.5
	Parnel Inlet	2.42	2.41	2.42	0.41
	Zeeco Inlet	2.01	2.09	2.05	4.1

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.60	---	---
n-Propyl mercaptan	Zeeco South	3.23	3.28	3.26	1.5
	FL-2009 Inlet	4.72	4.55	4.64	3.7
	Hero Inlet	12.8	12.6	12.7	1.6
	Parnel Inlet	12.5	12.2	12.3	2.9
	Zeeco Inlet	8.00	8.29	8.14	3.6
s-Butyl mercaptan	Zeeco South	4.23	4.34	4.29	2.6
	FL-2009 Inlet	6.18	6.01	6.10	2.8
	Hero Inlet	13.5	13.3	13.4	1.6
	Parnel Inlet	14.4	14.4	14.4	0.28
	Zeeco Inlet	9.91	10.7	10.3	7.8
i-Butyl mercaptan	Zeeco South	<0.40	<0.40	---	---
	FL-2009 Inlet	<0.40	<0.40	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	3.91	4.06	3.99	3.8
	FL-2009 Inlet	1.70	1.60	1.65	6.1
	Hero Inlet	5.66	5.55	5.61	2.0
	Parnel Inlet	10.7	10.6	10.6	1.2
	Zeeco Inlet	5.56	6.09	5.83	9.1
Tetrahydrothiophene	Zeeco South	2.70	2.75	2.73	1.8
	FL-2009 Inlet	3.00	2.96	2.98	1.3
	Hero Inlet	10.2	9.92	10.1	2.7
	Parnel Inlet	8.65	8.50	8.58	1.7
	Zeeco Inlet	5.25	5.69	5.47	8.1
Unidentified sulfurs	Zeeco South	9.71	10.5	10.1	7.5
	FL-2009 Inlet	11.1	10.4	10.7	6.4
	Hero Inlet	35.1	35.1	35.1	0.09
	Parnel Inlet	40.6	39.7	40.2	2.3
	Zeeco Inlet	21.5	23.2	22.4	7.4

Five Tedlar bag samples, laboratory numbers 22526-(4-8), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.8%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: *(Signature)* Branden Rodriguez	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22526-4	9.9.26	8:53am	X	X	X	X			
FL-2009 Inlet	LFG	-5	9.9.26	7:45am	X	X	X	X			
Hero Inlet	LFG	-6	9.9.26	8:40am	X	X	X	X			
Parnel Inlet	LFG	-7	9.9.26	8:25am	X	X	X	X			
Zeeco Inlet	LFG	-8	9.9.26	8:30am	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9.9.26	9:03	Ruben G	9/9/26	9:03
Relinquished by: *(Signature)* Ruben G	9/9/26	10:28	**Received by: *(Signature)***	**Date**	**Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by: *(Signature)***	9/9/26	10:26

Company Info:		Send Report to:		Analytical Laboratory
Company:	SCS Engineers	**Company:**	SCS Engineers	**AtmAA Inc.**
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:		**Email Address:**	CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 10, 2026
Date Received: September 10, 2026
Date Analyzed: September 10, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22536-8	22536-9	22536-10
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet
Components	*(Concentration in %v)*		
Oxygen	5.20	4.50	4.62
Nitrogen	23.39	25.12	25.79
Methane	30.10	25.68	10.09
Carbon Dioxide	35.88	37.86	46.72
Hydrogen	1.31	2.70	6.71
	(Concentration in ppmv)		
Carbon Monoxide	153	421	873
	(Concentration in %v, by component)		
TNMHC	0.306	0.346	1.019
	BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	335.3	295.3	178.0
BTU/ft3 (Wet @ 0.25636 psia)	329.4	290.2	174.9
BTU/lb (Dry @60F, 14.696 psia)	4199	3640	2014

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon. The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported. Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 10, 2026
Date Received: September 10, 2026
Date Analyzed: September 10, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	5.21	5.19	5.20	0.38
Nitrogen	Zeeco South	23.34	23.44	23.39	0.43
Methane	Zeeco South	30.11	30.08	30.10	0.10
Carbon Dioxide	Zeeco South	36.02	35.74	35.88	0.78
Hydrogen	Zeeco South	1.31	1.30	1.31	0.77
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	152	154	153	1.2
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.303	0.308	0.306	1.7

Three Tedlar bag samples, laboratory numbers 22536-(8-10), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from three Tedlar bag samples is 0.77%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 10, 2026
Date Received: September 10, 2026
Date Analyzed: September 10, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22536-8	22536-9	22536-10
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet
Components	*(Concentration in ppmv)*		
Hydrogen sulfide	188	214	166
Carbonyl sulfide	0.60	0.53	<1.60
Methyl mercaptan	95.5	177	414
Ethyl mercaptan	1.38	1.94	4.68
Dimethyl sulfide	284	484	1169
Carbon disulfide	<0.50	<0.50	<1.60
i-Propyl mercaptan	1.77	2.23	2.03
t-Butyl mercaptan	<0.50	<0.50	<1.60
n-Propyl mercaptan	3.65	5.62	14.5
s-Butyl mercaptan	5.32	7.60	14.8
i-Butyl mercaptan	<0.50	<0.50	<1.60
Dimethyl disulfide	4.58	2.27	6.89
Tetrahydrothiophene	2.98	3.52	12.1
Unidentified sulfurs	13.0	15.0	34.3
	(Concentration in ppmv, as H_2S)		
Total Sulfur	605.08	917.31	1844.77

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 10, 2026
Date Received: September 10, 2026
Date Analyzed: September 10, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	190	186	188	2.4
	FL-2009 Inlet	213	216	214	1.7
	Hero Inlet	166	166	166	0.45
Carbonyl sulfide	Zeeco South	0.59	0.60	0.60	1.7
	FL-2009 Inlet	0.52	0.53	0.53	2.7
	Hero Inlet	<1.60	<1.60	---	---
Methyl mercaptan	Zeeco South	95.0	95.9	95.5	0.96
	FL-2009 Inlet	175	180	177	2.4
	Hero Inlet	414	414	414	0.02
Ethyl mercaptan	Zeeco South	1.37	1.39	1.38	1.4
	FL-2009 Inlet	1.92	1.96	1.94	2.1
	Hero Inlet	4.68	4.68	4.68	0.00
Dimethyl sulfide	Zeeco South	287	281	284	2.1
	FL-2009 Inlet	477	492	484	3.2
	Hero Inlet	1165	1172	1169	0.65
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
i-Propyl mercaptan	Zeeco South	1.76	1.78	1.77	1.1
	FL-2009 Inlet	2.21	2.25	2.23	1.8
	Hero Inlet	2.04	2.01	2.03	1.5
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
n-Propyl mercaptan	Zeeco South	3.62	3.68	3.65	1.6
	FL-2009 Inlet	5.51	5.73	5.62	3.9
	Hero Inlet	14.5	14.5	14.5	0.14
s-Butyl mercaptan	Zeeco South	5.28	5.35	5.32	1.3
	FL-2009 Inlet	7.48	7.73	7.60	3.2
	Hero Inlet	14.8	14.7	14.8	0.95



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
Dimethyl disulfide	Zeeco South	4.48	4.68	4.58	4.4
	FL-2009 Inlet	2.25	2.29	2.27	1.6
	Hero Inlet	6.89	6.89	6.89	0.00
Tetrahydrothiophene	Zeeco South	2.92	3.03	2.98	3.7
	FL-2009 Inlet	3.54	3.50	3.52	1.1
	Hero Inlet	12.3	12.0	12.1	2.6
Unidentified sulfurs	Zeeco South	12.7	13.3	13.0	4.5
	FL-2009 Inlet	15.1	14.9	15.0	1.0
	Hero Inlet	33.4	35.1	34.3	4.8

Three Tedlar bag samples, laboratory numbers 22536-(8-10), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from three Tedlar bag samples is 1.9%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 4	
Sampler: *(Signature)* Brandon Rodriguez	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22536-8	9.10.26	8:40am	X	X	X	X			
FL-2009 Inlet	LFG	-9	9.10.26	7:35am	X	X	X	X			
Hero Inlet	LFG	-10	9.10.26	8:15am	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9.10.26	9:12		9.10.26	9:12
Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/10/26	10:19			
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date	Time
				9/10/26	10:19

Company Info:		Send Report to:	
Company:	SCS Engineers	**Company:**	SCS Engineers
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong
Fax No.:		**Email Address:**	CFong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 10, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22546-1
Sample I.D.:	Parnel Inlet

Components	*(Concentration in %v)*
Oxygen	5.79
Nitrogen	25.44
Methane	15.71
Carbon Dioxide	44.56
Hydrogen	4.92
	(Concentration in ppmv)
Carbon Monoxide	859
	(Concentration in %v, by component)
TNMHC	0.688
	BTU (HHV)
BTU/ft3 (Dry @60F, 14.696 psia)	209.9
BTU/ft3 (Wet @ 0.25636 psia)	206.3
BTU/lb (Dry @60F, 14.696 psia)	2436

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

B Fung

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 10, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Parnel Inlet	5.81	5.77	5.79	0.69
Nitrogen	Parnel Inlet	25.46	25.41	25.44	0.20
Methane	Parnel Inlet	15.62	15.80	15.71	1.1
Carbon Dioxide	Parnel Inlet	44.46	44.65	44.56	0.43
Hydrogen	Parnel Inlet	4.94	4.90	4.92	0.81
		(Concentration in ppmv)			
Carbon Monoxide	Parnel Inlet	864	854	859	1.2
		(Concentration in %v, by component)			
TNMHC	Parnel Inlet	0.688	0.688	0.688	0.00

One Tedlar bag sample, laboratory number 22546-1, was analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from one Tedlar bag sample is 0.64%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 10, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22546-1
Sample I.D.:	Parnel Inlet

Components	*(Concentration in ppmv)*
Hydrogen sulfide	219
Carbonyl sulfide	<1.60
Methyl mercaptan	401
Ethyl mercaptan	3.98
Dimethyl sulfide	907
Carbon disulfide	<1.60
i-Propyl mercaptan	2.61
t-Butyl mercaptan	<1.60
n-Propyl mercaptan	11.0
s-Butyl mercaptan	12.5
i-Butyl mercaptan	<1.60
Dimethyl disulfide	6.74
Tetrahydrothiophene	5.26
Unidentified sulfurs	18.5

(Concentration in ppmv, as H_2S)

Total Sulfur	1595.03

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 10, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Parnel Inlet	217	221	219	1.7
Carbonyl sulfide	Parnel Inlet	<1.60	<1.60	---	---
Methyl mercaptan	Parnel Inlet	400	403	401	0.80
Ethyl mercaptan	Parnel Inlet	4.00	3.96	3.98	1.0
Dimethyl sulfide	Parnel Inlet	907	907	907	0.04
Carbon disulfide	Parnel Inlet	<1.60	<1.60	---	---
i-Propyl mercaptan	Parnel Inlet	2.74	2.48	2.61	10
t-Butyl mercaptan	Parnel Inlet	<1.60	<1.60	---	---
n-Propyl mercaptan	Parnel Inlet	11.2	10.9	11.0	2.4
s-Butyl mercaptan	Parnel Inlet	12.7	12.4	12.5	2.9
i-Butyl mercaptan	Parnel Inlet	<1.60	<1.60	---	---
Dimethyl disulfide	Parnel Inlet	6.80	6.68	6.74	1.8
Tetrahydrothiophene	Parnel Inlet	5.14	5.39	5.26	4.8
Unidentified sulfurs	Parnel Inlet	18.8	18.2	18.5	3.4

One Tedlar bag sample, laboratory number 22546-1, was analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from one Tedlar bag sample is 2.9%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: (Signature)	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG				X	X	X	X			
FL-2009 Inlet	LFG				X	X	X	X			
Hero Inlet	LFG				X	X	X	X			
Parnel Inlet	LFG	22546-1	9.10.26	2:15pm	X	X	X	X			
Zeeco Inlet	LFG				X	X	X	X			

ANALYSES REQUESTED

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	9.11.26	0600		9-11-26	6:00am
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	9-11-26	9:00		9/11/26	9:00
Relinquished by: (Signature)	Date	Time	Received for Laboratory by: (Signature)	Date	Time
	9/11/26	10:10		9/11/26	10:10

Company Info:

Company: SCS Engineers
Street Address: 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach / CA / 90806
Telephone No.: 562-743-7895 /562-335-0002
Fax No.:

Send Report to:

Company: SCS Engineers
Street Address: 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach / CA / 90806
Project Manager: Cornelius Fong
Email Address: CFong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 11, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22546-2	22546-3	22546-4	22546-5
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet
Components	*(Concentration in %v)*			
Oxygen	6.48	3.81	5.18	3.71
Nitrogen	27.99	23.69	28.09	19.19
Methane	27.46	27.59	9.13	17.31
Carbon Dioxide	33.49	39.59	45.18	50.54
Hydrogen	1.29	2.67	6.84	5.86
	(Concentration in ppmv)			
Carbon Monoxide	166	384	890	1018
	(Concentration in %v, by component)			
TNMHC	0.283	0.333	0.902	0.761
	BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	304.0	310.1	163.1	234.6
BTU/ft3 (Wet @ 0.25636 psia)	298.7	304.7	160.2	230.5
BTU/lb (Dry @60F, 14.696 psia)	3812	3824	1856	2680

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 11, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.49	6.46	6.48	0.46
Nitrogen	Zeeco South	28.13	27.84	27.99	1.0
Methane	Zeeco South	27.33	27.58	27.46	0.91
Carbon Dioxide	Zeeco South	33.46	33.52	33.49	0.18
Hydrogen	Zeeco South	1.29	1.29	1.29	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	165	168	166	1.6
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.281	0.286	0.283	1.6

Four Tedlar bag samples, laboratory numbers 22546-(2-5), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.83%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 11, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22546-2	22546-3	22546-4	22546-5
Sample I.D.:	Zeeco South	FL-1995 Inlet	Hero Inlet	Parnel Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	160	200	151	258
Carbonyl sulfide	<0.50	0.51	<1.60	<1.60
Methyl mercaptan	97.8	149	393	475
Ethyl mercaptan	1.24	1.47	4.33	4.80
Dimethyl sulfide	248	420	1105	1083
Carbon disulfide	<0.50	<0.50	<1.60	<1.60
i-Propyl mercaptan	1.37	1.87	1.76	3.17
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60
n-Propyl mercaptan	2.86	4.31	13.5	13.7
s-Butyl mercaptan	4.23	5.88	13.5	16.8
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60
Dimethyl disulfide	1.84	1.90	6.39	7.26
Tetrahydrothiophene	2.09	2.70	11.1	8.69
Unidentified sulfurs	7.56	11.3	32.7	33.6
	(Concentration in ppmv, as H_2S)			
Total Sulfur	528.65	800.96	1738.74	1911.42

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 11, 2026
Date Received: September 11, 2026
Date Analyzed: September 11, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	158	161	160	2.1
	FL-1995 Inlet	201	198	200	1.5
	Hero Inlet	150	153	151	2.4
	Parnel Inlet	255	261	258	2.3
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-1995 Inlet	0.51	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
Methyl mercaptan	Zeeco South	97.0	98.5	97.8	1.6
	FL-1995 Inlet	149	149	149	0.11
	Hero Inlet	390	397	393	1.8
	Parnel Inlet	471	478	475	1.5
Ethyl mercaptan	Zeeco South	1.25	1.22	1.24	2.4
	FL-1995 Inlet	1.46	1.47	1.47	0.68
	Hero Inlet	4.35	4.30	4.33	1.2
	Parnel Inlet	4.77	4.83	4.80	1.3
Dimethyl sulfide	Zeeco South	249	247	248	1.1
	FL-1995 Inlet	420	421	420	0.24
	Hero Inlet	1095	1114	1105	1.7
	Parnel Inlet	1078	1089	1083	1.0
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
i-Propyl mercaptan	Zeeco South	1.35	1.39	1.37	2.9
	FL-1995 Inlet	1.90	1.83	1.87	3.8
	Hero Inlet	1.78	1.74	1.76	2.3
	Parnel Inlet	3.14	3.19	3.17	1.6
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	2.91	2.81	2.86	3.50
	FL-1995 Inlet	4.36	4.25	4.31	2.6
	Hero Inlet	13.5	13.6	13.5	0.66
	Parnel Inlet	13.8	13.6	13.7	0.80
s-Butyl mercaptan	Zeeco South	4.26	4.19	4.23	1.7
	FL-1995 Inlet	5.95	5.80	5.88	2.6
	Hero Inlet	13.3	13.7	13.5	2.4
	Parnel Inlet	16.8	16.7	16.8	0.66
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
Dimethyl disulfide	Zeeco South	1.84	1.84	1.84	0.00
	FL-1995 Inlet	1.94	1.86	1.90	4.2
	Hero Inlet	6.34	6.43	6.39	1.4
	Parnel Inlet	7.16	7.35	7.26	2.6
Tetrahydrothiophene	Zeeco South	2.03	2.15	2.09	5.7
	FL-1995 Inlet	2.70	2.70	2.70	0.00
	Hero Inlet	11.0	11.2	11.1	1.7
	Parnel Inlet	8.96	8.42	8.69	6.2
Unidentified sulfurs	Zeeco South	7.74	7.38	7.56	4.8
	FL-1995 Inlet	11.4	11.2	11.3	1.6
	Hero Inlet	32.0	33.5	32.7	4.4
	Parnel Inlet	33.0	34.2	33.6	3.5

Four Tedlar bag samples, laboratory numbers 22546-(2-5), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 2.1%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: *(Signature)* Brunden Rodriguez	**Chain of Custody Tape No.**

ANALYSES REQUESTED

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22546-2	9.11.26	8:35am	X	X	X	X			
FL-2009 Inlet	LFG	-3	9.11.26	7:15am	X	X	X	X			
Hero Inlet	LFG	-4	9.11.26	7:50am	X	X	X	X			
Parnel Inlet	LFG	-5	9.11.26	8:15am	X	X	X	X			
Zeeco Inlet	LFG				X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9.11.26	9:00	**Received by: *(Signature)*** Ruben G	9/11/26	9:00
Relinquished by: *(Signature)* Ruben G	9/11/26	10:10	**Received by: *(Signature)***	**Date**	**Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by: *(Signature)***	9/11/26	10:10

Company Info:	**Send Report to:**	**Analytical Laboratory**
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach / CA / 90806	**City/State/Zip:** Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895 /562-335-0002	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:	**Email Address:** CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 11, 2026
Date Received: September 12, 2026
Date Analyzed: September 14, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22556-3
Sample I.D.:	Zeeco Inlet

Components	*(Concentration in %v)*
Oxygen	5.08
Nitrogen	27.96
Methane	18.81
Carbon Dioxide	42.00
Hydrogen	3.37
	(Concentration in ppmv)
Carbon Monoxide	503
	(Concentration in %v, by component)
TNMHC	0.572
	BTU (HHV)
BTU/ft3 (Dry @60F, 14.696 psia)	232.4
BTU/ft3 (Wet @ 0.25636 psia)	228.4
BTU/lb (Dry @60F, 14.696 psia)	2735

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon. The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported. Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 11, 2026
Date Received: September 12, 2026
Date Analyzed: September 14, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco Inlet	5.07	5.08	5.08	0.20
Nitrogen	Zeeco Inlet	27.89	28.02	27.96	0.47
Methane	Zeeco Inlet	18.80	18.81	18.81	0.05
Carbon Dioxide	Zeeco Inlet	42.07	41.93	42.00	0.33
Hydrogen	Zeeco Inlet	3.36	3.37	3.37	0.30
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco Inlet	505	500	503	1.0
		(Concentration in %v, by component)			
TNMHC	Zeeco Inlet	0.573	0.570	0.572	0.51

One Tedlar bag sample, laboratory number 22556-3, was analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from one Tedlar bag sample is 0.41%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 11, 2026
Date Received: September 12, 2026
Date Analyzed: September 12, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22556-3
Sample I.D.:	Zeeco Inlet

Components	*(Concentration in ppmv)*
Hydrogen sulfide	121
Carbonyl sulfide	<1.20
Methyl mercaptan	267
Ethyl mercaptan	2.82
Dimethyl sulfide	811
Carbon disulfide	<1.20
i-Propyl mercaptan	1.91
t-Butyl mercaptan	<1.20
n-Propyl mercaptan	8.54
s-Butyl mercaptan	10.2
i-Butyl mercaptan	<1.20
Dimethyl disulfide	4.28
Tetrahydrothiophene	5.99
Unidentified sulfurs	23.9

(Concentration in ppmv, as H_2S)

Total Sulfur	1260.92

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 11, 2026
Date Received: September 12, 2026
Date Analyzed: September 12, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco Inlet	123.7	119	121	3.9
Carbonyl sulfide	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco Inlet	269	264	267	1.9
Ethyl mercaptan	Zeeco Inlet	2.67	2.97	2.82	11
Dimethyl sulfide	Zeeco Inlet	812	810	811	0.19
Carbon disulfide	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco Inlet	1.78	2.04	1.91	14
t-Butyl mercaptan	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco Inlet	8.44	8.64	8.54	2.3
s-Butyl mercaptan	Zeeco Inlet	9.98	10.5	10.2	4.9
i-Butyl mercaptan	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco Inlet	4.26	4.30	4.28	0.93
Tetrahydrothiophene	Zeeco Inlet	5.63	6.35	5.99	12
Unidentified sulfurs	Zeeco Inlet	23.0	24.8	23.9	7.6

One Tedlar bag sample, laboratory number 22556-3, was analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from one Tedlar bag sample is 5.8%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Turnaround Times:** Standard 10 day
	Expedited: 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
					ANALYSES REQUESTED						
Zeeco South station	LFG				X	X	X	X			
FL-2009 Inlet	LFG				X	X	X	X			
Hero Inlet	LFG				X	X	X	X			
Parnel Inlet	LFG				X	X	X	X			
Zeeco Inlet	LFG	22556-3	9.11.26	5:05pm	X	X	X	X			

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9.12.26	8:00am		9/12/26	9:09am
Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/12/26	9:09		9/12/26	10:15
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date	Time

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Sui	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach, CA 90806	**City/State/Zip:** Long Beach, CA 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Email Address:	**Email Address:** cfong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 12, 2026
Date Received: September 12, 2026
Date Analyzed: September 14, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22556-4	22556-5	22556-6	22556-7	22556-8
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	6.03	3.90	5.60	3.95	7.42
Nitrogen	27.96	23.07	30.16	19.50	35.77
Methane	29.97	31.27	9.55	18.76	15.83
Carbon Dioxide	34.46	37.86	44.95	49.76	36.20
Hydrogen	1.14	2.06	6.32	5.15	3.01
		(Concentration in ppmv)			
Carbon Monoxide	164	324	872	889	464
		(Concentration in %v, by component)			
TNMHC	0.232	0.267	0.935	0.701	0.476
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	318.1	340.7	163.1	243.7	194.1
BTU/ft3 (Wet @ 0.25636 psia)	312.6	334.8	160.2	239.5	190.7
BTU/lb (Dry @60F, 14.696 psia)	4017	4288	1859	2798	2319

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 12, 2026
Date Received: September 12, 2026
Date Analyzed: September 14, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	5.99	6.06	6.03	1.2
Nitrogen	Zeeco South	27.90	28.02	27.96	0.43
Methane	Zeeco South	30.04	29.89	29.97	0.50
Carbon Dioxide	Zeeco South	34.61	34.31	34.46	0.87
Hydrogen	Zeeco South	1.13	1.14	1.14	0.88
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	165	164	164	0.30
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.232	0.233	0.232	0.45

Five Tedlar bag samples, laboratory numbers 22556-(4-8), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.66%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 1, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 12, 2026
Date Received: September 12, 2026
Date Analyzed: September 12, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22556-4	22556-5	22556-6	22556-7	22556-8
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	143	206	175	271	102
Carbonyl sulfide	0.52	0.57	<1.60	<1.60	<1.20
Methyl mercaptan	48.4	95.7	452	474	232
Ethyl mercaptan	0.91	1.12	4.92	4.66	2.43
Dimethyl sulfide	170	274	1216	1105	705
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.27	1.94	2.09	3.26	1.59
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.24	3.02	14.8	13.8	7.33
s-Butyl mercaptan	3.36	4.52	15.2	17.3	8.80
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	1.31	0.70	5.75	9.80	3.26
Tetrahydrothiophene	1.66	1.93	12.6	8.70	4.91
Unidentified sulfurs	6.41	9.25	41.1	41.5	19.6
	(Concentration in ppmv, as H_2S)				
Total Sulfur	381.07	600.25	1944.96	1958.31	1089.80

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 12, 2026
Date Received: September 12, 2026
Date Analyzed: September 12, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	139	148	143	5.9
	FL-2009 Inlet	205	208	206	1.6
	Hero Inlet	175	175	175	0.17
	Parnel Inlet	267	275	271	2.8
	Zeeco Inlet	99.4	104	102	4.6
Carbonyl sulfide	Zeeco South	0.51	0.53	0.52	3.8
	FL-2009 Inlet	0.56	0.57	0.57	1.8
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	47.1	49.7	48.4	5.2
	FL-2009 Inlet	96.1	95.3	95.7	0.87
	Hero Inlet	451	453	452	0.42
	Parnel Inlet	467	481	474	2.9
	Zeeco Inlet	230	234	232	1.5
Ethyl mercaptan	Zeeco South	0.86	0.95	0.91	9.9
	FL-2009 Inlet	1.13	1.11	1.12	1.8
	Hero Inlet	4.90	4.94	4.92	0.81
	Parnel Inlet	4.62	4.70	4.66	1.7
	Zeeco Inlet	2.46	2.40	2.43	2.5
Dimethyl sulfide	Zeeco South	167	173	170	3.8
	FL-2009 Inlet	272	276	274	1.4
	Hero Inlet	1214	1218	1216	0.29
	Parnel Inlet	1087	1122	1105	3.2
	Zeeco Inlet	696	714	705	2.5
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.24	1.30	1.27	4.7
	FL-2009 Inlet	1.91	1.96	1.94	2.6
	Hero Inlet	2.08	2.09	2.09	0.48
	Parnel Inlet	3.17	3.34	3.26	5.2
	Zeeco Inlet	1.49	1.68	1.59	12

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.21	2.26	2.24	2.2
	FL-2009 Inlet	3.00	3.04	3.02	1.3
	Hero Inlet	14.7	14.8	14.8	1.0
	Parnel Inlet	13.6	14.0	13.8	3.1
	Zeeco Inlet	7.38	7.28	7.33	1.4
s-Butyl mercaptan	Zeeco South	3.30	3.42	3.36	3.6
	FL-2009 Inlet	4.44	4.60	4.52	3.5
	Hero Inlet	15.2	15.2	15.2	0.39
	Parnel Inlet	16.9	17.7	17.3	4.6
	Zeeco Inlet	8.96	8.64	8.80	3.6
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	1.30	1.31	1.31	0.77
	FL-2009 Inlet	0.69	0.70	0.70	1.4
	Hero Inlet	5.72	5.78	5.75	1.0
	Parnel Inlet	9.53	10.1	9.80	5.4
	Zeeco Inlet	3.28	3.23	3.26	1.5
Tetrahydrothiophene	Zeeco South	1.59	1.73	1.66	8.4
	FL-2009 Inlet	1.92	1.93	1.93	0.52
	Hero Inlet	12.6	12.7	12.6	1.0
	Parnel Inlet	8.52	8.88	8.70	4.1
	Zeeco Inlet	4.91	4.91	4.91	0.00
Unidentified sulfurs	Zeeco South	6.38	6.430	6.41	0.78
	FL-2009 Inlet	9.27	9.22	9.25	0.54
	Hero Inlet	40.7	41.4	41.1	1.7
	Parnel Inlet	39.7	43.3	41.5	8.6
	Zeeco Inlet	19.9	19.3	19.6	3.2

Five Tedlar bag samples, laboratory numbers 22556-(4-8), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.8%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)* Luis Cruz	**Turnaround Times:** Standard 10 day **Expedited:** 24hr / 48hr / 72hr / 5 day

ANALYSES REQUESTED

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22556-4	9/12/26	9:00 am	X	X	X	X			
FL-2009 Inlet	LFG	-5	9/12/26	8:54 am	X	X	X	X			
Hero Inlet	LFG	-6	9/12/26	8:45 am	X	X	X	X			
Parnel Inlet	LFG	-7	9/12/26	8:37 am	X	X	X	X			
Zeeco Inlet	LFG	-8	9/12/26	8:28 am	X	X	X	X			

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/12/26	9:09 am	Ruben G	9/12/26	9:09 am
Relinquished by: *(Signature)* Ruben G	9/12/26	10:15	**Received by:** *(Signature)*	**Date**	**Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by:** *(Signature)*	**Date**	**Time**

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Sui	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach, CA 90806	**City/State/Zip:** Long Beach, CA 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Email Address:	**Email Address:** cfong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 13, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22576-1	22576-2	22576-3	22576-4	22576-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	5.74	3.14	9.23	3.33	6.85
Nitrogen	27.20	20.96	40.69	18.26	33.56
Methane	28.31	31.37	7.03	17.88	15.52
Carbon Dioxide	35.11	39.78	36.31	50.66	37.98
Hydrogen	1.42	2.36	3.59	5.72	3.31
		(Concentration in ppmv)			
Carbon Monoxide	200	349	698	932	501
		(Concentration in %v, by component)			
TNMHC	0.288	0.321	0.798	0.842	0.604
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	310.1	347.0	121.8	245.7	199.8
BTU/ft3 (Wet @ 0.25636 psia)	304.7	341.0	119.7	241.4	196.3
BTU/lb (Dry @60F, 14.696 psia)	3879	4334	1400	2803	2362

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 13, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	5.71	5.76	5.74	0.87
Nitrogen	Zeeco South	27.14	27.25	27.20	0.40
Methane	Zeeco South	28.32	28.30	28.31	0.07
Carbon Dioxide	Zeeco South	35.14	35.08	35.11	0.17
Hydrogen	Zeeco South	1.42	1.42	1.42	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	200	200	200	0.06
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.289	0.288	0.288	0.41

Five Tedlar bag samples, laboratory numbers 22576-(1-5), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.28%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 13, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22576-1	22576-2	22576-3	22576-4	22576-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	134	191	146	273	125
Carbonyl sulfide	0.51	0.53	<1.60	<1.60	<1.20
Methyl mercaptan	57.3	96.4	381	497	265
Ethyl mercaptan	0.96	1.07	4.34	5.04	2.73
Dimethyl sulfide	202	278	1036	1130	784
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.37	1.77	1.77	3.45	1.88
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.56	2.98	13.1	14.5	8.56
s-Butyl mercaptan	3.72	4.45	12.8	17.5	9.94
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	2.88	1.09	5.22	8.44	6.72
Tetrahydrothiophene	1.83	1.89	10.8	9.36	5.78
Unidentified sulfurs	6.86	7.14	30.7	40.8	22.8
	(Concentration in ppmv, as H_2S)				
Total Sulfur	417.51	587.53	1646.59	2008.62	1240.23

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 13, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	135	133	134	1.5
	FL-2009 Inlet	186	196	191	5.3
	Hero Inlet	149	142	146	5.3
	Parnel Inlet	272	274	273	0.64
	Zeeco Inlet	125	126	125	0.65
Carbonyl sulfide	Zeeco South	0.51	0.50	0.51	2.0
	FL-2009 Inlet	<0.50	0.53	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	58.8	55.7	57.3	5.4
	FL-2009 Inlet	93.9	98.8	96.4	5.1
	Hero Inlet	391	370	381	5.6
	Parnel Inlet	492	503	497	2.2
	Zeeco Inlet	268	263	265	1.8
Ethyl mercaptan	Zeeco South	0.96	0.96	0.96	0.00
	FL-2009 Inlet	1.06	1.07	1.07	0.94
	Hero Inlet	4.44	4.24	4.34	4.6
	Parnel Inlet	4.95	5.13	5.04	3.6
	Zeeco Inlet	2.68	2.78	2.73	3.7
Dimethyl sulfide	Zeeco South	207	198	202	4.7
	FL-2009 Inlet	275	281	278	2.2
	Hero Inlet	1067	1006	1036	5.9
	Parnel Inlet	1118	1143	1130	2.2
	Zeeco Inlet	795	774	784	2.6
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.33	1.40	1.37	5.1
	FL-2009 Inlet	1.75	1.79	1.77	2.3
	Hero Inlet	1.87	1.66	1.77	12
	Parnel Inlet	3.42	3.47	3.45	1.5
	Zeeco Inlet	1.90	1.86	1.88	2.1

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.56	2.56	2.56	0.00
	FL-2009 Inlet	2.93	3.02	2.98	3.0
	Hero Inlet	13.5	12.8	13.1	4.8
	Parnel Inlet	14.3	14.7	14.5	2.7
	Zeeco Inlet	8.52	8.59	8.56	0.82
s-Butyl mercaptan	Zeeco South	3.72	3.71	3.72	0.27
	FL-2009 Inlet	4.40	4.49	4.45	2.0
	Hero Inlet	13.2	12.4	12.8	6.2
	Parnel Inlet	17.3	17.7	17.5	2.3
	Zeeco Inlet	9.69	10.2	9.94	5.0
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	2.90	2.85	2.88	1.7
	FL-2009 Inlet	1.07	1.10	1.09	2.8
	Hero Inlet	5.34	5.10	5.22	4.6
	Parnel Inlet	8.29	8.58	8.44	3.4
	Zeeco Inlet	6.59	6.84	6.72	3.7
Tetrahydrothiophene	Zeeco South	1.80	1.85	1.83	2.7
	FL-2009 Inlet	1.86	1.91	1.89	2.7
	Hero Inlet	11.1	10.5	10.8	5.8
	Parnel Inlet	9.19	9.53	9.36	3.6
	Zeeco Inlet	5.61	5.95	5.78	5.9
Unidentified sulfurs	Zeeco South	6.87	6.84	6.86	0.44
	FL-2009 Inlet	7.21	7.06	7.14	2.1
	Hero Inlet	30.9	30.5	30.7	1.3
	Parnel Inlet	39.8	41.8	40.8	4.8
	Zeeco Inlet	22.1	23.5	22.8	6.3

Five Tedlar bag samples, laboratory numbers 22576-(1-5), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 3.3%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Turnaround Times:** Standard 10 day
	Expedited: 24hr / 48hr / 72hr / 5 day

ANALYSES REQUESTED

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22576-1	09.13.26	1:00 PM	X	X	X	X			
FL-2009 Inlet	LFG	-2	09.13.26	12:15 PM	X	X	X	X			
Hero Inlet	LFG	-3	09.13.26	12:25 PM	X	X	X	X			
Parnel Inlet	LFG	-4	09.13.26	12:35 PM	X	X	X	X			
Zeeco Inlet	LFG	-5	09.13.26	12:40 PM	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9.14.26	6:00am	Received by: *(Signature)*	9.14.26	6:00am
Relinquished by: *(Signature)*	9.14.26	8:55	Received by: *(Signature)*	9/14/26	8:55
Relinquished by: *(Signature)*	9/14/26	10:05	Received for Laboratory by: *(Signature)*	9/14/26	10:05

Company Info:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Sui
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 14, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22576-6	22576-7	22576-8	22576-9	22576-10
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components			*(Concentration in %v)*		
Oxygen	6.65	4.38	6.09	5.92	7.90
Nitrogen	29.37	25.85	32.16	27.32	37.17
Methane	28.19	28.42	8.55	15.56	14.57
Carbon Dioxide	32.62	37.11	42.41	43.48	33.68
Hydrogen	1.04	2.25	6.14	4.86	2.91
			(Concentration in ppmv)		
Carbon Monoxide	129	324	747	777	397
			(Concentration in %v, by component)		
TNMHC	0.220	0.233	0.937	0.603	0.460
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	304.3	310.3	154.3	204.6	183.5
BTU/ft3 (Wet @ 0.25636 psia)	299.0	304.9	151.6	201.1	180.3
BTU/lb (Dry @60F, 14.696 psia)	3843	3884	1767	2388	2203

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 14, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.59	6.70	6.65	1.7
Nitrogen	Zeeco South	29.35	29.39	29.37	0.14
Methane	Zeeco South	28.19	28.19	28.19	0.00
Carbon Dioxide	Zeeco South	32.68	32.56	32.62	0.37
Hydrogen	Zeeco South	1.03	1.05	1.04	1.9
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	129	128	129	0.32
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.221	0.219	0.220	0.62

Five Tedlar bag samples, laboratory numbers 22576-(6-10), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.72%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 14, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22576-6	22576-7	22576-8	22576-9	22576-10
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	146	188	163	234	89.8
Carbonyl sulfide	<0.50	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	42.1	91.8	419	409	234
Ethyl mercaptan	0.81	1.03	4.66	4.11	2.48
Dimethyl sulfide	148	260	1119	919	691
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.31	1.66	1.97	2.82	1.88
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.10	2.82	13.9	11.4	7.62
s-Butyl mercaptan	3.19	3.95	14.2	13.7	9.65
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	2.33	0.78	5.30	5.64	5.88
Tetrahydrothiophene	1.43	1.38	11.2	6.22	5.14
Unidentified sulfurs	5.73	4.39	32.0	25.6	18.4
	(Concentration in ppmv, as H_2S)				
Total Sulfur	354.52	556.38	1789.27	1637.56	1071.32

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 14, 2026
Date Received: September 14, 2026
Date Analyzed: September 14, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	146	146	146	0.21
	FL-2009 Inlet	187	189	188	1.3
	Hero Inlet	164	163	163	0.99
	Parnel Inlet	234	234	234	0.05
	Zeeco Inlet	89.0	90.6	89.8	1.8
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	41.5	42.6	42.1	2.7
	FL-2009 Inlet	89.3	94.4	91.8	5.6
	Hero Inlet	413	424	419	2.6
	Parnel Inlet	409	410	409	0.34
	Zeeco Inlet	231	237	234	2.3
Ethyl mercaptan	Zeeco South	0.82	0.80	0.81	2.5
	FL-2009 Inlet	1.01	1.05	1.03	3.9
	Hero Inlet	4.54	4.77	4.66	4.9
	Parnel Inlet	4.08	4.14	4.11	1.5
	Zeeco Inlet	2.45	2.50	2.48	2.0
Dimethyl sulfide	Zeeco South	148	147	148	0.63
	FL-2009 Inlet	254	265	260	4.3
	Hero Inlet	1096	1141	1119	4.1
	Parnel Inlet	915	923	919	0.83
	Zeeco Inlet	686	695	691	1.3
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.29	1.33	1.31	3.1
	FL-2009 Inlet	1.59	1.72	1.66	7.9
	Hero Inlet	1.91	2.03	1.97	6.1
	Parnel Inlet	2.70	2.93	2.82	8.2
	Zeeco Inlet	1.93	1.83	1.88	5.3

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.09	2.10	2.10	0.48
	FL-2009 Inlet	2.72	2.92	2.82	7.1
	Hero Inlet	13.6	14.2	13.9	4.3
	Parnel Inlet	11.3	11.5	11.4	1.8
	Zeeco Inlet	7.49	7.75	7.62	3.4
s-Butyl mercaptan	Zeeco South	3.22	3.16	3.19	1.9
	FL-2009 Inlet	3.87	4.02	3.95	3.8
	Hero Inlet	13.9	14.6	14.2	5.27
	Parnel Inlet	13.7	13.7	13.7	0.15
	Zeeco Inlet	9.64	9.65	9.65	0.10
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	2.38	2.28	2.33	4.3
	FL-2009 Inlet	0.74	0.82	0.78	10
	Hero Inlet	5.16	5.43	5.30	5.1
	Parnel Inlet	5.62	5.66	5.64	0.71
	Zeeco Inlet	5.86	5.89	5.88	0.51
Tetrahydrothiophene	Zeeco South	1.43	1.43	1.43	0.00
	FL-2009 Inlet	1.23	1.53	1.38	22
	Hero Inlet	10.9	11.5	11.2	5.1
	Parnel Inlet	6.35	6.08	6.22	4.3
	Zeeco Inlet	5.12	5.16	5.14	0.78
Unidentified sulfurs	Zeeco South	5.74	5.71	5.73	0.52
	FL-2009 Inlet	4.24	4.53	4.39	6.6
	Hero Inlet	32.0	32.0	32.0	0.00
	Parnel Inlet	25.7	25.5	25.6	0.70
	Zeeco Inlet	18.4	18.3	18.4	0.38

Five Tedlar bag samples, laboratory numbers 22576-(6-10), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 3.3%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)* Brandon Rodriguez	**Turnaround Times:** Standard 10 day **Expedited:** 24hr / 48hr / 72hr / 5 day

ANALYSES REQUESTED

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22576-6	9-14-26	8:53am	X	X	X	X			
FL-2009 Inlet	LFG	-7	9-14-26	7:05am	X	X	X	X			
Hero Inlet	LFG	-8	9.14.26	8:00am	X	X	X	X			
Parnel Inlet	LFG	-9	9-14-26	8:15am	X	X	X	X			
Zeeco Inlet	LFG	-10	9-14-26	8:33am	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9.14.26	8:55	Received by: *(Signature)* Rubcm G	9/14/26	8:55
Relinquished by: *(Signature)* Rubcm G	9/14/26	10:05	Received by: *(Signature)*	Date	Time
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	9/14/26	10:05

Company Info:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Su
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 15, 2026
Date Received: September 15, 2026
Date Analyzed: September 15, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22586-19	22586-20	22586-21	22586-22
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components		*(Concentration in %v)*		
Oxygen	6.62	4.02	5.09	7.76
Nitrogen	29.84	24.90	27.71	36.97
Methane	27.15	28.47	7.86	13.84
Carbon Dioxide	31.92	38.23	47.26	33.90
Hydrogen	1.08	2.32	7.08	3.00
		(Concentration in ppmv)		
Carbon Monoxide	134	343	907	418
		(Concentration in %v, by component)		
TNMHC	0.230	0.279	1.039	0.483
		BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	298.1	313.8	155.2	178.9
BTU/ft3 (Wet @ 0.25636 psia)	292.9	308.4	152.5	175.8
BTU/lb (Dry @60F, 14.696 psia)	3760	3904	1743	2138

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 15, 2026
Date Received: September 15, 2026
Date Analyzed: September 15, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.66	6.57	6.62	1.4
Nitrogen	Zeeco South	29.90	29.77	29.84	0.44
Methane	Zeeco South	27.15	27.15	27.15	0.00
Carbon Dioxide	Zeeco South	31.94	31.89	31.92	0.16
Hydrogen	Zeeco South	1.08	1.07	1.08	0.93
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	135	133	134	1.5
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.230	0.229	0.230	0.43

Four Tedlar bag samples, laboratory numbers 22586-(19-22), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.68%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 15, 2026
Date Received: September 15, 2026
Date Analyzed: September 15, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22586-19	22586-20	22586-21	22586-22
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	146	207	172	127
Carbonyl sulfide	<0.50	0.55	<1.60	<1.20
Methyl mercaptan	51.5	117	487	247
Ethyl mercaptan	1.01	1.30	5.19	2.70
Dimethyl sulfide	170	328	1285	701
Carbon disulfide	<0.50	<0.50	<1.60	<1.20
i-Propyl mercaptan	1.41	2.02	2.04	1.76
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
n-Propyl mercaptan	2.54	3.71	15.8	8.42
s-Butyl mercaptan	3.65	5.30	16.3	10.2
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
Dimethyl disulfide	2.11	1.03	5.21	6.05
Tetrahydrothiophene	1.69	2.20	13.6	5.91
Unidentified sulfurs	6.51	7.95	39.0	22.2
	(Concentration in ppmv, as H_2S)			
Total Sulfur	388.22	677.74	2046.15	1138.90

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 15, 2026
Date Received: September 15, 2026
Date Analyzed: September 15, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	147	144	146	2.0
	FL-2009 Inlet	207	207	207	0.02
	Hero Inlet	173	171	172	1.1
	Zeeco Inlet	123	132	127	6.9
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	0.54	0.55	0.55	1.8
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	52.0	50.9	51.5	2.1
	FL-2009 Inlet	116	119	117	2.4
	Hero Inlet	489	484	487	1.1
	Zeeco Inlet	241	254	247	5.2
Ethyl mercaptan	Zeeco South	1.04	0.98	1.01	5.9
	FL-2009 Inlet	1.27	1.33	1.30	4.6
	Hero Inlet	5.24	5.13	5.19	2.1
	Zeeco Inlet	2.72	2.67	2.70	1.9
Dimethyl sulfide	Zeeco South	174	166	170	4.8
	FL-2009 Inlet	327	329	328	0.61
	Hero Inlet	1295	1275	1285	1.5
	Zeeco Inlet	687	716	701	4.1
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.43	1.39	1.41	2.8
	FL-2009 Inlet	2.00	2.04	2.02	2.0
	Hero Inlet	2.11	1.97	2.04	6.9
	Zeeco Inlet	1.67	1.84	1.76	9.7
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	2.59	2.48	2.54	4.3
	FL-2009 Inlet	3.70	3.72	3.71	0.54
	Hero Inlet	16.0	15.5	15.8	3.0
	Zeeco Inlet	8.06	8.77	8.42	8.4
s-Butyl mercaptan	Zeeco South	3.64	3.65	3.65	0.27
	FL-2009 Inlet	5.28	5.31	5.30	0.57
	Hero Inlet	16.6	15.9	16.3	4.4
	Zeeco Inlet	9.87	10.5	10.2	6.5
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.60	---	---
Dimethyl disulfide	Zeeco South	2.13	2.08	2.11	2.4
	FL-2009 Inlet	1.01	1.04	1.03	2.9
	Hero Inlet	5.31	5.11	5.21	3.8
	Zeeco Inlet	5.83	6.26	6.05	7.1
Tetrahydrothiophene	Zeeco South	1.78	1.60	1.69	11
	FL-2009 Inlet	2.20	2.19	2.20	0.46
	Hero Inlet	13.9	13.3	13.6	4.9
	Zeeco Inlet	5.53	6.28	5.91	13
Unidentified sulfurs	Zeeco South	6.66	6.36	6.51	4.6
	FL-2009 Inlet	8.04	7.86	7.95	2.3
	Hero Inlet	39.4	38.6	39.0	2.2
	Zeeco Inlet	21.5	22.9	22.2	6.2

Four Tedlar bag samples, laboratory numbers 22586-(19-22), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 3.8%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)* Brandon Rodriguez	**Turnaround Times:** Standard 10 day **Expedited:** 24hr / 48hr / 72hr / 5 day

ANALYSES REQUESTED

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22586-19	9.15.26	8:45am	X	X	X	X			
FL-2009 Inlet	LFG	-20	9.15.26	7:35am	X	X	X	X			
Hero Inlet	LFG	-21	9.15.26	8:10am	X	X	X	X			
Parnel Inlet	LFG				X	X	X	X			
Zeeco Inlet	LFG	-22	9.15.26	8:30am	X	X	X	X			

Relinquished by: *(Signature)*	Date 9.15.26	Time 9:15	Received by: *(Signature)* Ruben G	Date 9/15/26	Time 9:15
Relinquished by: *(Signature)* Ruben G	Date 9/15/26	Time 10:34	Received by: *(Signature)*	Date	Time
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date 9/15/26	Time 10:34

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	Company: SCS Engineers	AtmAA Inc.
Street Address: 3900 Kilroy Airport Way Suite 300	Street Address: 3900 Kilroy Airport Way Sui	5107 Douglas Fir Rd.
City/State/Zip: Long Beach, CA 90806	City/State/Zip: Long Beach, CA 90806	Calabasas, CA 91302
Telephone No.: 562-743-7895	Project Manager: Cornelius Fong	TEL: (818) 223-3277
Email Address:	Email Address: cfong@scsengineers.com	Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277

specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 16, 2026
Date Received: September 16, 2026
Date Analyzed: September 16, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22596-5	22596-6	22596-7	22596-8
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components	*(Concentration in %v)*			
Oxygen	6.61	4.52	4.90	7.51
Nitrogen	30.85	26.08	27.38	35.79
Methane	24.88	28.68	9.55	12.32
Carbon Dioxide	33.20	36.95	47.13	36.52
Hydrogen	1.93	2.12	6.83	4.04
	(Concentration in ppmv)			
Carbon Monoxide	221	297	809	491
	(Concentration in %v, by component)			
TNMHC	0.306	0.265	1.008	0.570
	BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	278.2	313.3	169.8	169.1
BTU/ft3 (Wet @ 0.25636 psia)	273.4	307.9	166.8	166.1
BTU/lb (Dry @60F, 14.696 psia)	3477	3921	1920	1999

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 16, 2026
Date Received: September 16, 2026
Date Analyzed: September 16, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.60	6.61	6.61	0.15
Nitrogen	Zeeco South	30.84	30.86	30.85	0.06
Methane	Zeeco South	24.81	24.95	24.88	0.56
Carbon Dioxide	Zeeco South	33.11	33.29	33.20	0.54
Hydrogen	Zeeco South	1.90	1.95	1.93	2.60
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	222	220	221	1.1
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.307	0.305	0.306	0.74

Four Tedlar bag samples, laboratory numbers 22596-(5-8), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.82%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 5, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 16, 2026
Date Received: September 16, 2026
Date Analyzed: September 16, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22596-5	22596-6	22596-7	22596-8
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	149	190	186	124
Carbonyl sulfide	0.52	0.51	<1.60	<1.20
Methyl mercaptan	115	103	465	347
Ethyl mercaptan	1.49	1.16	4.96	3.47
Dimethyl sulfide	333	282	1218	941
Carbon disulfide	<0.50	<0.50	<1.60	<1.20
i-Propyl mercaptan	1.47	1.78	2.22	1.85
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
n-Propyl mercaptan	3.78	3.19	15.0	10.3
s-Butyl mercaptan	5.04	4.62	15.9	11.5
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
Dimethyl disulfide	2.75	1.28	4.04	6.95
Tetrahydrothiophene	3.06	2.15	12.8	7.87
Unidentified sulfurs	8.43	6.32	34.0	24.8
	(Concentration in ppmv, as H_2S)			
Total Sulfur	626.49	597.81	1961.61	1485.72

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 16, 2026
Date Received: September 16, 2026
Date Analyzed: September 16, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	151	147	149	2.6
	FL-2009 Inlet	185	196	190	6.0
	Hero Inlet	186	187	186	0.71
	Zeeco Inlet	128	121	124	5.0
Carbonyl sulfide	Zeeco South	0.52	0.52	0.52	0.00
	FL-2009 Inlet	0.49	0.53	0.51	7.8
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	116	114	115	1.6
	FL-2009 Inlet	101	106	103	5.3
	Hero Inlet	461	468	465	1.4
	Zeeco Inlet	354	340	347	4.2
Ethyl mercaptan	Zeeco South	1.49	1.48	1.49	0.67
	FL-2009 Inlet	1.12	1.20	1.16	6.9
	Hero Inlet	4.90	5.01	4.96	2.2
	Zeeco Inlet	3.55	3.39	3.47	4.6
Dimethyl sulfide	Zeeco South	338	329	333	2.9
	FL-2009 Inlet	274	290	282	5.6
	Hero Inlet	1202	1234	1218	2.6
	Zeeco Inlet	951	931	941	2.1
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.48	1.45	1.47	2.0
	FL-2009 Inlet	1.73	1.83	1.78	5.6
	Hero Inlet	2.22	2.22	2.22	0.00
	Zeeco Inlet	1.83	1.87	1.85	2.2
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	3.84	3.71	3.78	3.4
	FL-2009 Inlet	3.03	3.34	3.19	9.7
	Hero Inlet	14.7	15.3	15.0	3.5
	Zeeco Inlet	10.4	10.2	10.3	2.4
s-Butyl mercaptan	Zeeco South	5.11	4.96	5.04	3.0
	FL-2009 Inlet	4.50	4.74	4.62	5.2
	Hero Inlet	15.8	16.1	15.9	1.9
	Zeeco Inlet	11.5	11.5	11.5	0.09
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	2.78	2.72	2.75	2.2
	FL-2009 Inlet	1.23	1.32	1.28	7.1
	Hero Inlet	3.97	4.11	4.04	3.5
	Zeeco Inlet	7.01	6.88	6.95	1.9
Tetrahydrothiophene	Zeeco South	3.09	3.03	3.06	2.0
	FL-2009 Inlet	2.27	2.02	2.15	12
	Hero Inlet	12.6	12.9	12.8	2.4
	Zeeco Inlet	7.92	7.82	7.87	1.3
Unidentified sulfurs	Zeeco South	8.49	8.36	8.43	1.5
	FL-2009 Inlet	6.13	6.50	6.32	5.9
	Hero Inlet	33.6	34.4	34.0	2.3
	Zeeco Inlet	24.4	25.2	24.8	3.2

Four Tedlar bag samples, laboratory numbers 22596-(5-8), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 3.5%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)* Emmanuel Melena	**Turnaround Times:** Standard 10 day **Expedited:** 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22596-5	9.16.25	8:55am	X	X	X	X			
FL-2009 Inlet	LFG	-6	9.16.25	7:25am	X	X	X	X			
Hero Inlet	LFG	-7	9.16.25	8:05am	X	X	X	X			
Parnel Inlet	LFG				X	X	X	X			
Zeeco Inlet	LFG	-8	9.16.25	8:35am	X	X	X	X			

Relinquished by: *(Signature)* EM	Date 9.16.26	Time 9:05am	Received by: *(Signature)* Ruben G	Date 9/16/26	Time 9:05
Relinquished by: *(Signature)* Ruben G	Date 9/16/26	Time 10:25	Received by: *(Signature)*	Date	Time
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date 9/16/26	Time 10:25

Company Info:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Sui
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277

specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 17, 2026
Date Received: September 17, 2026
Date Analyzed: September 17, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22606-5	22606-6	22606-7	22606-8	22606-9
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	5.46	5.97	5.65	4.28	7.70
Nitrogen	28.72	30.30	30.63	23.33	37.56
Methane	28.78	26.54	8.42	17.16	14.56
Carbon Dioxide	33.51	33.64	45.11	47.15	34.45
Hydrogen	1.06	1.98	6.66	5.21	2.86
		(Concentration in ppmv)			
Carbon Monoxide	127	277	802	822	387
		(Concentration in %v, by component)			
TNMHC	0.213	0.214	0.911	0.648	0.419
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	311.1	288.2	151.6	224.6	179.9
BTU/ft3 (Wet @ 0.25636 psia)	305.6	283.2	149.0	220.7	176.8
BTU/lb (Dry @60F, 14.696 psia)	3927	3632	1724	2600	2154

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 17, 2026
Date Received: September 17, 2026
Date Analyzed: September 17, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	5.42	5.49	5.46	1.3
Nitrogen	Zeeco South	28.63	28.81	28.72	0.63
Methane	Zeeco South	28.76	28.79	28.78	0.10
Carbon Dioxide	Zeeco South	33.52	33.49	33.51	0.09
Hydrogen	Zeeco South	1.06	1.06	1.06	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	125	128	127	2.3
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.213	0.212	0.213	0.43

Five Tedlar bag samples, laboratory numbers 22606-(5-9), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.69%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 17, 2026
Date Received: September 17, 2026
Date Analyzed: September 17, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22606-5	22606-6	22606-7	22606-8	22606-9
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	155	194	160	249	122
Carbonyl sulfide	0.58	0.50	<1.60	<1.60	<1.20
Methyl mercaptan	51.6	94.6	441	441	244
Ethyl mercaptan	0.89	1.06	4.74	4.44	2.66
Dimethyl sulfide	167	251	1171	1009	683
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.51	1.81	1.91	3.08	1.70
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.30	2.84	14.2	12.8	8.20
s-Butyl mercaptan	3.73	4.22	14.5	15.8	10.1
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	2.50	0.94	4.16	4.09	7.46
Tetrahydrothiophene	1.49	1.77	11.6	8.38	5.46
Unidentified sulfurs	5.76	5.05	29.3	28.3	20.7
	(Concentration in ppmv, as H_2S)				
Total Sulfur	394.72	559.35	1855.38	1780.79	1113.19

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 17, 2026
Date Received: September 17, 2026
Date Analyzed: September 17, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	157	152	155	2.8
	FL-2009 Inlet	193	195	194	1.3
	Hero Inlet	158	162	160	2.4
	Parnel Inlet	248	250	249	0.96
	Zeeco Inlet	125	119	122	4.9
Carbonyl sulfide	Zeeco South	0.59	0.57	0.58	3.4
	FL-2009 Inlet	<0.50	0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	52.1	51.2	51.6	1.7
	FL-2009 Inlet	95.3	93.9	94.6	1.5
	Hero Inlet	437	444	441	1.7
	Parnel Inlet	439	444	441	1.2
	Zeeco Inlet	250	239	244	4.5
Ethyl mercaptan	Zeeco South	0.90	0.88	0.89	2.2
	FL-2009 Inlet	1.10	1.01	1.06	8.5
	Hero Inlet	4.73	4.75	4.74	0.42
	Parnel Inlet	4.41	4.47	4.44	1.4
	Zeeco Inlet	2.63	2.68	2.66	1.9
Dimethyl sulfide	Zeeco South	168	167	167	0.51
	FL-2009 Inlet	253	250	251	1.5
	Hero Inlet	1167	1174	1171	0.59
	Parnel Inlet	1000	1019	1009	1.9
	Zeeco Inlet	694	671	683	3.4
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.52	1.49	1.51	2.0
	FL-2009 Inlet	1.81	1.81	1.81	0.00
	Hero Inlet	1.95	1.86	1.91	4.7
	Parnel Inlet	3.04	3.12	3.08	2.6
	Zeeco Inlet	1.72	1.68	1.70	2.4

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.28	2.31	2.30	1.3
	FL-2009 Inlet	2.83	2.85	2.84	0.70
	Hero Inlet	14.2	14.3	14.2	0.77
	Parnel Inlet	12.6	12.9	12.8	1.8
	Zeeco Inlet	8.27	8.12	8.20	1.8
s-Butyl mercaptan	Zeeco South	3.72	3.73	3.73	0.27
	FL-2009 Inlet	4.26	4.17	4.22	2.1
	Hero Inlet	14.7	14.4	14.5	1.7
	Parnel Inlet	15.8	15.9	15.8	0.76
	Zeeco Inlet	10.5	9.76	10.1	7.4
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	2.50	2.50	2.50	0.00
	FL-2009 Inlet	0.94	0.94	0.94	0.00
	Hero Inlet	4.17	4.14	4.16	0.72
	Parnel Inlet	4.03	4.15	4.09	2.9
	Zeeco Inlet	7.55	7.36	7.46	2.5
Tetrahydrothiophene	Zeeco South	1.48	1.49	1.49	0.67
	FL-2009 Inlet	1.82	1.71	1.77	6.2
	Hero Inlet	11.8	11.5	11.6	2.3
	Parnel Inlet	8.65	8.11	8.38	6.4
	Zeeco Inlet	5.54	5.38	5.46	2.9
Unidentified sulfurs	Zeeco South	5.56	5.96	5.76	6.9
	FL-2009 Inlet	4.98	5.11	5.05	2.6
	Hero Inlet	29.1	29.5	29.3	1.5
	Parnel Inlet	27.8	28.7	28.3	3.3
	Zeeco Inlet	20.6	20.9	20.7	1.4

Five Tedlar bag samples, laboratory numbers 22606-(5-8), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.3%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Turnaround Times:** Standard 10 day
	Expedited: 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22606-5	9.17.26	7:55am	X	X	X	X			
FL-2009 Inlet	LFG	-6	9.17.26	7:35am	X	X	X	X			
Hero Inlet	LFG	-7	9.17.26	8:20am	X	X	X	X			
Parnel Inlet	LFG	-8	9.17.26	9:05am	X	X	X	X			
Zeeco Inlet	LFG	-9	9.17.26	8:40am	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9.17.26	9:35		9/17/26	9:35
Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/17/26	10:27			
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date	Time
				9/17/26	10:27

Company Info:

Company: SCS Engineers
Street Address: 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address: 3900 Kilroy Airport Way Sui
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 18, 2026
Date Received: September 18, 2026
Date Analyzed: September 18, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22616-1	22616-2	22616-3	22616-4	22616-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components			*(Concentration in %v)*		
Oxygen	5.38	4.91	6.06	5.81	6.49
Nitrogen	26.18	28.45	32.35	29.43	34.31
Methane	31.21	25.71	10.70	12.98	17.65
Carbon Dioxide	33.38	37.34	42.03	42.52	36.65
Hydrogen	0.89	2.60	5.40	5.23	2.52
			(Concentration in ppmv)		
Carbon Monoxide	115	409	732	793	368
			(Concentration in %v, by component)		
TNMHC	0.196	0.330	0.700	0.646	0.436
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	336.9	285.5	161.8	184.0	210.7
BTU/ft3 (Wet @ 0.25636 psia)	331.1	280.5	159.0	180.8	207.0
BTU/lb (Dry @60F, 14.696 psia)	4292	3534	1871	2137	2522

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 18, 2026
Date Received: September 18, 2026
Date Analyzed: September 18, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	5.38	5.37	5.38	0.19
Nitrogen	Zeeco South	26.24	26.12	26.18	0.46
Methane	Zeeco South	31.23	31.19	31.21	0.13
Carbon Dioxide	Zeeco South	33.39	33.36	33.38	0.09
Hydrogen	Zeeco South	0.89	0.89	0.89	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	118	113	115	3.5
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.195	0.198	0.196	1.6

Five Tedlar bag samples, laboratory numbers 22616-(1-5), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.85%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 18, 2026
Date Received: September 18, 2026
Date Analyzed: September 18, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22616-1	22616-2	22616-3	22616-4	22616-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	218	177	166	182	160
Carbonyl sulfide	0.87	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	40.1	130	360	438	262
Ethyl mercaptan	0.83	1.38	4.32	4.40	2.79
Dimethyl sulfide	121	376	1044	1141	688
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	2.47	1.61	2.30	2.63	2.17
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	1.89	3.99	12.4	13.3	8.44
s-Butyl mercaptan	4.06	5.27	13.7	16.2	10.7
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	2.28	1.24	3.88	8.27	5.48
Tetrahydrothiophene	1.37	2.88	9.47	9.66	5.62
Unidentified sulfurs	6.82	9.22	25.0	38.0	26.8
	(Concentration in ppmv, as H_2S)				
Total Sulfur	402.45	710.36	1644.37	1861.87	1177.62

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 18, 2026
Date Received: September 18, 2026
Date Analyzed: September 18, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	219	218	218	0.68
	FL-2009 Inlet	175	179	177	2.7
	Hero Inlet	164	168	166	2.5
	Parnel Inlet	188	176	182	6.7
	Zeeco Inlet	163	157	160	3.7
Carbonyl sulfide	Zeeco South	0.86	0.88	0.87	2.3
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	40.2	40.0	40.1	0.47
	FL-2009 Inlet	130	130	130	0.06
	Hero Inlet	356	364	360	2.1
	Parnel Inlet	454	422	438	7.2
	Zeeco Inlet	263	261	262	0.68
Ethyl mercaptan	Zeeco South	0.84	0.82	0.83	2.4
	FL-2009 Inlet	1.36	1.39	1.38	2.2
	Hero Inlet	4.40	4.24	4.32	3.7
	Parnel Inlet	4.52	4.27	4.40	5.7
	Zeeco Inlet	2.72	2.86	2.79	5.0
Dimethyl sulfide	Zeeco South	121	121	121	0.00
	FL-2009 Inlet	373	380	376	1.8
	Hero Inlet	1045	1043	1044	0.24
	Parnel Inlet	1162	1119	1141	3.8
	Zeeco Inlet	688	689	688	0.23
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.60	---	---
i-Propyl mercaptan	Zeeco South	2.46	2.48	2.47	0.81
	FL-2009 Inlet	1.54	1.67	1.61	8.1
	Hero Inlet	2.26	2.33	2.30	3.1
	Parnel Inlet	2.53	2.72	2.63	7.2
	Zeeco Inlet	2.16	2.17	2.17	0.46



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	1.84	1.94	1.89	5.3
	FL-2009 Inlet	3.93	4.05	3.99	3.0
	Hero Inlet	12.3	12.6	12.4	2.4
	Parnel Inlet	13.4	13.3	13.3	1.1
	Zeeco Inlet	8.43	8.45	8.44	0.24
s-Butyl mercaptan	Zeeco South	3.99	4.12	4.06	3.2
	FL-2009 Inlet	5.10	5.43	5.27	6.3
	Hero Inlet	13.6	13.8	13.7	0.95
	Parnel Inlet	16.3	16.0	16.2	2.0
	Zeeco Inlet	10.9	10.5	10.7	4.3
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	2.26	2.29	2.28	1.3
	FL-2009 Inlet	1.21	1.26	1.24	4.0
	Hero Inlet	3.81	3.95	3.88	3.6
	Parnel Inlet	8.40	8.14	8.27	3.1
	Zeeco Inlet	5.49	5.46	5.48	0.55
Tetrahydrothiophene	Zeeco South	1.36	1.38	1.37	1.5
	FL-2009 Inlet	2.76	3.00	2.88	8.3
	Hero Inlet	9.38	9.56	9.47	1.9
	Parnel Inlet	9.96	9.35	9.66	6.3
	Zeeco Inlet	5.56	5.67	5.62	2.0
Unidentified sulfurs	Zeeco South	7.02	6.62	6.82	5.9
	FL-2009 Inlet	9.19	9.24	9.22	0.54
	Hero Inlet	24.6	25.5	25.0	3.6
	Parnel Inlet	38.6	37.4	38.0	3.2
	Zeeco Inlet	26.6	27.0	26.8	1.5

Five Tedlar bag samples, laboratory numbers 22616-(1-5), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.9%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)* Emmanuel Meleven	**Turnaround Times:** Standard 10 day **Expedited:** 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22616-1	9.18.26	8:55am	X	X	X	X			
FL-2009 Inlet	LFG	-2	9.18.26	7:35am	X	X	X	X			
Hero Inlet	LFG	-3	9.18.26	8:25am	X	X	X	X			
Parnel Inlet	LFG	-4	9.18.26	8:40am	X	X	X	X			
Zeeco Inlet	LFG	-5	9.18.26	8:45am	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)* EM	9.18.26	9:00am	Received by: *(Signature)* Ruben G	9/18/26	9:00
Relinquished by: *(Signature)* Ruben G	9/18/26	10:02	Received by: *(Signature)*	Date	Time
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	9/18/26	10:02

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Sui	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach, CA 90806	**City/State/Zip:** Long Beach, CA 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Email Address:	**Email Address:** cfong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 19, 2026
Date Received: September 19, 2026
Date Analyzed: September 21, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22626-1	22626-2	22626-3	22626-4	22626-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components			*(Concentration in %v)*		
Oxygen	7.00	4.19	6.50	6.44	7.26
Nitrogen	32.49	26.04	32.59	32.39	36.59
Methane	27.27	28.10	12.43	12.28	17.03
Carbon Dioxide	30.81	37.57	42.28	41.85	34.90
Hydrogen	1.07	2.46	5.42	5.05	2.50
			(Concentration in ppmv)		
Carbon Monoxide	135	378	741	771	355
			(Concentration in %v, by component)		
TNMHC	0.201	0.272	0.693	0.565	0.456
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	291.8	308.7	175.1	168.0	203.5
BTU/ft3 (Wet @ 0.25636 psia)	286.7	303.3	172.0	165.1	199.9
BTU/lb (Dry @60F, 14.696 psia)	3710	3855	2041	1958	2450

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 19, 2026
Date Received: September 19, 2026
Date Analyzed: September 21, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	7.04	6.95	7.00	1.3
Nitrogen	Zeeco South	32.64	32.33	32.49	0.95
Methane	Zeeco South	27.43	27.11	27.27	1.2
Carbon Dioxide	Zeeco South	31.01	30.61	30.81	1.3
Hydrogen	Zeeco South	1.07	1.07	1.07	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	135	136	135	0.36
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.201	0.202	0.201	0.71

Five Tedlar bag samples, laboratory numbers 22626-(1-5), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.83%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 19, 2026
Date Received: September 19, 2026
Date Analyzed: September 19, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22626-1	22626-2	22626-3	22626-4	22626-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	132	168	165	93.9	120
Carbonyl sulfide	<0.50	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	43.9	96.6	342	217	233
Ethyl mercaptan	0.83	1.03	4.02	2.08	2.36
Dimethyl sulfide	156	285	956	1111	644
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.34	1.51	2.16	<1.60	1.85
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	1.99	3.06	12.0	12.7	7.32
s-Butyl mercaptan	3.21	4.24	13.0	13.9	9.42
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	3.08	1.22	3.73	26.0	5.93
Tetrahydrothiophene	1.58	2.14	9.08	8.18	4.93
Unidentified sulfurs	6.62	5.72	26.9	31.4	21.0
	(Concentration in ppmv, as H_2S)				
Total Sulfur	352.87	569.60	1536.66	1541.37	1056.33

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 19, 2026
Date Received: September 19, 2026
Date Analyzed: September 19, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	134	130	132	2.9
	FL-2009 Inlet	165	171	168	3.3
	Hero Inlet	166	163	165	2.1
	Parnel Inlet	91.6	96.3	93.9	5.0
	Zeeco Inlet	122	118	120	3.9
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	44.4	43.3	43.9	2.5
	FL-2009 Inlet	95.9	97.2	96.6	1.4
	Hero Inlet	345	338	342	2.0
	Parnel Inlet	213	220	217	3.6
	Zeeco Inlet	235	231	233	1.5
Ethyl mercaptan	Zeeco South	0.81	0.84	0.83	3.6
	FL-2009 Inlet	1.06	1.00	1.03	5.8
	Hero Inlet	4.05	3.98	4.02	1.7
	Parnel Inlet	2.08	2.07	2.08	0.48
	Zeeco Inlet	2.35	2.36	2.36	0.42
Dimethyl sulfide	Zeeco South	156	155	156	0.81
	FL-2009 Inlet	286	284	285	0.41
	Hero Inlet	967	944	956	2.4
	Parnel Inlet	1100	1122	1111	2.0
	Zeeco Inlet	652	637	644	2.3
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.35	1.32	1.34	2.2
	FL-2009 Inlet	1.51	1.51	1.51	0.00
	Hero Inlet	2.19	2.13	2.16	2.8
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	1.85	1.85	1.85	0.00



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	1.96	2.01	1.99	2.5
	FL-2009 Inlet	3.04	3.08	3.06	1.3
	Hero Inlet	12.2	11.9	12.0	3.0
	Parnel Inlet	12.7	12.6	12.7	0.32
	Zeeco Inlet	7.31	7.32	7.32	0.14
s-Butyl mercaptan	Zeeco South	3.26	3.16	3.21	3.1
	FL-2009 Inlet	4.24	4.23	4.24	0.24
	Hero Inlet	13.1	12.8	13.0	2.2
	Parnel Inlet	14.0	13.8	13.9	1.0
	Zeeco Inlet	9.32	9.51	9.42	2.0
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	3.08	3.07	3.08	0.33
	FL-2009 Inlet	1.23	1.21	1.22	1.6
	Hero Inlet	3.77	3.68	3.73	2.4
	Parnel Inlet	25.9	26.1	26.0	0.96
	Zeeco Inlet	5.92	5.94	5.93	0.34
Tetrahydrothiophene	Zeeco South	1.56	1.60	1.58	2.5
	FL-2009 Inlet	2.15	2.13	2.14	0.93
	Hero Inlet	9.26	8.90	9.08	4.0
	Parnel Inlet	7.85	8.51	8.18	8.1
	Zeeco Inlet	4.97	4.89	4.93	1.6
Unidentified sulfurs	Zeeco South	6.70	6.53	6.62	2.6
	FL-2009 Inlet	5.74	5.69	5.72	0.87
	Hero Inlet	26.7	27.2	26.9	2.2
	Parnel Inlet	31.0	31.8	31.4	2.7
	Zeeco Inlet	20.6	21.4	21.0	4.0

Five Tedlar bag samples, laboratory numbers 22626-(1-5), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.1%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Turnaround Times:** Standard 10 day
	Expedited: 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22626-1	9/19/26	8:20am	X	X	X	X			
FL-2009 Inlet	LFG	-2	9/19/26	7:45am	X	X	X	X			
Hero Inlet	LFG	-3	9/19/26	8:05am	X	X	X	X			
Parnel Inlet	LFG	-4	9/19/26	8:10am	X	X	X	X			
Zeeco Inlet	LFG	-5	9/19/26	8:15am	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/19/26	9:18	Ruben G	9/19/26	9:16
Relinquished by: *(Signature)* Ruben G	9/19/26	9:56	Received by: *(Signature)*	9/19/26	9:56
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date	Time

Company Info:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Sui
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 20, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22646-1	22646-2	22646-3	22646-4	22646-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	6.67	3.72	5.22	5.36	8.94
Nitrogen	30.38	23.67	30.01	29.06	41.25
Methane	28.15	28.63	10.69	12.71	13.89
Carbon Dioxide	32.37	38.93	43.72	44.18	31.03
Hydrogen	1.08	2.61	5.75	5.57	2.32
		(Concentration in ppmv)			
Carbon Monoxide	138	427	834	794	349
		(Concentration in %v, by component)			
TNMHC	0.232	0.327	0.800	0.779	0.445
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	302.1	320.1	168.9	186.0	172.1
BTU/ft3 (Wet @ 0.25636 psia)	296.9	314.5	165.9	182.8	169.1
BTU/lb (Dry @60F, 14.696 psia)	3823	3976	1938	2147	2078

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 20, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.62	6.72	6.67	1.5
Nitrogen	Zeeco South	30.24	30.51	30.38	0.89
Methane	Zeeco South	28.23	28.06	28.15	0.60
Carbon Dioxide	Zeeco South	32.50	32.24	32.37	0.80
Hydrogen	Zeeco South	1.08	1.08	1.08	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	138	138	138	0.23
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.231	0.233	0.232	0.86

Five Tedlar bag samples, laboratory numbers 22646-(6-10), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.70%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 20, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22646-1	22646-2	22646-3	22646-4	22646-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	144	142	177	186	130
Carbonyl sulfide	<0.50	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	48.6	102	367	435	239
Ethyl mercaptan	1.00	1.12	4.35	4.53	2.60
Dimethyl sulfide	169	364	1023	1087	628
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.50	1.67	2.22	2.56	1.98
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.51	4.03	13.0	13.9	8.16
s-Butyl mercaptan	3.82	5.11	13.2	15.1	9.82
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	4.41	6.24	4.35	8.77	6.68
Tetrahydrothiophene	1.81	2.81	9.51	10.5	5.50
Unidentified sulfurs	7.63	22.6	29.7	41.9	23.6
	(Concentration in ppmv, as H_2S)				
Total Sulfur	388.43	658.15	1648.56	1814.63	1061.03

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 20, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	142	145	144	2.0
	FL-2009 Inlet	141	143	142	0.83
	Hero Inlet	177	178	177	0.3
	Parnel Inlet	189	183	186	2.9
	Zeeco Inlet	130	129	130	0.81
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	47.9	49.4	48.6	3.1
	FL-2009 Inlet	101	104	102	3.0
	Hero Inlet	368	367	367	0.38
	Parnel Inlet	440	431	435	2.0
	Zeeco Inlet	241	236	239	1.9
Ethyl mercaptan	Zeeco South	0.95	1.05	1.00	10
	FL-2009 Inlet	1.09	1.15	1.12	5.4
	Hero Inlet	4.41	4.29	4.35	2.8
	Parnel Inlet	4.60	4.46	4.53	3.1
	Zeeco Inlet	2.57	2.63	2.60	2.3
Dimethyl sulfide	Zeeco South	169	169	169	0.04
	FL-2009 Inlet	359	369	364	2.6
	Hero Inlet	1029	1017	1023	1.2
	Parnel Inlet	1099	1075	1087	2.1
	Zeeco Inlet	629	626	628	0.62
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.47	1.53	1.50	4.0
	FL-2009 Inlet	1.61	1.73	1.67	7.2
	Hero Inlet	2.26	2.17	2.22	4.1
	Parnel Inlet	2.57	2.55	2.56	0.78
	Zeeco Inlet	1.92	2.03	1.98	5.6



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.48	2.54	2.51	2.4
	FL-2009 Inlet	3.94	4.12	4.03	4.5
	Hero Inlet	13.4	12.6	13.0	5.7
	Parnel Inlet	14.1	13.7	13.9	2.9
	Zeeco Inlet	8.32	7.99	8.16	4.0
s-Butyl mercaptan	Zeeco South	3.80	3.84	3.82	1.0
	FL-2009 Inlet	4.97	5.24	5.11	5.3
	Hero Inlet	13.5	12.8	13.2	5.1
	Parnel Inlet	15.2	15.0	15.1	1.5
	Zeeco Inlet	9.80	9.83	9.82	0.31
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	4.37	4.44	4.41	1.6
	FL-2009 Inlet	6.14	6.33	6.24	3.0
	Hero Inlet	4.43	4.27	4.35	3.7
	Parnel Inlet	8.86	8.67	8.77	2.2
	Zeeco Inlet	6.56	6.80	6.68	3.6
Tetrahydrothiophene	Zeeco South	1.78	1.84	1.81	3.3
	FL-2009 Inlet	2.80	2.82	2.81	0.71
	Hero Inlet	9.79	9.23	9.51	5.9
	Parnel Inlet	10.5	10.4	10.5	0.76
	Zeeco Inlet	5.37	5.63	5.50	4.7
Unidentified sulfurs	Zeeco South	7.51	7.74	7.63	3.0
	FL-2009 Inlet	22.3	23.0	22.6	2.8
	Hero Inlet	30.5	28.9	29.7	5.3
	Parnel Inlet	41.5	42.3	41.9	2.0
	Zeeco Inlet	23.6	23.7	23.6	0.63

Five Tedlar bag samples, laboratory numbers 22646-(1-5), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.9%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Turnaround Times:** Standard 10 day
	Expedited: 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22646-1	9-20-26	12:45	X	X	X	X			
FL-2009 Inlet	LFG	-2	9-20-26	12:50	X	X	X	X			
Hero Inlet	LFG	-3	9-20-26	12:20	X	X	X	X			
Parnel Inlet	LFG	-4	9-20-26	12:30	X	X	X	X			
Zeeco Inlet	LFG	-5	9-20-26	12:35	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9-20-26	6:00am	Received by: *(Signature)*	9-21-26	6:00am
Relinquished by: *(Signature)*	9-21-26	9:10am	Received by: *(Signature)*	9/21/26	9:10
Relinquished by: *(Signature)*	9/21/26	10:10	Received for Laboratory by: *(Signature)*	9/21/26	10:10

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Sui	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach, CA 90806	**City/State/Zip:** Long Beach, CA 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Email Address:	**Email Address:** cfong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 21, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22646-6	22646-7	22646-8	22646-9	22646-10
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components			*(Concentration in %v)*		
Oxygen	8.08	4.42	5.10	6.74	6.86
Nitrogen	35.20	25.52	29.01	33.88	35.26
Methane	25.06	27.22	10.48	12.20	16.37
Carbon Dioxide	28.52	37.50	44.74	40.20	36.15
Hydrogen	1.05	2.64	6.24	5.05	2.90
			(Concentration in ppmv)		
Carbon Monoxide	122	384	753	668	406
			(Concentration in %v, by component)		
TNMHC	0.189	0.258	0.803	0.524	0.387
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	270.5	302.2	168.0	165.1	196.1
BTU/ft3 (Wet @ 0.25636 psia)	265.7	296.9	165.0	162.2	192.7
BTU/lb (Dry @60F, 14.696 psia)	3444	3765	1924	1940	2350

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 21, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	8.09	8.07	8.08	0.25
Nitrogen	Zeeco South	35.21	35.18	35.20	0.09
Methane	Zeeco South	25.11	25.00	25.06	0.44
Carbon Dioxide	Zeeco South	28.54	28.50	28.52	0.14
Hydrogen	Zeeco South	1.03	1.06	1.05	2.9
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	123	122	122	0.86
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.189	0.189	0.189	0.21

Five Tedlar bag samples, laboratory numbers 22646-(6-10), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.69%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 21, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22646-6	22646-7	22646-8	22646-9	22646-10
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	137	202	209	171	135
Carbonyl sulfide	<0.50	0.51	<1.60	<1.60	<1.20
Methyl mercaptan	45.5	136	422	377	247
Ethyl mercaptan	0.92	1.54	4.71	3.78	2.64
Dimethyl sulfide	152	351	1105	914	674
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.48	1.89	2.41	2.21	1.92
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.22	4.11	13.5	10.8	8.03
s-Butyl mercaptan	3.56	5.12	14.3	11.9	10.1
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	3.75	1.54	3.25	6.38	7.36
Tetrahydrothiophene	1.60	2.00	9.07	5.55	4.54
Unidentified sulfurs	6.65	6.42	27.2	23.9	17.5
	(Concentration in ppmv, as H_2S)				
Total Sulfur	357.95	712.78	1813.34	1533.08	1115.57

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 21, 2026
Date Received: September 21, 2026
Date Analyzed: September 21, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	135	138	137	2.7
	FL-2009 Inlet	200	204	202	1.8
	Hero Inlet	211	207	209	1.7
	Parnel Inlet	173	169	171	2.2
	Zeeco Inlet	134	137	135	2.6
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	0.49	0.53	0.51	7.8
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	45.6	45.5	45.5	0.22
	FL-2009 Inlet	133	138	136	3.6
	Hero Inlet	424	420	422	0.86
	Parnel Inlet	381	374	377	1.8
	Zeeco Inlet	243	251	247	3.4
Ethyl mercaptan	Zeeco South	0.92	0.91	0.92	1.1
	FL-2009 Inlet	1.53	1.54	1.54	0.65
	Hero Inlet	4.70	4.71	4.71	0.21
	Parnel Inlet	3.77	3.79	3.78	0.53
	Zeeco Inlet	2.56	2.72	2.64	6.1
Dimethyl sulfide	Zeeco South	150	154	152	2.8
	FL-2009 Inlet	345	356	351	3.0
	Hero Inlet	1107	1102	1105	0.49
	Parnel Inlet	920	909	914	1.2
	Zeeco Inlet	663	685	674	3.3
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.43	1.52	1.48	6.1
	FL-2009 Inlet	1.85	1.93	1.89	4.2
	Hero Inlet	2.40	2.41	2.41	0.42
	Parnel Inlet	2.26	2.16	2.21	4.5
	Zeeco Inlet	1.87	1.97	1.92	5.2

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.18	2.25	2.22	3.2
	FL-2009 Inlet	3.99	4.22	4.11	5.6
	Hero Inlet	13.6	13.4	13.5	0.82
	Parnel Inlet	10.8	10.8	10.8	0.09
	Zeeco Inlet	7.95	8.10	8.03	1.9
s-Butyl mercaptan	Zeeco South	3.45	3.67	3.56	6.2
	FL-2009 Inlet	5.04	5.20	5.12	3.1
	Hero Inlet	14.3	14.3	14.3	0.28
	Parnel Inlet	12.0	11.9	11.9	0.84
	Zeeco Inlet	9.84	10.3	10.1	4.5
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	3.66	3.83	3.75	4.5
	FL-2009 Inlet	1.48	1.59	1.54	7.2
	Hero Inlet	3.24	3.26	3.25	0.62
	Parnel Inlet	6.43	6.32	6.38	1.7
	Zeeco Inlet	7.12	7.59	7.36	6.4
Tetrahydrothiophene	Zeeco South	1.57	1.62	1.60	3.1
	FL-2009 Inlet	1.94	2.06	2.00	6.0
	Hero Inlet	9.06	9.07	9.07	0.11
	Parnel Inlet	5.60	5.50	5.55	1.8
	Zeeco Inlet	4.43	4.64	4.54	4.6
Unidentified sulfurs	Zeeco South	6.42	6.88	6.65	6.9
	FL-2009 Inlet	6.29	6.54	6.42	3.9
	Hero Inlet	27.0	27.3	27.2	1.0
	Parnel Inlet	24.3	23.6	23.9	2.9
	Zeeco Inlet	17.1	18.0	17.5	5.1

Five Tedlar bag samples, laboratory numbers 22646-(6-10), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 3.0%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)* Emmanuel Melena	**Turnaround Times:** Standard 10 day **Expedited:** 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22646-6	9.21.26	7:55am	X	X	X	X			
FL-2009 Inlet	LFG	-7	9.21.26	7:10am	X	X	X	X			
Hero Inlet	LFG	-8	9.21.26	7:25am	X	X	X	X			
Parnel Inlet	LFG	-9	9.21.26	8:55am	X	X	X	X			
Zeeco Inlet	LFG	-10	9.21.26	7:40am	X	X	X	X			

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9.21.26	9:10am		9/21/26	9:10
Relinquished by: *(Signature)*	**Date**	**Time**	**Received by:** *(Signature)*	**Date**	**Time**
	9/21/26	10:10			
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by:** *(Signature)*	**Date**	**Time**
				9/21/26	10:40

Company Info:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Sui
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 22, 2026
Date Received: September 22, 2026
Date Analyzed: September 22, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22656-1	22656-2	22656-3	22656-4	22656-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	6.54	4.60	5.45	6.83	6.43
Nitrogen	30.73	25.78	30.93	32.90	34.62
Methane	27.35	27.99	10.65	11.21	17.09
Carbon Dioxide	31.68	36.23	42.38	40.05	36.49
Hydrogen	1.06	2.22	5.72	5.31	2.73
		(Concentration in ppmv)			
Carbon Monoxide	126	319	734	705	362
		(Concentration in %v, by component)			
TNMHC	0.231	0.302	0.755	0.661	0.437
		BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	297.9	313.0	167.5	166.0	206.1
BTU/ft3 (Wet @ 0.25636 psia)	292.7	307.6	164.6	163.1	202.5
BTU/lb (Dry @60F, 14.696 psia)	3768	3917	1934	1938	2467

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 22, 2026
Date Received: September 22, 2026
Date Analyzed: September 22, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.51	6.56	6.54	0.77
Nitrogen	Zeeco South	30.75	30.71	30.73	0.13
Methane	Zeeco South	27.36	27.34	27.35	0.07
Carbon Dioxide	Zeeco South	31.70	31.65	31.68	0.16
Hydrogen	Zeeco South	1.06	1.06	1.06	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	124	127	126	2.2
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.230	0.231	0.231	0.80

Five Tedlar bag samples, laboratory numbers 22656-(1-5), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.59%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 22, 2026
Date Received: September 22, 2026
Date Analyzed: September 22, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22656-1	22656-2	22656-3	22656-4	22656-5
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	139	194	166	172	151
Carbonyl sulfide	0.51	0.49	<1.60	<1.60	<1.20
Methyl mercaptan	43.7	101	333	400	259
Ethyl mercaptan	0.85	1.15	3.93	4.05	2.72
Dimethyl sulfide	137	278	931	958	667
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.35	1.71	2.07	2.18	2.09
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	1.95	3.19	11.7	11.9	8.06
s-Butyl mercaptan	3.30	4.54	12.7	13.8	10.4
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	3.53	1.86	3.66	6.03	6.59
Tetrahydrothiophene	1.54	2.47	9.06	8.76	5.34
Unidentified sulfurs	7.01	9.49	27.3	34.3	25.0
	(Concentration in ppmv, as H_2S)				
Total Sulfur	343.57	599.86	1504.03	1617.14	1143.80

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 22, 2026
Date Received: September 22, 2026
Date Analyzed: September 22, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	136	142	139	4.7
	FL-2009 Inlet	194	195	194	0.43
	Hero Inlet	163	169	166	3.9
	Parnel Inlet	170	173	172	1.6
	Zeeco Inlet	150	152	151	1.1
Carbonyl sulfide	Zeeco South	0.49	0.52	0.51	5.9
	FL-2009 Inlet	0.51	0.47	0.49	8.2
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	42.4	45.0	43.7	6.0
	FL-2009 Inlet	102	100	101	1.5
	Hero Inlet	325	341	333	4.9
	Parnel Inlet	399	401	400	0.62
	Zeeco Inlet	256	263	259	2.8
Ethyl mercaptan	Zeeco South	0.84	0.86	0.85	2.4
	FL-2009 Inlet	1.14	1.15	1.15	0.87
	Hero Inlet	3.85	4.00	3.93	3.8
	Parnel Inlet	4.10	4.00	4.05	2.5
	Zeeco Inlet	2.69	2.74	2.72	1.8
Dimethyl sulfide	Zeeco South	134	140	137	4.4
	FL-2009 Inlet	279	277	278	0.60
	Hero Inlet	905	957	931	5.6
	Parnel Inlet	953	963	958	1.0
	Zeeco Inlet	666	667	667	0.18
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.30	1.40	1.35	7.4
	FL-2009 Inlet	1.73	1.69	1.71	2.3
	Hero Inlet	2.06	2.08	2.07	0.97
	Parnel Inlet	2.24	2.12	2.18	5.5
	Zeeco Inlet	2.15	2.02	2.09	6.2



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	1.89	2.00	1.95	5.7
	FL-2009 Inlet	3.21	3.16	3.19	1.6
	Hero Inlet	11.4	12.1	11.7	6.0
	Parnel Inlet	11.9	11.9	11.9	0.08
	Zeeco Inlet	8.10	8.02	8.06	0.99
s-Butyl mercaptan	Zeeco South	3.21	3.39	3.30	5.5
	FL-2009 Inlet	4.64	4.43	4.54	4.6
	Hero Inlet	12.4	13.0	12.7	5.1
	Parnel Inlet	13.7	13.9	13.8	1.5
	Zeeco Inlet	10.4	10.4	10.4	0.29
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	3.46	3.59	3.53	3.7
	FL-2009 Inlet	1.86	1.86	1.86	0.00
	Hero Inlet	3.59	3.72	3.66	3.6
	Parnel Inlet	5.98	6.07	6.03	1.5
	Zeeco Inlet	6.54	6.63	6.59	1.4
Tetrahydrothiophene	Zeeco South	1.54	1.53	1.54	0.65
	FL-2009 Inlet	2.54	2.39	2.47	6.1
	Hero Inlet	8.89	9.23	9.06	3.8
	Parnel Inlet	8.82	8.70	8.76	1.4
	Zeeco Inlet	5.18	5.50	5.34	6.0
Unidentified sulfurs	Zeeco South	6.96	7.06	7.01	1.4
	FL-2009 Inlet	9.40	9.58	9.49	1.9
	Hero Inlet	26.7	27.9	27.3	4.1
	Parnel Inlet	34.4	34.3	34.3	0.38
	Zeeco Inlet	24.8	25.2	25.0	1.2

Five Tedlar bag samples, laboratory numbers 22656-(1-5), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 3.0%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Turnaround Times:** Standard 10 day Expedited: 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	22656-1	9/22/26	8:50 AM	X	X	X	X			
FL-2009 Inlet	LFG	-2	9/22/26	8:40 AM	X	X	X	X			
Hero Inlet	LFG	-3	9/22/26	8:15 AM	X	X	X	X			
Parnel Inlet	LFG	-4	9/22/26	8:20 AM	X	X	X	X			
Zeeco Inlet	LFG	-5	9/22/26	7:55 AM	X	X	X	X			

ANALYSES REQUESTED

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9/22/26	8:55 AM	Received by: *(Signature)*	9/22/26	9:07
Relinquished by: *(Signature)*	9/22/26	10:17	Received by: *(Signature)*	Date	Time
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	9/22/26	10:17

Company Info:

Company: SCS Engineers
Street Address: 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address: 3900 Kilroy Airport Way Sui
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 23, 2026
Date Received: September 23, 2026
Date Analyzed: September 23, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22666-21	22666-22	22666-23	22666-24	22666-25
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components			*(Concentration in %v)*		
Oxygen	7.45	4.35	7.74	7.05	6.59
Nitrogen	35.21	26.65	39.17	34.55	35.68
Methane	23.58	27.04	9.10	10.80	17.42
Carbon Dioxide	29.66	37.17	36.45	40.21	35.88
Hydrogen	1.25	2.42	4.87	4.22	2.51
			(Concentration in ppmv)		
Carbon Monoxide	132	329	676	695	357
			(Concentration in %v, by component)		
TNMHC	0.230	0.246	0.657	0.645	0.422
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	259.7	298.3	140.1	155.7	206.3
BTU/ft3 (Wet @ 0.25636 psia)	255.2	293.1	137.7	153.0	202.7
BTU/lb (Dry @60F, 14.696 psia)	3272	3715	1648	1800	2478

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 23, 2026
Date Received: September 23, 2026
Date Analyzed: September 23, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	7.46	7.43	7.45	0.40
Nitrogen	Zeeco South	35.24	35.18	35.21	0.17
Methane	Zeeco South	23.59	23.57	23.58	0.08
Carbon Dioxide	Zeeco South	29.67	29.64	29.66	0.10
Hydrogen	Zeeco South	1.25	1.25	1.25	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	133	130	132	1.9
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.230	0.230	0.230	0.04

Five Tedlar bag samples, laboratory numbers 22666-(21-25), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.38%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 7, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 23, 2026
Date Received: September 23, 2026
Date Analyzed: September 23, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22666-21	22666-22	22666-23	22666-24	22666-25
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	111	192	145	168	157
Carbonyl sulfide	<0.50	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	43.7	101	288	388	248
Ethyl mercaptan	0.86	1.12	3.41	3.83	2.49
Dimethyl sulfide	176	298	815	924	656
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.11	1.58	1.91	2.12	1.99
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.21	3.12	10.0	11.1	7.41
s-Butyl mercaptan	3.27	4.10	10.9	12.7	10.0
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	3.61	1.15	3.36	6.13	4.74
Tetrahydrothiophene	1.67	1.58	7.12	6.87	4.80
Unidentified sulfurs	6.97	4.59	21.5	26.7	18.3
	(Concentration in ppmv, as H_2S)				
Total Sulfur	353.66	609.15	1308.91	1556.62	1114.87

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 23, 2026
Date Received: September 23, 2026
Date Analyzed: September 23, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	112	110	111	1.9
	FL-2009 Inlet	188	196	192	3.9
	Hero Inlet	143	146	145	2.5
	Parnel Inlet	167	170	168	1.8
	Zeeco Inlet	154	159	157	3.0
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	44.1	43.4	43.7	1.7
	FL-2009 Inlet	100	102	101	1.3
	Hero Inlet	285	292	288	2.4
	Parnel Inlet	385	392	388	1.7
	Zeeco Inlet	243	252	248	3.6
Ethyl mercaptan	Zeeco South	0.89	0.82	0.86	8.2
	FL-2009 Inlet	1.12	1.12	1.12	0.00
	Hero Inlet	3.32	3.50	3.41	5.3
	Parnel Inlet	3.79	3.86	3.83	1.8
	Zeeco Inlet	2.50	2.48	2.49	0.80
Dimethyl sulfide	Zeeco South	182	170	176	7.0
	FL-2009 Inlet	294	302	298	2.4
	Hero Inlet	803	826	815	2.8
	Parnel Inlet	916	932	924	1.7
	Zeeco Inlet	656	656	656	0.11
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.16	1.05	1.11	10
	FL-2009 Inlet	1.57	1.58	1.58	0.63
	Hero Inlet	1.88	1.94	1.91	3.1
	Parnel Inlet	2.06	2.17	2.12	5.2
	Zeeco Inlet	2.02	1.96	1.99	3.0

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.25	2.17	2.21	3.6
	FL-2009 Inlet	3.07	3.16	3.12	2.9
	Hero Inlet	10.0	10.1	10.0	0.80
	Parnel Inlet	11.1	11.1	11.1	0.27
	Zeeco Inlet	7.41	7.41	7.41	0.00
s-Butyl mercaptan	Zeeco South	3.28	3.25	3.27	0.92
	FL-2009 Inlet	3.96	4.24	4.10	6.8
	Hero Inlet	10.7	11.1	10.9	3.0
	Parnel Inlet	12.7	12.7	12.7	0.08
	Zeeco Inlet	10.0	10.1	10.0	1.0
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	3.62	3.60	3.61	0.55
	FL-2009 Inlet	1.09	1.20	1.15	9.6
	Hero Inlet	3.32	3.40	3.36	2.4
	Parnel Inlet	6.10	6.16	6.13	0.98
	Zeeco Inlet	4.75	4.72	4.74	0.63
Tetrahydrothiophene	Zeeco South	1.70	1.64	1.67	3.6
	FL-2009 Inlet	1.50	1.66	1.58	10
	Hero Inlet	7.09	7.15	7.12	0.84
	Parnel Inlet	6.78	6.96	6.87	2.6
	Zeeco Inlet	4.82	4.78	4.80	0.83
Unidentified sulfurs	Zeeco South	7.04	6.90	6.97	2.0
	FL-2009 Inlet	4.39	4.79	4.59	8.7
	Hero Inlet	21.3	21.7	21.5	1.5
	Parnel Inlet	26.6	26.8	26.7	0.67
	Zeeco Inlet	18.3	18.4	18.3	0.38

Five Tedlar bag samples, laboratory numbers 22666-(21-25), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 2.8%.

CHAIN OF CUSTODY RECORD

Client/Project Name:	Project Location:
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project Number:	**Fieldbook Log No.**
07224200.24 Task 1	
Sampler: *(Signature)* EM	**Turnaround Times:** Standard 10 day **Expedited:** 24hr / 48hr / 72hr / 5 day

Client Sample Identification	Type of Sample Canister ID	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2 (1946)	CO (EPA ALT-144)	HHV (3588)			Special Remarks
Zeeco South station	LFG	226666-21	9-23-26	8:	X	X	X	X			
FL-2009 Inlet	LFG	-22	9-23-26	7:25am	X	X	X	X			
Hero Inlet	LFG	-23	9-23-26	7:35am	X	X	X	X			
Parnel Inlet	LFG	-24	9-23-26	7:55am	X	X	X	X			
Zeeco Inlet	LFG	-25	9-23-26	8:10am	X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)* EM	9-23-26	0530AM	Received by: *(Signature)*	9/23/26	0530
Relinquished by: *(Signature)*	9-23-26	0530PM	Received by: *(Signature)* Ruben G	9/23/26	10:10
Relinquished by: *(Signature)* Ruben G	9/23/26	11:05	Received for Laboratory by: *(Signature)*	Date	Time

Company Info:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Suite 300
City/State/Zip: Long Beach, CA 90806
Telephone No.: 562-743-7895
Email Address:

Send Report to:

Company: SCS Engineers
Street Address 3900 Kilroy Airport Way Sui
City/State/Zip: Long Beach, CA 90806
Project Manager: Cornelius Fong
Email Address: cfong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 24, 2026
Date Received: September 24, 2026
Date Analyzed: September 24, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22676-19	22676-20	22676-21	22676-22	22676-23
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	7.12	4.85	6.34	6.84	6.18
Nitrogen	33.89	26.68	33.52	33.33	34.47
Methane	24.53	27.12	10.11	11.22	17.68
Carbon Dioxide	30.69	35.69	40.07	40.21	36.74
Hydrogen	1.28	2.27	5.28	5.19	2.73
		(Concentration in ppmv)			
Carbon Monoxide	150	332	739	696	335
		(Concentration in %v, by component)			
TNMHC	0.236	0.293	0.760	0.708	0.441
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	269.1	304.8	160.1	167.0	211.6
BTU/ft3 (Wet @ 0.25636 psia)	264.5	299.5	157.3	164.1	207.9
BTU/lb (Dry @60F, 14.696 psia)	3387	3811	1857	1946	2537

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 24, 2026
Date Received: September 24, 2026
Date Analyzed: September 24, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	7.07	7.16	7.12	1.3
Nitrogen	Zeeco South	33.75	34.02	33.89	0.80
Methane	Zeeco South	24.59	24.47	24.53	0.49
Carbon Dioxide	Zeeco South	30.62	30.75	30.69	0.42
Hydrogen	Zeeco South	1.26	1.29	1.28	2.4
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	150	151	150	0.23
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.236	0.236	0.236	0.20

Five Tedlar bag samples, laboratory numbers 22676-(19-23), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.82%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 24, 2026
Date Received: September 24, 2026
Date Analyzed: September 24, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22676-19	22676-20	22676-21	22676-22	22676-23
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	122	185	145	149	164
Carbonyl sulfide	<0.50	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	49.0	95.1	310	378	272
Ethyl mercaptan	1.01	1.12	3.64	3.80	2.88
Dimethyl sulfide	202	276	889	958	712
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.33	1.61	1.78	1.99	2.36
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.66	3.13	11.0	11.8	8.89
s-Butyl mercaptan	3.86	4.37	11.7	13.7	11.6
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	5.01	1.66	5.41	9.08	6.45
Tetrahydrothiophene	2.09	2.29	8.63	9.21	6.15
Unidentified sulfurs	11.4	10.1	29.0	37.4	29.0
	(Concentration in ppmv, as H_2S)				
Total Sulfur	405.83	582.04	1421.28	1581.50	1220.95

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 24, 2026
Date Received: September 24, 2026
Date Analyzed: September 24, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	124	120	122	3.3
	FL-2009 Inlet	183	186	185	1.8
	Hero Inlet	145	145	145	0.14
	Parnel Inlet	151	148	149	1.4
	Zeeco Inlet	164	163	164	0.26
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	49.8	48.1	49.0	3.6
	FL-2009 Inlet	94.4	95.9	95.1	1.5
	Hero Inlet	311	309	310	0.91
	Parnel Inlet	380	376	378	0.95
	Zeeco Inlet	275	268	272	2.6
Ethyl mercaptan	Zeeco South	1.04	0.98	1.01	5.9
	FL-2009 Inlet	1.07	1.17	1.12	8.9
	Hero Inlet	3.65	3.62	3.64	0.83
	Parnel Inlet	3.80	3.79	3.80	0.26
	Zeeco Inlet	2.89	2.87	2.88	0.69
Dimethyl sulfide	Zeeco South	205	200	202	2.6
	FL-2009 Inlet	273	280	276	2.6
	Hero Inlet	898	881	889	1.9
	Parnel Inlet	958	957	958	0.08
	Zeeco Inlet	718	706	712	1.8
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.33	1.33	1.33	0.00
	FL-2009 Inlet	1.57	1.65	1.61	5.0
	Hero Inlet	1.74	1.81	1.78	3.9
	Parnel Inlet	1.96	2.01	1.99	2.5
	Zeeco Inlet	2.35	2.36	2.36	0.42

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.69	2.63	2.66	2.3
	FL-2009 Inlet	3.03	3.22	3.13	6.1
	Hero Inlet	11.1	10.9	11.0	2.0
	Parnel Inlet	11.8	11.8	11.8	0.00
	Zeeco Inlet	8.96	8.81	8.89	1.7
s-Butyl mercaptan	Zeeco South	3.87	3.85	3.86	0.52
	FL-2009 Inlet	4.18	4.55	4.37	8.5
	Hero Inlet	11.7	11.6	11.7	1.0
	Parnel Inlet	13.9	13.5	13.7	3.1
	Zeeco Inlet	11.7	11.4	11.6	2.4
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	5.08	4.94	5.01	2.8
	FL-2009 Inlet	1.59	1.73	1.66	8.4
	Hero Inlet	5.46	5.35	5.41	2.0
	Parnel Inlet	9.14	9.01	9.08	1.4
	Zeeco Inlet	6.58	6.32	6.45	4.0
Tetrahydrothiophene	Zeeco South	2.14	2.03	2.09	5.3
	FL-2009 Inlet	2.17	2.41	2.29	10
	Hero Inlet	8.71	8.55	8.63	1.9
	Parnel Inlet	9.48	8.93	9.21	6.0
	Zeeco Inlet	6.18	6.12	6.15	0.98
Unidentified sulfurs	Zeeco South	11.6	11.1	11.4	4.1
	FL-2009 Inlet	9.73	10.5	10.1	8.0
	Hero Inlet	29.1	28.9	29.0	0.62
	Parnel Inlet	39.0	35.8	37.4	8.7
	Zeeco Inlet	29.4	28.6	29.0	2.9

Five Tedlar bag samples, laboratory numbers 22676-(19-23), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 3.0%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22076-19	9/24/26	8:10 PM	X	X	X	X			
FL-2009 Inlet	LFG	-20	9/24/26	9:09 PM	X	X	X	X			
Hero Inlet	LFG	-21	9/24/26	9:05	X	X	X	X			
Parnel Inlet	LFG	-22	9/24/26	8:40 PM	X	X	X	X			
Zeeco Inlet	LFG	-23	9/24/26	8:25 PM	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/24/26	9:10 PM	Ruben G	9/24/26	9:16
Relinquished by: *(Signature)* Ruben G	**Date** 9/24/26	**Time** 10:14	**Received by: *(Signature)***	**Date**	**Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by: *(Signature)***	**Date**	**Time**

Company Info:		Send Report to:	
Company:	SCS Engineers	**Company:**	SCS Engineers
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong
Fax No.:		**Email Address:**	CFong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 25, 2026
Date Received: September 25, 2026
Date Analyzed: September 25, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was caiculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22686-15	22686-16	22686-17	22686-18
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components		*(Concentration in %v)*		
Oxygen	8.94	4.66	5.55	6.08
Nitrogen	39.79	26.45	30.85	34.36
Methane	19.42	28.15	10.62	16.81
Carbon Dioxide	27.66	36.41	42.77	36.98
Hydrogen	1.55	2.18	5.82	2.87
		(Concentration in ppmv)		
Carbon Monoxide	185	321	788	410
		(Concentration in %v, by component)		
TNMHC	0.266	0.223	0.798	0.418
		BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	218.6	307.2	168.0	203.1
BTU/ft3 (Wet @ 0.25636 psia)	214.8	301.9	165.1	199.6
BTU/lb (Dry @60F, 14.696 psia)	2737	3852	1937	2427

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

B Fung

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 25, 2026
Date Received: September 25, 2026
Date Analyzed: September 25, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	9.00	8.87	8.94	1.5
Nitrogen	Zeeco South	39.86	39.72	39.79	0.35
Methane	Zeeco South	19.40	19.43	19.42	0.15
Carbon Dioxide	Zeeco South	27.56	27.75	27.66	0.69
Hydrogen	Zeeco South	1.54	1.55	1.55	0.65
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	187	184	185	1.3
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.264	0.268	0.266	1.6

Four Tedlar bag samples, laboratory numbers 22686-(15-18), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.87%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 25, 2026
Date Received: September 25, 2026
Date Analyzed: September 25, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22686-15	22686-16	22686-17	22686-18
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	104	203	198	158
Carbonyl sulfide	<0.50	0.49	<1.60	<1.20
Methyl mercaptan	65.6	118	381	285
Ethyl mercaptan	1.10	1.32	4.32	3.04
Dimethyl sulfide	228	296	1024	721
Carbon disulfide	<0.50	<0.50	<1.60	<1.20
i-Propyl mercaptan	1.17	1.96	2.33	2.39
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
n-Propyl mercaptan	3.15	3.70	12.6	9.53
s-Butyl mercaptan	4.10	5.20	13.7	12.4
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
Dimethyl disulfide	4.24	1.33	3.67	6.10
Tetrahydrothiophene	2.42	1.93	9.19	5.75
Unidentified sulfurs	11.3	6.18	28.4	26.8
	(Concentration in ppmv, as H_2S)			
Total Sulfur	429.33	639.69	1680.04	1236.13

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 25, 2026
Date Received: September 25, 2026
Date Analyzed: September 25, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	108	101	104	7.2
	FL-2009 Inlet	208	198	203	4.8
	Hero Inlet	194	202	198	4.4
	Zeeco Inlet	154	163	158	6.2
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	0.50	0.47	0.49	6.2
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	66.9	64.4	65.6	3.8
	FL-2009 Inlet	121	114	118	5.5
	Hero Inlet	374	388	381	3.8
	Zeeco Inlet	276	294	285	6.4
Ethyl mercaptan	Zeeco South	1.13	1.06	1.10	6.4
	FL-2009 Inlet	1.33	1.31	1.32	1.5
	Hero Inlet	4.22	4.42	4.32	4.6
	Zeeco Inlet	2.98	3.09	3.04	3.5
Dimethyl sulfide	Zeeco South	233	222	228	5.1
	FL-2009 Inlet	297	295	296	0.63
	Hero Inlet	1008	1039	1024	3.0
	Zeeco Inlet	708	734	721	3.6
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.18	1.15	1.17	2.6
	FL-2009 Inlet	1.95	1.96	1.96	0.51
	Hero Inlet	2.29	2.36	2.33	3.0
	Zeeco Inlet	2.32	2.46	2.39	5.9
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	3.20	3.09	3.15	3.5
	FL-2009 Inlet	3.71	3.68	3.70	0.81
	Hero Inlet	12.4	12.7	12.6	2.5
	Zeeco Inlet	9.20	9.86	9.53	6.9
s-Butyl mercaptan	Zeeco South	4.06	4.13	4.10	1.7
	FL-2009 Inlet	5.23	5.17	5.20	1.2
	Hero Inlet	13.4	14.0	13.7	4.2
	Zeeco Inlet	12.2	12.6	12.4	3.2
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	4.23	4.24	4.24	0.24
	FL-2009 Inlet	1.31	1.34	1.33	2.3
	Hero Inlet	3.67	3.66	3.67	0.27
	Zeeco Inlet	5.92	6.27	6.10	5.7
Tetrahydrothiophene	Zeeco South	2.40	2.43	2.42	1.2
	FL-2009 Inlet	1.90	1.95	1.93	2.6
	Hero Inlet	9.10	9.27	9.19	1.9
	Zeeco Inlet	5.52	5.98	5.75	7.9
Unidentified sulfurs	Zeeco South	11.4	11.3	11.3	1.4
	FL-2009 Inlet	6.20	6.16	6.18	0.65
	Hero Inlet	28.4	28.3	28.4	0.46
	Zeeco Inlet	25.7	28.0	26.8	8.7

Four Tedlar bag samples, laboratory numbers 22686-(15-18), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 3.6%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: (Signature) Emmanuel Melena	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	226886-15	9-25-26	8:55am	X	X	X	X			
FL-2009 Inlet	LFG	-16	9-25-26	7:25am	X	X	X	X			
Hero Inlet	LFG	-17	9.25.26	8:20am	X	X	X	X			
Parnel Inlet	LFG				X	X	X	X			
Zeeco Inlet	LFG	-18	9-25-26	8:50am	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	9.25.26	9:10am		9/25/26	9:10
Relinquished by: (Signature)	Date	Time	Received by: (Signature)	Date	Time
	9/25/26	10:00			
Relinquished by: (Signature)	Date	Time	Received for Laboratory by: (Signature)	Date	Time
				9/25/26	10:00

Company Info:		Send Report to:	
Company:	SCS Engineers	Company:	SCS Engineers
Street Address	3900 Kilroy Airport Way Suite 300	Street Address	3900 Kilroy Airport Way Suite 300
City/State/Zip:	Long Beach / CA / 90806	City/State/Zip:	Long Beach / CA / 90806
Telephone No.:	562-743-7895 /562-335-0002	Project Manager:	Cornelius Fong
Fax No.:		Email Address:	CFong@scsengineers.com

Analytical Laboratory

AtmAA Inc.
5107 Douglas Fir Rd.
Calabasas, CA 91302
TEL: (818) 223-3277
Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277

specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 26, 2026
Date Received: September 26, 2026
Date Analyzed: September 28, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22696-1	22696-2	22696-3	22696-4
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components		*(Concentration in %v)*		
Oxygen	7.19	4.91	5.45	6.80
Nitrogen	34.82	27.39	30.44	37.15
Methane	21.13	27.01	10.71	16.31
Carbon Dioxide	31.50	35.31	44.43	35.62
Hydrogen	2.02	2.10	5.68	2.48
		(Concentration in ppmv)		
Carbon Monoxide	235	344	809	392
		(Concentration in %v, by component)		
TNMHC	0.201	0.169	0.560	0.287
		BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	235.4	295.5	152.8	186.7
BTU/ft3 (Wet @ 0.25636 psia)	231.3	290.3	150.1	183.4
BTU/lb (Dry @60F, 14.696 psia)	2930	3707	1758	2243

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 26, 2026
Date Received: September 26, 2026
Date Analyzed: September 28, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	7.14	7.24	7.19	1.4
Nitrogen	Zeeco South	34.78	34.86	34.82	0.23
Methane	Zeeco South	21.14	21.11	21.13	0.14
Carbon Dioxide	Zeeco South	31.50	31.49	31.50	0.03
Hydrogen	Zeeco South	2.02	2.01	2.02	0.50
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	237	232	235	2.1
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.201	0.201	0.201	0.02

Four Tedlar bag samples, laboratory numbers 22696-(1-4), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.63%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 26, 2026
Date Received: September 26, 2026
Date Analyzed: September 26, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22696-1	22696-2	22696-3	22696-4
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	119	194	195	161
Carbonyl sulfide	<0.50	<0.50	<1.60	<1.20
Methyl mercaptan	91.8	108	380	286
Ethyl mercaptan	1.25	1.05	3.97	2.68
Dimethyl sulfide	312	280	960	716
Carbon disulfide	<0.50	<0.50	<1.60	<1.20
i-Propyl mercaptan	1.09	1.52	2.11	2.05
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
n-Propyl mercaptan	2.78	2.43	9.65	6.33
s-Butyl mercaptan	2.95	2.86	8.22	6.29
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
Dimethyl disulfide	1.66	0.59	1.23	2.41
Tetrahydrothiophene	0.88	0.59	2.25	1.41
Unidentified sulfurs	1.91	1.29	6.15	2.67
	(Concentration in ppmv, as H_2S)			
Total Sulfur	537.32	592.52	1569.73	1189.98

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 26, 2026
Date Received: September 26, 2026
Date Analyzed: September 26, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	119	119	119	0.04
	FL-2009 Inlet	193	194	194	0.70
	Hero Inlet	196	194	195	0.79
	Zeeco Inlet	164	159	161	3.1
Carbonyl sulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	90.7	92.9	91.8	2.4
	FL-2009 Inlet	108	108	108	0.31
	Hero Inlet	381	379	380	0.51
	Zeeco Inlet	289	284	286	1.8
Ethyl mercaptan	Zeeco South	1.29	1.21	1.25	6.4
	FL-2009 Inlet	1.08	1.02	1.05	5.7
	Hero Inlet	3.97	3.96	3.97	0.25
	Zeeco Inlet	2.74	2.62	2.68	4.5
Dimethyl sulfide	Zeeco South	311	314	312	1.1
	FL-2009 Inlet	280	279	280	0.27
	Hero Inlet	962	958	960	0.47
	Zeeco Inlet	726	707	716	2.7
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.12	1.06	1.09	5.5
	FL-2009 Inlet	1.52	1.51	1.52	0.66
	Hero Inlet	2.12	2.09	2.11	1.4
	Zeeco Inlet	1.95	2.14	2.05	9.3
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	2.80	2.75	2.78	1.8
	FL-2009 Inlet	2.46	2.39	2.43	2.9
	Hero Inlet	9.59	9.70	9.65	1.1
	Zeeco Inlet	6.36	6.29	6.33	1.1
s-Butyl mercaptan	Zeeco South	3.00	2.89	2.95	3.7
	FL-2009 Inlet	2.88	2.83	2.86	1.8
	Hero Inlet	8.19	8.24	8.22	0.61
	Zeeco Inlet	6.30	6.27	6.29	0.48
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	1.63	1.68	1.66	3.0
	FL-2009 Inlet	0.60	0.57	0.59	5.1
	Hero Inlet	1.25	1.21	1.23	3.3
	Zeeco Inlet	2.38	2.43	2.41	2.1
Tetrahydrothiophene	Zeeco South	0.88	0.87	0.88	1.1
	FL-2009 Inlet	0.59	0.58	0.59	1.7
	Hero Inlet	2.25	2.24	2.25	0.45
	Zeeco Inlet	1.36	1.45	1.41	6.4
Unidentified sulfurs	Zeeco South	1.90	1.92	1.91	1.0
	FL-2009 Inlet	1.33	1.25	1.29	6.2
	Hero Inlet	6.09	6.20	6.15	1.8
	Zeeco Inlet	2.66	2.68	2.67	0.75

Four Tedlar bag samples, laboratory numbers 22696-(1-4), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 2.4%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Chain of Custody Tape No.**

ANALYSES REQUESTED

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22696-1	9.26.26	9:05 am	X	X	X	X			
FL-2009 Inlet	LFG	-2	9.26.26	9:50 am	X	X	X	X			
Hero Inlet	LFG	-3	9.26.26	9:30 am	X	X	X	X			
~~Parnel Inlet~~ EA	LFG		~~9.26.26~~		X	X	X	X			
Zeeco Inlet	LFG	-4	9.26.26	8:40 am	X	X	X	X			

Relinquished by: *(Signature)*	**Date** 9/26/26	**Time** 9:17	**Received by: *(Signature)***	**Date** 9/26/26 **Time** 9:17
Relinquished by: *(Signature)*	**Date** 9/26/26	**Time** 10:10	**Received by: *(Signature)***	**Date** **Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by: *(Signature)***	**Date** 9/26/26 **Time** 10:10

Company Info:	Send Report to:	Analytical Laboratory
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach / CA / 90806	**City/State/Zip:** Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895 /562-335-0002	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:	**Email Address:** CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 27, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22716-26	22716-27	22716-28	22716-29	22716-30
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components		*(Concentration in %v)*			
Oxygen	6.63	4.60	4.35	5.96	5.93
Nitrogen	32.47	25.48	25.93	30.48	33.66
Methane	23.74	28.31	11.85	12.30	16.59
Carbon Dioxide	32.59	37.22	47.93	42.80	37.31
Hydrogen	1.66	2.36	6.54	5.53	2.82
		(Concentration in ppmv)			
Carbon Monoxide	210	362	866	727	412
		(Concentration in %v, by component)			
TNMHC	0.178	0.164	0.589	0.404	0.291
			BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	259.2	305.6	168.7	161.8	194.8
BTU/ft3 (Wet @ 0.25636 psia)	254.7	300.3	165.8	159.0	191.4
BTU/lb (Dry @60F, 14.696 psia)	3237	3830	1932	1890	2327

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

B Fung

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 27, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.64	6.62	6.63	0.30
Nitrogen	Zeeco South	32.52	32.42	32.47	0.31
Methane	Zeeco South	23.72	23.76	23.74	0.17
Carbon Dioxide	Zeeco South	32.60	32.57	32.59	0.09
Hydrogen	Zeeco South	1.66	1.66	1.66	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	209	212	210	1.3
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.178	0.178	0.178	0.31

Five Tedlar bag samples, laboratory numbers 22716-(26-30), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 0.35%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 27, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22716-26	22716-27	22716-28	22716-29	22716-30
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Parnel Inlet	Zeeco Inlet
Components	*(Concentration in ppmv)*				
Hydrogen sulfide	136	182	220	168	165
Carbonyl sulfide	0.51	<0.50	<1.60	<1.60	<1.20
Methyl mercaptan	59.9	102	411	383	286
Ethyl mercaptan	1.04	0.93	4.33	3.41	2.67
Dimethyl sulfide	223	237	1012	790	663
Carbon disulfide	<0.50	<0.50	<1.60	<1.60	<1.20
i-Propyl mercaptan	1.27	1.18	2.18	1.77	1.87
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
n-Propyl mercaptan	2.24	1.90	10.0	6.95	6.51
s-Butyl mercaptan	2.32	1.80	8.50	5.74	6.12
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.60	<1.20
Dimethyl disulfide	1.40	<0.50	<1.60	2.16	2.18
Tetrahydrothiophene	<0.50	<0.50	2.04	<1.60	<1.20
Unidentified sulfurs	1.08	0.61	6.17	3.17	3.87
	(Concentration in ppmv, as H_2S)				
Total Sulfur	430.37	527.20	1676.40	1365.55	1139.67

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 27, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	141	132	136	6.5
	FL-2009 Inlet	179	184	182	2.8
	Hero Inlet	220	221	220	0.55
	Parnel Inlet	169	166	168	1.5
	Zeeco Inlet	161	170	165	5.5
Carbonyl sulfide	Zeeco South	0.51	0.50	0.51	2.0
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	60.9	58.9	59.9	3.3
	FL-2009 Inlet	102	102	102	0.13
	Hero Inlet	408	415	411	1.8
	Parnel Inlet	388	378	383	2.6
	Zeeco Inlet	280	292	286	4.3
Ethyl mercaptan	Zeeco South	1.07	1.00	1.04	6.8
	FL-2009 Inlet	0.94	0.92	0.93	2.2
	Hero Inlet	4.28	4.37	4.33	2.1
	Parnel Inlet	3.46	3.36	3.41	2.9
	Zeeco Inlet	2.55	2.78	2.67	8.6
Dimethyl sulfide	Zeeco South	226	220	223	2.3
	FL-2009 Inlet	240	235	237	2.1
	Hero Inlet	1002	1022	1012	2.0
	Parnel Inlet	807	772	790	4.3
	Zeeco Inlet	644	682	663	5.8
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.28	1.25	1.27	2.4
	FL-2009 Inlet	1.16	1.19	1.18	2.6
	Hero Inlet	2.19	2.16	2.18	1.4
	Parnel Inlet	1.81	1.72	1.77	5.1
	Zeeco Inlet	1.84	1.90	1.87	3.2

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
n-Propyl mercaptan	Zeeco South	2.26	2.22	2.24	1.8
	FL-2009 Inlet	1.87	1.93	1.90	3.2
	Hero Inlet	9.85	10.2	10.0	3.1
	Parnel Inlet	7.23	6.67	6.95	8.1
	Zeeco Inlet	6.22	6.80	6.51	8.9
s-Butyl mercaptan	Zeeco South	2.34	2.29	2.32	2.2
	FL-2009 Inlet	1.74	1.85	1.80	6.1
	Hero Inlet	8.47	8.52	8.50	0.59
	Parnel Inlet	5.86	5.61	5.74	4.4
	Zeeco Inlet	5.97	6.27	6.12	4.9
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	1.41	1.38	1.40	2.2
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Parnel Inlet	2.21	2.10	2.16	5.1
	Zeeco Inlet	2.11	2.24	2.18	6.0
Tetrahydrothiophene	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	1.97	2.10	2.04	6.4
	Parnel Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
Unidentified sulfurs	Zeeco South	1.08	1.07	1.08	0.93
	FL-2009 Inlet	0.60	0.62	0.61	3.3
	Hero Inlet	6.14	6.19	6.17	0.81
	Parnel Inlet	3.25	3.08	3.17	5.4
	Zeeco Inlet	3.74	4.00	3.87	6.7

Five Tedlar bag samples, laboratory numbers 22716-(26-30), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from five Tedlar bag samples is 3.6%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22716-26	9/27/26	215PM	X	X	X	X			
FL-2009 Inlet	LFG	-27	9/27/26	145PM	X	X	X	X			
Hero Inlet	LFG	-28	9/27/26	200PM	X	X	X	X			
Parnel Inlet	LFG	-29	9/27/26	230PM	X	X	X	X			
Zeeco Inlet	LFG	-30	9/27/26	210PM	X	X	X	X			

ANALYSES REQUESTED

Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9/27/26	330PM		9.28.26	0600
Relinquished by: *(Signature)*	Date	Time	Received by: *(Signature)*	Date	Time
	9.28.26	8:50am		9/28/26	8:50
Relinquished by: *(Signature)*	Date	Time	Received for Laboratory by: *(Signature)*	Date	Time
	9/28/26	9:53		9/28/26	9:53

Company Info:		Send Report to:		Analytical Laboratory
Company:	SCS Engineers	Company:	SCS Engineers	AtmAA Inc.
Street Address	3900 Kilroy Airport Way Suite 300	Street Address	3900 Kilroy Airport Way Suite 300	5107 Douglas Fir Rd.
City/State/Zip:	Long Beach / CA / 90806	City/State/Zip:	Long Beach / CA / 90806	Calabasas, CA 91302
Telephone No.:	562-743-7895 /562-335-0002	Project Manager:	Cornelius Fong	TEL: (818) 223-3277
Fax No.:		Email Address:	CFong@scsengineers.com	Email Address: info@atmaa.com

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 28, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22716-31	22716-32	22716-33	22716-34
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco inlet
Components	*(Concentration in %v)*			
Oxygen	8.23	5.51	5.83	6.36
Nitrogen	36.33	29.11	30.84	35.53
Methane	23.46	25.39	10.83	15.69
Carbon Dioxide	29.36	35.58	42.49	36.55
Hydrogen	1.45	2.57	5.94	2.94
	(Concentration in ppmv)			
Carbon Monoxide	176	404	848	446
	(Concentration in %v, by component)			
TNMHC	0.242	0.242	0.717	0.408
	BTU (HHV)			
BTU/ft3 (Dry @60F, 14.696 psia)	255.2	279.8	166.4	191.2
BTU/ft3 (Wet @ 0.25636 psia)	250.7	275.0	163.5	187.9
BTU/lb (Dry @60F, 14.696 psia)	3223	3493	1927	2281

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 28, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	8.07	8.39	8.23	3.9
Nitrogen	Zeeco South	35.89	36.77	36.33	2.4
Methane	Zeeco South	23.74	23.17	23.46	2.4
Carbon Dioxide	Zeeco South	29.70	29.02	29.36	2.3
Hydrogen	Zeeco South	1.45	1.45	1.45	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	175	177	176	1.3
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.241	0.244	0.242	1.0

Four Tedlar bag samples, laboratory numbers 22716-(31-34), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 1.9%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 28, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22716-31	22716-32	22716-33	22716-34
Sample I.D.:	Zeeco South	FL-2009 Inlet	Hero Inlet	Zeeco inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	159	175	186	165
Carbonyl sulfide	0.63	<0.50	<1.60	<1.20
Methyl mercaptan	56.4	123	355	297
Ethyl mercaptan	0.93	1.29	4.07	2.91
Dimethyl sulfide	226	320	959	777
Carbon disulfide	<0.50	<0.50	<1.60	<1.20
i-Propyl mercaptan	1.74	1.45	2.26	2.29
t-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
n-Propyl mercaptan	2.78	3.44	11.6	8.54
s-Butyl mercaptan	4.20	4.31	12.8	10.8
i-Butyl mercaptan	<0.50	<0.50	<1.60	<1.20
Dimethyl disulfide	4.09	0.75	3.21	4.47
Tetrahydrothiophene	2.29	1.88	8.63	5.06
Unidentified sulfurs	10.3	4.61	24.9	21.2
	(Concentration in ppmv, as H_2S)			
Total Sulfur	472.10	636.16	1569.94	1298.19

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 28, 2026
Date Received: September 28, 2026
Date Analyzed: September 28, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	155	163	159	5.3
	FL-2009 Inlet	173	176	175	1.8
	Hero Inlet	191	181	186	5.5
	Zeeco inlet	172	158	165	8.9
Carbonyl sulfide	Zeeco South	0.61	0.64	0.63	4.8
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco inlet	<1.20	<1.20	---	---
Methyl mercaptan	Zeeco South	55.2	57.5	56.4	4.1
	FL-2009 Inlet	123	122	123	0.58
	Hero Inlet	364	346	355	5.1
	Zeeco inlet	306	287	297	6.4
Ethyl mercaptan	Zeeco South	0.91	0.95	0.93	4.3
	FL-2009 Inlet	1.26	1.32	1.29	4.7
	Hero Inlet	4.26	3.88	4.07	9.3
	Zeeco inlet	2.99	2.83	2.91	5.5
Dimethyl sulfide	Zeeco South	219	232	226	5.9
	FL-2009 Inlet	324	317	320	2.0
	Hero Inlet	981	936	959	4.7
	Zeeco inlet	789	765	777	3.1
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco inlet	<1.20	<1.20	---	---
i-Propyl mercaptan	Zeeco South	1.73	1.74	1.74	0.58
	FL-2009 Inlet	1.43	1.46	1.45	2.1
	Hero Inlet	2.31	2.20	2.26	4.9
	Zeeco inlet	2.43	2.14	2.29	13
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco inlet	<1.20	<1.20	---	---



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	2.78	2.77	2.78	0.36
	FL-2009 Inlet	3.34	3.53	3.44	5.5
	Hero Inlet	11.9	11.2	11.6	6.1
	Zeeco inlet	8.90	8.18	8.54	8.4
s-Butyl mercaptan	Zeeco South	4.14	4.26	4.20	2.9
	FL-2009 Inlet	4.15	4.46	4.31	7.2
	Hero Inlet	13.4	12.2	12.8	9.1
	Zeeco inlet	11.4	10.2	10.8	11
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	FL-2009 Inlet	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco inlet	<1.20	<1.20	---	---
Dimethyl disulfide	Zeeco South	4.00	4.17	4.09	4.2
	FL-2009 Inlet	0.75	0.74	0.75	1.3
	Hero Inlet	3.26	3.16	3.21	3.1
	Zeeco inlet	4.70	4.24	4.47	10
Tetrahydrothiophene	Zeeco South	2.32	2.26	2.29	2.6
	FL-2009 Inlet	1.70	2.06	1.88	19
	Hero Inlet	8.86	8.40	8.63	5.3
	Zeeco inlet	5.46	4.66	5.06	16
Unidentified sulfurs	Zeeco South	10.3	10.3	10.3	0.29
	FL-2009 Inlet	4.67	4.54	4.61	2.8
	Hero Inlet	25.2	24.6	24.9	2.3
	Zeeco inlet	22.7	19.8	21.2	14

Four Tedlar bag samples, laboratory numbers 22716-(31-34), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 5.7%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)* Emmanuel Medina	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22716-31	9-28-26	8:40am	X	X	X	X			
FL-2009 Inlet	LFG	-32	9-28-26	7:10am	X	X	X	X			
Hero Inlet	LFG	-33	9-28-26	8:10am	X	X	X	X			
Parnel Inlet	LFG	~~-34~~			X	X	X	X			
Zeeco Inlet	LFG	~~-34~~ 34	9-28-26	8:25am	X	X	X	X			
		KDM									

Relinquished by: *(Signature)* EM	**Date** 9-28-26	**Time** 8:50am	**Received by: *(Signature)*** Ruben G	**Date** 9/28/26	**Time** 8:50
Relinquished by: *(Signature)* Ruben G	**Date** 9/28/26	**Time** 9:53	**Received by: *(Signature)***	**Date**	**Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by: *(Signature)***	**Date** 9/28/26	**Time** 9:53

Company Info:	**Send Report to:**	**Analytical Laboratory**
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach / CA / 90806	**City/State/Zip:** Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895 /562-335-0002	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:	**Email Address:** CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 29, 2026
Date Received: September 29, 2026
Date Analyzed: September 29, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22726-1	22726-2	22726-3	22726-4
Sample I.D.:	Zeeco South	Hero Inlet	Zeeco Inlet	FL-1995 Inlet
Components		*(Concentration in %v)*		
Oxygen	7.15	5.06	7.95	5.78
Nitrogen	32.55	29.15	40.24	30.43
Methane	26.15	10.84	14.32	24.34
Carbon Dioxide	31.24	45.23	32.94	35.98
Hydrogen	1.43	5.95	2.59	1.45
		(Concentration in ppmv)		
Carbon Monoxide	166	858	400	394
		(Concentration in %v, by component)		
TNMHC	0.245	0.807	0.445	0.239
		BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	283.9	170.6	176.4	266.4
BTU/ft3 (Wet @ 0.25636 psia)	279.0	167.6	173.3	261.7
BTU/lb (Dry @60F, 14.696 psia)	3592	1949	2121	3269

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 29, 2026
Date Received: September 29, 2026
Date Analyzed: September 29, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	7.15	7.15	7.15	0.00
Nitrogen	Zeeco South	32.61	32.48	32.55	0.40
Methane	Zeeco South	26.11	26.18	26.15	0.27
Carbon Dioxide	Zeeco South	31.24	31.24	31.24	0.00
Hydrogen	Zeeco South	1.42	1.43	1.43	0.70
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	168	164	166	2.6
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.244	0.246	0.245	1.0

Four Tedlar bag samples, laboratory numbers 22726-(1-4), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.71%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 29, 2026
Date Received: September 29, 2026
Date Analyzed: September 29, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22726-1	22726-2	22726-3	22726-4
Sample I.D.:	Zeeco South	Hero Inlet	Zeeco Inlet	FL-1995 Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	172	212	118	128
Carbonyl sulfide	0.69	<1.60	<1.20	<0.50
Methyl mercaptan	48.7	455	285	117
Ethyl mercaptan	0.87	4.88	2.75	1.19
Dimethyl sulfide	224	1122	793	385
Carbon disulfide	<0.50	<1.60	<1.20	<0.50
i-Propyl mercaptan	1.90	2.55	2.21	1.18
t-Butyl mercaptan	<0.50	<1.60	<1.20	<0.50
n-Propyl mercaptan	2.51	13.9	8.33	3.68
s-Butyl mercaptan	4.29	15.6	10.8	4.64
i-Butyl mercaptan	<0.50	<1.60	<1.20	<0.50
Dimethyl disulfide	3.35	3.42	3.67	3.55
Tetrahydrothiophene	2.28	11.4	5.60	2.10
Unidentified sulfurs	11.9	34.8	24.3	11.7
	(Concentration in ppmv, as H_2S)			
Total Sulfur	475.30	1879.52	1257.97	662.49

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 29, 2026
Date Received: September 29, 2026
Date Analyzed: September 29, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	166	178	172	6.9
	Hero Inlet	210	214	212	2.0
	Zeeco Inlet	114	122	118	7.2
	FL-1995 Inlet	126	131	128	3.5
Carbonyl sulfide	Zeeco South	0.68	0.69	0.69	1.5
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
Methyl mercaptan	Zeeco South	47.6	49.8	48.7	4.4
	Hero Inlet	454	457	455	0.50
	Zeeco Inlet	280	290	285	3.6
	FL-1995 Inlet	115	119	117	3.7
Ethyl mercaptan	Zeeco South	0.85	0.88	0.87	3.5
	Hero Inlet	4.97	4.78	4.88	3.9
	Zeeco Inlet	2.70	2.80	2.75	3.6
	FL-1995 Inlet	1.15	1.23	1.19	6.7
Dimethyl sulfide	Zeeco South	216	231	224	6.4
	Hero Inlet	1124	1120	1122	0.40
	Zeeco Inlet	774	813	793	5.0
	FL-1995 Inlet	371	399	385	7.4
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
i-Propyl mercaptan	Zeeco South	1.87	1.92	1.90	2.6
	Hero Inlet	2.59	2.50	2.55	3.5
	Zeeco Inlet	2.15	2.26	2.21	5.0
	FL-1995 Inlet	1.15	1.21	1.18	5.1
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	2.46	2.55	2.51	3.6
	Hero Inlet	13.9	13.9	13.9	0.58
	Zeeco Inlet	8.33	8.33	8.33	0.00
	FL-1995 Inlet	3.54	3.82	3.68	7.6
s-Butyl mercaptan	Zeeco South	4.25	4.32	4.29	1.6
	Hero Inlet	15.7	15.6	15.6	0.26
	Zeeco Inlet	10.4	11.1	10.8	7.1
	FL-1995 Inlet	4.47	4.80	4.64	7.1
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995 Inlet	<0.50	<0.50	---	---
Dimethyl disulfide	Zeeco South	3.34	3.36	3.35	0.60
	Hero Inlet	3.43	3.40	3.42	0.88
	Zeeco Inlet	3.68	3.66	3.67	0.54
	FL-1995 Inlet	3.42	3.68	3.55	7.3
Tetrahydrothiophene	Zeeco South	2.23	2.32	2.28	4.0
	Hero Inlet	11.7	11.1	11.4	4.9
	Zeeco Inlet	5.44	5.76	5.60	5.7
	FL-1995 Inlet	2.06	2.14	2.10	3.8
Unidentified sulfurs	Zeeco South	11.7	12.1	11.9	3.5
	Hero Inlet	35.5	34.0	34.8	4.2
	Zeeco Inlet	23.8	24.7	24.3	3.6
	FL-1995 Inlet	11.6	11.8	11.7	1.3

Four Tedlar bag samples, laboratory numbers 22726-(1-4), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 3.8%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No. 07224200.24 Task 1	**Field Logbook No.**
Sampler: *(Signature)*	**Chain of Custody Tape No.**

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22726-1	9-29-26		X	X	X	X			
FL-2009 Inlet	LFG				X	X	X	X			
Hero Inlet	LFG	-2	9-29-26		X	X	X	X			
* Parnel Inlet	LFG	-3	9-29-26		X	X	X	X			* Sample not received KRm
Zeeco Inlet	LFG	22726-3-3	9-29-26		X	X	X	X			
FL-1995-Inlet	LFG	-4-4	9-29-26		X	X	X	X			

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9-29-26	8:35A	**Received by: *(Signature)***	9/29/26	8:52
Relinquished by: *(Signature)*	9/29/26	9:50	**Received by: *(Signature)***	Date	Time
Relinquished by: *(Signature)*	Date	Time	**Received for Laboratory by: *(Signature)***	9/29/26	9:50

Company Info:	**Send Report to:**	**Analytical Laboratory**
Company: SCS Engineers	**Company:** SCS Engineers	**AtmAA Inc.**
Street Address 3900 Kilroy Airport Way Suite 300	**Street Address** 3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip: Long Beach / CA / 90806	**City/State/Zip:** Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.: 562-743-7895 /562-335-0002	**Project Manager:** Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:	**Email Address:** CFong@scsengineers.com	**Email Address: info@atmaa.com**

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277

specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Permanent Gases, Carbon Monoxide, and BTU Analysis in Tedlar Bag Sample

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 30, 2026
Date Received: September 30, 2026
Date Analyzed: September 30, 2026

ANALYSIS DESCRIPTION

Permanent gases were measured by thermal conductivity detection/gas chromatography (TCD/GC) ASTM D1946-90. Carbon monoxide was measured by flame ionization detection/total combustion analysis (FID/TCA), EPA Method ALT-144. BTU was calculated using normalized labortatory analysis results for methane, carbon dioxide, nitrogen, oxygen, TNMHC, and sulfur compounds in equations that include gross/net heating and specific gas volume values taken from the GPA-2145 Midstream Standard. Heating value factor is a calculated according to ASTM 3588-98 (14.696 psia and 60°F).

AtmAA Lab No.:	22736-14	22736-15	22736-16	22736-17
Sample I.D.:	Zeeco South	Hero Inlet	Zeeco Inlet	FL-1995-Inlet
Components		*(Concentration in %v)*		
Oxygen	6.99	4.72	6.62	6.47
Nitrogen	32.14	28.02	35.89	32.90
Methane	26.29	10.64	15.94	22.67
Carbon Dioxide	31.88	45.73	35.90	34.28
Hydrogen	1.42	6.42	2.84	2.58
		(Concentration in ppmv)		
Carbon Monoxide	153	757	367	375
		(Concentration in %v, by component)		
TNMHC	0.251	0.904	0.449	0.262
		BTU (HHV)		
BTU/ft3 (Dry @60F, 14.696 psia)	285.1	174.8	195.5	251.7
BTU/ft3 (Wet @ 0.25636 psia)	280.1	171.8	192.1	247.3
BTU/lb (Dry @60F, 14.696 psia)	3597	1995	2337	3125

The reported oxygen concentration includes any argon present in the sample. Calibration is based on a standard atmosphere containing 20.95% oxygen and 0.93% argon.
The accuracy of permanent gas analysis by TCD/GC is +/- 2%, actual results are reported.
Actual analysis results are reported on a "wet" basis.

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 30, 2026
Date Received: September 30, 2026
Date Analyzed: September 30, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in %v)			
Oxygen	Zeeco South	6.92	7.05	6.99	1.9
Nitrogen	Zeeco South	32.03	32.24	32.14	0.65
Methane	Zeeco South	26.38	26.20	26.29	0.68
Carbon Dioxide	Zeeco South	31.88	31.87	31.88	0.03
Hydrogen	Zeeco South	1.42	1.42	1.42	0.00
		(Concentration in ppmv)			
Carbon Monoxide	Zeeco South	154	151	153	2.1
		(Concentration in %v, by component)			
TNMHC	Zeeco South	0.251	0.251	0.251	0.19

Four Tedlar bag samples, laboratory numbers 22736-(14-17), were analyzed for permanent gases, carbon monoxide, and ASTM 3588 HHV. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 0.79%.

AtmAA Inc.
5107 Douglas Fir Rd., Calabasas, CA 91302 • (818) 223-3277
specialized air assessment laboratory
atmaa.com

LABORATORY ANALYSIS REPORT

Hydrogen Sulfide and Reduced Sulfur Compounds
Analysis in Tedlar Bag Sample by SCAQMD Method 307.91

Report Date: October 9, 2026
Client: SCS Engineers
Project Name: Chiquita Canyon Landfill
Project No.: 07224200.24 Task 1
Date Sampled: September 30, 2026
Date Received: September 30, 2026
Date Analyzed: September 30, 2026

ANALYSIS DESCRIPTION

Total sulfur analysis measured by gas chromatography with sulfur chemiluminescence detector (SCD), SCAQMD 307.91.

AtmAA Lab No.:	22736-14	22736-15	22736-16	22736-17
Sample I.D.:	Zeeco South	Hero Inlet	Zeeco Inlet	FL-1995-Inlet
Components	*(Concentration in ppmv)*			
Hydrogen sulfide	171	223	153	142
Carbonyl sulfide	0.65	<1.60	<1.20	<0.50
Methyl mercaptan	50.4	502	316	123
Ethyl mercaptan	0.93	5.28	3.34	1.26
Dimethyl sulfide	211	1218	831	379
Carbon disulfide	<0.50	<1.60	<1.20	<0.50
i-Propyl mercaptan	1.84	2.71	2.49	1.34
t-Butyl mercaptan	<0.50	<1.60	<1.20	<0.50
n-Propyl mercaptan	2.61	14.9	9.75	3.95
s-Butyl mercaptan	4.24	16.5	12.7	4.89
i-Butyl mercaptan	<0.50	<1.60	<1.20	<0.50
Dimethyl disulfide	4.48	3.56	5.99	2.91
Tetrahydrothiophene	2.19	11.7	6.44	2.54
Unidentified sulfurs	9.98	33.4	28.0	10.8
	(Concentration in ppmv, as H_2S)			
Total Sulfur	463.46	2035.15	1374.44	674.10

Brian W. Fung
Laboratory Director

QUALITY ASSURANCE SUMMARY
(Repeat Analyses)

Project Name: Chiquita Canyon Landfill
Date Sampled: September 30, 2026
Date Received: September 30, 2026
Date Analyzed: September 30, 2026

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
Hydrogen sulfide	Zeeco South	176	165	171	6.3
	Hero Inlet	223	223	223	0.19
	Zeeco Inlet	151	156	153	3.2
	FL-1995-Inlet	143	141	142	1.6
Carbonyl sulfide	Zeeco South	0.66	0.63	0.65	4.7
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995-Inlet	<0.50	<0.50	---	---
Methyl mercaptan	Zeeco South	51.6	49.1	50.4	5.0
	Hero Inlet	499	505	502	1.2
	Zeeco Inlet	310	321	316	3.6
	FL-1995-Inlet	122	123	123	1.4
Ethyl mercaptan	Zeeco South	0.96	0.89	0.93	7.6
	Hero Inlet	5.29	5.26	5.28	0.57
	Zeeco Inlet	3.33	3.35	3.34	0.60
	FL-1995-Inlet	1.25	1.27	1.26	1.6
Dimethyl sulfide	Zeeco South	212	210	211	0.83
	Hero Inlet	1217	1220	1218	0.27
	Zeeco Inlet	824	838	831	1.6
	FL-1995-Inlet	376	382	379	1.7
Carbon disulfide	Zeeco South	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995-Inlet	<0.50	<0.50	---	---
i-Propyl mercaptan	Zeeco South	1.86	1.82	1.84	2.2
	Hero Inlet	2.72	2.70	2.71	0.74
	Zeeco Inlet	2.39	2.58	2.49	7.6
	FL-1995-Inlet	1.32	1.35	1.34	2.2
t-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995-Inlet	<0.50	<0.50	---	---



QUALITY ASSURANCE SUMMARY
(Repeat Analyses)
(continued)

Components	Sample ID	Repeat Analysis Run #1	Repeat Analysis Run #2	Mean Conc.	% RPD
		(Concentration in ppmv)			
n-Propyl mercaptan	Zeeco South	2.67	2.54	2.61	5.0
	Hero Inlet	14.78	15.0	14.9	1.3
	Zeeco Inlet	9.52	9.97	9.75	4.6
	FL-1995-Inlet	3.90	3.99	3.95	2.3
s-Butyl mercaptan	Zeeco South	4.33	4.14	4.24	4.5
	Hero Inlet	16.5	16.6	16.5	0.61
	Zeeco Inlet	12.1	13.2	12.7	8.6
	FL-1995-Inlet	4.90	4.87	4.89	0.61
i-Butyl mercaptan	Zeeco South	<0.50	<0.50	---	---
	Hero Inlet	<1.60	<1.60	---	---
	Zeeco Inlet	<1.20	<1.20	---	---
	FL-1995-Inlet	<0.50	<0.50	---	---
Dimethyl disulfide	Zeeco South	4.58	4.37	4.48	4.7
	Hero Inlet	3.53	3.58	3.56	1.4
	Zeeco Inlet	5.74	6.24	5.99	8.4
	FL-1995-Inlet	2.85	2.96	2.91	3.8
Tetrahydrothiophene	Zeeco South	2.24	2.14	2.19	4.6
	Hero Inlet	11.7	11.8	11.7	0.60
	Zeeco Inlet	6.06	6.81	6.44	12
	FL-1995-Inlet	2.54	2.53	2.54	0.39
Unidentified sulfurs	Zeeco South	10.3	9.65	10.0	6.5
	Hero Inlet	34.2	32.5	33.4	5.0
	Zeeco Inlet	26.7	29.3	28.0	9.5
	FL-1995-Inlet	10.6	11.0	10.8	4.1

Four Tedlar bag samples, laboratory numbers 22736-(14-17), were analyzed for total sulfur compounds. Agreement between repeat analyses is a measure of precision and is shown above in the column "% RPD". The average % RPD from four Tedlar bag samples is 3.5%.

CHAIN OF CUSTODY RECORD

Client/Project Name	Project Location
SCS Engineers / Chiquita Canyon Landfill	29201 Henry Mayo Drive, Castaic, CA 91384
Project No.	**Field Logbook No.**
07224200.24 Task 1	
Sampler: *(Signature)*	**Chain of Custody Tape No.**

ANALYSES REQUESTED

Sample No./ Identification	Type of Sample	AtmAA Lab Number	Sampling Date	Sampling Time	TRS (307.91)	CH4, CO2, O2, N2, H2 (1946)	CO (EPA alt-144)	HHV (3588)			Special Remarks
Zeeco South Station	LFG	22736-14	9-30-26	7:00a	X	X	X	X			
FL-2009 Inlet	LFG				X	X	X	X			
Hero Inlet	LFG	-15	9-30-26	6:30a	X	X	X	X			
Parnel Inlet	LFG				X	X	X	X			
Zeeco Inlet	LFG	-16	9-30-26	6:45a	X	X	X	X			
FL-1995-Inlet	LFG	-17	9-30-26	7:10a							

	Date	Time		Date	Time
Relinquished by: *(Signature)*	9-30-26	7:22a	**Received by: *(Signature)***	9/30/26	9:08
Relinquished by: *(Signature)*	9/30/26	10:36	**Received by: *(Signature)***	**Date**	**Time**
Relinquished by: *(Signature)*	**Date**	**Time**	**Received for Laboratory by: *(Signature)***	9/30/26	10:34

Company Info:		**Send Report to:**		**Analytical Laboratory**
Company:	SCS Engineers	**Company:**	SCS Engineers	**AtmAA Inc.**
Street Address	3900 Kilroy Airport Way Suite 300	**Street Address**	3900 Kilroy Airport Way Suite 300	**5107 Douglas Fir Rd.**
City/State/Zip:	Long Beach / CA / 90806	**City/State/Zip:**	Long Beach / CA / 90806	**Calabasas, CA 91302**
Telephone No.:	562-743-7895 /562-335-0002	**Project Manager:**	Cornelius Fong	**TEL: (818) 223-3277**
Fax No.:		**Email Address:**	CFong@scsengineers.com	**Email Address: info@atmaa.com**

Attachment B

Calculations

Chiquita Canyon Landfill
Total Emissions
Monthly Report Period: September 2026

	Flare No. 1 John Zink (FL-150) (FL-1995)				Flare No. 2 John Zink (Zule) (FL-100) (FL-2009)				Flare No. 3 John Zink (Zule) (FL-2023)				Zeeco 1				Zeeco 6				Zeeco 7				Parnel Vapor Combustor				Hero Vapor Combustor				All Control Devices (Flare No. 1, Flare No. 2, Flare No. 3, Zeeco 1, Zeeco 6, Zeeco 7, Parnel, Hero)			Lab Analysis Total Reduced Sulfur (TRS) as H2S (ppmv)
Date	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Runtime (hr)	Flow Rate (scfm)	Flow Rate (scf/hr)	Total LFG Combusted (scf/day)	Total Flow Rate (scfm)	Total Flow Rate (scf/hr)	
9/1/2026	3,930,813	24.00	2,730	163,784	4,713,401	23.98	3,273	196,392	6,877,005	23.12	4,776	286,542	1,389,250	23.43	965	57,885	1,390,954	24.00	966	57,956	1,588,516	24.00	1,103	66,188	1,283,694	24.00	891	53,487	2,743,951	23.80	1,906	114,331	23,917,584	16,609	996,566	632
9/2/2026	4,342,341	24.00	3,016	180,931	3,513,017	18.55	2,440	146,376	6,626,655	21.32	4,602	276,111	1,411,706	23.93	980	58,821	1,302,388	23.27	904	54,266	1,397,178	23.97	970	58,216	1,326,566	23.83	921	55,274	2,731,529	23.53	1,897	113,814	22,651,380	15,730	943,808	631
9/3/2026	4,206,514	24.00	2,921	175,271	4,577,868	23.98	3,179	190,745	5,827,061	19.05	4,047	242,794	1,453,741	23.97	1,010	60,573	1,290,075	23.93	896	53,753	1,692,764	20.53	1,176	70,532	1,291,426	24.00	897	53,809	2,675,666	23.37	1,858	111,486	23,015,115	15,983	958,963	651
9/4/2026	4,466,850	24.00	3,102	186,119	4,797,232	24.00	3,331	199,885	3,076,144	10.32	2,136	128,173	1,493,043	23.97	1,037	62,210	1,352,047	23.97	939	56,335	1,623,076	20.77	1,127	67,628	1,379,108	23.97	958	57,463	2,632,537	23.07	1,828	109,689	20,820,037	14,458	867,502	644
9/5/2026	4,345,817	24.00	3,018	181,076	4,654,713	24.00	3,232	193,946	4,478,873	15.05	3,110	186,620	1,532,603	23.90	1,064	63,858	1,372,382	23.97	953	57,183	1,220,576	24.00	848	50,857	1,302,804	24.00	905	54,284	2,588,347	23.77	1,797	107,848	21,496,115	14,928	895,671	108
9/6/2026	4,062,040	24.00	2,821	169,252	4,495,826	23.98	3,122	187,326	7,011,708	23.22	4,869	292,155	1,207,677	22.87	839	50,320	1,326,269	23.97	921	55,261	409,216	10.47	284	17,051	1,365,824	24.00	948	56,909	2,462,401	23.50	1,710	102,600	22,340,961	15,515	930,873	699
9/7/2026	4,809,316	24.00	3,340	200,388	1,434,756	7.37	996	59,782	7,572,485	23.67	5,259	315,520	1,558,341	24.00	1,082	64,931	1,305,800	23.93	907	54,408	830,614	11.33	577	34,609	1,445,136	24.00	1,004	60,214	2,542,935	23.67	1,766	105,956	21,499,383	14,930	895,808	521
9/8/2026	4,912,524	24.00	3,411	204,689	614,790	3.30	427	25,616	7,690,044	24.00	5,340	320,419	1,488,766	22.53	1,034	62,032	1,247,074	23.97	866	51,961	1,615,130	24.00	1,122	67,297	1,373,256	24.00	954	57,219	2,574,764	23.67	1,788	107,282	21,516,348	14,942	896,515	571
9/9/2026	4,423,379	24.00	3,072	184,307	4,605,338	23.65	3,198	191,889	7,161,241	23.72	4,973	298,385	1,594,397	23.93	1,107	66,433	1,257,845	23.93	874	52,410	527,134	8.93	366	21,964	865,104	15.87	601	36,046	2,430,911	23.43	1,688	101,288	22,865,349	15,879	952,723	858
9/10/2026	4,445,073	24.00	3,087	185,211	4,074,567	20.87	2,830	169,774	7,257,574	24.00	5,040	302,399	1,578,497	23.50	1,096	65,771	1,385,054	23.53	962	57,711	0	0.00	0	0	552,346	11.17	384	23,014	2,563,597	23.83	1,780	106,817	21,856,708	15,178	910,696	917
9/11/2026	4,126,075	24.00	2,865	171,920	4,461,483	23.68	3,098	185,895	6,595,663	22.72	4,580	274,819	1,624,703	23.97	1,128	67,696	1,190,249	23.17	827	49,594	891,882	8.73	619	37,162	1,188,502	24.00	825	49,521	2,507,460	23.87	1,741	104,478	22,586,017	15,685	941,084	801
9/12/2026	3,957,077	24.00	2,748	164,878	4,406,651	24.00	3,060	183,610	3,548,841	12.55	2,464	147,868	1,613,478	23.93	1,120	67,228	1,443,693	24.00	1,003	60,154	2,862,510	24.00	1,988	119,271	1,271,234	24.00	883	52,968	2,502,738	23.67	1,738	104,281	21,606,222	15,004	900,259	600
9/13/2026	4,114,513	24.00	2,857	171,438	4,556,188	23.98	3,164	189,841	4,682,667	16.30	3,252	195,111	1,585,345	23.97	1,101	66,056	1,358,906	24.00	944	56,621	2,978,380	24.00	2,068	124,099	1,290,986	24.00	897	53,791	2,458,471	23.57	1,707	102,436	23,025,456	15,990	959,394	588
9/14/2026	4,011,375	24.00	2,786	167,141	4,328,471	23.95	3,006	180,353	6,049,645	21.25	4,201	252,069	1,509,969	22.87	1,049	62,915	1,268,470	24.00	881	52,853	3,063,586	24.00	2,127	127,649	801,038	14.93	556	33,377	2,468,154	23.70	1,714	102,840	23,500,708	16,320	979,196	556
9/15/2026	3,979,712	24.00	2,764	165,821	4,333,394	23.98	3,009	180,558	6,888,878	24.00	4,784	287,037	1,574,753	24.00	1,094	65,615	1,220,880	24.00	848	50,870	3,245,798	24.00	2,254	135,242	0	0.00	0	0	2,488,652	23.83	1,728	103,694	23,732,067	16,481	988,836	678
9/16/2026	4,030,675	24.00	2,799	167,945	4,399,761	24.00	3,055	183,323	6,101,056	21.40	4,237	254,211	1,595,631	24.00	1,108	66,485	1,227,806	24.00	853	51,159	3,271,080	24.00	2,272	136,295	0	0.00	0	0	2,527,348	23.67	1,755	105,306	23,153,357	16,079	964,723	598
9/17/2026	4,031,381	23.97	2,800	167,974	4,093,798	22.50	2,843	170,575	6,810,416	23.68	4,729	283,767	1,603,305	24.00	1,113	66,804	1,340,390	24.00	931	55,850	3,172,678	24.00	2,203	132,195	815,484	15.53	566	33,979	2,396,699	23.43	1,664	99,862	24,264,151	16,850	1,011,006	559
9/18/2026	4,537,265	24.00	3,151	189,053	1,977,992	10.78	1,374	82,416	4,986,159	16.32	3,463	207,757	1,599,807	24.00	1,111	66,659	1,333,869	24.00	926	55,578	3,228,752	24.00	2,242	134,531	1,596,600	21.90	1,109	66,525	2,503,155	23.77	1,738	104,298	21,763,599	15,114	906,817	710
9/19/2026	3,758,345	24.00	2,610	156,598	2,969,634	18.25	2,062	123,735	6,793,734	24.00	4,718	283,072	1,502,735	23.93	1,044	62,614	1,215,667	24.00	844	50,653	3,173,564	24.00	2,204	132,232	1,052,122	14.80	731	43,838	2,395,123	23.67	1,663	99,797	22,860,924	15,876	952,539	570
9/20/2026	3,491,515	24.00	2,425	145,480	3,919,090	23.98	2,722	163,295	6,435,826	24.00	4,469	268,159	1,448,672	23.97	1,006	60,361	1,191,094	24.00	827	49,629	3,130,114	24.00	2,174	130,421	208,716	3.40	145	8,697	2,371,370	23.63	1,647	98,807	22,196,397	15,414	924,850	658
9/21/2026	3,465,962	21.10	2,407	144,415	3,658,299	20.32	2,540	152,429	7,027,675	24.00	4,880	292,820	1,455,106	23.97	1,010	60,629	1,110,951	23.73	771	46,290	3,062,892	24.00	2,127	127,621	377,798	5.67	262	15,742	2,324,066	23.87	1,614	96,836	22,482,749	15,613	936,781	713
9/22/2026	4,157,224	24.00	2,887	173,218	3,840,218	20.83	2,667	160,009	6,507,282	21.87	4,519	271,137	1,539,618	23.93	1,069	64,151	1,021,797	23.97	710	42,575	2,992,226	24.00	2,078	124,676	846,126	10.93	588	35,255	2,186,366	23.50	1,518	91,099	23,090,857	16,035	962,119	600
9/23/2026	4,226,705	24.00	2,935	176,113	3,426,703	18.57	2,380	142,779	7,144,538	23.97	4,961	297,689	1,522,542	23.97	1,057	63,439	1,208,690	24.00	839	50,362	3,004,802	24.00	2,087	125,200	976,744	12.13	678	40,698	2,171,915	23.67	1,508	90,496	23,682,639	16,446	986,777	609
9/24/2026	4,019,132	23.07	2,791	167,464	3,278,443	17.37	2,277	136,602	6,875,565	23.33	4,775	286,482	1,487,220	23.93	1,033	61,968	1,856,826	23.07	1,289	77,368	2,994,864	24.00	2,080	124,786	956,210	14.63	664	39,842	2,156,029	23.63	1,497	89,835	23,624,289	16,406	984,345	582
9/25/2026	3,983,342	24.00	2,766	165,973	3,354,113	18.80	2,329	139,755	6,834,136	24.00	4,746	284,756	1,605,912	23.37	1,115	66,913	2,393,111	24.00	1,662	99,713	2,942,502	24.00	2,043	122,604	34,874	0.53	24	1,453	2,136,230	23.60	1,483	89,010	23,284,220	16,170	970,176	640
9/26/2026	3,923,322	24.00	2,725	163,472	4,418,994	23.92	3,069	184,125	4,961,841	18.10	3,446	206,743	1,542,210	21.77	1,071	64,259	2,416,291	24.00	1,678	100,679	2,948,172	24.00	2,047	122,841	0	0.00	0	0	2,183,160	23.67	1,516	90,965	22,393,990	15,551	933,083	593
9/27/2026	4,270,220	24.00	2,965	177,926	4,784,341	23.98	3,322	199,348	3,474,133	12.00	2,413	144,756	1,778,451	24.00	1,235	74,102	2,377,818	24.00	1,651	99,076	2,931,950	24.00	2,036	122,165	106,502	1.47	74	4,438	2,253,524	23.77	1,565	93,897	21,976,939	15,262	915,706	527
9/28/2026	4,449,718	24.00	3,090	185,405	2,438,512	12.97	1,693	101,605	7,299,336	24.00	5,069	304,139	1,732,622	23.83	418	72,193	2,265,480	23.80	418	94,395	2,823,466	23.93	418	117,644	0	0.00	0	0	2,256,520	23.73	1,567	94,022	23,265,654	16,157	969,402	636
9/29/2026	4,351,332	23.98	3,022	181,306	2,839,725	15.37	1,972	118,322	7,128,731	23.98	4,951	297,030	1,713,007	23.17	418	71,375	2,264,711	23.97	418	94,363	2,822,846	24.00	418	117,619	27,264	0.60	19	1,136	2,206,261	23.70	1,532	91,928	23,353,877	16,218	973,078	663
9/30/2026	4,564,138	24.00	3,170	190,172	1,705,668	8.57	1,184	71,070	7,386,764	24.00	5,130	307,782	1,640,123	24.00	418	68,338	2,228,125	23.93	418	92,839	2,783,174	24.00	418	115,966	151,862	2.33	105	6,328	2,092,584	22.63	1,453	87,191	22,552,438	15,661	939,685	674

*Flare Flow and Runtime from chart recorder data. Ameresco's variance was approved on February 15, 2023 and Ameresco began operations on February 16, 2023.
*Date of lab data based on date sampled.

Chiquita Canyon Landfill
Higher Heating Value Calculations
Monthly Report Period: September 2026

	Flare No. 1 John Zink (FL-150) (FL-1995)				Flare No. 2 John Zink (Zule) (FL-100) (FL-2009)				Flare No. 3 John Zink (Zule) (FL-2023)				Zeeco 1				Zeeco 6				Zeeco 7				Parnel Vapor Combustor				Hero Vapor Combustor			
Date	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (MMBTU)	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (BTU)	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (BTU)	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (BTU)	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (BTU)	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (BTU)	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (BTU)	Total LFG Combusted (scf/day)	Methane (% v/v)	Higher Heating Value (BTU/scf)	Heat Input (BTU)
9/1/2026	3,930,813	23.69	240	943	4,713,401	23.69	240	1,131	6,877,005	23.69	240	1,650	1,389,250	23.83	241	335	1,390,954	23.83	241	336	1,588,516	11.54	117	186	1,283,694	18.31	185	238	2,743,951	11.32	115	315
9/2/2026	4,342,341	25.98	263	1,143	3,513,017	25.98	263	925	6,626,655	25.98	263	1,744	1,411,706	23.80	241	340	1,302,388	23.80	241	314	1,397,178	13.11	133	186	1,326,566	18.17	184	244	2,731,529	11.80	120	327
9/3/2026	4,206,514	27.10	275	1,155	4,577,868	27.10	275	1,257	5,827,061	27.10	275	1,600	1,453,741	27.02	274	398	1,290,075	27.02	274	353	1,692,764	13.03	132	223	1,291,426	18.51	188	242	2,675,666	10.93	111	296
9/4/2026	4,466,850	32.35	328	1,464	4,797,232	32.35	328	1,572	3,076,144	32.35	328	1,008	1,493,043	15.80	160	239	1,352,047	15.80	160	216	1,623,076	15.51	157	255	1,379,108	17.08	173	239	2,632,537	10.54	107	281
9/5/2026	4,345,817	6.22	63	274	4,654,713	6.22	63	293	4,478,873	6.22	63	282	1,532,603	28.74	291	446	1,372,382	28.74	291	400	1,220,576	15.75	160	195	1,302,804	17.16	174	226	2,588,347	11.23	114	294
9/6/2026	4,062,040	27.56	279	1,134	4,495,826	27.56	279	1,255	7,011,708	27.56	279	1,958	1,207,677	31.07	315	380	1,326,269	31.07	315	417	409,216	15.05	152	62	1,365,824	13.13	133	182	2,462,401	10.42	106	260
9/7/2026	4,809,316	27.28	276	1,329	1,434,756	27.28	276	396	7,572,485	27.28	276	2,093	1,558,341	28.15	285	444	1,305,800	28.15	285	372	830,614	14.72	149	124	1,445,136	12.73	129	186	2,542,935	10.47	106	270
9/8/2026	4,912,524	30.19	306	1,502	614,790	30.19	306	188	7,690,044	30.19	306	2,352	1,488,766	26.58	269	401	1,247,074	26.58	269	336	1,615,130	18.81	190	308	1,373,256	16.28	165	226	2,574,764	9.70	98	253
9/9/2026	4,423,379	26.89	272	1,205	4,605,338	26.89	272	1,254	7,161,241	26.89	272	1,951	1,594,397	25.65	260	414	1,257,845	25.65	260	327	527,134	15.83	160	85	865,104	13.67	138	120	2,430,911	10.58	107	261
9/10/2026	4,445,073	25.68	260	1,156	4,074,567	25.68	260	1,060	7,257,574	25.68	260	1,888	1,578,497	30.10	305	481	1,385,054	30.10	305	422	0	15.52	157	0	552,346	15.71	159	88	2,563,597	10.09	102	262
9/11/2026	4,126,075	27.59	279	1,153	4,461,483	27.59	279	1,247	6,595,663	27.59	279	1,843	1,624,703	27.46	278	452	1,190,249	27.46	278	331	891,882	14.57	148	132	1,188,502	17.31	175	208	2,507,460	9.13	92	232
9/12/2026	3,957,077	31.27	317	1,253	4,406,651	31.27	317	1,396	3,548,841	31.27	317	1,124	1,613,478	29.97	304	490	1,443,693	29.97	304	438	2,862,510	13.84	140	401	1,271,234	18.76	190	242	2,502,738	9.55	97	242
9/13/2026	4,114,513	31.37	318	1,308	4,556,188	31.37	318	1,448	4,682,667	31.37	318	1,488	1,585,345	28.31	287	455	1,358,906	28.31	287	390	2,978,380	12.32	125	372	1,290,986	17.88	181	234	2,458,471	7.03	71	175
9/14/2026	4,011,375	28.42	288	1,155	4,328,471	28.42	288	1,246	6,049,645	28.42	288	1,742	1,509,969	28.19	286	431	1,268,470	28.19	286	362	3,063,586	14.56	147	452	801,038	15.56	158	126	2,468,154	8.55	87	214
9/15/2026	3,979,712	28.47	288	1,148	4,333,394	28.47	288	1,250	6,888,878	28.47	288	1,987	1,574,753	27.15	275	433	1,220,880	27.15	275	336	3,245,798	17.65	179	580	0	17.16	174	0	2,488,652	7.86	80	198
9/16/2026	4,030,675	28.68	291	1,171	4,399,761	28.68	291	1,278	6,101,056	28.68	291	1,773	1,595,631	24.88	252	402	1,227,806	24.88	252	309	3,271,080	17.03	173	564	0	12.98	131	0	2,527,348	9.55	97	244
9/17/2026	4,031,381	26.54	269	1,084	4,093,798	26.54	269	1,101	6,810,416	26.54	269	1,831	1,603,305	28.78	291	467	1,340,390	28.78	291	391	3,172,678	13.89	141	446	815,484	12.28	124	101	2,396,699	8.42	85	204
9/18/2026	4,537,265	25.71	260	1,182	1,977,992	25.71	260	515	4,986,159	25.71	260	1,299	1,599,807	31.21	316	506	1,333,869	31.21	316	422	3,228,752	16.37	166	535	1,596,600	12.71	129	206	2,503,155	10.70	108	271
9/19/2026	3,758,345	28.10	285	1,070	2,969,634	28.10	285	845	6,793,734	28.10	285	1,934	1,502,735	27.27	276	415	1,215,667	27.27	276	336	3,173,564	17.09	173	549	1,052,122	12.20	124	130	2,395,123	12.43	126	302
9/20/2026	3,491,515	28.63	290	1,013	3,919,090	28.63	290	1,137	6,435,826	28.63	290	1,867	1,448,672	28.15	285	413	1,191,094	28.15	285	340	3,130,114	17.42	176	552	208,716	11.21	114	24	2,371,370	10.69	108	257
9/21/2026	3,465,962	27.22	276	956	3,658,299	27.22	276	1,009	7,027,675	27.22	276	1,938	1,455,106	25.06	254	369	1,110,951	25.06	254	282	3,062,892	17.68	179	549	377,798	10.80	109	41	2,324,066	10.48	106	247
9/22/2026	4,157,224	27.99	284	1,179	3,840,218	27.99	284	1,089	6,507,282	27.99	284	1,845	1,539,618	27.35	277	427	1,021,797	27.35	277	283	2,992,226	16.81	170	510	846,126	11.22	114	96	2,186,366	10.65	108	236
9/23/2026	4,226,705	27.04	274	1,158	3,426,703	27.04	274	939	7,144,538	27.04	274	1,957	1,522,542	23.58	239	364	1,208,690	23.58	239	289	3,004,802	16.31	165	496	976,744	12.30	125	122	2,171,915	9.10	92	200
9/24/2026	4,019,132	27.12	275	1,104	3,278,443	27.12	275	901	6,875,565	27.12	275	1,889	1,487,220	24.53	248	370	1,856,826	24.53	248	461	2,994,864	16.59	168	503	956,210	12.30	125	119	2,156,029	10.11	102	221
9/25/2026	3,983,342	28.15	285	1,136	3,354,113	28.15	285	956	6,834,136	28.15	285	1,949	1,605,912	19.42	197	316	2,393,111	19.42	197	471	2,942,502	15.69	159	468	34,874	12.30	125	4	2,136,230	10.62	108	230
9/26/2026	3,923,322	27.01	274	1,073	4,418,994	27.01	274	1,209	4,961,841	27.01	274	1,358	1,542,210	21.13	214	330	2,416,291	21.13	214	517	2,948,172	14.32	145	428	0	12.30	125	0	2,183,160	10.71	108	237
9/27/2026	4,270,220	28.31	287	1,225	4,784,341	28.31	287	1,372	3,474,133	28.31	287	996	1,778,451	23.74	240	428	2,377,818	23.74	240	572	2,931,950	15.94	161	473	106,502	12.30	125	13	2,253,524	11.85	120	271
9/28/2026	4,449,718	25.39	257	1,144	2,438,512	25.39	257	627	7,299,336	25.39	257	1,877	1,732,622	23.46	238	412	2,265,480	23.46	238	538	2,823,466	15.94	161	456	0	12.30	125	0	2,256,520	10.83	110	248
9/29/2026	4,351,332	24.34	247	1,073	2,839,725	24.34	247	700	7,128,731	24.34	247	1,758	1,713,007	26.15	265	454	2,264,711	26.15	265	600	2,822,846	15.94	161	456	27,264	12.30	125	3	2,206,261	10.84	110	242
9/30/2026	4,564,138	22.67	230	1,048	1,705,668	22.67	230	392	7,386,764	22.67	230	1,696	1,640,123	26.29	266	437	2,228,125	26.29	266	593	2,783,174	15.94	161	449	151,862	12.30	125	19	2,092,584	10.64	108	226

*Lab Sample Concentrations of Methane collected daily; converted to HHV (BTU/scf) by multiplying the methane concentration by 1,013 BTU/scf, the higher heating value of methane.
*Date of lab data based on date sampled.

Chiquita Canyon Landfill
LFG Not Combusted
Monthly Report Period: September 2026

Date	Flare 1, 2, 3, Zeeco 1, 6, 7, Parnel, Hero Total Flow Rate (scf/day)	2024 Baseline Flow Rate (scf/day)	LFG Not Combusted (scf/day)[1]	Ameresco LFG Processed (scf/day)[2]	LFG Not Combusted (scfm)
9/1/2026	23,917,584	--	--	0	--
9/2/2026	22,651,380	--	--	0	--
9/3/2026	23,015,115	--	--	0	
9/4/2026	20,820,037	--	--	0	--
9/5/2026	21,496,115	--	--	0	--
9/6/2026	22,340,961	--	--	0	--
9/7/2026	21,499,383	--	--	0	--
9/8/2026	21,516,348	--	--	0	--
9/9/2026	22,865,349	--	--	0	--
9/10/2026	21,856,708	--	--	0	--
9/11/2026	22,586,017	--	--	0	--
9/12/2026	21,606,222	--	--	0	--
9/13/2026	23,025,456	--	--	0	--
9/14/2026	23,500,708	--	--	0	--
9/15/2026	23,732,067	--	--	0	--
9/16/2026	23,153,357	--	--	0	--
9/17/2026	24,264,151	--	--	0	--
9/18/2026	21,763,599	--	--	0	--
9/19/2026	22,860,924	--	--	0	--
9/20/2026	22,196,397	--	--	0	--
9/21/2026	22,482,749	--	--	0	--
9/22/2026	23,090,857	--	--	0	--
9/23/2026	23,682,639	--	--	0	--
9/24/2026	23,624,289	--	--	0	--
9/25/2026	23,284,220	--	--	0	--
9/26/2026	22,393,990	--	--	0	--
9/27/2026	21,976,939	--	--	0	--
9/28/2026	23,265,654	--	--	0	--
9/29/2026	23,353,877	--	--	0	--
9/30/2026	22,552,438	--	--	0	--
Total/Average			--		**--**

[1]Total LFG not combusted is calculated based on the difference from modeled flow rate from all control devices in 2024 (baseline) and flow rate from Flares 1, 2, 3, and the Zeeco, Parnel, and Hero Thermal Oxidizers during the reporting period. Ameresco applied for variance to operate the LFG turbine plant under a variance order, and their variance was approved on February 15, 2023. Ameresco restarted operations on February 16, 2023, returning LFG collection and control system at CCL to full capacity. Therefore, the daily flow of LFG not flared per Section B ended on February 17, 2023, except for periods when the Ameresco Plant and/or the Flares are offline or processing less LFG for other reasons.

[2]Actual Ameresco LFG flow rate after restarting operations are greater than the unflared amount while Ameresco was off-line.

*Flare Flow and Runtime from chart recorder data.

*Date of lab data based on date sampled.

2024 Baseline Flow Rate					
Devices	**Gas Recovery (scf)**	**Flow Rate (scf/day)**	**Flow Rate (scfm)**	**LandGEM Generation (scfm)**	**% Change**
2022	4,351,276,471	11,921,305	8,279	12,800	
2023	5,373,366,012	14,721,551	10,223	13,400	4.69%
2024	5,613,964,490	**15,380,725**	10,681	14,000	4.48%

*Flare flow from chart recorder data. LFGTE Facility flow from Ameresco.

Attachment C-1

Surface Emissions Monitoring

2026 Chiquita Surface Emissions Exceedance

Integrated (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >25 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
155					1/6/26		55.77	1/8/26	Cover Compaction	1/14/26	23.7													
210					1/7/26		77.42	1/8/26	Flow Increase	1/14/26	19.7													
215					1/7/26		69.91	1/8/26	Cover Compaction; Flow Increase	1/14/26	17.8													
242					1/13/26		30.25	1/15/26	Flow Increase	1/20/26	22.11													
93					1/14/26		47.34	1/15/26	Flow Increase	1/20/26	16.19													
252					1/14/26		49.50	1/15/26	Flow Increase	1/20/26	19.34													
237					1/14/26		27.40	1/15/26	Flow Increase	1/20/26	11.7													
95					1/14/26		72.84	1/15/26	Flow Increase	1/20/26	13.93													
98					1/14/26		51.70	1/15/26	Flow Increase	1/20/26	17.89													
104					1/14/26		58.42	1/15/26	Flow Increase	1/20/26	23.41													
185					1/19/26		114.00	1/22/26	Flow Increase	1/28/26	21.6													
179					1/19/26		111.20	1/22/26	Flow Increase	1/28/26	17.1													
177					1/19/26		49.50	1/22/26	Flow Increase	1/28/26	23.67													
156					1/19/26		70.96	1/22/26	Flow Increase	1/28/26	10.3													
157					1/19/26		49.20	1/22/26	Flow Increase	1/28/26	17.2													
172					1/19/26		105.00	1/22/26	Flow Increase	1/28/26	19.5													
173					1/19/26		50.10	1/22/26	Flow Increase	1/28/26	21.16													
53					1/19/26		35.10	1/22/26	Flow Increase	1/28/26	18.6													
148					1/19/26		64.60	1/22/26	Flow Increase	1/28/26	22.84													
171					1/19/26		27.50	1/22/26	Flow Increase	1/28/26	20.5													
187					1/19/26		25.52	1/22/26	Flow Increase	1/28/26	16.2													
188					1/19/26		77.95	1/22/26	Flow Increase	1/28/26	17.7													
186					1/19/26		91.67	1/22/26	Flow Increase	1/28/26	18.3													
193					1/19/26		91.02	1/22/26	Flow Increase	1/28/26	15.9													
170					1/19/26		64.70	1/22/26	Flow Increase	1/28/26	10.4													
169					1/19/26		88.90	1/22/26	Flow Increase	1/28/26	19.5													
174					1/19/26		61.73	1/22/26	Flow Increase	1/28/26	15.3													
202					1/19/26		99.07	1/22/26	Flow Increase	1/28/26	22.16													
205					1/19/26		27.63	1/22/26	Flow Increase	1/28/26	16.18													
79					1/19/26		26.56	1/22/26	Flow Increase	1/28/26	20.35													
176					1/19/26		43.20	1/22/26	Flow Increase	1/28/26	24.41													
175					1/19/26		51.60	1/22/26	Flow Increase	1/28/26	22.37													
181					1/19/26		59.40	1/22/26	Flow Increase	1/28/26	20.87													
200					1/19/26		39.70	1/22/26	Flow Increase	1/28/26	21.39													
67					1/19/26		41.60	1/22/26	Flow Increase	1/28/26	18.77													
75					1/19/26		47.60	1/22/26	Flow Increase	1/28/26	20.85													
198					1/20/26		52.83	1/22/26	Flow Increase	1/29/26	15.7													
196					1/20/26		55.25	1/22/26	Flow Increase	1/29/26	16.3													
162					1/20/26		156.00	1/22/26	Flow Increase	1/29/26	18.9													
88					1/20/26		96.57	1/22/26	Flow Increase	1/29/26	13.45													
86					1/20/26		53.17	1/22/26	Flow Increase	1/29/26	22.32													
164					1/20/26		74.93	1/22/26	Flow Increase	1/29/26	14.5													
209					1/20/26		52.29	1/22/26	Flow Increase	1/29/26	9.79													
208					1/20/26		45.02	1/22/26	Flow Increase	1/29/26	8.59													
204					1/20/26		43.05	1/22/26	Flow Increase	1/29/26	10.41													
203					1/20/26		92.80	1/22/26	Flow Increase	1/29/26	24.32													
160					1/20/26		78.20	1/22/26	Flow Increase	1/29/26	15.31													
165					1/20/26		42.30	1/22/26	Flow Increase	1/29/26	10.71													
166					1/20/26		46.80	1/22/26	Flow Increase	1/29/26	10.85													
167					1/20/26		48.60	1/22/26	Flow Increase	1/29/26	10.2													
168					1/20/26		35.20	1/22/26	Flow Increase	1/29/26	10.07													
199					1/20/26		37.10	1/22/26	Flow Increase	1/29/26	16.71													
197					1/20/26		47.20	1/22/26	Flow Increase	1/29/26	21.72													
195					1/20/26		46.50	1/22/26	Flow Increase	1/29/26	16.82													
194					1/20/26		38.50	1/22/26	Flow Increase	1/29/26	15.97													
96					1/20/26		40.20	1/22/26	Flow Increase	1/29/26	17.42													
210					1/20/26		62.63	1/22/26	Flow Increase	1/29/26	13.09													
207					1/20/26		40.37	1/22/26	Flow Increase	1/29/26	16.41													
31					1/20/26		191.00	1/22/26	Flow Increase	1/29/26	20.4													
85					1/20/26		210.00	1/22/26	Flow Increase	1/29/26	19.69													

2026 Chiquita Surface Emissions Exceedance

Integrated (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >25 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
89					1/20/26		51.10	1/22/26	Flow Increase	1/29/26	12.9													
161					1/20/26		49.30	1/22/26	Flow Increase	1/29/26	14.16													
163					1/20/26		51.90	1/22/26	Flow Increase	1/29/26	18.13													
218					1/20/26		34.40	1/22/26	Flow Increase	1/29/26	19.3													
217					1/20/26		31.20	1/22/26	Flow Increase	1/29/26	21.13													
216					1/20/26		32.90	1/22/26	Flow Increase	1/29/26	14.72													
99					1/20/26		41.70	1/22/26	Flow Increase	1/29/26	20.62													
100					1/20/26		71.40	1/22/26	Flow Increase	1/29/26	21.72													
83					1/20/26		52.47	1/22/26	Flow Increase	1/29/26	22.8													
30					1/20/26		50.16	1/22/26	Flow Increase	1/29/26	10.05													
84					1/20/26		41.22	1/22/26	Flow Increase	1/29/26	8.16													
90					1/20/26		45.11	1/22/26	Flow Increase	1/29/26	16.6													
155					1/20/26		31.18	1/22/26	Flow Increase	1/29/26	6.21													
213					1/20/26		34.21	1/22/26	Flow Increase	1/29/26	12.42													
214					1/20/26		39.14	1/22/26	Flow Increase	1/29/26	17.91													
215					1/20/26		72.16	1/22/26	Flow Increase	1/29/26	17.75													
220					1/20/26		61.13	1/22/26	Flow Increase	1/29/26	23.48													
219					1/20/26		59.25	1/22/26	Flow Increase	1/29/26	12.6													
85					1/21/26		25.07	1/22/26	Flow Increase	1/29/26	19.2													
87					1/21/26		36.27	1/22/26	Flow Increase	1/29/26	10.35													
93					1/21/26		41.07	1/22/26	Flow Increase	1/29/26	18.22													
32					1/21/26		55.40	1/22/26	Flow Increase	1/29/26	12.31													
36					1/21/26		48.70	1/22/26	Flow Increase	1/29/26	13.62													
37					1/21/26		38.17	1/22/26	Flow Increase	1/29/26	12.25													
49					1/21/26		47.30	1/22/26	Flow Increase	1/29/26	15.32													
50					1/21/26		30.10	1/22/26	Flow Increase	1/29/26	10.02													
59					1/21/26		40.30	1/22/26	Flow Increase	1/29/26	10.8													
60					1/21/26		49.12	1/22/26	Flow Increase	1/29/26	11.4													
61					1/21/26		111.00	1/22/26	Flow Increase	1/29/26	12.3													
62					1/21/26		39.60	1/22/26	Flow Increase	1/29/26	11.8													
63					1/21/26		42.10	1/22/26	Flow Increase	1/29/26	11.1													
98					1/21/26		61.91	1/22/26	Flow Increase	1/29/26	20.68													
97					1/21/26		52.01	1/22/26	Flow Increase	1/29/26	19.29													
104					1/21/26		56.85	1/22/26	Flow Increase	1/29/26	20.5													
103					1/21/26		40.23	1/22/26	Flow Increase	1/29/26	6.91													
236					1/22/26		36.50	1/22/26	Flow Increase	1/29/26	18.29													
235					1/22/26		41.20	1/22/26	Flow Increase	1/29/26	16.94													
234					1/22/26		52.50	1/22/26	Flow Increase	1/29/26	20.61													
233					1/22/26		56.44	1/22/26	Flow Increase	1/29/26	17.53													
253					1/22/26		78.20	1/22/26	Flow Increase	1/29/26	22.02													
244					1/22/26		178.00	1/22/26	Flow Increase	1/29/26	24.33													
243					1/22/26		183.00	1/22/26	Flow Increase	1/29/26	23.97													
242					1/22/26		145.00	1/22/26	Flow Increase	1/29/26	24.27													
241					1/22/26		53.01	1/22/26	Flow Increase	1/29/26	20.64													
240					1/22/26		70.05	1/22/26	Flow Increase	1/29/26	18.39													
245					1/22/26		31.70	1/22/26	Flow Increase	1/29/26	12.53													
246					1/22/26		160.00	1/22/26	Flow Increase	1/29/26	24.29													
247					1/22/26		93.75	1/22/26	Flow Increase	1/29/26	23.73													
248					1/22/26		110.00	1/22/26	Flow Increase	1/29/26	23.28													
249					1/22/26		75.19	1/22/26	Flow Increase	1/29/26	19.48													
38					1/22/26		111.00	1/22/26	Flow Increase	1/29/26	23.54													
221					1/22/26		27.82	1/22/26	Flow Increase	1/29/26	10.06													
222					1/22/26		33.11	1/22/26	Flow Increase	1/29/26	11.21													
229					1/22/26		27.22	1/22/26	Flow Increase	1/29/26	13.74													
83					2/4/26		41.13	2/12/26	Flow Increase	2/12/26	18.31													
205					2/5/26		37.28	2/12/26	Flow Increase	2/12/26	9.1													
176					2/5/26		49.95	2/12/26	Flow Increase	2/12/26	9.19													
182					2/5/26		25.73	2/12/26	Flow Increase	2/12/26	8.67													
200					2/5/26		25.99	2/12/26	Flow Increase	2/12/26	8.73													
181					2/5/26		36.91	2/12/26	Flow Increase	2/12/26	9.61													
176					2/9/26		25.35	2/20/26	Flow Increase	2/20/26	5.25													

2026 Chiquita Surface Emissions Exceedance

Integrated (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >25 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
165					2/9/26		40.78	2/20/26	Flow Increase	2/20/26	4.03													
82					2/9/26		76.65	2/20/26	Flow Increase	2/20/26	5.72													
83					2/9/26		105.00	2/20/26	Flow Increase	2/20/26	6.04													
155					2/9/26		77.67	2/20/26	Flow Increase	2/20/26	4.91													
30					2/23/26		28.20	3/4/26	Flow Increase	3/4/26	19.7													
175					2/23/26		35.75	3/4/26	Flow Increase	3/4/26	11.6													
210					3/3/26		39.47	3/9/26	Flow Increase	3/11/26	20.7													
215					3/3/26		26.17	3/4/26	Flow Increase	3/11/26	18.9													
250					3/4/26		27.67	3/9/26	Flow Increase	3/11/26	3.6													
87					3/4/26		41.46	3/5/26	Flow Increase	3/11/26	9.9													
91					3/4/26		43.11	3/5/26	Flow Increase	3/11/26	15.2													
93					3/4/26		35.40	3/11/26	Flow Increase	3/11/26	9.1													
94					3/4/26		65.21	3/6/26	Flow Increase	3/11/26	14.4													
95					3/4/26		30.40	3/6/26	Flow Increase	3/11/26	17.4													
203					3/9/26		28.81	3/11/26	Flow Increase	3/19/26	5.3													
173					3/16/26		52.57	3/18/26	Flow Increase	3/27/26	19.1													
150					3/16/26		25.16	3/19/26	Flow Increase	3/27/26	7.9													
78					3/16/26		47.56	3/17/26	Flow Increase	3/27/26	13.7													
180					4/6/26		40.53	4/15/26	Flow Increase	4/16/26	21.54													
77					4/6/26		36.11	4/8/26	Flow Increase	4/16/26	19.83													
91					4/15/26		42.66	4/22/26	Flow Increase	4/21/26	19.2													
92					4/15/26		47.20	4/15/26	Flow Increase	4/21/26	19.9													
93					4/15/26		65.58	4/22/26	Flow Increase	4/21/26	23.4													
155					4/28/26		27.51	4/29/26	Flow Increase	5/7/26	19.15													
84					4/28/26		34.81	5/4/26	Flow Increase	5/7/26	18.3													
145					5/12/26		56.12	5/14/26	Cover Compaction	5/20/26	24.14													
77					5/12/26		34.23	5/14/26	Cover Compaction	5/20/26	23.81													
237					5/21/26		35.72	5/22/26	Flow Increase	5/29/26	2.1													
245					5/21/26		42.71	5/22/26	Flow Increase	5/29/26	2.56													
205					6/2/26		25.60	6/4/26	Flow Increase	6/11/26	8.13													
215					6/2/26		31.60	6/4/26	Flow Increase	6/11/26	17.9													
92					6/3/26		30.18	6/4/26	Flow Increase	6/11/26	11.42													
149					6/11/26		40.65	6/12/26	Flow Increase	6/17/26	15.16													
83					6/11/26		40.45	6/12/26	Flow Increase	6/17/26	24.69													
171					6/15/26		33.20	6/16/26	Flow Increase	6/24/26	6.32													
80					6/15/26		29.41	6/16/26	Flow Increase	6/24/26	8.28													
82					6/23/26		39.43	6/24/26	Flow Increase	6/30/26	17.41													
181					6/23/26		47.07	6/24/26	Flow Increase	6/30/26	12.25													
243					7/23/26		26.63	7/24/26	Flow Increase	7/30/26	4.22													
247					7/23/26		38.12	7/24/26	Flow Increase	7/30/26	7.2													
83					7/27/26		26.50	7/28/26	Flow Increase	8/5/26	19.1													
90					7/27/26		26.80	7/28/26	Flow Increase	8/5/26	13.7													
240					8/12/26		41.80	8/13/26	Flow Increase	8/20/26	22.52													
245					8/12/26		34.50	8/13/26	Flow Increase	8/20/26	18.45													
163					8/19/26		44.50	8/20/26	Flow Increase	8/27/26	15.9													
167					8/19/26		56.40	8/20/26	Flow Increase	8/27/26	7.1													
160					8/25/26		26.67	8/26/26	Flow Increase	8/31/26	18.9													
79					9/8/26		25.60	9/9/26	Flow Increase	9/16/26	18.6													
80					9/8/26		25.20	9/9/26	Flow Increase	9/16/26	7.19													
215					9/9/26		25.71	9/10/26	Cover Compaction	9/16/26	11.02													
153					9/14/26		30.41	9/15/26	Flow Increase	9/21/26	12.88													
151					9/14/26		27.82	9/17/26	Flow Increase	9/21/26	6.18													
163					9/14/26		29.21	9/17/26	Flow Increase	9/21/26	3.24													
83					9/14/26		28.36	9/17/26	Flow Increase	9/21/26	9.46													
211					9/29/26		28.70	9/30/26	Flow Increase	10/8/26	3.9													
210					9/29/26		84.90	9/30/26	Flow Increase	10/8/26	14.09													
215					9/29/26		69.50	9/30/26	Flow Increase	10/8/26	5.22													
214					9/29/26		31.29	9/30/26	Flow Increase	10/8/26	8.97													

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
176	Y21	CV-24032	34.43510	-118.64962	1/7/26	7:48	797	1/8/26	Boot Repaired	1/14/26	16.7					1/8/26	Boot Repaired	2/6/26	32.3					
176	Y22	CV-24031 (FP-032 was flagged)	34.43488	-118.64982	1/7/26	7:54	1,248	1/8/26	Flow Increase	1/14/26	61.9					1/8/26	Flow Increase	2/6/26	5.7					
202	Y23	CV-24142	34.43402	-118.65133	1/7/26	8:13	506	1/8/26	Flow Increase	1/14/26	26.3					1/8/26	Flow Increase	2/6/26	9.6					
173	Y24	CV-24036	34.43447	-118.64970	1/7/26	8:31	600	1/8/26	Flow Increase	1/14/26	16.8					1/8/26	Flow Increase	2/6/26	153					
173	Y25	FP-030	34.43453	-118.64968	1/7/26	8:34	1,100	1/8/26	Flow Increase	1/14/26	15.1					1/8/26	Flow Increase	2/6/26	488					
156	Y26	Surface	34.43569	-118.64841	1/7/26	8:56	609	1/8/26	Cover Repaired	1/14/26	11.8					1/8/26	Cover Repaired	2/6/26	7.7					
164	Y61	CV-24176	34.43262	-118.64884	1/7/26	8:02	541	1/8/26	Flow Increase	1/14/26	11.3					1/8/26	Flow Increase	2/6/26	17.9					
163	Y62	H-1760S	34.43276	-118.64790	1/7/26	8:18	768	1/8/26	Flow Increase	1/14/26	23.2					1/8/26	Flow Increase	2/6/26	21.1					
89	Y63	CV-24107	34.43257	-118.64616	1/7/26	8:33	1,718	1/8/26	Cover Compaction; Flow Increase	1/14/26	17.6					1/8/26	Cover Compaction; Flow Increase	2/6/26	15.5					
160	Y64	CV-24088	34.43360	-118.64768	1/7/26	9:03	667	1/8/26	Boot Repaired	1/14/26	16					1/8/26	Boot Repaired	2/6/26	11					
155	Y65	CV-24160	34.43381	-118.64624	1/7/26	9:18	1,013	1/8/26	Cover Compaction	1/14/26	23.7					1/8/26	Cover Compaction	2/6/26	63.4					
83	Y66	CV-24161	34.43387	-118.64562	1/7/26	9:24	537	1/8/26	Flow Increase	1/14/26	34.1					1/8/26	Flow Increase	2/6/26	42.4					
53	Y67	CV-2559	34.43574	-118.64551	1/7/26	9:46	903	1/8/26	Flow Increase	1/14/26	26.7					1/8/26	Flow Increase	2/6/26	47.7					
183	Y41	CV-2337	34.43547	-118.65077	1/7/26	8:41	714	1/8/26	Cover Compaction	1/14/26	19.6					1/8/26	Cover Compaction	2/6/26	7.4					
180	Y42	Riser	34.43532	-118.65047	1/7/26	8:47	2,131	1/8/26	Flow Increase	1/14/26	12.4					1/8/26	Flow Increase	2/6/26	432					
183	Y43	CV-2326	34.43617	-118.65052	1/7/26	8:53	2,408	1/8/26	Boot Repaired	1/14/26	11.3					1/8/26	Boot Repaired	2/6/26	5.9					
183	Y44	CV-24011	34.43618	-118.65022	1/7/26	9:08	83,274	1/8/26	Boot Repaired; Flow Increase	1/14/26	10.1					1/8/26	Boot Repaired; Flow Increase	2/6/26	6					
184	Y45	Surface	34.43622	-118.64970	1/7/26	9:21	18,036	1/8/26	Cover Repaired	1/14/26	10.8					1/8/26	Cover Repaired	2/6/26	5.9					
184	Y46	CV-24012	34.43616	-118.64939	1/7/26	9:27	89,095	1/8/26	Flow Increase	1/14/26	13.9					1/8/26	Flow Increase	2/6/26	6.2					
185	Y47	CV-24021	34.43615	-118.64906	1/7/26	9:48	981	1/8/26	Boot Repaired; Flow Increase	1/14/26	11.3					1/8/26	Boot Repaired; Flow Increase	2/6/26	7.3					
185	Y48	CV-24014	34.43677	-118.64894	1/7/26	9:53	3,399	1/8/26	Flow Increase	1/14/26	13					1/8/26	Flow Increase	2/6/26	12.4					
185	Y49	CV-24013	34.43662	-118.64925	1/7/26	9:55	96,075	1/9/26	Flow Increase	1/14/26	31.4					1/9/26	Flow Increase	2/6/26	6.3					
76	Y61	CV-2008	34.43625	-118.64625	1/8/26	8:49	650	1/8/26	Cover Compaction	1/14/26	20.4					1/8/26	Cover Compaction	2/5/26	111					
215	Y1	H-105A	34.43116	-118.65063	1/8/26	8:23	500	1/8/26	Cover Compaction	1/14/26	448					1/8/26	Cover Compaction	2/5/26	146					
211	B1	CV-24188	34.43156	-118.65007	1/8/26	7:57	225	1/8/26	Flow Increase	1/14/26	6.8													
214	B2	H-2059W	34.43110	-118.65023	1/8/26	8:07	200	1/8/26	Flow Increase	1/14/26	29.3													
76	B61	H-1771A	34.43637	-118.64643	1/8/26	8:48	325	1/8/26	Flow Increase	1/14/26	19.1													
79	B62	Surface	34.43724	-118.64545	1/8/26	8:25	230	1/8/26	Flow Increase	1/14/26	7.7													
215	Y1	Surface	34.43118	-118.65062	1/16/26	8:01	1,172	1/22/26	Flow Increase	1/26/26	15.43					1/22/26	Flow Increase	2/12/26	125					
210	Y2	Surface	34.43173	-118.65075	1/16/26	8:07	1,352	1/22/26	Flow Increase	1/26/26	6.42					1/22/26	Flow Increase	2/12/26	69.71					
162	Y3	CV-24106	34.43211	-118.64673	1/16/26	8:32	610	1/22/26	Flow Increase	1/26/26	331					1/22/26	Flow Increase	2/12/26	132					
161	Y4	CV-24175	34.43286	-118.64768	1/16/26	8:52	10,157	1/22/26	Flow Increase	1/26/26	34.2					1/22/26	Flow Increase	2/12/26	9.83					
149	Y15	Surface	34.43435	-118.64576	1/16/26	8:34	1,424	1/22/26	Flow Increase	1/26/26	96.03					1/22/26	Flow Increase	2/12/26	7.93					
177	Y30	Surface	34.43518	-118.64890	1/16/26	8:47	860	1/22/26	Flow Increase	1/26/26	103					1/22/26	Flow Increase	2/12/26	340					
173	B45	Surface	34.43439	-118.64951	1/16/26	8:54	275	1/22/26	Flow Increase	1/26/26	105													
176	Y21	Surface	34.43491	-118.64984	1/26/26	8:08	1,756	1/30/26	Cover Compaction	2/5/26	42.16					1/30/26	Cover Compaction	2/25/26	5.9					
176	Y23	CV-24031	34.43490	-118.64986	1/26/26	8:11	2,345	1/30/26	Cover Compaction	2/5/26	46.1					1/30/26	Cover Compaction	2/25/26	6.2					
176	Y24	CV-24032	34.43511	-118.64962	1/26/26	8:18	6,421	1/30/26	Cover Compaction	2/5/26	32.79					1/30/26	Cover Compaction	2/25/26	5.3					
177	Y25	Surface	34.43521	-118.64920	1/26/26	8:22	623	1/30/26	Cover Compaction	2/5/26	17.11					1/30/26	Cover Compaction	2/25/26	4.9					
177	Y26	Near CV-2303	34.43533	-118.64914	1/26/26	8:26	599	1/30/26	Boot Repaired	2/5/26	38.96					1/30/26	Boot Repaired	2/25/26	5.2					
77	Y27	6x4 reducer near CV-113	34.43696	-118.64674	1/26/26	9:05	562	1/30/26	Pipe Repaired	2/5/26	10.19					1/30/26	Pipe Repaired	2/25/26	22.3					
77	Y28	Hero Sump	34.43734	-118.64678	1/26/26	9:30	962	1/30/26	Cover Compaction	2/5/26	22.15					1/30/26	Cover Compaction	2/25/26	16.2					
78	Y29	CV-2563	34.43730	-118.64578	1/26/26	9:52	5,623	1/29/26	Flow Increase	2/5/26	13.12					1/29/26	Flow Increase	2/25/26	51.4					
86	Y81	Riser	34.43239	-118.64574	1/26/26	8:29	1,863	1/29/26	Cover Compaction	2/5/26	22.11					1/29/26	Cover Compaction	2/25/26	19.2					
88	Y82	H-2275E	34.43241	-118.64624	1/26/26	8:35	2,971	1/29/26	Cover Compaction; Flow Increase	2/5/26	38.62					1/29/26	Cover Compaction; Flow Increase	2/25/26	28.2					
162	Y83	CV-24106	34.43215	-118.64677	1/26/26	8:41	3,884	1/29/26	Flow Increase	2/5/26	197					1/29/26	Flow Increase	2/25/26	64.2					
197	Y84	CV-24198	34.43157	-118.64760	1/26/26	8:51	2,191	1/30/26	Flow Increase	2/5/26	19.03					1/30/26	Flow Increase	2/25/26	415					
198	Y85	CV-24104	34.43173	-118.64811	1/26/26	9:02	4,756	1/30/26	Flow Increase	2/5/26	37.13					1/30/26	Flow Increase	2/25/26	23.9					
212	Y86	CV-2539	34.43171	-118.64923	1/26/26	9:17	2,849	1/29/26	Flow Increase	2/5/26	29.76					1/29/26	Flow Increase	2/25/26	19.1					
212	Y87	CV-2565	34.43198	-118.64901	1/26/26	9:45	2,771	1/29/26	Flow Increase	2/5/26	11.13					1/29/26	Flow Increase	2/25/26	75.9					
197	Y88	CV-2503	34.43123	-118.64777	1/26/26	10:28	5,939	1/30/26	Flow Increase	2/5/26	27.63					1/30/26	Flow Increase	2/25/26	22.4					
194	Y89	CV-24203	34.43154	-118.64601	1/26/26	10:48	845	1/30/26	Cover Compaction; Flow Increase	2/5/26	311					1/30/26	Cover Compaction; Flow Increase	2/25/26	117					
82	Y61	H-1804B	34.43426	-118.64567	1/26/26	8:26	1,200	1/29/26	Cover Compaction; Flow Increase	2/5/26	34.68					1/29/26	Cover Compaction; Flow Increase	2/25/26	47.7					
160	Y62	CV-24172	34.43299	-118.64732	1/26/26	9:03	765	1/30/26	Cover Compaction; Flow Increase	2/5/26	19.28					1/30/26	Cover Compaction; Flow Increase	2/25/26	16.6					
160	Y63	CV-24168	34.43329	-118.64735	1/26/26	9:10	1,300	1/30/26	Flow Increase	2/5/26	17.13					1/30/26	Flow Increase	2/25/26	7.9					
161	Y64	H-2274B	34.43266	-118.64696	1/26/26	10:36	1,100	1/29/26	Flow Increase	2/5/26	29.63					1/29/26	Flow Increase	2/25/26	8.5					
85	Y65	CV-24210	34.43265	-118.64562	1/26/26	11:06	1,000	1/29/26	Cover Compaction; Flow Increase	2/5/26	43.76					1/29/26	Cover Compaction; Flow Increase	2/25/26	9.2					
172	Y41	CV-24038	34.43485	-118.64879	1/26/26	8:37	2,200	1/30/26	Seal Repaired; Flow Increase	2/5/26	5.85					1/30/26	Seal Repaired; Flow Increase	2/25/26	7.5					
172	Y42	CV-24045	34.43471	-118.64855	1/26/26	10:53	1,500	1/30/26	Seal Repaired; Flow Increase	2/5/26	13.18					1/30/26	Seal Repaired; Flow Increase	2/25/26	303					
173	Y43	CV-24032	34.43476	-118.64945	1/26/26	8:45	890	1/30/26	Cover Compaction	2/5/26	24					1/30/26	Cover Compaction	2/25/26	7.1					
202	Y44	CV-1532A	34.43385	-118.65095	1/26/26	8:57	700	1/29/26	Cover Compaction	2/5/26	15.5					1/29/26	Cover Compaction	2/25/26	17.7					
169	Y45	CV-24050	34.43358	-118.64995	1/26/26	9:34	650	1/29/26	Flow Increase	2/5/26	24.13					1/29/26	Flow Increase	2/25/26	30.1					
68	Y102	CV-2009	34.43627	-118.64529	1/26/26	8:40	10,000	1/30/26	Flow Increase	2/5/26	37.61					1/30/26	Flow Increase	2/25/26	10.9					
69	Y103	CV-24214	34.43674	-118.64355	1/26/26	9:00	797	1/30/26	Flow Increase	2/5/26	386					1/30/26	Flow Increase	2/25/26	7.1					
78	B22	Riser	34.43733	-118.64588	1/26/26	9:46	200	1/30/26	Flow Increase	2/5/26	21.14													
76	B23	Surface	34.43638	-118.64599	1/26/26	10:45	200	1/30/26	Flow Increase	2/5/26	38.66													
83	B61	CV-24190	34.43380	-118.64628	1/26/26	8:34	325	1/30/26	Flow Increase	2/5/26	88.17													
84	B62	CV-24092	34.43332	-118.64616	1/26/26	10:49	210	1/30/26	Flow Increase	2/5/26	9.17													
84	B63	H-1764N	34.43316	-118.64565	1/26/26	10:59	315	1/30/26	Flow Increase	2/5/26	194													
67	B101	Surface	34.43623	-118.64488	1/26/26	8:33	233	1/30/26	Flow Increase	2/5/26	17.77													
32	Y21	CV-24110	34.43455	-118.64478	1/27/26	8:28	940	1/30/26	Flow Increase	2/4/26	210					1/30/26	Flow Increase	2/26/26	44.2					
33	Y22	CV-24109	34.43400	-118.64485	1/27/26	8:33	1,200	1/29/26	Cover Compaction	2/4/26	413					1/29/26	Cover Compaction	2/26/26	18.3					
30	Y23	H-1805B	34.43372	-118.64510	1/27/26	8:34	1,000	1/29/26	Cover Compaction	2/4/26	18.59					1/29/26	Cover Compaction	2/26/26	104					
30	Y24	CV-24162	34.43357	-118.64515	1/27/26	8:38	650	1/29/26	Flow Increase	2/4/26	31.66					1/29/26	Flow Increase	2/26/26	4.6					
34	Y25	CV-24163	34.43340	-118.64455	1/27/26	8:45	700	1/30/26	Flow Increase	2/4/26	9.13					1/30/26	Flow Increase	2/26/26	11.1					
50	Y26	CV-2531	34.43264	-118.64321	1/27/26	9:12	1,300	1/30/26	Flow Increase	2/4/26	421					1/30/26	Flow Increase	2/26/26	470					
36	Y27	H-1957B	34.43448	-118.64388	1/27/26	9:29	800	1/29/26	Flow Increase	2/4/26	34.08					1/29/26	Flow Increase	2/26/26	303					

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
41	Y28	CV-2011A	34.43446	-118.64306	1/27/26	9:35	620	1/30/26	Flow Increase	2/4/26	12.36					1/30/26	Flow Increase	2/26/26	30.2					
42	Y29	CV-24119	34.43376	-118.64239	1/27/26	10:23	2,000	1/30/26	Cover Compaction	2/4/26	409					1/30/26	Cover Compaction	2/26/26	113					
43	Y30	CV-2529	34.43317	-118.64245	1/27/26	10:31	900	1/30/26	Cover Compaction	2/4/26	69.11					1/30/26	Cover Compaction	2/26/26	14.4					
48	Y1	C-10	34.43473	-118.64120	1/27/26	8:44	1,048	1/30/26	Cover Compaction	2/4/26	167					1/30/26	Cover Compaction	2/26/26	5.2					
48	Y2	C-8	34.43365	-118.64087	1/27/26	8:50	875	1/30/26	Cover Compaction; Flow Increase	2/4/26	169					1/30/26	Cover Compaction; Flow Increase	2/26/26	12.6					
45	Y30	CV-2529	34.43317	-118.64245	1/27/26	10:31	1,082	1/30/26	Cover Compaction	2/4/26	126					1/30/26	Cover Compaction	2/26/26	77.1					
45	Y4	CV-2525	34.43499	-118.64176	1/27/26	9:05	1,698	1/30/26	Flow Increase	2/4/26	281					1/30/26	Flow Increase	2/26/26	411					
47	Y5	CV-2528	34.43381	-118.64125	1/27/26	9:10	4,975	1/30/26	Flow Increase	2/4/26	479					1/30/26	Flow Increase	2/26/26	37.9					
51	Y6	CV-05	34.43285	-118.64223	1/27/26	9:43	2,480	1/30/26	Flow Increase	2/4/26	80.67					1/30/26	Flow Increase	2/26/26	20.9					
52	Y7	CV-04	34.43314	-118.64169	1/27/26	9:49	650	1/30/26	Flow Increase	2/4/26	61.36					1/30/26	Flow Increase	2/26/26	27.6					
47	Y8	CV-24222	34.43358	-118.64201	1/27/26	10:10	578	1/30/26	Flow Increase	2/4/26	73.06					1/30/26	Flow Increase	2/26/26	13.7					
47	Y9	H-2170S	34.43361	-118.64151	1/27/26	10:18	1,650	1/30/26	Flow Increase	2/4/26	105					1/30/26	Flow Increase	2/26/26	33.4					
226	Y61	CV-2512	34.42926	-118.65063	1/27/26	9:14	1,842	1/30/26	Flow Increase	2/4/26	111					1/30/26	Flow Increase	2/26/26	10.8					
223	Y62	CV-2508	34.42971	-118.64878	1/27/26	9:40	1,054	1/30/26	Cover Compaction; Flow Increase	2/4/26	21.63					1/30/26	Cover Compaction; Flow Increase	2/26/26	40.6					
222	Y63	CV-2507	34.43014	-118.64817	1/27/26	9:51	792	1/30/26	Flow Increase	2/4/26	222					1/30/26	Flow Increase	2/26/26	183					
233	Y64	CV-2514	34.42962	-118.64782	1/27/26	10:20	1,394	1/30/26	Cover Compaction; Flow Increase	2/4/26	99.64					1/30/26	Cover Compaction; Flow Increase	2/26/26	29.2					
38	Y21	CV-1701S	34.43358	-118.64334	1/28/26	8:58	10,000	1/30/26	Cover Compaction; Flow Increase	2/5/26	328					1/30/26	Cover Compaction; Flow Increase	2/26/26	467					
38	Y22	Surface	34.43332	-118.64341	1/28/26	9:02	1,400	1/30/26	Cover Compaction	2/5/26	75.67					1/30/26	Cover Compaction	2/26/26	371					
38	Y23	CV-24118	34.43329	-118.64386	1/28/26	10:33	10,000	1/30/26	Cover Compaction	2/5/26	23.1					1/30/26	Cover Compaction	2/26/26	179					
87	Y24	CV-24208	34.43182	-118.64500	1/28/26	9:28	20,000	1/30/26	Cover Compaction; Flow Increase	2/5/26	53.71					1/30/26	Cover Compaction; Flow Increase	2/26/26	23.2					
87	Y25	CV-2534	34.43131	-118.64481	1/28/26	9:38	4,671	1/30/26	Flow Increase	2/5/26	160					1/30/26	Flow Increase	2/26/26	42.7					
249	Y26	GAB1C	34.42745	-118.64864	1/28/26	10:13	4,631	1/30/26	Cover Compaction	2/5/26	390					1/30/26	Cover Compaction	2/26/26	56.1					
87	B21	Surface	34.43123	-118.64516	1/28/26	9:36	270	1/30/26	Flow Increase	2/5/26	51.13													
241	B22	Surface	34.42824	-118.64989	1/28/26	9:55	341	1/30/26	Flow Increase	2/5/26	30.16													
172	Y41	FP-019	34.43471	-118.64906	2/2/26	8:22	900	2/4/26	Cover Compaction	2/12/26	5.51					2/4/26	Cover Compaction	2/26/26	11.2					
169	Y42	CV-2341	34.43362	-118.65031	2/2/26	8:54	800	2/4/26	Cover Compaction; Flow Increase	2/12/26	6.62					2/4/26	Cover Compaction; Flow Increase	2/26/26	13.8					
55	Y43	CV-2207	34.43602	-118.64423	2/2/26	9:47	660	2/4/26	Cover Compaction; Flow Increase	2/12/26	8.11					2/4/26	Cover Compaction; Flow Increase	2/26/26	7.7					
176	Y21	CV-1902A	34.43464	-118.65032	2/2/26	8:27	700	2/4/26	Cover Compaction	2/12/26	480					2/4/26	Cover Compaction	2/26/26	16.2					
79	Y22	CV-48R	34.43730	-118.64586	2/2/26	9:27	625	2/4/26	Flow Increase	2/12/26	8.71					2/4/26	Flow Increase	2/26/26	21.6					
79	Y23	CV-2563	34.43727	-118.64576	2/2/26	9:30	900	2/4/26	Flow Increase	2/12/26	7.88					2/4/26	Flow Increase	2/26/26	13.9					
84	Y81	CV-24108	34.43316	-118.64544	2/2/26	9:14	3,571	2/4/26	Cover Compaction; Flow Increase	2/12/26	7.82					2/4/26	Cover Compaction; Flow Increase	2/26/26	11.7					
85	Y82	CV-24210	34.43298	-118.64545	2/2/26	9:47	4,790	2/4/26	Flow Increase	2/12/26	12.61					2/4/26	Flow Increase	2/26/26	9.8					
162	Y83	CV-24106	34.43214	-118.64674	2/2/26	9:38	3,396	2/4/26	Flow Increase	2/12/26	13.15					2/4/26	Flow Increase	2/26/26	13.3					
163	Y84	CV-24090	34.43268	-118.64755	2/2/26	9:56	2,987	2/4/26	Cover Compaction	2/12/26	17.05					2/4/26	Cover Compaction	2/26/26	7.9					
196	Y85	CV-2567	34.43195	-118.64807	2/2/26	10:20	589	2/4/26	Cover Compaction	2/12/26	8.21					2/4/26	Cover Compaction	2/26/26	19.1					
198	Y86	CV-24104	34.43172	-118.64809	2/2/26	10:18	4,990	2/4/26	Cover Compaction	2/12/26	18.733					2/4/26	Cover Compaction	2/26/26	22.3					
215	Y87	Riser	34.43113	-118.65056	2/2/26	10:59	1,237	2/4/26	Cover Compaction; Removed Riser	2/12/26	23.51					2/4/26	Cover Compaction; Removed Riser	2/26/26	147					
82	B62	FP-057	34.43472	-118.64555	2/2/26	9:23	302	2/4/26	Flow Increase	2/12/26	8.52													
207	B72	West side perimeter header	34.43244	-118.65107	2/2/26	10:54	200	2/4/26	Cover Compaction; Flow Increase	2/12/26	6.52													
71	B21	CV-24133	34.43742	-118.64273	2/2/26	10:16	285	2/4/26	Flow Increase	2/12/26	51.17													
56	Y41	CV-24213	34.43659	-118.64297	2/3/26	8:45	10,900	2/5/26	Cover Compaction; Flow Increase	2/12/26	47.5					2/5/26	Cover Compaction; Flow Increase	2/27/26	137					
228	Y61	CV-2510	34.42906	-118.64985	2/3/26	8:38	1,371	2/6/26	Flow Increase	2/12/26	432					2/6/26	Flow Increase	2/27/26	193					
33	Y81	CV-24109	34.43396	-118.64483	2/3/26	8:38	911	2/5/26	Flow Increase	2/12/26	20.48					2/5/26	Flow Increase	2/27/26	13.2					
30	Y82	CV-24162	34.43364	-118.64515	2/3/26	8:42	1,200	2/5/26	Cover Compaction	2/12/26	387					2/5/26	Cover Compaction	2/27/26	19.9					
34	Y83	CV-24163	34.43342	-118.64451	2/3/26	8:46	800	2/6/26	Cover Compaction; Flow Increase	2/12/26	54.83					2/6/26	Cover Compaction; Flow Increase	2/27/26	11.7					
35	Y84	TC-1961E	34.43274	-118.64437	2/3/26	8:52	1,400	2/5/26	Cover Compaction; Flow Increase	2/12/26	32.64					2/5/26	Cover Compaction; Flow Increase	2/27/26	22.4					
42	Y85	CV-24119	34.43388	-118.64230	2/3/26	9:19	2,000	2/6/26	Flow Increase	2/12/26	321					2/6/26	Flow Increase	2/27/26	16.6					
43	Y86	CV-2529	34.43310	-118.64225	2/3/26	9:36	850	2/5/26	Cover Compaction; Flow Increase	2/12/26	21.61					2/5/26	Cover Compaction; Flow Increase	2/27/26	30.1					
51	Y87	CV-05	34.43280	-118.64220	2/3/26	9:42	1,000	2/5/26	Flow Increase	2/12/26	210					2/5/26	Flow Increase	2/27/26	14.6					
50	Y89	CV-06	34.43251	-118.64285	2/3/26	9:46	690	2/5/26	Flow Increase	2/12/26	221					2/5/26	Flow Increase	2/27/26	52.1					
49	Y90	CV-2532	34.43221	-118.64382	2/3/26	9:53	1,700	2/5/26	Cover Compaction; Flow Increase	2/12/26	111					2/5/26	Cover Compaction; Flow Increase	2/27/26	210					
93	Y121	A-1	34.43122	-118.64377	2/3/26	9:41	1,147	2/6/26	Cover Compaction; Flow Increase	2/12/26	163					2/6/26	Cover Compaction; Flow Increase	2/27/26	80.1					
93	Y122	South Manifold	34.43120	-118.64424	2/3/26	9:45	9,471	2/5/26	Added Dirt; Cover Compaction	2/12/26	185					2/5/26	Added Dirt; Cover Compaction	2/27/26	76.4					
93	Y123	2-in steel pipe	34.43110	-118.64445	2/3/26	9:48	10,000	2/5/26	Added Dirt; Cover Compaction	2/12/26	142					2/5/26	Added Dirt; Cover Compaction	2/27/26	44.8					
91	Y124	South Manifold Pump 1	34.43150	-118.64416	2/3/26	9:52	1,153	2/5/26	Cover Compaction	2/12/26	219					2/5/26	Cover Compaction	2/27/26	31					
91	Y125	CV-2533	34.43190	-118.64414	2/3/26	10:03	1,336	2/6/26	Cover Compaction; Flow Increase	2/12/26	165					2/6/26	Cover Compaction; Flow Increase	2/27/26	61.7					
92	Y126	2 in pipe	34.43205	-118.64380	2/3/26	10:05	517	2/5/26	Sealed Pipe	2/12/26	105					2/5/26	Sealed Pipe	2/27/26	56.2					
92	Y127	Surface	34.43153	-118.64370	2/3/26	10:09	523	2/5/26	Cover Compaction	2/12/26	135					2/5/26	Cover Compaction	2/27/26	63.3					
92	Y128	Surface	34.43171	-118.64398	2/3/26	10:13	5,160	2/5/26	Cover Compaction	2/12/26	202					2/5/26	Cover Compaction	2/27/26	305					
181	Y1	Lorentz panel for CV-2532	34.43516	-118.65114	2/3/26	8:32	600	2/6/26	Cover Compaction	2/12/26	5.36					2/6/26	Cover Compaction	2/27/26	9.5					
180	Y2	Surface	34.43530	-118.65050	2/3/26	8:46	3,242	2/6/26	Repaired Liner	2/12/26	155					2/6/26	Repaired Liner	2/27/26	479					
183	Y3	Surface	34.43589	-118.65025	2/3/26	8:58	5,213	2/6/26	Cover Compaction	2/12/26	4.36					2/6/26	Cover Compaction	2/27/26	2.3					
183	Y4	CV-24016	34.43591	-118.65028	2/3/26	9:03	542	2/6/26	Inspected; 2/10/26 reconnected well	2/12/26	4.41					2/6/26	Inspected; 2/10/26 reconnected well	2/27/26	2.4					
183	Y5	CV-2336	34.43599	-118.65091	2/3/26	9:10	541	2/6/26	Cover Compaction	2/12/26	4.35					2/6/26	Cover Compaction	2/27/26	2.7					
184	Y6	CV-2311	34.43631	-118.64989	2/3/26	9:33	546	2/5/26	Cover Compaction; Boot Repaired	2/12/26	6.26					2/5/26	Cover Compaction; Boot Repaired	2/27/26	2.5					
184	Y7	Surface	34.43622	-118.64962	2/3/26	9:38	5,421	2/5/26	Flow Increase	2/12/26	4.28					2/5/26	Flow Increase	2/27/26	3					
179	Y8	4-in 90 fittng near CV-24033	34.43577	-118.64975	2/3/26	9:46	1,245	2/6/26	Cover Compaction	2/12/26	4.34					2/6/26	Cover Compaction	2/27/26	2.8					
179	Y9	CV-24026	34.43567	-118.64926	2/3/26	9:50	543	2/6/26	Inspected; 2/12/26 reconnected well	2/12/26	5.31					2/6/26	Inspected; 2/12/26 reconnected well	2/27/26	5.1					
179	Y10	Surface	34.43567	-118.64926	2/3/26	9:51	4,123	2/6/26	Flow Increase	2/12/26	5.21					2/6/26	Flow Increase	2/27/26	3.9					
178	Y11	CV-2308	34.43588	-118.64890	2/3/26	9:59	4,128	2/5/26	Boot Repaired	2/12/26	4.8					2/5/26	Boot Repaired	2/27/26	2.9					
178	Y12	CV-24027	34.43612	-118.64872	2/3/26	10:00	1,359	2/6/26	New liner being installed	2/12/26	4.42					2/6/26	New liner being installed	2/27/26	3.6					
185	Y13	CV-24022	34.43650	-118.64882	2/3/26	10:05	1,723	2/5/26	Cover Compaction; 2/10/26 Reconnected Well	2/12/26	4.58					2/5/26	Cover Compaction; 2/10/26 Reconnected Well	2/27/26	6.8					
185	Y14	CV-24013	34.43658	-118.64923	2/3/26	10:09	523	2/6/26	New liner being installed	2/12/26	4.5					2/6/26	New liner being installed	2/27/26	2.7					
185	Y15	CV-24014	34.43674	-118.64895	2/3/26	10:14	529	2/6/26	New liner being installed	2/12/26	4.8					2/6/26	New liner being installed	2/27/26	7.3					
93	B121	HV-044A	34.43095	-118.64407	2/3/26	9:38	334	2/4/26	Flow Increase	2/12/26	57.59													
91	B122	South Manifold Pump 1	34.43152	-118.64437	2/3/26	9:55	376	2/4/26	Flow Increase	2/12/26	125													

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
182	B1	CV-24141	34.43550	-118.65132	2/3/26	8:24	223	2/4/26	Flow Increase	2/12/26	24.52													
220	B29	CV-24023	34.43056	-118.65024	2/3/26	8:26	400	2/4/26	Flow Increase	2/12/26	9.04													
227	B30	H-2401N	34.42944	-118.65106	2/3/26	9:24	300	2/4/26	Flow Increase	2/12/26	154													
175	B2	Surface	34.43574	-118.64950	2/3/26	9:48	200	2/4/26	Flow Increase	2/12/26	4.56													
79	Y121	Force main on east perimeter	34.43767	-118.64431	2/10/26	10:29	10,000	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	58					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	22.1					
80	Y122	H-01	34.43767	-118.64416	2/10/26	9:25	10,000	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	60.13					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	117					
171	Y41	CV-24061	34.43434	-118.64862	2/10/26	8:10	937	2/11/26	Flow Increase	2/20/26	5.33					2/11/26	Flow Increase	3/4/26	16.2					
173	Y42	CV-24044	34.43439	-118.64939	2/10/26	8:26	767	2/11/26	Flow Increase	2/20/26	90.41					2/11/26	Flow Increase	3/4/26	21.5					
175	Y43	CV-2338	34.43487	-118.65050	2/10/26	8:58	988	2/11/26	Flow Increase	2/20/26	42.11					2/11/26	Flow Increase	3/4/26	14.3					
181	Y2	Near CV-2352	34.43494	-118.65094	2/10/26	10:13	5,695	2/11/26	Flow Increase	2/20/26	4.34					2/11/26	Flow Increase	3/4/26	6.3					
180	Y4	Lorentz panel near CV-2338	34.43535	-118.65051	2/10/26	10:24	1,043	2/11/26	Flow Increase; 2/23/26 Boot Repaired	2/20/26	15.22					2/11/26	Flow Increase; 2/23/26 Boot Repaired	3/4/26	470					
180	Y5	2 inch steel pipe	34.43532	-118.65031	2/10/26	10:26	1,506	2/11/26	Flow Increase; 2/23/26 Taped Pipe	2/20/26	3.86					2/11/26	Flow Increase; 2/23/26 Taped Pipe	3/4/26	8.3					
179	Y6	CV-2303	34.43543	-118.64969	2/10/26	10:32	633	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	31.25					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	63.7					
179	Y7	CV-24033	34.43540	-118.64946	2/10/26	10:34	607	2/11/26	Flow Increase	2/20/26	17.64					2/11/26	Flow Increase	3/4/26	104					
178	Y8	CV-24040	34.43567	-118.64839	2/10/26	10:43	801	2/11/26	Flow Increase	2/20/26	10.28					2/11/26	Flow Increase	3/4/26	482					
178	Y9	CV-24027	34.43615	-118.64872	2/10/26	10:49	789	2/11/26	Flow Increase; Boot Repaired	2/20/26	4.03					2/11/26	Flow Increase; Boot Repaired	3/4/26	5					
172	Y21	CV-2304	34.43456	-118.64876	2/10/26	8:08	2,148	2/11/26	Flow Increase	2/20/26	3.61					2/11/26	Flow Increase	3/4/26	19.1					
172	Y22	CV-24045	34.43475	-118.64906	2/10/26	8:10	1,192	2/11/26	Flow Increase	2/20/26	5.07					2/11/26	Flow Increase	3/4/26	12.8					
156	Y23	CV-24039	34.43528	-118.64870	2/10/26	8:17	527	2/11/26	Flow Increase	2/20/26	22.54					2/11/26	Flow Increase	3/4/26	463					
158	Y24	CV-24073	34.43465	-118.64771	2/10/26	8:34	723	2/11/26	Flow Increase; Boot Repaired	2/20/26	4.88					2/11/26	Flow Increase; Boot Repaired	3/4/26	4.9					
153	Y25	FP-050	34.43490	-118.64725	2/10/26	8:39	4,213	2/11/26	Flow Increase	2/20/26	3.65					2/11/26	Flow Increase	3/4/26	4.9					
153	Y26	CV-24149	34.43480	-118.64696	2/10/26	8:48	527	2/11/26	Flow Increase	2/20/26	4.73					2/11/26	Flow Increase	3/4/26	4.8					
148	Y27	CV-24148	34.43507	-118.64668	2/10/26	8:52	757	2/11/26	Flow Increase	2/20/26	3.61					2/11/26	Flow Increase	3/4/26	7.1					
78	Y28	Near CV-2563	34.43729	-118.64604	2/10/26	9:35	4,856	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	8.42					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	14.7					
178	Y29	CV-48R	34.43733	-118.64585	2/10/26	9:41	821	2/11/26	Flow Increase	2/20/26	165					2/11/26	Flow Increase	3/4/26	33.2					
82	Y61	CV-2549	34.43438	-118.64527	2/10/26	8:40	561	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	4.42					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	6.7					
82	Y62	CV-2548	34.43435	-118.64557	2/10/26	8:46	2,584	2/11/26	Flow Increase	2/20/26	4.54					2/11/26	Flow Increase	3/4/26	5.6					
83	Y63	H-1804B	34.43425	-118.64564	2/10/26	8:52	1,202	2/11/26	Flow Increase	2/20/26	4.28					2/11/26	Flow Increase	3/4/26	277					
149	Y64	CV-24154	34.43427	-118.64609	2/10/26	8:57	4,391	2/11/26	Flow Increase	2/20/26	3.67					2/11/26	Flow Increase	3/4/26	6					
154	Y65	CV-24152	34.43435	-118.64710	2/10/26	9:13	3,499	2/11/26	Flow Increase; Boot Repaired	2/20/26	3.59					2/11/26	Flow Increase; Boot Repaired	3/4/26	5.6					
154	Y66	CV-2544	34.43403	-118.64723	2/10/26	9:19	4,563	2/11/26	Flow Increase	2/20/26	3.5					2/11/26	Flow Increase	3/4/26	5.8					
159	Y67	H-1952S	34.43382	-118.64764	2/10/26	9:29	633	2/11/26	Flow Increase	2/20/26	3.72					2/11/26	Flow Increase	3/4/26	5					
155	Y68	CV-24160	34.43380	-118.64627	2/10/26	9:39	3,884	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	7.6					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	137					
83	Y69	Surface	34.43406	-118.64567	2/10/26	9:48	1,124	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	9.23					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	14.2					
90	Y70	CV-24171	34.43317	-118.64665	2/10/26	9:55	1,071	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	6.86					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	9.4					
160	Y71	CV-24207	34.43328	-118.64694	2/10/26	10:00	3,637	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	3.75					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	12					
160	Y72	H-1408E	34.43335	-118.64717	2/10/26	10:06	7,279	2/11/26	Flow Increase	2/20/26	3.78					2/11/26	Flow Increase	3/4/26	7.2					
160	Y73	CV-24168	34.43331	-118.64733	2/10/26	10:10	4,982	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	3.64					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	10.8					
163	Y74	H-1760S	34.43277	-118.64789	2/10/26	10:28	635	2/11/26	Flow Increase	2/20/26	4.21					2/11/26	Flow Increase	3/4/26	16.1					
89	Y75	Surface	34.43265	-118.64629	2/10/26	10:43	1,053	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	3.35					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/4/26	15.6					
88	Y76	H-2275E	34.43242	-118.64621	2/10/26	10:48	978	2/11/26	Flow Increase	2/20/26	3.77					2/11/26	Flow Increase	3/4/26	22.3					
170	B41	CV-2553	34.43419	-118.64891	2/10/26	8:20	462	2/11/26	Flow Increase	2/20/26	4.91													
181	B1	Surface	34.43499	-118.65097	2/10/26	10:11	205	2/11/26	Flow Increase	2/20/26	5.66													
180	B3	CV-2337	34.43550	-118.65078	2/10/26	10:20	243	2/11/26	Flow Increase	2/20/26	4.08													
156	B21	CV-24010	34.43566	-118.64838	2/10/26	8:24	200	2/11/26	Flow Increase	2/20/26	9.12													
212	Y21	CV-2565	34.43199	-118.64902	2/13/26	7:41	920	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	72.5					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/11/26	30.2					
196	Y22	CV-24195	34.43182	-118.64788	2/13/26	7:57	5,231	2/11/26	Flow Increase	2/20/26	19.7					2/11/26	Flow Increase	3/11/26	11.4					
196	Y23	CV-24104	34.43177	-118.64804	2/13/26	8:00	4,213	2/11/26	Flow Increase	2/20/26	23.9					2/11/26	Flow Increase	3/11/26	26.3					
214	Y41	H-104A	34.43108	-118.65022	2/13/26	8:08	1,590	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	210					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/11/26	166					
215	Y42	H-2059W	34.43111	-118.65057	2/13/26	8:14	5,762	2/11/26	Flow Increase	2/20/26	179					2/11/26	Flow Increase	3/11/26	213					
217	Y81	CV-24114	34.43076	-118.64853	2/13/26	7:57	825	2/11/26	Flow Increase; 2/23/26 Cover Compaction	2/20/26	24.7					2/11/26	Flow Increase; 2/23/26 Cover Compaction	3/11/26	16.6					
77	Y1	CV-48R	34.43737	-118.64679	2/20/26	9:49	526	2/24/26	Flow Increase	2/27/26	17.4					2/24/26	Flow Increase	3/20/26	414					
78	Y2	CV-2563	34.43732	-118.64580	2/20/26	10:00	946	2/23/26	Cover Compaction; Flow Increase	2/27/26	21.8					2/23/26	Cover Compaction; Flow Increase	3/20/26	152					
32	Y61	CV-24110	34.43471	-118.64467	2/20/26	8:10	750	2/24/26	Flow Increase	2/27/26	31.4					2/24/26	Flow Increase	3/20/26	12.2					
36	Y62	H-2168E	34.43448	-118.64383	2/20/26	9:22	800	2/24/26	Flow Increase	2/27/26	125					2/24/26	Flow Increase	3/20/26	71.2					
90	Y81	CV-24092	34.43333	-118.64614	2/20/26	9:28	3,659	2/24/26	Flow Increase	2/27/26	319					2/24/26	Flow Increase	3/20/26	8.6					
212	Y82	CV-2565	34.43201	-118.64899	2/20/26	10:50	1,265	2/23/26	Cover Compaction; Flow Increase	2/27/26	8.5					2/23/26	Cover Compaction; Flow Increase	3/20/26	14.1					
84	Y101	CV-1905	34.43350	-118.64597	2/20/26	8:07	887	2/23/26	Flow Increase	2/27/26	42.4					2/23/26	Flow Increase	3/20/26	67.4					
38	Y103	CV-24118	34.43331	-118.64384	2/20/26	8:28	1,326	2/24/26	Cover Compaction; Flow Increase	2/27/26	47.7					2/24/26	Cover Compaction; Flow Increase	3/20/26	54.6					
215	Y161	2 inch steel pipe	34.43117	-118.65037	2/20/26	9:15	2,361	2/24/26	Cover Compaction	2/27/26	313					2/24/26	Cover Compaction	3/20/26	412					
215	Y162	Surface	34.43144	-118.65062	2/20/26	9:26	1,078	2/24/26	Cover Compaction	2/27/26	240					2/24/26	Cover Compaction	3/20/26	121					
84	B102	H-1764N	34.43316	-118.64561	2/20/26	8:11	304	2/27/26	Flow Increase	2/27/26	13.6													
218	B104	CV-1701S	34.43362	-118.64335	2/20/26	8:33	218	2/27/26	Flow Increase	2/27/26	24.6													
42	B105	CV-24119	34.43372	-118.64234	2/20/26	8:42	204	2/27/26	Flow Increase	2/27/26	109													
196	B221	Surface	34.43154	-118.64785	2/21/26	8:28	320	2/27/26	Flow Increase	2/27/26	14.8													
244	Y241	Near CV-24244	34.42889	-118.65133	2/21/26	9:08	625	2/24/26	Added Dirt; Cover Compaction; Flow Increase	2/27/26	112					2/24/26	Added Dirt; Cover Compaction; Flow Increase	3/19/26	88.1					
210	Y61	Near Sump CWHSMP01	34.43163	-118.65071	3/10/26	8:11	612	3/12/26	Cover Compaction	3/19/26	247					3/12/26	Cover Compaction	4/9/26	109					
215	Y62	H-104A	34.43111	-118.65059	3/10/26	8:25	500	3/12/26	Cover Compaction	3/19/26	137					3/12/26	Cover Compaction	4/9/26	217					
211	Y63	CV-24100	34.43204	-118.65048	3/10/26	8:47	652	3/12/26	Flow Increase; Boot Repaired	3/19/26	206					3/12/26	Flow Increase; Boot Repaired	4/9/26	64.1					
196	Y64	Temperature Probe TP-28	34.43191	-118.64835	3/10/26	9:38	1,123	3/12/26	Cover Compaction	3/19/26	110					3/12/26	Cover Compaction	4/9/26	33.7					
163	Y65	H-1760S	34.43273	-118.64791	3/10/26	10:05	1,112	3/12/26	Cover Compaction; Flow Increase	3/19/26	24.7					3/12/26	Cover Compaction; Flow Increase	4/9/26	13.9					
163	Y66	CV-24090	34.43271	-118.64756	3/10/26	10:22	1,845	3/12/26	Cover Compaction; Flow Increase	3/19/26	114					3/12/26	Cover Compaction; Flow Increase	4/9/26	40.6					
162	Y67	CV-24106	34.43215	-118.64673	3/10/26	10:48	650	3/12/26	Flow Increase	3/19/26	462					3/12/26	Flow Increase	4/9/26	313					
194	Y81	CV-24116	34.43166	-118.64572	3/10/26	8:54	554	3/12/26	Cover Compaction; Flow Increase	3/19/26	130					3/12/26	Cover Compaction; Flow Increase	4/9/26	19.2					
194	Y82	Surface	34.43127	-118.64546	3/10/26	9:02	20,000	3/12/26	Cover Compaction	3/19/26	364					3/12/26	Cover Compaction	4/9/26	466					
96	Y83	CV-2536	34.43102	-118.64588	3/10/26	9:07	674	3/13/26	Cover Compaction	3/19/26	229					3/13/26	Cover Compaction	4/9/26	26.2					

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
150	Y1	CV-24034	34.43613	-118.64812	3/10/26	9:58	2,789	3/12/26	Cover Compaction	3/19/26	91.1					3/12/26	Cover Compaction	4/9/26	17.9					
77	Y2	CV-24122	34.43718	-118.64665	3/10/26	10:41	3,646	3/12/26	Boot Repaired	3/19/26	33.9					3/12/26	Boot Repaired	4/9/26	10.1					
77	Y3	Sump CCNSMP01	34.43736	-118.64676	3/10/26	10:56	4,227	3/12/26	Cover Compaction	3/19/26	119					3/12/26	Cover Compaction	4/9/26	317					
78	Y4	CV-2563	34.43730	-118.64580	3/10/26	11:03	4,986	3/12/26	Flow Increase	3/19/26	262					3/12/26	Flow Increase	4/9/26	90.6					
156	Y21	Reaction Area Sump 3	34.43543	-118.64836	3/10/26	10:02	800	3/12/26	Seal Repaired	3/19/26	5.4					3/12/26	Seal Repaired	4/9/26	8.3					
156	Y22	CV-24040	34.43564	-118.64839	3/10/26	10:04	900	3/12/26	Attempted to restore system vacuum; 3/16/26 Flow Increase	3/19/26	257					3/12/26	Attempted to restore system vacuum; 3/16/26 Flow Increase	4/9/26	12.4					
177	Y23	CV-24039	34.43528	-118.64881	3/10/26	10:31	1,200	3/12/26	Boot Repaired	3/19/26	298					3/12/26	Boot Repaired	4/9/26	11.9					
215	B61	Surface	34.43110	-118.65056	3/10/26	8:28	243	3/19/26	Flow Increase	3/19/26	119													
211	B62	CV-24101	34.43183	-118.65030	3/10/26	8:42	245	3/19/26	Flow Increase	3/19/26	127													
211	B63	Surface	34.43186	-118.65027	3/10/26	8:44	232	3/19/26	Flow Increase	3/19/26	97.3													
194	B81	Surface	34.43125	-118.64557	3/10/26	8:59	291	3/19/26	Flow Increase	3/19/26	17.4													
77	Y41	2" steel pipe next to Hero Sump	34.43736	-118.64677	3/17/26	9:39	3,421	3/18/26	Cover Compaction	3/27/26	116					3/18/26	Cover Compaction	4/16/26	209					
78	Y42	Electricity pole near Hero Flare	34.43774	-118.64682	3/17/26	9:43	700	3/18/26	Cover Compaction	3/27/26	4.8					3/18/26	Cover Compaction	4/16/26	6.2					
78	Y43	CV-24146	34.43742	-118.64639	3/17/26	9:48	832	3/18/26	Cover Compaction; Flow Increase	3/27/26	26.6					3/18/26	Cover Compaction; Flow Increase	4/16/26	49.1					
78	Y44	CV-24123	34.43733	-118.64626	3/17/26	9:50	2,413	3/18/26	Flow Increase	3/27/26	54.1					3/18/26	Flow Increase	4/16/26	30.8					
78	Y45	CV-48R	34.43733	-118.64587	3/17/26	9:52	848	3/18/26	Flow Increase	3/27/26	396					3/18/26	Flow Increase	4/16/26	251					
78	Y46	CV-2563	34.43733	-118.64579	3/17/26	9:54	845	3/18/26	Flow Increase	3/27/26	131					3/18/26	Flow Increase	4/16/26	396					
83	Y61	H-1804B	34.43420	-118.64565	3/17/26	8:46	900	3/18/26	Cover Compaction; Flow Increase	3/27/26	76.8					3/18/26	Cover Compaction; Flow Increase	4/16/26	182					
155	Y62	CV-24160	34.43378	-118.64636	3/17/26	8:54	550	3/19/26	Flow Increase	3/27/26	35.1					3/19/26	Flow Increase	4/16/26	494					
90	Y63	Zeeco Sump	34.43341	-118.64651	3/17/26	9:00	640	3/19/26	Cover Compaction	3/27/26	12.2					3/19/26	Cover Compaction	4/16/26	6.2					
163	Y64	CV-24090	34.43262	-118.64755	3/17/26	9:50	1,000	3/19/26	Flow Increase	3/27/26	116					3/19/26	Flow Increase	4/16/26	20					
83	Y66	CV-24161	34.43379	-118.64564	3/17/26	10:18	720	3/18/26	Cover Compaction	3/27/26	20.9					3/18/26	Cover Compaction	4/16/26	9.2					
156	Y22	Reaction Area Sump 3	34.43537	-118.64834	3/17/26	8:29	6,946	3/18/26	Seal Repaired	3/27/26	3.8					3/18/26	Seal Repaired	4/16/26	10.8					
177	Y23	CV-24039	34.43528	-118.64868	3/17/26	8:35	1,897	3/18/26	Flow Increase	3/27/26	64.7					3/18/26	Flow Increase	4/16/26	399					
172	Y24	Reaction Area Sump 4	34.43475	-118.64847	3/17/26	8:43	4,996	3/19/26	Cover Compaction	3/27/26	4.1					3/19/26	Cover Compaction	4/16/26	3.9					
172	Y25	CV-24045	34.43476	-118.64906	3/17/26	8:52	4,368	3/18/26	Cover Compaction; Boot Repaired	3/27/26	5.3					3/18/26	Cover Compaction; Boot Repaired	4/16/26	5.6					
173	Y27	CV-24036	34.43449	-118.64973	3/17/26	9:28	20,000	3/19/26	Flow Increase	3/27/26	145					3/19/26	Flow Increase	4/16/26	3.8					
175	Y28	CV-2338	34.43488	-118.65049	3/17/26	9:38	1,684	3/19/26	Cover Compaction	3/27/26	8.7					3/19/26	Cover Compaction	4/16/26	27.3					
160	B65	CV-24164	34.43327	-118.64733	3/17/26	10:02	350	3/27/26	Flow Increase	3/27/26	79.1													
156	B21	CV-24040	34.43566	-118.64837	3/17/26	8:23	378	3/27/26	Flow Increase	3/27/26	16.6													
177	B26	Reaction Area Sump 2	34.43553	-118.64888	3/17/26	8:59	483	3/27/26	Flow Increase	3/27/26	12.2													
182	Y11	CV-24141	34.43551	-118.65131	3/19/26	8:32	760	3/20/26	Cover Compaction	3/27/26	102					3/20/26	Cover Compaction	4/16/26	47.7					
181	Y21	CV-2337	34.43547	-118.65079	3/19/26	8:34	4,821	3/20/26	Cover Compaction	3/27/26	115					3/20/26	Cover Compaction	4/16/26	306					
181	Y22	CV-2352	34.43490	-118.65105	3/19/26	8:39	2,410	3/20/26	Cover Compaction	3/27/26	417					3/20/26	Cover Compaction	4/16/26	441					
180	Y23	CV-24018	34.43562	-118.65006	3/19/26	8:45	675	3/20/26	Cover Compaction	3/27/26	4.9					3/20/26	Cover Compaction	4/16/26	463					
180	Y24	FP-033	34.43539	-118.64993	3/19/26	8:48	1,180	3/20/26	Cover Compaction; Flow Increase	3/27/26	3.8					3/20/26	Cover Compaction; Flow Increase	4/16/26	4.5					
178	Y25	CV-2308	34.43590	-118.64892	3/19/26	8:53	2,780	3/20/26	Cover Compaction; Flow Increase	3/27/26	5.4					3/20/26	Cover Compaction; Flow Increase	4/16/26	5.7					
163	Y61	H-1760S	34.43274	-118.64790	3/23/26	9:06	500	3/24/26	Flow Increase	4/2/26	64.1					3/24/26	Flow Increase	4/21/26	52.8					
83	Y62	Surface	34.43383	-118.64635	3/23/26	9:42	1,500	3/27/26	Flow Increase	4/2/26	32.3					3/27/26	Flow Increase	4/21/26	427					
156	Y21	Reaction Area Sump 3	34.43537	-118.64834	3/23/26	9:14	30,000	3/25/26	Cover Compaction	4/2/26	5.9					3/25/26	Cover Compaction	4/21/26	7.4					
157	Y22	CV-24046	34.43510	-118.64840	3/23/26	9:25	50,000	3/26/26	Boot Repaired	4/2/26	5.8					3/26/26	Boot Repaired	4/21/26	5.3					
172	Y23	Reaction Area Sump 4	34.43478	-118.64848	3/23/26	9:30	50,000	3/25/26	Well Repaired	4/2/26	6.3					3/25/26	Well Repaired	4/21/26	12.3					
158	Y24	CV-2555	34.43484	-118.64771	3/23/26	9:47	2,759	3/24/26	Well Repaired	4/2/26	74.4					3/24/26	Well Repaired	4/21/26	119					
173	Y25	CV-24044	34.43442	-118.64940	3/23/26	10:14	5,781	3/25/26	Cover Compaction	4/2/26	57.7					3/25/26	Cover Compaction	4/21/26	84.6					
173	Y26	CV-24037	34.43477	-118.64944	3/23/26	10:21	2,539	3/25/26	Flow Increase	4/2/26	477					3/25/26	Flow Increase	4/21/26	489					
175	Y27	CV-2338	34.43488	-118.65048	3/23/26	10:32	1,855	3/26/26	Cover Compaction	4/2/26	6.4					3/26/26	Cover Compaction	4/21/26	6.1					
175	Y28	CV-1902A	34.43464	-118.65029	3/23/26	10:37	4,198	3/26/26	Cover Compaction	4/2/26	14.8					3/26/26	Cover Compaction	4/21/26	10.9					
182	Y1	CV-24141	34.43554	-118.65132	3/23/26	9:22	973	3/26/26	Cover Compaction	4/2/26	12.6					3/26/26	Cover Compaction	4/21/26	29.3					
183	Y2	CV-24016	34.43593	-118.65027	3/23/26	9:36	2,813	3/26/26	Cover Compaction	4/2/26	5.9					3/26/26	Cover Compaction	4/21/26	4.3					
185	Y3	CV-24014	34.43678	-118.64896	3/23/26	9:57	640	3/26/26	Flow Increase	4/2/26	6.1					3/26/26	Flow Increase	4/21/26	4.4					
178	Y4	CV-24027	34.43614	-118.64872	3/23/26	10:02	1,081	3/25/26	Boot Repaired	4/2/26	5.8					3/25/26	Boot Repaired	4/21/26	4.6					
178	Y5	CV-24021	34.43617	-118.64904	3/23/26	10:07	870	3/25/26	Boot Repaired	4/2/26	6.2					3/25/26	Boot Repaired	4/21/26	5.1					
178	Y6	CV-2308	34.43593	-118.64892	3/23/26	10:06	20,000	3/25/26	Boot Repaired	4/2/26	10.5					3/25/26	Boot Repaired	4/21/26	13.3					
178	Y7	CV-2206	34.43609	-118.64842	3/23/26	10:11	2,028	3/25/26	Cover Compaction	4/2/26	9.8					3/25/26	Cover Compaction	4/21/26	7.7					
179	Y8	CV-24026	34.43570	-118.64926	3/23/26	10:17	3,800	3/25/26	Flow Increase	4/2/26	9.4					3/25/26	Flow Increase	4/21/26	6.8					
179	Y9	CV-24020	34.43601	-118.64937	3/23/26	10:20	1,756	3/26/26	Well Repaired	4/2/26	6.3					3/26/26	Well Repaired	4/21/26	4.9					
179	Y10	FP-023	34.43592	-118.64954	3/23/26	4:53	1,551	3/25/26	Flow Increase	4/2/26	5.9					3/25/26	Flow Increase	4/21/26	9.4					
179	Y11	Panel near CV-24019	34.43583	-118.64976	3/23/26	10:31	10,500	3/25/26	Boot Repaired	4/2/26	6.1					3/25/26	Boot Repaired	4/21/26	7.6					
180	Y12	CV-24018	34.43564	-118.65005	3/23/26	10:35	657	3/26/26	Cover Compaction	4/2/26	15					3/26/26	Cover Compaction	4/21/26	24.3					
180	Y13	Surface	34.43532	-118.65045	3/23/26	10:40	50,000	3/27/26	Liner Repaired	4/2/26	28710	4/8/26	Flow Increase	4/9/26 9:08	417	4/8/26	Flow Increase	4/21/26	491					
181	Y14	CV-2352	34.43491	-118.65103	3/23/26	10:47	6,580	3/26/26	Cover Compaction	4/2/26	13.4					3/26/26	Cover Compaction	4/21/26	20.3					
181	Y15	H-1774B	34.43513	-118.65091	3/23/26	10:51	1,456	3/27/26	Boot Repaired	4/2/26	6.9					3/27/26	Boot Repaired	4/21/26	17.9					
96	Y16	Surface	34.43100	-118.64592	3/23/26	11:32	978	3/27/26	Cover Compaction	4/2/26	110					3/27/26	Cover Compaction	4/21/26	183					
77	Y41	Panel near CV-113	34.43699	-118.64672	3/23/26	10:14	4,932	3/24/26	Sealed Support	4/2/26	236					3/24/26	Sealed Support	4/21/26	311					
77	Y42	2" steel pipe	34.43711	-118.64676	3/23/26	10:20	2,623	3/24/26	Boot Repaired	4/2/26	427					3/24/26	Boot Repaired	4/21/26	456					
77	Y43	2" steel pipe	34.43711	-118.64685	3/23/26	10:22	726	3/24/26	Boot Repaired	4/2/26	16.4					3/24/26	Boot Repaired	4/21/26	23.6					
77	Y44	Surface	34.43722	-118.64690	3/23/26	10:23	2,845	3/24/26	Liner Repaired	4/2/26	160					3/24/26	Liner Repaired	4/21/26	114					
78	Y45	HERO TOx Sump	34.43736	-118.64674	3/23/26	10:25	1,822	3/24/26	Cover Compaction	4/2/26	7989	4/7/26	Installed bentonite plug around sump	4/9/26 9:33	317	4/7/26	Installed bentonite plug around sump	4/21/26	472					
78	Y46	CV-48R	34.43735	-118.64585	3/23/26	10:28	515	3/24/26	Flow Increase	4/2/26	76.6					3/24/26	Flow Increase	4/21/26	94.3					
183	B1	CV-1901	34.43572	-118.65079	3/23/26	9:38	265	4/2/26	Flow Increase	4/2/26	6					4/2/26	Flow Increase							
155	Y81	CV-24160	34.43389	-118.64631	4/8/26	8:28	690	4/13/26	Flow Increase	4/16/26	494.0					4/13/26	Flow Increase	5/7/26	43.5					
90	Y82	Zeeco Sump	34.43331	-118.64652	4/8/26	8:36	720	4/13/26	Added dirt; Cover Compaction	4/16/26	6.2					4/13/26	Added dirt; Cover Compaction	5/7/26	113					
160	Y83	CV-24107	34.43321	-118.64707	4/8/26	8:42	550	4/13/26	Cover Compaction	4/16/26	6.8					4/13/26	Monitored well and compacted dirt	5/7/26	12.24					
165	Y84	CV-24170	34.43306	-118.64853	4/8/26	8:52	800	4/13/26	Flow Increase	4/16/26	4.5					4/13/26	Flow Increase	5/7/26	244					
164	Y85	CV-24175	34.43264	-118.64861	4/8/26	8:58	900	4/14/26	Flow Increase	4/16/26	4.1					4/14/26	Flow Increase	5/7/26	10.94					

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
209	Y86	CV-24085	34.43241	-118.64919	4/8/26	9:14	520	4/13/26	Flow Increase; Well Repaired	4/16/26	4.4					4/13/26	Flow Increase; Well Repaired	5/7/26	27.22					
163	Y87	CV-24089	34.43236	-118.64798	4/8/26	9:26	1,000	4/13/26	Cover Compaction	4/16/26	4.1					4/13/26	Cover Compaction	5/7/26	127					
161	Y88	CV-24184	34.43249	-118.64716	4/8/26	9:29	1,500	4/14/26	Flow Increase	4/16/26	5.5					4/14/26	Flow Increase	5/7/26	12.4					
162	Y89	CV-24196	34.43202	-118.64715	4/8/26	9:41	800	4/13/26	Flow Increase	4/16/26	4.9					4/13/26	Flow Increase	5/7/26	31.66					
76	Y41	CV-24135	34.43642	-118.64599	4/8/26	8:21	1,712	4/10/26	Flow Increase; 4/13/26: Well Repaired	4/16/26	4.6					4/10/26	Flow Increase; 4/13/26: Well Repaired	5/7/26	4.78					
76	Y42	CV-24134	34.43639	-118.64651	4/8/26	8:42	638	4/13/26	Flow Increase; Well Repaired	4/16/26	4.6					4/13/26	Flow Increase; Well Repaired	5/7/26	7					
66	Y43	CV-2316	34.43607	-118.64638	4/8/26	8:51	1,541	4/10/26	Flow Increase	4/16/26	12.8					4/10/26	Flow Increase	5/7/26	5.23					
157	Y44	CV-24046	34.43510	-118.64838	4/8/26	9:18	3,891	4/13/26	Well Repaired	4/16/26	3.8					4/13/26	Well Repaired	5/7/26	5.59					
172	Y45	Reaction Area Sump 4	34.43475	-118.64845	4/8/26	9:24	10,000	4/14/26	Boot Repaired	4/16/26	3.9					4/14/26	Boot Repaired	5/7/26	11.22					
173	Y46	CV-24044	34.43441	-118.64941	4/8/26	9:35	20,000	4/14/26	Cover Compaction; Flow Increase	4/16/26	253.0					4/14/26	Cover Compaction; Flow Increase	5/7/26	33.75					
173	Y47	CV-24036	34.43450	-118.64971	4/8/26	9:49	20,000	4/14/26	Cover Compaction	4/16/26	3.8					4/14/26	Cover Compaction	5/7/26	33.48					
215	Y48	H-102A	34.43113	-118.65058	4/8/26	10:30	5,971	4/14/26	Flow Increase	4/16/26	472.0					4/14/26	Flow Increase	5/7/26	82.8					
198	Y101	CV-24181	34.43219	-118.64840	4/8/26	8:18	850	4/13/26	Cover Compaction; Flow Increase	4/16/26	4.3					4/13/26	Cover Compaction; Flow Increase	5/7/26	22.61					
199	Y102	CV-1601S	34.43115	-118.64869	4/8/26	8:51	640	4/14/26	Cover Compaction	4/16/26	253.0					4/14/26	Cover Compaction	5/7/26	28.3					
99	Y103	CV-2535	34.43097	-118.64694	4/8/26	9:33	900	4/14/26	Flow Increase	4/16/26	197.0					4/14/26	Flow Increase	5/7/26	72.8					
175	Y21	Surface	34.43455	-118.65080	4/8/26	8:23	500	4/14/26	Sealed Support	4/16/26	4.8					4/14/26	Sealed Support	5/7/26	4.74					
175	Y22	Surface	34.43476	-118.65072	4/8/26	8:29	4,823	4/14/26	Sealed Support	4/16/26	5.6					4/14/26	Sealed Support	5/7/26	119					
181	Y23	CV-2352	34.43490	-118.65107	4/8/26	8:33	523	4/14/26	Cover Compaction	4/16/26	441.0					4/14/26	Cover Compaction	5/7/26	5.43					
181	Y24	Above CV-2006	34.43532	-118.65048	4/8/26	8:50	2,282	4/14/26	Flow Increase	4/16/26	493.0					4/14/26	Flow Increase	5/7/26	50.35					
176	Y25	Surface	34.43502	-118.65027	4/8/26	8:56	563	4/14/26	Sealed Support	4/16/26	14.7					4/14/26	Sealed Support	5/7/26	26.55					
176	Y26	Surface	34.43492	-118.65022	4/8/26	8:58	982	4/14/26	Sealed Support	4/16/26	4.4					4/14/26	Sealed Support	5/7/26	4.66					
176	Y27	Surface	34.43502	-118.65018	4/8/26	8:59	4,521	4/14/26	Sealed Support	4/16/26	13.2					4/14/26	Sealed Support	5/7/26	12.91					
177	Y28	CV-24040	34.43552	-118.64887	4/8/26	9:38	523	4/14/26	Attempted to dewater lateral	4/16/26	406.0					4/14/26	Attempted to dewater lateral	5/7/26	14.17					
156	Y29	Reaction Area Sump 2	34.43565	-118.64838	4/8/26	9:44	5,721	4/14/26	Sealed Support	4/16/26	3.8					4/14/26	Sealed Support	5/7/26	25.72					
151	Y30	CV-24041	34.43587	-118.64809	4/8/26	9:48	505	4/13/26	Attempted to dewater lateral	4/16/26	4.0					4/13/26	Attempted to dewater lateral	5/7/26	25.99					
151	Y31	2-inch steel pipe support	34.43576	-118.64746	4/8/26	9:52	7,512	4/14/26	Tightened clamp	4/16/26	3.6					4/14/26	Tightened clamp	5/7/26	6.45					
146	Y32	CV-24049	34.43597	-118.64722	4/8/26	9:56	562	4/13/26	Flow Increase	4/16/26	4.0					4/13/26	Flow Increase	5/7/26	9.04					
146	Y33	Surface	34.43598	-118.64717	4/8/26	9:58	8,421	4/13/26	Sealed Support	4/16/26	4.0					4/13/26	Sealed Support	5/7/26	6.53					
146	Y34	CV-25100D	34.43616	-118.64711	4/8/26	10:01	522	4/13/26	Boot Repaired	4/16/26	4.0					4/13/26	Boot Repaired	5/7/26	9.65					
150	Y35	Surface	34.43644	-118.64792	4/8/26	10:10	540	4/13/26	Sealed Support	4/16/26	3.7					4/13/26	Sealed Support	5/7/26	14.46					
78	Y36	CV-24123	34.43743	-118.64638	4/8/26	10:32	754	4/8/26	Flow Increase	4/16/26	10.6					4/8/26	Flow Increase	5/7/26	57.53					
78	Y37	CV-2563	34.43730	-118.64579	4/8/26	10:42	613	4/10/26	Flow Increase	4/16/26	456.0					4/10/26	Flow Increase	5/7/26	81.83					
78	Y38	CV-48R	34.43729	-118.64583	4/8/26	10:47	678	4/10/26	Flow Increase; 4/13/26: Cover Compaction	4/16/26	251.0					4/10/26	Flow Increase; 4/13/26: Cover Compaction	5/7/26	44.51					
79	Y39	CV-24147	34.43752	-118.64593	4/8/26	10:51	724	4/13/26	Cover Compaction; Flow Increase	4/16/26	483.0					4/13/26	Cover Compaction; Flow Increase	5/7/26	4.8					
80	Y40	Near North Sump 4	34.43770	-118.64416	4/8/26	10:59	1,437	4/13/26	Cover Compaction	4/16/26	473.0					4/13/26	Cover Compaction	5/7/26	25.68					
180	B1	CV-24018	34.43560	-118.65006	4/8/26	8:20	333	4/8/26	Flow Increase	4/16/26	194													
181	B22	Surface	34.43509	-118.65094	4/8/26	8:46	223	4/8/26	Flow Increase	4/16/26	6													
78	B23	CV-24014	34.43742	-118.64638	4/8/26	10:33	223	4/8/26	Flow Increase	4/16/26	11													
80	Y1	North Sump 4	34.43761	-118.64412	4/14/26	8:17	1,915	4/16/26	Tightened bolts	4/22/26	111					4/16/26	Tightened bolts	5/13/26	132					
71	Y2	C-20	34.43781	-118.64245	4/14/26	8:26	3,196	4/16/26	Cover Compaction; Flow Increase	4/22/26	309					4/16/26	Cover Compaction; Flow Increase	5/13/26	7.97					
58	Y3	Riser near C-26	34.43681	-118.64141	4/14/26	8:35	4,328	4/16/26	Cover Compaction	4/22/26	489					4/16/26	Cover Compaction	5/13/26	4.55					
58	Y4	C-26	34.43667	-118.64128	4/14/26	8:40	2,198	4/16/26	Flow Increase	4/22/26	167					4/16/26	Flow Increase	5/13/26	10.09					
65	Y5	C-15	34.43629	-118.64106	4/14/26	8:44	839	4/16/26	Cover Compaction and tightened clamps	4/22/26	44					4/16/26	Cover Compaction and tightened clamps	5/13/26	26.42					
65	Y6	C-27	34.43619	-118.64098	4/14/26	8:47	2,383	4/16/26	Cover Compaction	4/22/26	84					4/16/26	Cover Compaction	5/13/26	21.83					
65	Y7	C-12	34.43599	-118.64087	4/14/26	8:50	6,603	4/16/26	Cover Compaction; Flow Increase	4/22/26	74					4/16/26	Cover Compaction; Flow Increase	5/13/26	24.65					
51	Y8	CV-05	34.43286	-118.64223	4/14/26	9:23	3,836	4/15/26	Flow Increase	4/22/26	251					4/15/26	Flow Increase	5/13/26	23.15					
50	Y9	CV-06	34.43268	-118.64284	4/14/26	9:30	6,829	4/15/26	Flow Increase	4/22/26	299					4/15/26	Flow Increase	5/13/26	23.11					
39	Y10	CV-2530	34.43276	-118.64294	4/14/26	9:33	5,681	4/15/26	Cover Compaction; Flow Increase	4/22/26	426					4/15/26	Cover Compaction; Flow Increase	5/13/26	18.03					
50	Y11	CV-2531	34.43254	-118.64333	4/14/26	9:39	4,276	4/15/26	Cover Compaction	4/22/26	389					4/15/26	Cover Compaction	5/13/26	14.6					
38	Y13	CV-1701D	34.43362	-118.64334	4/14/26	9:55	5,026	4/17/26	Flow Increase	4/22/26	477					4/17/26	Flow Increase	5/13/26	30.12					
38	Y14	CV-1701S	34.43360	-118.64333	4/14/26	9:56	4,753	4/17/26	Flow Increase and tightened clamps	4/22/26	144					4/17/26	Flow Increase and tightened clamps	5/13/26	18.45					
38	Y15	CV-56D	34.43383	-118.64316	4/14/26	10:00	1,012	4/16/26	Cover Compaction and tightened clamps	4/22/26	72					4/16/26	Cover Compaction and tightened clamps	5/13/26	43.03					
38	Y16	CV-56S	34.43383	-118.64315	4/14/26	10:01	1,365	4/16/26	Tightened clamp	4/22/26	98					4/16/26	Tightened clamp	5/13/26	31.92					
36	Y17	H-2168E	34.43458	-118.64394	4/14/26	10:13	1,347	4/16/26	Flow Increase	4/22/26	90					4/16/26	Flow Increase	5/13/26	55.33					
37	Y18	CV-2205	34.43430	-118.64410	4/14/26	10:17	615	4/16/26	Flow Increase	4/22/26	125					4/16/26	Flow Increase	5/13/26	40.61					
37	Y19	H-2169E	34.43426	-118.64421	4/14/26	10:20	1,107	4/16/26	Flow Increase	4/22/26	98					4/16/26	Flow Increase	5/13/26	16.33					
77	Y42	North Sump 1	34.43703	-118.64694	4/14/26	10:38	1,500	4/16/26	Boot Repaired; tightened clamps	4/22/26	45					4/16/26	Boot Repaired; tightened clamps	5/13/26	13.2					
156	Y84	CV-24039	34.43529	-118.64869	4/14/26	8:48	2,770	4/16/26	Cover Compaction (liner installation)	4/22/26	179					4/16/26	Cover Compaction (liner installation)	5/13/26	15.88					
185	Y63	CV-24014	34.43679	-118.64894	4/14/26	8:32	515	4/16/26	Cover Compaction	4/22/26	64					4/16/26	Cover Compaction	5/13/26	2.96					
180	Y64	CV-24018	34.43564	-118.65007	4/14/26	9:16	6,000	4/16/26	Cover Compaction (liner installation)	4/22/26	467					4/16/26	Cover Compaction (liner installation)	5/13/26	5.3					
63	Y21	CV-2519	34.43618	-118.64205	4/14/26	8:38	500	4/16/26	Flow Increase	4/22/26	62					4/16/26	Flow Increase	5/13/26	12.86					
214	Y141	CV-24227	34.43098	-118.64980	4/15/26	8:42	521	4/17/26	Flow Increase	4/22/26	74.3					4/17/26	Flow Increase	5/14/26	15.18					
220	Y142	CV-24237	34.43064	-118.65020	4/15/26	8:50	2,206	4/17/26	Cover Compaction; Flow Increase	4/22/26	91.6					4/17/26	Cover Compaction; Flow Increase	5/14/26	18.64					
226	Y143	Near CV-24236	34.43017	-118.65041	4/15/26	8:58	770	4/17/26	Cover Compaction	4/22/26	61.4					4/17/26	Cover Compaction	5/14/26	11.33					
220	Y144	H-2057W	34.43068	-118.65064	4/15/26	9:04	4,323	4/17/26	Cover Compaction; Flow Increase	4/22/26	164					4/17/26	Cover Compaction; Flow Increase	5/14/26	5					
215	Y145	H-101W	34.43112	-118.65055	4/15/26	9:10	8,091	4/17/26	Flow Increase	4/22/26	319					4/17/26	Flow Increase	5/14/26	51.46					
215	Y146	Riser	34.43113	-118.65057	4/15/26	9:11	14,602	4/17/26	Cover Compaction	4/22/26	452					4/17/26	Cover Compaction	5/14/26	49.5					
215	Y147	H-102A	34.43113	-118.65057	4/15/26	9:11	12,909	4/17/26	Flow Increase	4/22/26	480					4/17/26	Flow Increase	5/14/26	81.12					
227	Y148	H-2401N	34.42951	-118.65094	4/15/26	9:21	1,722	4/17/26	Cover Compaction	4/22/26	109					4/17/26	Cover Compaction	5/14/26	14.7					
244	Y149	H-2401S	34.42892	-118.65121	4/15/26	9:28	3,642	4/17/26	Flow Increase	4/22/26	442					4/17/26	Flow Increase	5/14/26	43.06					
242	Y150	CV-24243	34.42879	-118.65067	4/15/26	9:32	8,101	4/17/26	Flow Increase	4/22/26	481					4/17/26	Flow Increase	5/14/26	13.56					
226	Y151	CV-2512	34.42931	-118.65057	4/15/26	9:38	9,430	4/17/26	Flow Increase	4/22/26	495					4/17/26	Flow Increase	5/14/26	4.61					
228	Y152	CV-2510	34.42909	-118.64981	4/15/26	9:45	3,805	4/17/26	Cover Compaction; Flow Increase	4/22/26	267					4/17/26	Cover Compaction; Flow Increase	5/14/26	90.3					
230	Y153	CV-2509	34.42927	-118.64918	4/15/26	9:51	7,455	4/17/26	Cover Compaction; Flow Increase	4/22/26	298					4/17/26	Cover Compaction; Flow Increase	5/14/26	4.68					
241	Y154	CV-24245	34.42851	-118.65012	4/15/26	9:58	544	4/17/26	Cover Compaction; Flow Increase	4/22/26	143					4/17/26	Cover Compaction; Flow Increase	5/14/26	63.48					
176	Y21	2-inch steel pipe support	34.43482	-118.65023	4/20/26	8:50	623	4/22/26	Boot Repaired	4/30/26	273					4/22/26	Boot Repaired	5/18/26	3.53					
156	Y22	Lateral near CV-2201	34.43555	-118.64889	4/20/26	9:03	823	4/22/26	Well Adjusted	4/30/26	183					4/22/26	Well Adjusted	5/18/26	34.48					

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
145	Y23	2-inch steel pipe support	34.43691	-118.64759	4/20/26	9:34	1,523	4/22/26	Repaired boot and tightened clamps	4/30/26	5.6					4/22/26	Repaired boot and tightened clamps	5/18/26	28.73					
77	Y24	2-inch steel pipe support	34.43701	-118.64717	4/20/26	9:40	682	4/22/26	Repaired boot and tightened clamps	4/30/26	54.2					4/22/26	Repaired boot and tightened clamps	5/18/26	12.91					
77	Y25	2-inch steel pipe support	34.43705	-118.64726	4/20/26	9:42	548	4/22/26	Repaired boot and tightened clamps	4/30/26	5.5					4/22/26	Repaired boot and tightened clamps	5/18/26	24.19					
77	Y26	2-inch steel pipe support	34.43708	-118.64682	4/20/26	9:48	652	4/22/26	Repaired boot and tightened clamps	4/30/26	5.4					4/22/26	Repaired boot and tightened clamps	5/18/26	48.24					
77	Y27	2-inch steel pipe support	34.43720	-118.64696	4/20/26	9:50	580	4/22/26	Repaired boot and tightened clamps	4/30/26	5.3					4/22/26	Repaired boot and tightened clamps	5/18/26	38.24					
78	Y28	Hero Sump	34.43738	-118.64676	4/20/26	9:57	720	4/22/26	Cover Compaction	4/30/26	338					4/22/26	Cover Compaction	5/18/26	47.38					
77	Y29	North Sump 1	34.43721	-118.64699	4/20/26	9:52	623	4/22/26	Boot Repaired	4/30/26	6.7					4/22/26	Boot Repaired	5/18/26	43.73					
78	Y30	CV-2563	34.43735	-118.64581	4/20/26	10:04	1,423	4/22/26	Flow Increase	4/30/26	262					4/22/26	Flow Increase	5/18/26	8.3					
77	Y31	2-inch steel pipe support	34.43705	-118.64705	4/20/26	9:44	548	4/22/26	Sealed Support	4/30/26	7.3					4/22/26	Sealed Support	5/18/26	13.93					
173	Y41	CV-24037	34.43461	-118.64942	4/20/26	8:48	500	4/22/26	Cover Compaction; Flow Increase	4/30/26	82.6					4/22/26	Cover Compaction; Flow Increase	5/18/26	5.99					
82	Y42	H-1804B	34.43432	-118.64563	4/20/26	9:49	650	4/22/26	Cover Compaction; Flow Increase	4/30/26	59.3					4/22/26	Cover Compaction; Flow Increase	5/18/26	15.59					
149	Y61	CV-24154	34.43428	-118.64610	4/20/26	8:17	10,000	4/22/26	Cover Compaction; Flow Increase	4/30/26	463					4/22/26	Cover Compaction; Flow Increase	5/18/26	23.8					
155	Y62	CV-24160	34.43380	-118.64627	4/20/26	8:31	10,000	4/22/26	Cover Compaction; Flow Increase	4/30/26	482					4/22/26	Cover Compaction; Flow Increase	5/18/26	16.71					
175	B21	CV-2338	34.43487	-118.65046	4/20/26	8:47	289	4/22/26	Flow Increase	4/30/26	60.9													
78	B23	Riser	34.43735	-118.64583	4/20/26	10:06	221	4/22/26	Flow Increase	4/30/26	102													
173	Y41	CV-24036	34.43447	-118.64968	5/4/26	9:02	1,200	5/6/26	Cover Compaction	5/14/26	30.74					5/6/26	Cover Compaction	6/3/26	4.31					
180	Y1	CV-24025	34.43529	-118.64989	5/4/26	8:18	3,792	5/6/26	Cover Compaction; Flow Increase	5/14/26	3.84					5/6/26	Cover Compaction; Flow Increase	6/3/26	4.8					
183	Y2	CV-24016	34.43592	-118.65025	5/4/26	8:24	1,736	5/6/26	Flow Increase; Boot Repaired	5/14/26	4.55					5/6/26	Flow Increase; Boot Repaired	6/3/26	4.46					
178	Y3	CV-24027	34.43612	-118.64868	5/4/26	8:59	10,000	5/6/26	Flow Increase	5/14/26	3.84					5/6/26	Flow Increase	6/3/26	5.06					
181	Y4	CV-2337	34.43548	-118.65074	5/4/26	9:21	1,972	5/6/26	Cover Compaction; Boot Repaired	5/14/26	5.25					5/6/26	Cover Compaction; Boot Repaired	6/3/26	3.8					
150	Y21	FP-008	34.43633	-118.64811	5/4/26	8:40	600	5/6/26	Cover Compaction	5/14/26	3.03					5/6/26	Cover Compaction	6/3/26	3.92					
150	Y22	CV-24023	34.43661	-118.64834	5/4/26	8:43	700	5/6/26	Cover Compaction; Flow Increase	5/14/26	37.59					5/6/26	Cover Compaction; Flow Increase	6/3/26	5.6					
145	Y23	CV-2333	34.43652	-118.64721	5/4/26	8:50	750	5/6/26	Cover Compaction	5/14/26	173					5/6/26	Cover Compaction	6/3/26	3.34					
77	Y24	CV-24122	34.43683	-118.64711	5/4/26	9:35	800	5/6/26	Cover Compaction; Flow Increase	5/14/26	3.82					5/6/26	Cover Compaction; Flow Increase	6/3/26	4.78					
78	Y25	CV-48R	34.43733	-118.64592	5/4/26	9:14	505	5/6/26	Flow Increase	5/14/26	13.97					5/6/26	Flow Increase	6/3/26	13.27					
73	Y26	CV-24132	34.43723	-118.64414	5/4/26	10:17	8,900	5/6/26	Flow Increase	5/14/26	21.83					5/6/26	Flow Increase	6/3/26	12.5					
210	Y101	Surface	34.43162	-118.65071	5/4/26	8:24	500	5/6/26	Cover Compaction	5/14/26	22.64					5/6/26	Cover Compaction	6/3/26	29.98					
210	Y102	Surface	34.43156	-118.65059	5/4/26	8:30	1,378	5/6/26	Cover Compaction	5/14/26	5.44					5/6/26	Cover Compaction	6/3/26	76.32					
198	Y103	CV-24194	34.43188	-118.64848	5/4/26	8:51	560	5/6/26	Cover Compaction; Flow Increase	5/14/26	9.42					5/6/26	Cover Compaction; Flow Increase	6/3/26	19.39					
198	Y104	Surface	34.43191	-118.64844	5/4/26	8:56	1,384	5/6/26	Cover Compaction	5/14/26	7.97					5/6/26	Cover Compaction	6/3/26	41.11					
198	Y105	RMC Temp Probe	34.43191	-118.64833	5/4/26	9:00	1,082	5/6/26	Cover Compaction	5/14/26	5.98					5/6/26	Cover Compaction	6/3/26	10.7					
85	Y106	Near CV-24210	34.43264	-118.64557	5/4/26	9:24	1,330	5/6/26	Cover Compaction; Flow Increase	5/14/26	15.3					5/6/26	Cover Compaction; Flow Increase	6/3/26	5.74					
84	Y107	H-1764N	34.43317	-118.64563	5/4/26	9:32	606	5/6/26	Flow Increase	5/14/26	31.97					5/6/26	Flow Increase	6/3/26	80.19					
36	Y108	H-2168E	34.43452	-118.64390	5/4/26	9:47	507	5/6/26	Flow Increase	5/14/26	40.44					5/6/26	Flow Increase	6/3/26	13.21					
163	Y81	CV-24173	34.43292	-118.64764	5/4/26	8:37	881	5/6/26	Cover Compaction; Flow Increase	5/14/26	116					5/6/26	Cover Compaction; Flow Increase	6/3/26	57.14					
90	Y82	CV-1905	34.43351	-118.64597	5/4/26	9:07	1,832	5/6/26	Flow Increase; Boot Repaired	5/14/26	75.8					5/6/26	Flow Increase; Boot Repaired	6/3/26	53.74					
155	Y83	CV-24160	34.43377	-118.64628	5/4/26	9:55	602	5/6/26	Flow Increase	5/14/26	29.86					5/6/26	Flow Increase	6/3/26	21.91					
82	Y85	CV-2549	34.43440	-118.64527	5/4/26	10:18	502	5/6/26	Cover Compaction; Flow Increase	5/14/26	38.14					5/6/26	Cover Compaction; Flow Increase	6/3/26	16.81					
60	Y87	CV-2010A	34.43572	-118.64364	5/4/26	11:11	711	5/6/26	Flow Increase	5/14/26	2.96					5/6/26	Flow Increase	6/3/26	8.72					
62	Y89	CV-2522	34.43553	-118.64237	5/4/26	11:27	1,102	5/6/26	Flow Increase	5/14/26	9.09					5/6/26	Flow Increase	6/3/26	15.46					
220	B121	H-2161W	34.43090	-118.65023	5/4/26	10:13	257	5/7/26	Flow Increase	5/14/26	13.55													
210	B101	Surface	34.43148	-118.65067	5/4/26	8:27	218	5/7/26	Flow Increase	5/14/26	20.01													
83	B84	H-1804B	34.43421	-118.64564	5/4/26	10:06	302	5/13/26	Flow Increase	5/14/26	38.31													
32	B86	H-2168C	34.43442	-118.64480	5/4/26	10:48	244	5/6/26	Flow Increase	5/14/26	19.19													
61	B88	CV-2521	34.43549	-118.64304	5/4/26	11:22	262	5/4/26	Flow Increase	5/14/26	17.32													
221	Y61	CV-2507	34.43017	-118.64817	5/5/26	8:30	633	5/8/26	Cover Compaction; Flow Increase	5/14/26	11.17					5/8/26	Cover Compaction; Flow Increase	6/4/26	52.36					
230	Y101	CV-2509	34.42927	-118.64918	5/5/26	8:44	676	5/8/26	Cover Compaction; Flow Increase	5/14/26	31.31					5/8/26	Cover Compaction; Flow Increase	6/4/26	6.04					
228	Y102	CV-2510	34.42912	-118.64984	5/5/26	8:51	3,921	5/8/26	Flow Increase	5/14/26	49.5					5/8/26	Flow Increase	6/4/26	36.43					
42	Y1	CV-24119	34.43374	-118.64232	5/5/26	8:12	500	5/8/26	Cover Compaction	5/14/26	11.22					5/8/26	Cover Compaction	6/4/26	7.32					
52	Y2	CV-2529	34.43313	-118.64230	5/5/26	8:23	800	5/8/26	Flow Increase	5/14/26	10.28					5/8/26	Flow Increase	6/4/26	12.85					
21	Y3	C-8	34.43367	-118.64088	5/5/26	8:38	700	5/8/26	Cover Compaction; Flow Increase	5/14/26	16.93					5/8/26	Cover Compaction; Flow Increase	6/4/26	4.12					
38	Y21	Surface	34.43389	-118.64394	5/5/26	8:07	711	5/8/26	Cover Compaction	5/14/26	35.04					5/8/26	Cover Compaction	6/4/26	18.21					
38	Y22	CV-1701D	34.43362	-118.64333	5/5/26	8:15	3,506	5/8/26	Flow Increase	5/14/26	100					5/8/26	Flow Increase	6/4/26	7.11					
42	Y23	CV-24119	34.43374	-118.64233	5/5/26	8:22	1,487	5/8/26	Cover Compaction	5/14/26	30.01					5/8/26	Cover Compaction	6/4/26	6.18					
50	Y25	CV-2531	34.43257	-118.64336	5/5/26	8:48	6,704	5/8/26	Flow Increase	5/14/26	18.22					5/8/26	Flow Increase	6/4/26	26.33					
51	Y26	CV-05	34.43284	-118.64221	5/5/26	8:54	1,064	5/8/26	Cover Compaction	5/14/26	7.17					5/8/26	Cover Compaction	6/4/26	32.14					
243	Y81	Surface	34.42867	-118.65097	5/5/26	8:33	1,172	5/8/26	Cover Compaction	5/14/26	35.66					5/8/26	Cover Compaction	6/4/26	23.94					
242	Y82	Surface	34.42837	-118.65047	5/5/26	8:48	541	5/8/26	Cover Compaction	5/14/26	32.41					5/8/26	Cover Compaction	6/4/26	39.02					
241	Y83	2-inch header support	34.42848	-118.64988	5/5/26	8:55	541	5/8/26	Cover Compaction	5/14/26	55.41					5/8/26	Cover Compaction	6/4/26	41.73					
237	Y84	Surface	34.42813	-118.64810	5/5/26	9:25	1,325	5/8/26	Cover Compaction	5/14/26	3.09					5/8/26	Cover Compaction	6/4/26	3.72					
247	Y85	2-inch pipe near Tank Farm 7	34.42725	-118.64970	5/5/26	10:46	1,742	5/8/26	Boot Repaired	5/14/26	3.38					5/8/26	Boot Repaired	6/4/26	30.63					
45	B1	CV-2524	34.43481	-118.64250	5/5/26	8:05	395	5/11/26	Flow Increase	5/14/26	15.21													
50	B24	CV-06	34.43270	-118.64284	5/5/26	8:43	223	5/11/26	Flow Increase	5/14/26	19.09													
242	B81	Surface	34.42846	-118.65025	5/5/26	8:51	242	5/8/26	Flow Increase	5/14/26	10.31													
203	Y101	Lorentz Panel for CV-24095	34.43335	-118.65127	5/13/26	9:27	40,000	5/14/26	Boot Repaired	5/20/26	10.98					5/14/26	Boot Repaired	6/11/26	4.12					
203	Y102	CV-24095	34.43338	-118.65129	5/13/26	9:31	3,700	5/14/26	Monitored Well; 5/20/26 Lateral Repaired; Flow Increase	5/20/26	12.28					5/14/26	Monitored Well; 5/20/26 Lateral Repaired; Flow Increase	6/11/26	4.91					
203	Y103	CV-1534A	34.43361	-118.65078	5/13/26	9:36	8,845	5/14/26	Cover Compaction	5/20/26	13.44					5/14/26	Cover Compaction	6/11/26	3.97					
82	Y41	CV-2549	34.43438	-118.64525	5/13/26	8:33	660	5/14/26	Cover Compaction; Flow Increase	5/20/26	6.46					5/14/26	Cover Compaction; Flow Increase	6/11/26	53.11					
82	Y42	CV-2548	34.43441	-118.64559	5/13/26	8:34	600	5/14/26	Cover Compaction; Flow Increase	5/20/26	15.78					5/14/26	Cover Compaction; Flow Increase	6/11/26	48.2					
149	Y43	CV-25154	34.43427	-118.64615	5/13/26	8:36	1,200	5/14/26	Flow Increase	5/20/26	10.12					5/14/26	Flow Increase	6/11/26	53.46					
173	Y44	CV-24036	34.43441	-118.64959	5/13/26	9:32	800	5/14/26	Boot Repaired	5/20/26	8.91					5/14/26	Boot Repaired	6/11/26	3.27					
175	Y21	CV-1902A	34.43462	-118.65030	5/13/26	7:59	900	5/14/26	Cover Compaction; Flow Increase	5/20/26	8.49					5/14/26	Cover Compaction; Flow Increase	6/11/26	3.16					
176	Y22	Support pipe on 2 inch line	34.43470	-118.65023	5/13/26	8:02	562	5/14/26	Cover Compaction	5/20/26	17.06					5/14/26	Cover Compaction	6/11/26	3.88					
176	Y23	CV-24032	34.43512	-118.64960	5/13/26	8:10	620	5/14/26	Flow Increase; Boot Repaired	5/20/26	3.56					5/14/26	Flow Increase; Boot Repaired	6/11/26	2.86					
177	Y24	FP-021	34.43521	-118.64915	5/13/26	8:25	780	5/14/26	Flow Increase	5/20/26	3.73					5/14/26	Flow Increase	6/11/26	3.22					
177	Y25	FP-025	34.43526	-118.64913	5/13/26	8:29	980	5/14/26	Flow Increase	5/20/26	3.16					5/14/26	Flow Increase	6/11/26	3.39					

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
177	Y26	Lorentz Panel	34.43544	-118.64887	5/13/26	8:32	723	5/14/26	Boot Repaired	5/20/26	10.52					5/14/26	Boot Repaired	6/11/26	2.97					
145	Y27	Surface	34.43652	-118.64734	5/13/26	9:30	1,925	5/14/26	Cover Compaction	5/20/26	3.15					5/14/26	Cover Compaction	6/11/26	3.01					
145	Y28	Surface	34.43652	-118.64740	5/13/26	9:32	1,147	5/14/26	Cover Compaction	5/20/26	4.24					5/14/26	Cover Compaction	6/11/26	5.76					
77	Y29	Support pipe on 2 inch line	34.43701	-118.64709	5/13/26	9:44	1,438	5/14/26	Boot Repaired	5/20/26	30.17					5/14/26	Boot Repaired	6/11/26	11.61					
77	Y30	Hero Sump	34.43735	-118.64674	5/13/26	9:51	1,053	5/14/26	Cover Compaction	5/20/26	103					5/14/26	Cover Compaction	6/11/26	3.91					
78	Y31	CV-24123	34.43729	-118.64621	5/13/26	9:57	1,447	5/14/26	Flow Increase; 5/15/26 Lateral Repaired	5/20/26	5.46					5/14/26	Flow Increase; 5/15/26 Lateral Repaired	6/11/26	40.33					
78	Y32	CV-24147	34.43753	-118.64593	5/13/26	10:16	1,148	5/14/26	Cover Compaction; Flow Increase	5/20/26	45.6					5/14/26	Cover Compaction; Flow Increase	6/11/26	60.01					
180	B1	Riser	34.43534	-118.65013	5/13/26	8:37	342	5/13/26	Flow Increase	5/20/26	4.01													
145	Y21	RMC Temp Probe TP-18	34.43652	-118.64736	5/26/26	8:16	1,375	5/29/26	Cover Compaction	6/4/26	3.72					5/29/26	Cover Compaction	6/24/26	6.8					
145	Y22	CV-2333	34.43654	-118.64733	5/26/26	8:21	1,452	5/29/26	Cover Compaction	6/4/26	8.2					5/29/26	Cover Compaction	6/24/26	7.44					
77	Y23	2-inch header support	34.43710	-118.64683	5/26/26	8:36	1,723	5/28/26	Boot Repaired	6/4/26	14.53					5/28/26	Boot Repaired	6/24/26	9.73					
77	Y24	North Sump 1	34.43721	-118.64694	5/26/26	8:42	4,523	5/28/26	Boot Repaired; Flange Tightened	6/4/26	4.74					5/28/26	Boot Repaired; Flange Tightened	6/24/26	6.56					
78	Y25	Lorentz panel	34.43730	-118.64624	5/26/26	8:52	3,452	5/28/26	Boot Repaired	6/4/26	13.64					5/28/26	Boot Repaired	6/24/26	8.11					
78	Y26	CV-24123	34.43730	-118.64620	5/26/26	8:56	5,412	5/28/26	Boot Repaired, Lateral Repaired	6/4/26	34.4					5/28/26	Boot Repaired, Lateral Repaired	6/24/26	28.71					
78	Y27	CV-2563	34.43728	-118.64573	5/26/26	8:59	700	5/28/26	Cover Compaction	6/4/26	53.71					5/28/26	Cover Compaction	6/24/26	13.65					
79	Y29	CV-24147	34.43753	-118.64591	5/26/26	9:07	1,123	5/28/26	Cover Compaction	6/4/26	46.87					5/28/26	Cover Compaction	6/24/26	9.54					
80	Y30	North Sump 4	34.43758	-118.64411	5/26/26	9:16	1,130	5/28/26	Cover Compaction	6/4/26	35.16					5/28/26	Cover Compaction	6/24/26	4.32					
196	Y81	CV-24195	34.43185	-118.64783	5/26/26	9:39	567	5/28/26	Cover Compaction; Flow Increase	6/4/26	21.65					5/28/26	Cover Compaction; Flow Increase	6/24/26	7.62					
162	Y82	CV-24196	34.43207	-118.64713	5/26/26	9:47	674	5/28/26	Flow Increase	6/4/26	8.33					5/28/26	Flow Increase	6/24/26	6.3					
161	Y83	CV-24184	34.43253	-118.64724	5/26/26	9:55	849	5/28/26	Cover Compaction	6/4/26	11.5					5/28/26	Cover Compaction	6/24/26	3.22					
162	Y84	CV-24106	34.43209	-118.64667	5/26/26	10:08	10,000	5/28/26	Cover Compaction	6/4/26	8.13					5/28/26	Cover Compaction	6/24/26	15.06					
86	Y85	CV-24117	34.43235	-118.64493	5/26/26	10:20	10,000	5/28/26	Cover Compaction	6/4/26	5.75					5/28/26	Cover Compaction	6/24/26	4.46					
84	Y86	CV-24108	34.43316	-118.64542	5/26/26	10:34	2,148	5/28/26	Flow Increase	6/4/26	7.43					5/28/26	Flow Increase	6/24/26	5.51					
84	Y87	H-1764N	34.43317	-118.64560	5/26/26	10:39	1,214	5/28/26	Flow Increase	6/4/26	115					5/28/26	Flow Increase	6/24/26	35					
150	Y1	Surface	34.43660	-118.64840	5/26/26	7:51	717	5/29/26	Cover Compaction	6/4/26	3.63					5/29/26	Cover Compaction	6/24/26	4.17					
180	Y3	Surface	34.43530	-118.65048	5/26/26	8:10	987	5/29/26	Cover Compaction	6/4/26	11.48					5/29/26	Cover Compaction	6/24/26	3.54					
183	Y5	CV-24016	34.43592	-118.65021	5/26/26	8:48	975	5/29/26	Cover Compaction	6/4/26	4.24					5/29/26	Cover Compaction	6/24/26	3.71					
187	Y6	CV-24007	34.43651	-118.65007	5/26/26	9:57	971	5/29/26	Cover Compaction; Flow Increase	6/4/26	4.03					5/29/26	Cover Compaction; Flow Increase	6/24/26	3.97					
156	Y41	CV-24040	34.43564	-118.64837	5/26/26	8:01	890	5/29/26	Flow Increase	6/4/26	4.12					5/29/26	Flow Increase	6/24/26	3.41					
177	Y42	Riser	34.43557	-118.64881	5/26/26	8:07	934	5/29/26	Boot Repaired	6/4/26	22.62					5/29/26	Boot Repaired	6/24/26	3.91					
177	Y43	Reaction Area Sump 2	34.43552	-118.64871	5/26/26	8:12	1,313	5/29/26	Boot Repaired; Flange Tightened	6/4/26	5.56					5/29/26	Boot Repaired; Flange Tightened	6/24/26	3.24					
176	Y44	RMC Temp Probe TP-21	34.43478	-118.64955	5/26/26	8:43	735	5/29/26	Boot Repaired; Clamps Tightened	6/4/26	4.96					5/29/26	Boot Repaired; Clamps Tightened	6/24/26	10.67					
36	Y61	H-2168E	34.43450	-118.64394	5/26/26	8:17	800	5/28/26	Flow Increase	6/4/26	49.81					5/28/26	Flow Increase	6/24/26	36.78					
82	Y62	CV-2549	34.43434	-118.64528	5/26/26	8:30	1,200	5/28/26	Cover Compaction; Flow Increase	6/4/26	44.66					5/28/26	Cover Compaction; Flow Increase	6/24/26	203					
83	Y63	CV-2547	34.43390	-118.64595	5/26/26	8:37	700	5/28/26	Cover Compaction; Flow Increase	6/4/26	52.6					5/28/26	Cover Compaction; Flow Increase	6/24/26	31.8					
220	Y102	H-2057W	34.43065	-118.65060	5/26/26	9:26	800	5/28/26	Flow Increase	6/4/26	22.81					5/28/26	Flow Increase	6/24/26	5.7					
78	B28	CV-48R	34.43733	-118.64583	5/26/26	9:05	212	5/29/26	Flow Increase	6/4/26	20.11													
77	B21	Surface	34.43708	-118.64679	5/26/26	8:31	200	5/29/26	Flow Increase	6/4/26	10.94													
180	B2	Riser	34.43562	-118.65003	5/26/26	8:03	283	5/29/26	Flow Increase	6/4/26	4.4													
180	B4	Surface	34.43483	-118.65098	5/26/26	8:27	215	5/29/26	Flow Increase	6/4/26	9.12													
176	B41	FP-031	34.43484	-118.64971	5/26/26	9:11	255	5/29/26	Flow Increase	6/4/26	7.22													
215	B101	Riser	34.43108	-118.65057	5/26/26	9:36	350	5/29/26	Flow Increase	6/4/26	13.3													
58	Y1	C-26	34.43661	-118.64123	5/27/26	8:11	997	5/29/26	Flow Increase	6/4/26	12.8					5/29/26	Flow Increase	6/25/26	5.17					
58	Y2	Surface	34.43691	-118.64145	5/27/26	8:16	887	5/29/26	Cover Compaction	6/4/26	12.85					5/29/26	Cover Compaction	6/25/26	6.61					
65	Y4	C-15	34.43626	-118.64102	5/27/26	8:22	1,382	5/29/26	Cover Compaction	6/4/26	17.05					5/29/26	Cover Compaction	6/25/26	5.22					
65	Y5	C-12	34.43595	-118.64083	5/27/26	8:24	1,142	5/29/26	Cover Compaction; Flow Increase	6/4/26	24.8					5/29/26	Cover Compaction; Flow Increase	6/25/26	7.51					
64	Y6	C-28	34.43542	-118.64132	5/27/26	8:30	2,268	5/29/26	Flow Increase	6/4/26	5.82					5/29/26	Flow Increase	6/25/26	3.39					
69	Y7	H-29	34.43544	-118.64174	5/27/26	8:35	662	5/29/26	Cover Compaction; Flow Increase	6/4/26	50.08					5/29/26	Cover Compaction; Flow Increase	6/25/26	4.62					
96	Y21	CV-2537	34.43104	-118.64663	5/27/26	8:17	623	5/29/26	Cover Compaction	6/4/26	2.9					5/29/26	Cover Compaction	6/25/26	18.3					
96	Y22	Surface	34.43065	-118.64605	5/27/26	8:28	500	5/29/26	Cover Compaction	6/4/26	4.45					5/29/26	Cover Compaction	6/25/26	41.24					
96	Y23	Surface	34.43071	-118.64600	5/27/26	8:31	523	5/29/26	Cover Compaction	6/4/26	4.72					5/29/26	Cover Compaction	6/25/26	76.97					
94	Y24	Header support pipe	34.43110	-118.64443	5/27/26	8:42	606	5/29/26	Cover Compaction	6/4/26	114					5/29/26	Cover Compaction	6/25/26	8.6					
93	Y25	Southeast Manifold	34.43118	-118.64424	5/27/26	8:46	2,345	5/29/26	Cover Compaction; Boot Repaired	6/4/26	264					5/29/26	Cover Compaction; Boot Repaired	6/25/26	3.54					
93	Y26	Vessel ST2-IN	34.43105	-118.64396	5/27/26	8:53	525	5/29/26	Cover Compaction	6/4/26	27					5/29/26	Cover Compaction	6/25/26	12.4					
242	Y61	ARV-15	34.42834	-118.65046	5/27/26	7:50	7,379	5/29/26	Flange Tightened	6/4/26	12.25					5/29/26	Flange Tightened	6/25/26	70.74					
58	B3	C-25	34.43710	-118.64162	5/27/26	8:18	221	5/29/26	Flow Increase	6/4/26	6.13													
42	B7	CV-24119	34.43376	-118.64231	5/27/26	8:48	325	5/29/26	Flow Increase	6/4/26	15.22													
94	B21	Riser	34.43117	-118.64430	5/27/26	8:45	222	5/29/26	Flow Increase	6/4/26	68.51													
95	B22	Surface	34.43051	-118.64464	5/27/26	9:05	302	5/29/26	Flow Increase	6/4/26	195													
222	B41	CV-2507	34.43015	-118.64815	5/27/26	8:12	246	5/29/26	Flow Increase	6/4/26	11.99													
84	Y101	CV-1905	34.43351	-118.64597	6/8/26	8:28	1,000	06/09/26	Cover Compaction; Flow Increase	6/17/26	78					06/09/26	Cover Compaction; Flow Increase	7/8/26	70.8					
85	Y102	CV-24210	34.43264	-118.64557	6/8/26	8:37	500	06/09/26	Cover Compaction; Boot Repaired	6/17/26	99					06/09/26	Cover Compaction; Boot Repaired	7/8/26	6.9					
82	Y61	CV-2549	34.43433	-118.64523	6/8/26	8:23	800	06/09/26	Cover Compaction	6/17/26	69.85					06/09/26	Cover Compaction	7/8/26	376					
83	Y62	CV-24161	34.43390	-118.64561	6/8/26	8:32	670	06/09/26	Cover Compaction	6/17/26	77.05					06/09/26	Cover Compaction	7/8/26	46.9					
33	Y63	H-1956B	34.43412	-118.64463	6/8/26	8:43	740	06/09/26	Cover Compaction	6/17/26	18.04					06/09/26	Cover Compaction	7/8/26	38.6					
61	Y64	H-1958C	34.43543	-118.64337	6/8/26	9:41	900	06/09/26	Flow Increase	6/17/26	23.5					06/09/26	Flow Increase	7/8/26	4.8					
78	Y21	CV-1902A	34.43732	-118.64578	6/8/26	9:44	3,515	06/09/26	Cover Compaction	6/17/26	21.3					06/09/26	Cover Compaction	7/8/26	3.7					
78	Y22	CV-48R	34.43734	-118.64585	6/8/26	9:45	505	06/09/26	Flow Increase	6/17/26	18.6					06/09/26	Flow Increase	7/8/26	3.9					
250	Y23	CV-24029	34.43641	-118.64804	6/8/26	9:21	2,145	06/09/26	Cover Compaction	6/17/26	15.8					06/09/26	Cover Compaction	7/8/26	486					
175	B21	Riser	34.43460	-118.65028	6/8/26	8:12	200	06/09/26	Flow Increase	6/17/26	98.5													
245	Y61	ARV-16	34.42832	-118.65054	6/9/26	8:05	1,186	06/10/26	Boot repaired; bolts tightened	6/19/26	420					06/10/26	Boot repaired; bolts tightened	7/8/26	442					
97	Y21	Surface	34.43064	-118.64610	6/9/26	8:15	523	06/10/26	Cover Compaction	6/19/26	291					06/10/26	Cover Compaction	7/8/26	19.8					
93	Y22	CV-2534	34.43118	-118.64425	6/9/26	9:04	521	06/10/26	Flow Increase	6/19/26	380					06/10/26	Flow Increase	7/8/26	404					
93	Y23	D-04	34.43116	-118.64427	6/9/26	9:06	550	06/10/26	Flow Increase	6/19/26	320					06/10/26	Flow Increase	7/8/26	157					
97	B21	Surface	34.43182	-118.64453	6/9/26	8:47	200	06/10/26	Cover Compaction	6/19/26	120													
97	B22	South manifold	34.43181	-118.64424	6/9/26	8:52	221	06/10/26	Cover Compaction	6/19/26	180													
93	B23	2-inch header support pipe	34.43095	-118.64442	6/9/26	9:14	245	06/10/26	Cover Compaction	6/19/26	150													

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
162	Y81	CV-24106	34.43209	-118.64669	6/16/26	8:49	10,000	06/19/26	Cover Compaction; Flow Increase	6/25/26	10.36					06/19/26	Cover Compaction; Flow Increase	7/15/26	463					
215	Y82	H-102A	34.43111	-118.65055	6/16/26	9:52	523	06/19/26	Cover Compaction; Flow Increase	6/25/26	28.51					06/19/26	Cover Compaction; Flow Increase	7/15/26	375					
197	Y83	CV-2503	34.43124	-118.64774	6/16/26	10:30	10,000	06/19/26	Cover Compaction; Flow Increase	6/25/26	5.74					06/19/26	Cover Compaction; Flow Increase	7/15/26	472					
83	Y61	Surface	34.43397	-118.64545	6/16/26	9:52	543	06/19/26	Cover Compaction	6/25/26	33.47					06/19/26	Cover Compaction	7/15/26	34.1					
155	Y62	Lorentz panel pole	34.43378	-118.64657	6/16/26	10:15	563	06/19/26	Cover Compaction	6/25/26	5.94					06/19/26	Cover Compaction	7/15/26	44.56					
155	Y63	TP-12	34.43378	-118.64688	6/16/26	10:37	60,000	06/19/26	Cover Compaction	6/25/26	5.11					06/19/26	Cover Compaction	7/15/26	6.88					
185	Y1	CV-24014	34.43671	-118.64889	6/16/26	8:57	1,739	06/19/26	Cover Compaction; Flow Increase	6/25/26	2.64					06/19/26	Cover Compaction; Flow Increase	7/15/26	6.25					
77	Y21	CV-113	34.43696	-118.64674	6/16/26	9:43	921	06/19/26	Cover Compaction; Flow Increase	6/25/26	4.31					06/19/26	Cover Compaction; Flow Increase	7/15/26	58.3					
77	Y22	Surface	34.43713	-118.64661	6/16/26	9:46	770	06/19/26	Cover Compaction	6/25/26	7.11					06/19/26	Cover Compaction	7/15/26	4.87					
77	Y23	Surface	34.43712	-118.64675	6/16/26	9:52	721	06/19/26	Cover Compaction	6/25/26	6.54					06/19/26	Cover Compaction	7/15/26	169					
77	Y24	Surface	34.43703	-118.64710	6/16/26	9:57	723	06/19/26	Cover Compaction	6/25/26	27.84					06/19/26	Cover Compaction	7/15/26	7.74					
78	Y25	Surface	34.43736	-118.64677	6/16/26	10:03	623	06/19/26	Installed liner	6/25/26	43.6					06/19/26	Installed liner	7/15/26	99.81					
78	Y26	CV-24147	34.43754	-118.64593	6/16/26	10:26	725	06/19/26	Cover Compaction; Flow Increase	6/25/26	53.3					06/19/26	Cover Compaction; Flow Increase	7/15/26	5.48					
78	Y27	CV-24123	34.43732	-118.64623	6/16/26	10:12	726	06/19/26	Cover Compaction; Flow Increase	6/25/26	6.15					06/19/26	Cover Compaction; Flow Increase	7/15/26	306					
78	Y29	CV-48R	34.43728	-118.64576	6/16/26	10:22	729	06/19/26	Cover Compaction; Flow Increase	6/25/26	4.89					06/19/26	Cover Compaction; Flow Increase	7/15/26	5.73					
78	B28	CV-24146	34.43742	-118.64638	6/16/26	10:17	452	06/19/26	Cover Compaction	6/25/26	15.67													
150	B21	CV-24029	34.43650	-118.64808	6/16/26	9:31	212	06/19/26	Flow Increase	6/25/26	2.32													
208	Y21	Surface	34.43218	-118.65062	6/17/26	8:34	881	06/19/26	Cover Compaction	6/24/26	3.23					06/19/26	Cover Compaction	7/15/26	19.32					
77	Y21	North Sump 1	34.43724	-118.64691	6/22/26	9:20	700	06/24/26	Boot Repaired; Clamps Tightened	6/30/26	21.9					06/24/26	Boot Repaired; Clamps Tightened	7/22/26	6.8					
149	Y61	CV-24154	34.43428	-118.64608	6/22/26	8:50	9,874	06/24/26	Cover Compaction	6/30/26	49.51					06/24/26	Cover Compaction	7/22/26	427					
83	Y81	CV-2547	34.43395	-118.64591	6/22/26	8:19	520	06/24/26	Cover Compaction	6/30/26	8.97					06/24/26	Cover Compaction	7/22/26	26.96					
155	Y82	CV-24160	34.43379	-118.64634	6/22/26	8:21	600	06/24/26	Flow Increase	6/30/26	6.72					06/24/26	Flow Increase	7/22/26	91.8					
78	B21	CV-24123	34.43730	-118.64620	6/22/26	9:30	279	06/24/26	Flow Increase	6/30/26	13.4													
78	B22	CV-24146	34.43740	-118.64640	6/22/26	9:33	307	06/24/26	Cover Compaction; Flow Increase	6/30/26	20.56													
41	Y141	Electric panel	34.43437	-118.64276	7/1/26	8:42	6,675	7/2/26	Boot repaired	7/9/26	129					7/2/26	Boot repaired	7/27/26	37.86					
41	Y142	CV-55R	34.43439	-118.64277	7/1/26	8:45	90,000	7/2/26	Valve adjustment: Increased flow	7/9/26	200					7/2/26	Valve adjustment: Increased flow	7/27/26	269					
41	Y143	CV-2527	34.43411	-118.64286	7/1/26	8:49	5,757	7/2/26	Boot repaired; Flow Increase	7/9/26	244					7/2/26	Boot repaired; Flow Increase	7/27/26	479					
41	Y144	CV-2011A	34.43454	-118.64316	7/1/26	8:53	4,500	7/2/26	Valve adjustment: Increased flow	7/9/26	6.79					7/2/26	Valve adjustment: Increased flow	7/27/26	7.46					
41	Y145	4 inch pipe	34.4346	-118.64294	7/1/26	8:58	850	7/2/26	Boot repaired	7/9/26	109					7/2/26	Boot repaired	7/27/26	23.31					
172	Y41	Reaction Area Sump 4 Pump 2	34.43476	-118.64844	7/1/26	8:12	514	7/2/26	Boot repaired	7/9/26	138					7/2/26	Boot repaired	7/27/26	17.76					
173	Y43	CV-24036	34.43446	-118.64967	7/1/26	9:17	679	7/2/26	Cover Compaction; Flow Increase	7/9/26	6.39					7/2/26	Cover Compaction; Flow Increase	7/27/26	80.55					
180	Y21	Surface	34.4353	-118.65046	7/1/26	8:36	600	7/2/26	Unsafe area; 7/8/26 Flow Increase	7/9/26	20.63					7/8/26	Flow Increase	7/27/26	6.19					
149	Y61	CV-24154	34.43427	-118.64607	7/1/26	8:07	800	7/2/26	Cover Compaction; Flow Increase	7/9/26	89.41					7/2/26	Cover Compaction; Flow Increase	7/27/26	370					
172	B42	CV-2304	34.43457	-118.64873	7/1/26	9:06	249	7/2/26	Cover Compaction; Flow Increase	7/9/26	190													
182	B1	CV-24141	34.4353	-118.65096	7/1/26	8:56	204	7/2/26	Cover Compaction; Flow Increase	7/9/26	47.12													
181	B21	CV-2352	34.43488	-118.65102	7/1/26	8:23	200	7/2/26	Cover Compaction; Flow Increase	7/9/26	60.77													
181	Y1	Surface	34.43507	-118.65098	7/13/26	8:05	761	7/16/26	Cover compaction	7/22/26	8.76					7/16/26	Cover compaction	8/12/26	310					
182	Y2	CV-24141	34.4355	-118.65129	7/13/26	8:52	527	7/16/26	Cover compaction	7/22/26	416					7/16/26	Cover compaction	8/12/26	325					
243	Y21	Surface	34.4312	-118.64421	7/15/26	8:20	823	7/16/26	Cover compaction	7/22/26	77.48					7/16/26	Cover compaction	8/12/26	200					
243	Y22	2" header support steel pipe	34.42876	-118.65098	7/15/26	8:12	582	7/16/26	Cover compaction	7/22/26	455					7/16/26	Cover compaction	8/12/26	400					
243	Y23	2" header support steel pipe	34.42878	-118.65101	7/15/26	8:14	8,123	7/16/26	Cover compaction	7/22/26	429					7/16/26	Cover compaction	8/12/26	210					
242	Y24	2" header support steel pipe	34.42834	-118.65053	7/15/26	8:28	805	7/16/26	Cover compaction	7/22/26	480					7/16/26	Cover compaction	8/12/26	380					
242	Y25	Surface	34.42858	-118.65022	7/15/26	8:30	921	7/16/26	Cover compaction	7/22/26	472					7/16/26	Cover compaction	8/12/26	400					
241	Y26	Surface	34.42856	-118.65012	7/15/26	8:34	923	7/16/26	Cover compaction	7/22/26	212					7/16/26	Cover compaction	8/12/26	100					
48	Y101	C-08	34.43377	-118.641	7/15/26	9:28	20,680	7/16/26	Cover Compaction; Flow Increase	7/22/26	84.53					7/16/26	Cover Compaction; Flow Increase	8/12/26	210					
52	Y102	Surface	34.43262	-118.64162	7/15/26	9:39	823	7/16/26	Cover compaction	7/22/26	413					7/16/26	Cover compaction	8/12/26	220					
52	Y103	CV-2529	34.43313	-118.64227	7/15/26	9:44	1,250	7/16/26	Cover compaction	7/22/26	492					7/16/26	Cover compaction	8/12/26	210					
52	Y104	CV-05	34.43289	-118.64224	7/15/26	9:47	2,564	7/16/26	Cover Compaction; Flow Increase	7/22/26	80.96					7/16/26	Cover Compaction; Flow Increase	8/12/26	300					
93	Y21	Surface	34.4312	-118.64421	7/15/26	8:20	656	7/16/26	Cover compaction	7/22/26	78.47					7/16/26	Cover compaction	8/12/26	219					
242	B21	Surface	34.42838	-118.65046	7/15/26	8:25	283	7/16/26	Cover compaction	7/22/26	32.5													
48	B101	C-09	34.43424	-118.641	7/15/26	9:32	254	7/16/26	Cover compaction	7/22/26	145													
173	Y21	CV-24036	34.43448	-118.6497	7/28/26	8:06	685	8/1/26	Cover compaction	8/6/26	291					8/1/26	Cover compaction	8/27/26	187					
171	Y22	CV-2304	34.43458	-118.64871	7/28/26	9:03	900	8/1/26	Cover compaction	8/6/26	445.3					8/1/26	Cover compaction	8/27/26	98.7					
80	Y101	H-2171N	34.438	-118.64325	7/28/26	9:05	1,328	8/1/26	Liner installed; tightened clamps	8/6/26	2.7					8/1/26	Liner installed; tightened clamps	8/27/26	61.3					
41	Y102	CV-55R	34.43439	-118.64274	7/28/26	9:35	7,605	8/1/26	Valve adjustment: Increased flow	8/6/26	9.15					8/1/26	Valve adjustment: Increased flow	8/27/26	200					
82	Y103	CV-2548	34.43439	-118.64555	7/28/26	9:56	963	8/1/26	Cover compaction	8/6/26	401					8/1/26	Cover compaction	8/27/26	423					
82	Y104	H-1804B	34.43427	-118.6456	7/28/26	10:02	782	8/1/26	Cover compaction	8/6/26	16.2					8/1/26	Cover compaction	8/27/26	19.5					
83	Y105	CV-2547	34.43395	-118.64597	7/28/26	10:12	681	8/1/26	Cover compaction	8/6/26	362					8/1/26	Cover compaction	8/27/26	426					
194	Y106	CV-2536	34.43095	-118.64579	7/28/26	10:45	4,815	8/1/26	Cover compaction; area backfilled	8/6/26	225					8/1/26	Cover compaction; area backfilled	8/27/26	18.4					
172	Y21	CV-2304	34.43458	-118.64874	8/3/26	8:33	1,000	8/5/26	Increased flow and cover compaction	8/12/26	420					8/5/26	Increased flow and cover compaction	8/31/26	60					
82	Y61	CV-2548	34.43435	-118.64557	8/3/26	9:16	10,000	8/5/26	Increased flow and cover compaction	8/12/26	106					8/5/26	Increased flow and cover compaction	8/31/26	70					
48	B101	Surface	34.43364	-118.64085	8/3/26	9:41	204	8/5/26	Cover compaction	8/12/26	96.4													
49	Y1	CV-2532	34.43231	-118.64372	8/4/26	8:49	2,468	8/6/26	Increased flow and cover compaction	8/12/26	226					8/6/26	Increased flow and cover compaction	8/31/26	488					
50	Y2	CV-2531	34.43257	-118.64332	8/4/26	8:54	1,153	8/6/26	Increased flow and cover compaction	8/12/26	199					8/6/26	Increased flow and cover compaction	8/31/26	204					
51	Y3	CV-2688	34.43275	-118.64236	8/4/26	9:07	60,000	8/6/26	Increased flow and cover compaction	8/12/26	243					8/6/26	Increased flow and cover compaction	8/31/26	68.4					
102	Y81	Surface	34.43	-118.64727	8/4/26	8:08	1,546	8/6/26	Cover compaction	8/12/26	483					8/6/26	Cover compaction	8/31/26	11.5					
103	Y82	Surface	34.42982	-118.64726	8/4/26	8:13	5,452	8/6/26	Cover compaction	8/12/26	489					8/6/26	Cover compaction	8/31/26	30.6					
103	Y83	CV-2572	34.42984	-118.64707	8/4/26	8:17	528	8/6/26	Increased flow and cover compaction	8/12/26	8.4					8/6/26	Increased flow and cover compaction	8/31/26	168					
101	Y84	CV-2610	34.42988	-118.64656	8/4/26	8:21	1,615	8/6/26	Well cap repaired; increased flow	8/12/26	4					8/6/26	Well cap repaired; increased flow	8/31/26	71.1					
101	Y85	D-09	34.43012	-118.64629	8/4/26	8:24	983	8/6/26	Increased flow and cover compaction	8/12/26	4.7					8/6/26	Increased flow and cover compaction	8/31/26	101					
98	Y86	H-2057E	34.43021	-118.6458	8/4/26	8:28	570	8/6/26	Increased flow and cover compaction	8/12/26	3.6					8/6/26	Increased flow and cover compaction	8/31/26	19.3					
197	Y21	CV-2503	34.43125	-118.64772	8/4/26	8:18	500	8/6/26	Broken well head to be repaired	8/12/26	10					8/6/26	Broken well head to be repaired	8/31/26	81.4					
242	Y61	CV-24243	34.42879	-118.65064	8/4/26	8:13	2,453	8/6/26	Increased flow and cover compaction	8/12/26	18.6					8/6/26	Increased flow and cover compaction	8/31/26	42.2					
242	Y62	Riser	34.42839	-118.65048	8/4/26	8:28	523	8/6/26	Cover compaction	8/12/26	310					8/6/26	Cover compaction	8/31/26	68.8					
242	Y63	Riser	34.42835	-118.65053	8/4/26	8:32	2,132	8/6/26	Cover compaction	8/12/26	116					8/6/26	Cover compaction	8/31/26	46.2					
240	Y64	Surface	34.42834	-118.64928	8/4/26	9:21	500	8/6/26	Cover compaction	8/12/26	481					8/6/26	Cover compaction	8/31/26	109					
241	Y65	Surface	34.42853	-118.65012	8/4/26	8:48	523	8/6/26	Cover compaction	8/12/26	35					8/6/26	Cover compaction	8/31/26	4.7					

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
239	Y66	Surface	34.42832	-118.64919	8/4/26	9:23	580	8/6/26	Cover compaction	8/12/26	440					8/6/26	Cover compaction	8/31/26	72.3					
237	Y67	Riser	34.42845	-118.65019	8/4/26	8:43	530	8/6/26	Tightened bolts	8/12/26	90					8/6/26	Tightened bolts	8/31/26	85.5					
238	Y37	Riser	34.42822	-118.64866	8/4/26	9:38	5,213	8/6/26	Cover compaction	8/12/26	330					8/6/26	Cover compaction	8/31/26	36.3					
238	Y38	Surface	34.42794	-118.64851	8/4/26	9:44	500	8/6/26	Cover compaction	8/12/26	4.1					8/6/26	Cover compaction	8/31/26	47.6					
243	B61	Surface	34.42845	-118.65103	8/4/26	8:02	200	8/6/26	Cover compaction	8/12/26	100													
243	B62	Surface	34.42843	-118.65096	8/4/26	8:06	230	8/6/26	Cover compaction	8/12/26	140													
241	B63	Riser	34.42845	-118.65019	8/4/26	8:45	321	8/6/26	Cover compaction	8/12/26	90													
84	Y61	CV-1905	34.4335	-118.64599	8/17/26	8:39	747	8/20/26	Increased flow and cover compaction	8/27/26	50.7					8/20/26	Increased flow and cover compaction	9/16/26	79.08					
215	Y81	Surface	34.43123	-118.65044	8/17/26	9:04	540	8/20/26	Cover compaction	8/27/26	25.5					8/20/26	Cover compaction	9/16/26	411					
197	Y101	Surface	34.43274	-118.64594	8/17/26	8:00	4,122	8/20/26	Cover compaction	8/27/26	24					8/20/26	Cover compaction	9/16/26	32.5					
89	Y102	CV-2503	34.43122	-118.64773	8/17/26	9:02	500	8/20/26	Increased flow and cover compaction	8/27/26	68.7					8/20/26	Increased flow and cover compaction	9/16/26	86.21					
173	Y21	CV-24036	34.43447	-118.64969	8/17/26	7:58	1,610	8/20/26	Increased flow and cover compaction	8/27/26	141					8/20/26	Increased flow and cover compaction	9/16/26	3.83					
171	Y22	CV-2304	34.43454	-118.64874	8/17/26	8:53	2,201	8/20/26	Increased flow and cover compaction	8/27/26	228					8/20/26	Increased flow and cover compaction	9/16/26	408					
169	Y23	CV-1532A	34.43389	-118.65082	8/17/26	9:12	2,281	8/20/26	Increased flow and cover compaction	8/27/26	71.2					8/20/26	Increased flow and cover compaction	9/16/26	53.11					
43	Y142	CV-2529	34.4331	-118.64229	8/17/26	8:56	651	8/19/26	Increased flow and cover compaction	8/27/26	13.1					8/19/26	Increased flow and cover compaction	9/16/26	460					
51	Y143	CV-2688	34.43275	-118.64241	8/17/26	9:17	796	8/19/26	Increased flow and cover compaction	8/27/26	4.2					8/19/26	Increased flow and cover compaction	9/16/26	11.23					
39	Y144	CV-2530	34.43277	-118.64286	8/17/26	9:32	987	8/19/26	Increased flow and cover compaction	8/27/26	394					8/19/26	Increased flow and cover compaction	9/16/26	485					
39	Y145	CV-2689	34.43284	-118.64335	8/17/26	9:36	550	8/19/26	Increased flow and cover compaction	8/27/26	11.8					8/19/26	Increased flow and cover compaction	9/16/26	149					
35	Y146	CV-24211	34.4327	-118.64387	8/17/26	10:17	503	8/20/26	Increased flow and cover compaction	8/27/26	18.2					8/20/26	Increased flow and cover compaction	9/16/26	281					
50	Y147	CV-2531	34.43253	-118.64333	8/17/26	10:32	722	8/19/26	Increased flow and cover compaction	8/27/26	52					8/19/26	Increased flow and cover compaction	9/16/26	492					
91	Y148	CV-2533	34.43192	-118.64413	8/17/26	11:00	1,342	8/19/26	Increased flow and cover compaction	8/27/26	49.8					8/19/26	Increased flow and cover compaction	9/16/26	338					
57	B121	H-75	34.43639	-118.64205	8/17/26	9:31	240	8/20/26	Valve adjustment: Increased flow	8/27/26	33.1													
65	B122	C-27	34.43614	-118.641	8/17/26	10:10	427	8/20/26	Cover compaction	8/27/26	100													
64	B123	C-12	34.43599	-118.64085	8/17/26	10:12	446	8/20/26	Increased flow and cover compaction	8/27/26	12.4													
197	B101	Surface	34.43123	-118.64736	8/17/26	9:19	210	8/20/26	Cover compaction	8/27/26	112													
42	B141	H-79	34.43394	-118.64279	8/17/26	8:18	215	8/20/26	Increased flow; boot repair	8/27/26	28.8													
93	B149	18 in pipe	34.43121	-118.64424	8/17/26	11:19	327	8/19/26	Cover compaction	8/27/26	19.2													
40	Y1	Surface	34.43487	-118.64303	8/18/26	9:07	971	8/21/26	Cover compaction	8/27/26	89.4					8/21/26	Cover compaction	9/16/26	131					
40	Y2	Surface	34.43511	-118.64317	8/18/26	9:11	4,476	8/21/26	Cover compaction	8/27/26	19.5					8/21/26	Cover compaction	9/16/26	443					
40	Y3	CV-2663	34.43508	-118.64332	8/18/26	9:13	10,650	8/21/26	Valve adjustment: Increased flow	8/27/26	47.8					8/21/26	Valve adjustment: Increased flow	9/16/26	488					
40	Y4	Surface	34.43501	-118.64331	8/18/26	9:16	10,000	8/21/26	Cover compaction	8/27/26	50					8/21/26	Cover compaction	9/16/26	325					
44	Y5	C-11	34.43526	-118.64129	8/18/26	9:27	5,632	8/21/26	Increased flow and cover compaction	8/27/26	65.6					8/21/26	Increased flow and cover compaction	9/16/26	4.4					
48	Y61	Surface	34.42887	-118.65117	8/18/26	8:10	750	8/21/26	Cover compaction	8/27/26	389					8/21/26	Cover compaction	9/16/26	5.63					
48	Y7	C-9	34.43418	-118.64105	8/18/26	9:41	2,950	8/21/26	Cover compaction	8/27/26	74.1					8/21/26	Cover compaction	9/16/26	473					
48	Y8	C-8	34.43362	-118.64086	8/18/26	9:45	1,083	8/21/26	Increased flow and cover compaction	8/27/26	229					8/21/26	Increased flow and cover compaction	9/16/26	26.4					
223	Y42	CV-2508	34.42971	-118.64874	8/18/26	9:25	501	8/21/26	Valve adjustment: Increased flow	8/27/26	51.5					8/21/26	Valve adjustment: Increased flow	9/16/26	49.01					
226	Y43	CV-2512	34.42923	-118.65063	8/18/26	10:06	540	8/21/26	Increased flow and cover compaction	8/27/26	12.5					8/21/26	Increased flow and cover compaction	9/16/26	19.91					
228	Y44	CV-2510	34.42907	-118.64981	8/18/26	10:37	970	8/21/26	Valve adjustment: Increased flow	8/27/26	114					8/21/26	Valve adjustment: Increased flow	9/16/26	32.88					
243	Y61	Surface	34.42887	-118.65117	8/18/26	8:10	4,623	8/21/26	Cover compaction	8/27/26	96.4					8/21/26	Cover compaction	9/16/26	450					
243	Y62	Surface	34.42882	-118.65107	8/18/26	8:13	4,212	8/21/26	Cover compaction	8/27/26	71.6					8/21/26	Cover compaction	9/16/26	299					
243	Y63	Surface	34.42876	-118.651	8/18/26	8:16	2,343	8/21/26	Cover compaction	8/27/26	10.6					8/21/26	Cover compaction	9/16/26	73.14					
243	Y64	Surface	34.42873	-118.65086	8/18/26	8:22	7,421	8/21/26	Cover compaction	8/27/26	34.6					8/21/26	Cover compaction	9/16/26	489					
243	Y65	Surface	34.42844	-118.65097	8/18/26	8:28	723	8/21/26	Cover compaction	8/27/26	486					8/21/26	Cover compaction	9/16/26	30.36					
242	Y66	ARV	34.42834	-118.65053	8/18/26	8:45	725	8/21/26	Cover compaction	8/27/26	285					8/21/26	Cover compaction	9/16/26	239					
242	Y67	ARV	34.42838	-118.65047	8/18/26	8:46	762	8/21/26	Cover compaction	8/27/26	296					8/21/26	Cover compaction	9/16/26	200					
242	Y68	ARV	34.42847	-118.65022	8/18/26	8:48	823	8/21/26	Cover compaction	8/27/26	131					8/21/26	Cover compaction	9/16/26	75.24					
241	Y69	Surface	34.42855	-118.65013	8/18/26	9:00	893	8/21/26	Cover compaction	8/27/26	59.41					8/21/26	Cover compaction	9/16/26	19.8					
240	Y70	Surface	34.42838	-118.6494	8/18/26	9:17	587	8/21/26	Cover compaction	8/27/26	478					8/21/26	Cover compaction	9/16/26	336					
221	B41	CV-2507	34.43015	-118.64817	8/18/26	9:02	302			8/27/26	15.9													
244	B61	Riser	34.42889	-118.65122	8/18/26	8:08	323			8/27/26	42.4													
241	B62	Surface	34.42851	-118.6499	8/18/26	9:08	200			8/27/26	25.9													
163	Y61	H-1760S	34.43273	-118.64788	8/24/26	8:52	647	8/26/26	Valve adjustment: Increased flow	8/31/26	4.5					8/26/26	Valve adjustment: Increased flow	9/21/26	4.6					
215	Y81	2 in pipe holding header	34.43129	-118.6506	8/24/26	8:18	612	8/26/26	Cover compaction	8/31/26	110					8/26/26	Cover compaction	9/21/26	12.54					
215	Y82	Surface	34.43129	-118.6505	8/24/26	8:21	800	8/26/26	Cover compaction	8/31/26	86.8					8/26/26	Cover compaction	9/21/26	37.66					
198	Y83	Near H-1563S	34.43121	-118.65038	8/24/26	8:27	5,123	8/26/26	Cover compaction	8/31/26	340					8/26/26	Cover compaction	9/21/26	47.96					
196	Y84	Surface	34.43185	-118.64846	8/24/26	9:26	5,412	8/26/26	Cover compaction	8/31/26	163					8/26/26	Cover compaction	9/21/26	5.87					
215	B81	2 in pipe holding header	34.43136	-118.65051	8/24/26	8:23	300	8/26/26	Cover compaction	8/31/26	123													
214	B82	2 in pipe holding header	34.43118	-118.64982	8/24/26	8:38	322	8/26/26	Cover compaction	8/31/26	3.2													
196	B83	CV-24194	34.43187	-118.64846	8/24/26	9:25	321	8/26/26	Increased flow and cover compaction	8/31/26	56.1													
194	B101	CV-2634	34.43138	-118.64545	8/24/26	9:40	223	8/26/26	Increased flow and cover compaction	8/31/26	71.1													
180	Y1	Surface	34.43528	-118.65045	9/1/26	8:19	4,512	9/3/26	Unsafe area; 9/9/26 flow increase	9/11/26	7.22					9/3/26	Unsafe area; 9/9/26 flow increase	9/28/26	286					
180	Y2	Surface	34.43528	-118.65028	9/1/26	8:23	7,542	9/3/26	Tear on liner scheduled repair	9/11/26	6.02					9/3/26	Tear on liner scheduled repair	9/28/26	9.12					
74	Y41	ARV-05	34.437	-118.64469	9/1/26	10:10	612	9/3/26	Boot repaired	9/11/26	51.13					9/3/26	Boot repaired	9/28/26	455					
77	Y42	CV-24121	34.43698	-118.64697	9/1/26	10:26	7,986	9/3/26	Increased flow; Boot repaired	9/11/26	19.74					9/3/26	Increased flow; Boot repaired	9/28/26	34.82					
78	Y43	CV-24123	34.43733	-118.64627	9/1/26	10:38	2,482	9/3/26	Increased flow; Boot repaired	9/11/26	15.16					9/3/26	Increased flow; Boot repaired	9/28/26	231					
82	Y61	CV-2548	34.43435	-118.64558	9/1/26	9:36	1,075	9/3/26	Increased flow and cover compaction	9/11/26	206					9/3/26	Increased flow and cover compaction	9/28/26	26.18					
82	Y62	CV-2549	34.43437	-118.64527	9/1/26	9:39	2,374	9/3/26	Increased flow and cover compaction	9/11/26	143					9/3/26	Increased flow and cover compaction	9/28/26	433					
149	Y63	CV-24154	34.43426	-118.64608	9/1/26	9:46	5,942	9/3/26	Increased flow and cover compaction	9/11/26	24.3					9/3/26	Increased flow and cover compaction	9/28/26	23.44					
160	Y81	CV-24207	34.4333	-118.64693	9/1/26	10:02	878	9/3/26	Increased flow and cover compaction	9/11/26	11.64					9/3/26	Increased flow and cover compaction	9/28/26	69.48					
161	Y82	CV-24185	34.43269	-118.64695	9/1/26	10:09	1,450	9/3/26	Increased flow and cover compaction	9/11/26	17.53					9/3/26	Increased flow and cover compaction	9/28/26	381					
161	Y83	Surface next to CV-24185	34.43267	-118.64692	9/1/26	10:11	3,037	9/3/26	Valve adjustment: Increased flow	9/11/26	24.04					9/3/26	Valve adjustment: Increased flow	9/28/26	88.15					
161	Y84	CV-24184	34.43255	-118.64725	9/1/26	10:16	50,000	9/3/26	Increased flow and cover compaction	9/11/26	5.21					9/3/26	Increased flow and cover compaction	9/28/26	201					
196	Y85	CV-24104	34.4319	-118.64805	9/1/26	10:43	876	9/3/26	Increased flow and cover compaction	9/11/26	6.26					9/3/26	Increased flow and cover compaction	9/28/26	7.23					
196	Y86	CV-24195	34.43195	-118.64761	9/1/26	10:46	3,365	9/3/26	Increased flow and cover compaction	9/11/26	405					9/3/26	Increased flow and cover compaction	9/28/26	11.62					
163	Y87	CV-24090	34.43271	-118.64753	9/1/26	10:56	4,360	9/3/26	Increased flow and cover compaction	9/11/26	263					9/3/26	Increased flow and cover compaction	9/28/26	74.99					
164	Y88	CV-24178	34.43237	-118.64859	9/1/26	11:10	9,765	9/3/26	Increased flow and cover compaction	9/11/26	6.08					9/3/26	Increased flow and cover compaction	9/28/26	466					
164	Y89	Surface next to CV-24176	34.43259	-118.64894	9/1/26	11:15	1,105	9/3/26	Valve adjustment: Increased flow	9/11/26	5.57					9/3/26	Valve adjustment: Increased flow	9/28/26	47.91					

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)

Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
196	B81	CV-2568	34.43219	-118.64774	9/1/26	10:41	420	9/3/26	Increased flow; Boot repaired	9/11/26	64.28													
163	B82	Surface	34.43278	-118.64801	9/1/26	11:02	254	9/3/26	Cover compaction	9/11/26	12.81													
198	B83	CV-24194	34.43188	-118.64851	9/1/26	11:24	244	9/3/26	Increased flow and cover compaction	9/11/26	26.43													
198	B84	CV-24180	34.43213	-118.64881	9/1/26	11:30	345	9/3/26	Construction rerouted vacuum line	9/11/26	19.64													
194	Y61	CV-2634	34.4314	-118.64543	9/2/26	10:23	950	9/4/26	Increased flow and cover compaction	9/11/26	383					9/4/26	Increased flow and cover compaction	9/28/26	18.03					
199	Y62	CV-2501	34.4313	-118.6485	9/2/26	11:18	500	9/4/26	Increased flow and cover compaction	9/11/26	92.17					9/4/26	Increased flow and cover compaction	9/28/26	31.18					
56	Y1	CV-24213	34.43661	-118.64297	9/2/26	8:03	502	9/4/26	Increased flow; Boot repaired	9/11/26	9.52					9/4/26	Increased flow; Boot repaired	9/28/26	198					
69	Y3	Surface	34.43678	-118.64346	9/2/26	10:17	892	9/4/26	Boot repaired	9/11/26	7.19					9/4/26	Boot repaired	9/28/26	5.18					
73	Y4	ARV-04	34.43695	-118.644	9/2/26	10:35	589	9/4/26	Boot repaired	9/11/26	7.24					9/4/26	Boot repaired	9/28/26	4.66					
73	Y5	Surface	34.43727	-118.64363	9/2/26	10:49	702	9/4/26	Boot repaired	9/11/26	6.84					9/4/26	Boot repaired	9/28/26	68.04					
220	Y41	CV-24237	34.43062	-118.65017	9/2/26	8:26	1,162	9/4/26	Increased flow and cover compaction	9/11/26	21.12					9/4/26	Increased flow and cover compaction	9/28/26	7.24					
219	Y42	CV-24227	34.4309	-118.64976	9/2/26	8:37	517	9/4/26	Increased flow and cover compaction	9/11/26	7.72					9/4/26	Increased flow and cover compaction	9/28/26	45.85					
226	Y43	CV-2512	34.42925	-118.65062	9/2/26	9:35	2,296	9/4/26	Increased flow and cover compaction	9/11/26	7.05					9/4/26	Increased flow and cover compaction	9/28/26	105					
228	Y44	CV-2510	34.42908	-118.64982	9/2/26	10:08	1,413	9/4/26	Increased flow and cover compaction	9/11/26	342					9/4/26	Increased flow and cover compaction	9/28/26	12.56					
229	Y45	H-2404N	34.42931	-118.64956	9/2/26	10:19	1,723	9/4/26	Increased flow and cover compaction	9/11/26	22.14					9/4/26	Increased flow and cover compaction	9/28/26	4.33					
229	Y46	CV-24246	34.42871	-118.64948	9/2/26	10:28	7,620	9/4/26	Increased flow and cover compaction	9/11/26	10.13					9/4/26	Increased flow and cover compaction	9/28/26	26.19					
230	Y47	CV-2509	34.42923	-118.64917	9/2/26	10:43	9,847	9/4/26	Increased flow and cover compaction	9/11/26	6.42					9/4/26	Increased flow and cover compaction	9/28/26	251					
209	Y101	CV-24085	34.4324	-118.649	9/2/26	8:34	654	9/4/26	Increased flow and cover compaction	9/11/26	8.26					9/4/26	Increased flow and cover compaction	9/28/26	198					
212	Y102	CV-2565	34.43195	-118.64899	9/2/26	8:42	584	9/4/26	Increased flow and cover compaction	9/11/26	6.98					9/4/26	Increased flow and cover compaction	9/28/26	99.07					
214	Y104	Surface	34.43091	-118.65016	9/2/26	9:50	10,580	9/4/26	Cover compaction	9/11/26	435					9/4/26	Cover compaction	9/28/26	171					
214	Y105	Surface	34.43106	-118.65021	9/2/26	9:52	834	9/4/26	Cover compaction	9/11/26	7.05					9/4/26	Cover compaction	9/28/26	92.1					
210	Y106	Surface	34.43157	-118.65085	9/2/26	10:33	650	9/4/26	Added dirt; Cover Compaction	9/11/26	11.62					9/4/26	Added dirt; Cover Compaction	9/28/26	56.02					
210	Y107	Surface	34.43194	-118.65116	9/2/26	10:39	760	9/4/26	Added dirt; Cover Compaction	9/11/26	7.52					9/4/26	Added dirt; Cover Compaction	9/28/26	306					
210	Y108	Surface	34.43193	-118.65118	9/2/26	10:42	1,050	9/4/26	Added dirt; Cover Compaction	9/11/26	10.13					9/4/26	Added dirt; Cover Compaction	9/28/26	4					
215	Y109	H-1575	34.43118	-118.65045	9/2/26	10:57	4,180	9/4/26	Abandoned well to be buried, cover compaction	9/11/26	39.42					9/4/26	Abandoned well to be buried, cover compaction	9/28/26	211					
215	Y110	Surface	34.431	-118.65051	9/2/26	11:01	30,000	9/4/26	Cover compaction	9/11/26	375					9/4/26	Cover compaction	9/28/26	67.84					
42	Y21	H-79	34.43394	-118.64276	9/2/26	8:19	920	9/4/26	Repaired sample port	9/11/26	22.87					9/4/26	Repaired sample port	9/28/26	8.22					
43	Y22	CV-2529	34.43309	-118.6423	9/2/26	9:23	620	9/4/26	Increased flow and cover compaction	9/11/26	64.31					9/4/26	Increased flow and cover compaction	9/28/26	230					
42	Y23	Surface	34.43394	-118.64229	9/2/26	8:27	500	9/4/26	Boot repaired	9/11/26	401					9/4/26	Boot repaired	9/28/26	3.85					
51	Y24	CV-2688	34.43273	-118.6424	9/2/26	9:32	523	9/4/26	Increased flow and cover compaction	9/11/26	396					9/4/26	Increased flow and cover compaction	9/28/26	71.26					
51	Y25	Surface	34.43258	-118.64227	9/2/26	9:43	520	9/4/26	Cover compaction	9/11/26	83.23					9/4/26	Cover compaction	9/28/26	17.88					
50	Y26	CV-2690	34.43239	-118.64288	9/2/26	9:50	814	9/4/26	Increased flow and cover compaction	9/11/26	25.83					9/4/26	Increased flow and cover compaction	9/28/26	23.42					
92	Y27	Surface	34.43198	-118.64377	9/2/26	10:08	902	9/4/26	Cover compaction	9/11/26	375					9/4/26	Cover compaction	9/28/26	5.56					
92	Y28	CV-2692	34.43163	-118.64446	9/2/26	10:33	1,813	9/4/26	Increased flow and cover compaction	9/11/26	151					9/4/26	Increased flow and cover compaction	9/28/26	19.04					
91	Y29	SMS Pump	34.43153	-118.64432	9/2/26	10:42	1,342	9/4/26	Cover compaction	9/11/26	175					9/4/26	Cover compaction	9/28/26	43.12					
93	Y30	Surface	34.43141	-118.64358	9/2/26	10:48	2,143	9/4/26	Cover compaction	9/11/26	22.19					9/4/26	Cover compaction	9/28/26	432					
56	B2	H-1807N	34.43646	-118.64352	9/2/26	8:14	322	9/4/26	Increased flow; Boot repaired	9/11/26	8.1													
213	B101	CV-24192	34.43128	-118.64941	9/2/26	8:58	209	9/4/26	Increased flow and cover compaction	9/11/26	9.3													
210	B102	H-1406W	34.43216	-118.65079	9/2/26	10:16	223	9/4/26	Increased flow and cover compaction	9/11/26	154													
215	B103	CWHSMP01	34.43128	-118.65064	9/2/26	10:51	337	9/4/26	Cover compaction	9/11/26	16.92													
52	B21	Surface	34.433	-118.64167	9/2/26	9:08	221	9/4/26	Cover compaction	9/11/26	54.13													
51	B22	CV-05	34.43284	-118.64223	9/2/26	9:35	321	9/4/26	Increased flow and cover compaction	9/11/26	87.6													
93	B23	HV-045A	34.43123	-118.64382	9/2/26	10:53	231	9/4/26	Increased flow and cover compaction	9/11/26	54.73													
93	B24	Surface	34.43104	-118.64401	9/2/26	10:55	312	9/4/26	Cover compaction	9/11/26	39.72													
197	Y22	CV-2503	34.43121	-118.64773	9/9/26	9:26	824	9/11/26	Increased flow; Boot repaired	9/16/26	188													
194	Y23	CV-2634	34.4314	-118.64545	9/9/26	9:56	9,601	9/11/26	Increased flow and cover compaction	9/16/26	77.95													
96	Y24	CV-2627	34.431	-118.64617	9/9/26	10:03	925	9/11/26	Increased flow and cover compaction	9/16/26	83.38													
41	Y41	CV-55R	34.43439	-118.64279	9/9/26	10:04	2,174	9/11/26	Increased flow; Boot repaired	9/16/26	82.64													
41	Y42	2-inch pipe near CV-55R	34.4344	-118.64277	9/9/26	10:06	1,666	9/11/26	Boot repaired	9/16/26	5.5													
41	Y43	CV-2011A	34.43455	-118.64317	9/9/26	10:11	854	9/11/26	Increased flow; Boot repaired	9/16/26	236													
208	Y44	2-inch pipe near CV-2001	34.43227	-118.6506	9/9/26	10:56	2,460	9/10/26	Boot repaired	9/16/26	19.66													
208	Y45	2-inch pipe	34.43234	-118.65089	9/9/26	11:00	892	9/10/26	Boot repaired	9/16/26	15.07													
208	Y46	Surface	34.43227	-118.65112	9/9/26	11:03	2,700	9/10/26	Cover compaction	9/16/26	25.81													
210	Y47	H-1406W	34.43215	-118.65081	9/9/26	11:11	2,862	9/10/26	Increased flow and cover compaction	9/16/26	373													
210	Y48	Surface	34.43192	-118.65075	9/9/26	11:08	2,653	9/10/26	Cover compaction	9/16/26	53.13													
210	Y49	Surface	34.43167	-118.6505	9/9/26	11:17	20,000	9/10/26	Cover compaction	9/16/26	11.26													
215	Y50	Surface	34.4313	-118.65052	9/9/26	11:37	510	9/10/26	Cover compaction	9/16/26	33.97													
215	Y51	H-1575	34.43119	-118.65041	9/9/26	11:35	3,462	9/10/26	Cover compaction	9/16/26	107													
215	Y52	Surface	34.43102	-118.65047	9/9/26	11:33	50,000	9/10/26	Cover compaction	9/16/26	227													
218	Y21	CV-2502	34.43089	-118.6491	9/9/26	8:35	2,441	9/11/26	Increased flow; Boot repaired	9/16/26	12.28													
78	Y21	CV-24146	34.43732	-118.64627	9/10/26	9:25	2,848	9/11/26	Valve adjustment: Increased flow	9/16/26	3.67													
28	Y22	Surface near CV-24146	34.43733	-118.64627	9/10/26	9:26	500	9/11/26	Valve adjustment: Increased flow	9/16/26	5.13													
180	Y41	Surface	34.4353	-118.65049	9/10/26	8:29	640	9/11/26	Liner repaired	9/16/26	49.53													
172	Y42	CV-2304	34.43458	-118.64872	9/10/26	9:45	20,000	9/11/26	Increased flow; Boot repaired	9/16/26	407													
170	Y101	CV-24058	34.43379	-118.64943	9/10/26	8:44	10,000	9/11/26	Increased flow and tightened clamps	9/16/26	3.71													
133	Y102	CV-24036	34.43446	-118.64967	9/10/26	8:56	587	9/11/26	Increased flow and cover compaction	9/16/26	3.81													
210	Y101	Surface	34.43172	-118.65086	9/21/26	8:47	502	9/23/26	Cover compaction	9/28/26	323													
211	Y102	Surface	34.43154	-118.6501	9/21/26	9:20	1,623	9/23/26	Cover compaction	9/28/26	9.12													
211	Y103	CV-24188	34.43151	-118.65012	9/21/26	9:23	842	9/23/26	Increased flow and cover compaction	9/28/26	338													
211	Y104	2 in pipe	34.43147	-118.64962	9/21/26	9:37	2,848	9/23/26	Cover compaction	9/28/26	207													
213	Y105	Surface	34.43137	-118.64937	9/21/26	9:39	500	9/23/26	Cover compaction	9/28/26	250													
217	Y106	6 in riser out of liner	34.43077	-118.64851	9/21/26	10:05	4,232	9/23/26	Boot repaired	9/28/26	96.83													
197	Y107	CV-2503	34.43122	-118.64776	9/21/26	10:21	1,742	9/23/26	Increased flow; Boot repaired	9/28/26	159													
197	Y108	H-1408CR	34.43156	-118.64759	9/21/26	10:27	500	9/23/26	Increased flow; Boot repaired	9/28/26	100													
195	Y109	CV-24201	34.43175	-118.64664	9/21/26	10:36	2,513	9/23/26	Wellhead crack reported; 9/28/26 Increased flow	9/28/26	161													

2026 Chiquita Surface Emissions Exceedance

Instantaneous (Monthly)																							
Grid	Flag	Location Description	Latitude	Longitude	Initial Date	Initial Time	Initial Exceedance >500, 200-499 (PPM)	10-Day Corrective Action Date	10-Day Corrective Action	First Remonitoring Date (10-days)	PPM	2nd 10-Day Corrective Action Date	2nd 10-Day Corrective Action	Second Remonitoring Date (10-days)	PPM	Monthly Corrective Action Date	Monthly Corrective Action	Monthly Remonitoring Date	PPM	45-Day Corrective Action Deadline	45-Day Corrective Action Date	45-Day Corrective Action	45-Day Corrective Action Date / Remonitoring Date	PPM
195	Y110	CV-24206	34.43152	-118.64677	9/21/26	10:43	3,241	9/23/26	Increased flow; Boot repaired	9/28/26	399													
99	Y111	Surface	34.43132	-118.64681	9/21/26	10:45	923	9/23/26	Liner was installed	9/28/26	18.43													
88	Y81	CV-24202	34.4319	-118.64628	9/21/26	11:25	605	9/23/26	Increased flow; Boot repaired	9/28/26	10.85													
82	Y61	CV-2548	34.43434	-118.64556	9/21/26	9:33	2,365	9/23/26	Increased flow and cover compaction	9/28/26	81.03													
84	Y62	CV-1905	34.43349	-118.646	9/21/26	9:46	1,214	9/23/26	Increased flow and cover compaction	9/28/26	296													
33	Y63	H-2169E	34.43422	-118.64421	9/21/26	10:29	10,000	9/23/26	Increased flow and cover compaction	9/28/26	480													
194	B81	CV-2634	34.43138	-118.64547	9/21/26	11:40	365	9/23/26	Cover compaction	9/28/26	176													

Attachment C-2

Aerial Survey Maps

September 2026 Condition 77 Data

Chiquita Canyon Landfill (Chiquita) recorded fewer peak methane events in September 2026 than in August 2026, although the peak methane value remained unchanged and the average verified peak methane value increased during the same period.

All 24 peak methane events recorded in September occurred during four drone surveys conducted on September 1, 9, 16, and 22, 2026. No peak methane events were identified during the September 30, 2026 drone survey. These events coincided with temporary equipment downtime, surface cracking, or both, as described below.

The drone survey conducted on September 1, 2026, occurred during and following an unplanned downtime of Flare 3 and coincided with surface cracking. This survey accounted for 5 of the 24 (~21%) peak methane events recorded in September. The surface cracking was addressed through the addition of soil and track walking on September 3.

The drone survey conducted on September 9, 2026, occurred during unplanned downtimes of the Zeeco #7 and Parnel thermal oxidizers and coincided with surface cracking. This survey accounted for 13 of the 24 (~54%) peak methane events recorded in September. The surface cracking was addressed through the addition of soil and track walking on September 11.

The drone survey conducted on September 16, 2026, occurred on the same day as unplanned downtimes of Flare 3 and coincided with surface cracking. This survey accounted for 5 of the 24 (~21%) peak methane events recorded in September. The surface cracking was addressed through the addition of soil and track walking on September 17.

The drone survey conducted on September 22, 2026, occurred on the same day as unplanned downtimes involving Flares 2 and 3 and the Parnel thermal oxidizer and coincided with surface cracking. This survey accounted for 1 of the 24 (~4%) peak methane events recorded in September. The surface cracking was addressed through the addition of soil and track walking on September 23.

The drone survey conducted on September 30, 2026, identified no peak methane events. Results from the continuation of that survey on October 1, 2026, will be included in the October monthly report, to be submitted in November 2026.

Chiquita expects the number of peak methane events and associated methane values to trend downward provided the relevant systems remain online and in good working order.

September 2026 Tracking Spreadsheet

Chiquita Canyon Landfill (September 2026) - Prepared Pursuant to Condition 77 of the Stipulated Order for Abatement in Case No. 6177-4

Aerial Surveillance Reading Date (UTC)	Aerial Surveillance Reading Time (UTC)	Follow-up Field Inspection Date (UTC)	Follow-up Field Inspection Time (UTC)	Grid	Verified Lat	Verified Long	Sniffer Drone PPM	Verified PPM	Action Required (≥ 500 PPM)	Cause of Exceedance (≥ 500 ppmv methane)	Action Taken	Date Action Taken
9/1/26	19:38	9/1/2026	20:04	149	34.43436	-118.64579	273	2,000	Yes	crack on surface	added soil track walk	9/3/2026
9/1/26	22:42	9/1/2026	23:06	164	34.43269	-118.64825	262	2,000	Yes	crack on surface	added soil track walk	9/3/2026
9/1/26	22:46	9/1/2026	23:12	89	34.43285	-118.64622	340	1,000	Yes	crack on surface	added soil track walk	9/3/2026
9/1/26	23:44	9/2/2026	0:11	95	34.43028	-118.64479	460	1,000	Yes	crack on surface	added soil track walk	9/3/2026
9/1/26	23:46	9/2/2026	0:19	92	34.43177	-118.64374	272	640	Yes	crack on surface	added soil track walk	9/3/2026
9/9/26	14:57	Unable to manually verify	-	210	-	-	540	-	No			
9/9/26	14:57	Unable to manually verify	-	210	-	-	202	-	No			
9/9/26	16:05	9/9/2026	16:19	215	34.43138	-118.65053	978	1,000	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	16:07	9/9/2026	16:25	226	34.42984	-118.65062	395	680	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	16:39	9/9/2026	17:00	240	34.42829	-118.64930	205	570	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	16:39	9/9/2026	17:04	240	34.42839	-118.64967	204	3,000	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	16:45	9/9/2026	17:12	221	34.43018	-118.64816	237	1,000	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	16:51	9/9/2026	17:59	194	34.43133	-118.64561	638	2,000	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	17:21	9/9/2026	17:44	161	34.43287	-118.64676	463	1,000	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	17:23	9/9/2026	17:46	89	34.43281	-118.64623	338	550	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	17:23	9/9/2026	17:48	89	34.43259	-118.64636	213	690	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	18:17	9/9/2026	18:31	95	34.43036	-118.64471	255	500	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	18:17	9/9/2026	18:34	95	34.43022	-118.64488	278	520	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	18:20	9/9/2026	18:47	92	34.43168	-118.64367	273	720	Yes	crack on surface	added soil track walk	9/11/2026
9/9/26	18:21	9/9/2026	18:40	87	34.43133	-118.64494	1,750	7,000	Yes	crack on surface	added soil track walk	9/11/2026
9/16/26	15:57	9/16/2026	17:09	84	34.43322	-118.64558	208	2,000	Yes	crack on surface	added soil track walk	9/17/2016
9/16/26	16:36	9/16/2026	16:52	95	34.43036	-118.64477	213	2,000	Yes	crack on surface	added soil track walk	9/17/2016
9/16/26	16:40	9/16/2026	16:56	93	34.43121	-118.64446	425	570	Yes	crack on surface	added soil track walk	9/17/2016
9/16/26	16:41	9/16/2026	16:59	92	34.43171	-118.64409	260	540	Yes	crack on surface	added soil track walk	9/17/2016
9/16/26	18:27	9/16/2026	18:46	239	34.42832	-118.64921	217	990	Yes	crack on surface	added soil track walk	9/17/2016
9/22/26	16:28	9/22/2026	16:59	91	34.43169	-118.64422	202	800	Yes	crack on surface	added soil track walk	9/23/2026
9/30/26	22:52	N/A	N/A	N/A	N/A	N/A	No peaks detected	N/A	No			

Week 36 (September 1, 2026)

Waste Connections - Chiquita Canyon Landfill
Project: 2026 09 Week 36 Emission Study
Job: Non-Compliance Emission Study
Report Submitted Sep 2, 2026

Emission Study Daily Peaks Verification Report

Information presented within provides results from the emissions monitoring inspection performed by technicians with Sniffer Robotics, Inc. associated with the emission study site and date listed herein. Following the inspection, this report will be updated and disseminated by no later than 12:00 PM local time the next morning.

This report provides details of methane leak locations as determined by the SnifferDRONE™ and manual verification of those leak locations as determined by handheld methane detectors. When an aerial surveillance reading reaches or exceeds 200 PPM methane, a follow-up ground-based surface emissions monitoring field inspection is conducted according to the procedures of OTM-51 and U.S. EPA Method 21, except in the case(s) that the site is unable to monitor the locations due to inaccessibility or dangerous conditions. Report details include: coordinate locations of SnifferDRONE leaks and manual verifications, associated location descriptions (where applicable), date and time of verified readings, SnifferDRONE identified and manually verified PPM values, additional notes, map(s) displaying locations of leaks, and photographic documentation of leaks.

Key

Manual Verification ≥ 500 ppm
Manual Verification < 500 ppm

This daily report is not meant for compliance purposes and only intended for customer review.

WEATHER CONDITIONS	
Date:	**1-Sep**
Sky:	Clear Sky
Ground:	Dry
Temperature:	83 °F
Wind Direction:	SW
Wind Speed:	6 MPH
Barometric Pressure:	30.45"
Humidity:	32%

LOCATION DETAILS						INSPECTION RESULTS						
Ref	**SnifferDRONE Lat**	**SnifferDRONE Long**	**Verified Lat**	**Verified Long**	**Location Description**	**SnifferDRONE Date (UTC)**	**SnifferDRONE Time (UTC)**	**SnifferDRONE PPM**	**Verified Date (UTC)**	**Verified Time (UTC)**	**Verified PPM**	**Notes**
1	34.434269	-118.645784	34.434363	-118.645791		9/1/2026	19:38	273	9/1/2026	20:04	***2,000***	
2	34.432691	-118.648335	34.432691	-118.648251		9/1/2026	22:42	262	9/1/2026	23:06	***2,000***	
3	34.432872	-118.646257	34.432852	-118.646222		9/1/2026	22:46	340	9/1/2026	23:12	***1,000***	
4	34.430262	-118.644853	34.430280	-118.644791		9/1/2026	23:44	460	9/2/2026	0:11	***1,000***	
5	34.431753	-118.643693	34.431768	-118.643737		9/1/2026	23:46	272	9/2/2026	0:19	***640***	

Peak Verification Map

Project: 2026 09 Week 36 Emission Study
Job: Emission Study
Report Submitted Sep 2, 2026



Legend

Peak Verification	Drone Flight Peaks
0 – 499 PPM	200 - 499 PPM
500+ PPM	500 + PPM

This map provides an overview of all increased meter readings of methane, or "Drone Flight Peaks", over the course of the inspection and the manual verification measurements taken at each peak.

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 200 400 800

Feet



Vantor



1. SnifferDRONE Verification



2. SnifferDRONE Verification



3. SnifferDRONE Verification



4. SnifferDRONE Verification



5. SnifferDRONE Verification



Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
1-Sep	Clear Sky	83 °F	6 MPH	SW	32%	30.45"

sniffer

Chiquita Canyon Interpolated Methane Emissions Change as Recorded by the SnifferDRONE™, Aug 2026 to Sep 2026

08/27/26 - 09/01/26

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N
3. Mean change from Aug. 2026 to Sep. 2026 was a 0.99 PPM decrease. Colors represent standard deviations from the mean. PPMs within one standard deviation are not shown.

Legend

- 875 - 38 PPM Decrease
- 37 - 23 PPM Decrease
- 22 - 8 PPM Decrease
- 7 PPM Decrease - 6 PPM Increase
- 7 - 21 PPM Increase
- 22 - 228 PPM Increase



Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
1-Sep	Clear Sky	83 °F	6 MPH	SW	32%	30.45"

Chiquita Canyon Landfill Interpolated Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing & High-Res Image

Sep 1, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 200 400 800
Feet

Legend

CH4 PPM

200
156.64
117.58
78.52
39.45
0



	Leak Count	Estimated Exceedance*
200-499 PPM	5	3
500-1000 PPM	0	0
1000-2000 PPM	0	0
2000-5000 PPM	0	0
5000+ PPM	0	0
Total	5	3

* Calculated using probabilities of peak locations manually verified to have emissions of 500+ ppm based on ongoing field studies

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
1-Sep	Clear Sky	83 °F	6 MPH	SW	32%	30.45"

sniffer

Chiquita Canyon Landfill Methane Emissions Local Peak Values as Recorded by the SnifferDRONE™, over As-Built Drawing & High-Res Image

Sep 1, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N


Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 4,999 PPM
- 5000 + PPM

N

0 200 400 800

Feet

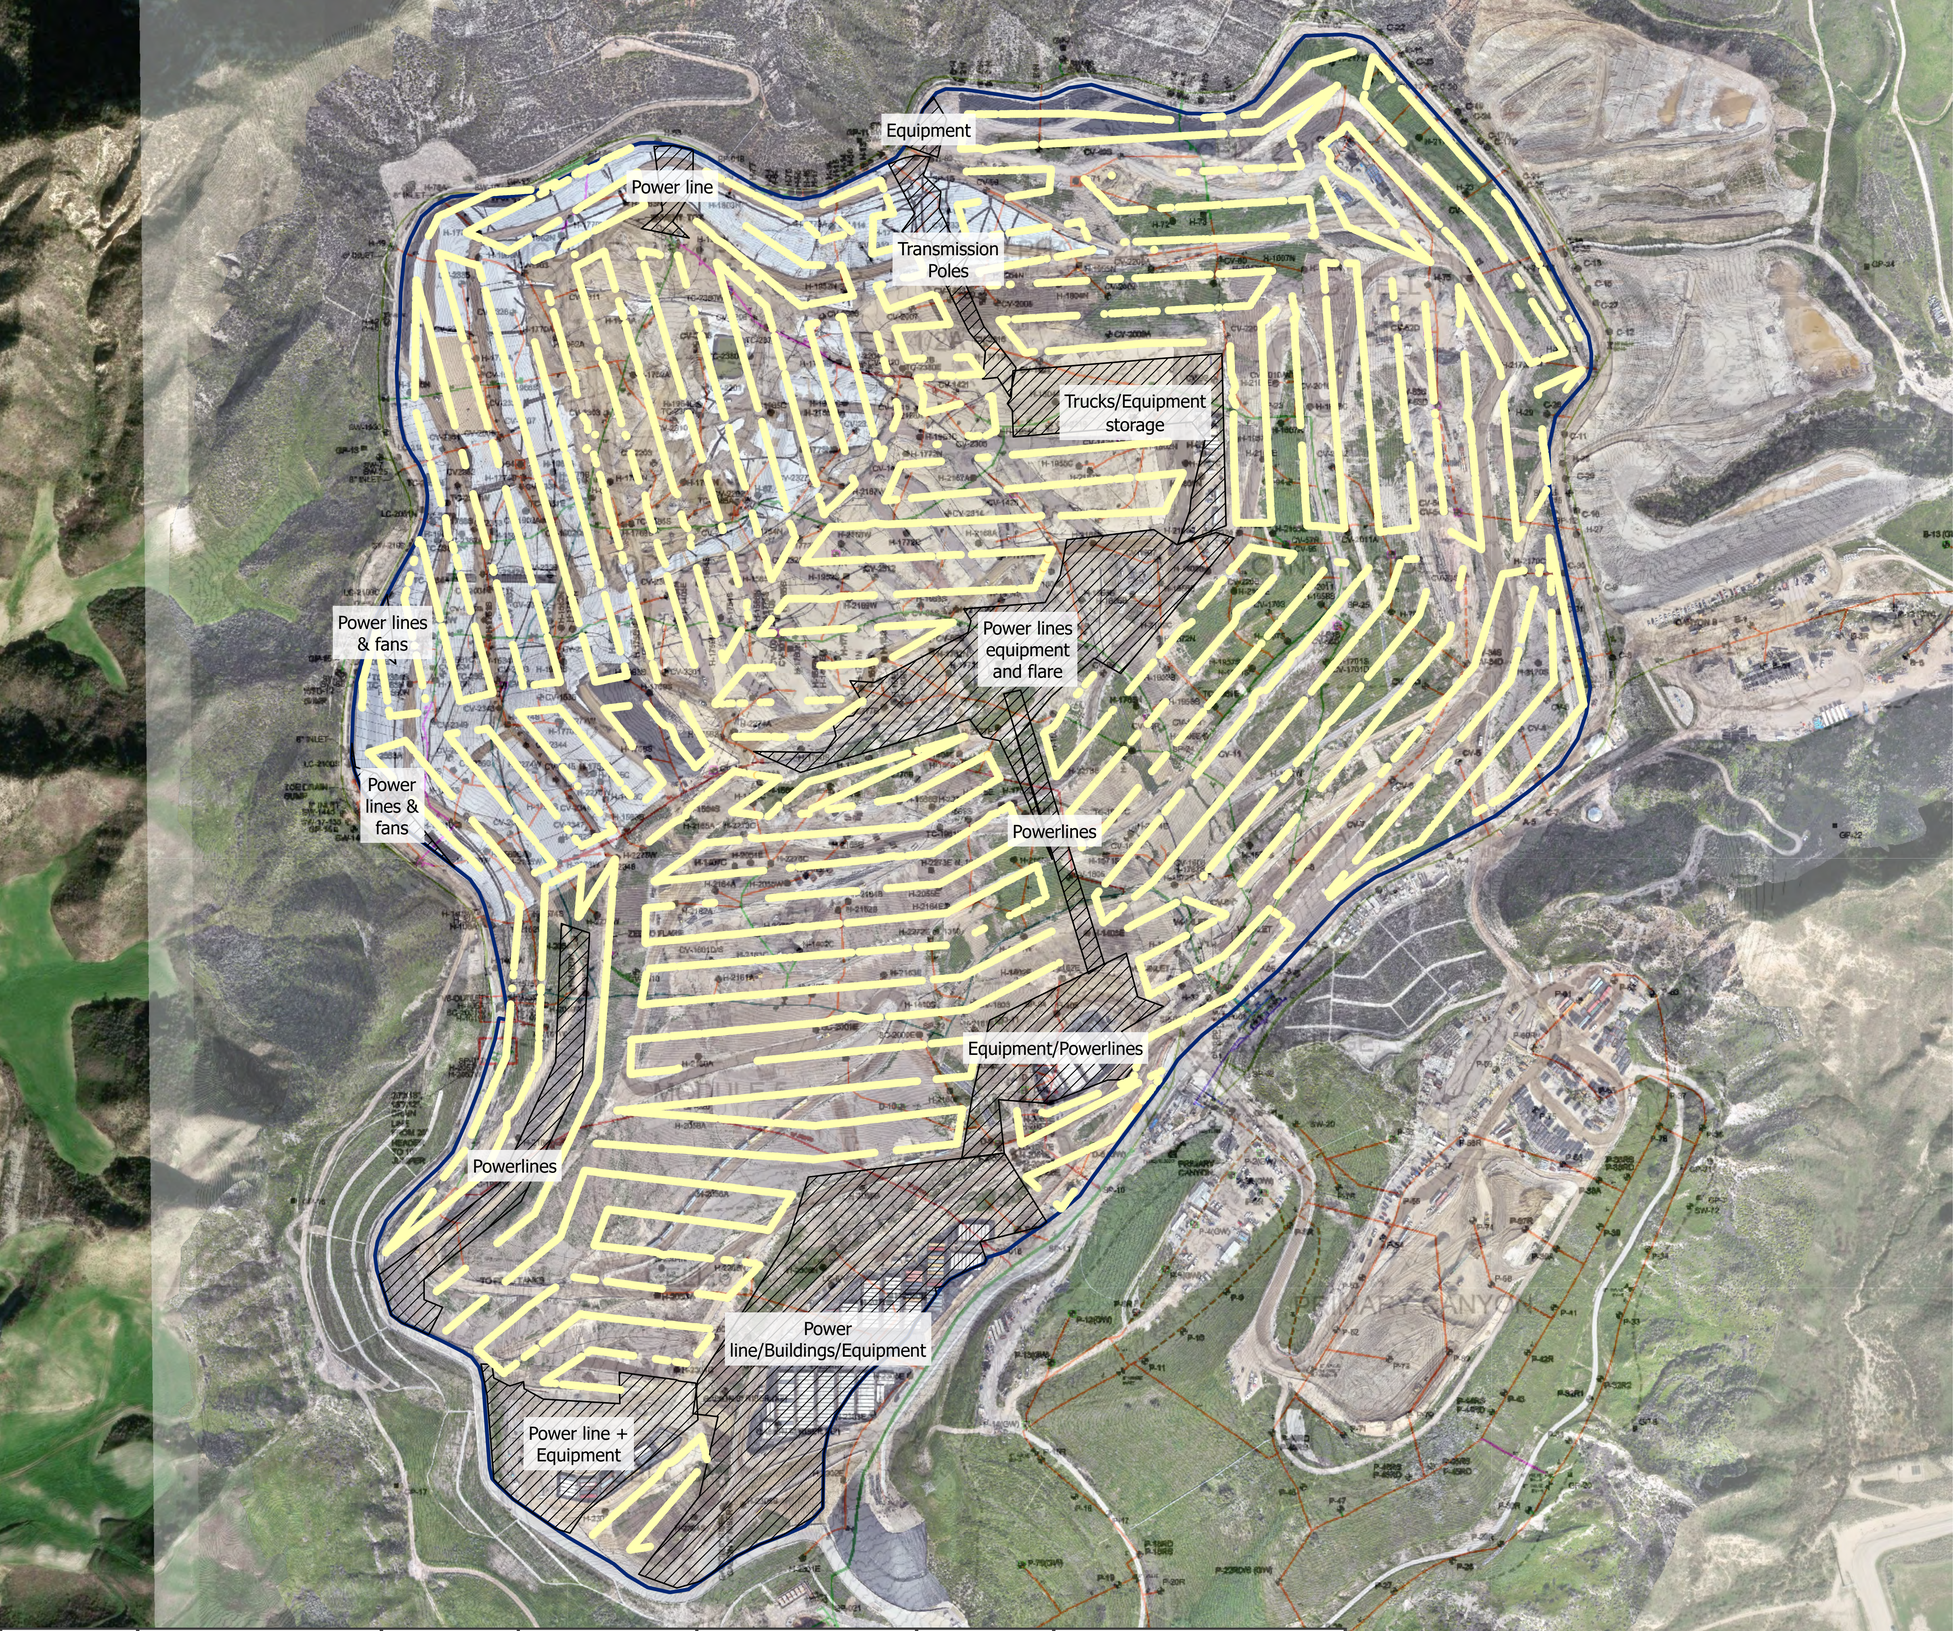

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
1-Sep	Clear Sky	83 °F	6 MPH	SW	32%	30.45"

Chiquita Canyon Landfill Point Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing & High-Res Image

Sep 1, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 200 400 800
Feet

Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 5,000 PPM
- 5,000 + PPM

Week 37 (September 9, 2026)

Waste Connections - Chiquita Canyon Landfill
Project: 2026 09 Week 37 Emission Study
Job: Non-Compliance Emission Study
Report Submitted Sep 10, 2026

Emission Study Daily Peaks Verification Report

Information presented within provides results from the emissions monitoring inspection performed by technicians with Sniffer Robotics, Inc. associated with the emission study site and date listed herein. Following the inspection, this report will be updated and disseminated by no later than 12:00 PM local time the next morning.

This report provides details of methane leak locations as determined by the SnifferDRONE™ and manual verification of those leak locations as determined by handheld methane detectors. When an aerial surveillance reading reaches or exceeds 200 PPM methane, a follow-up ground-based surface emissions monitoring field inspection is conducted according to the procedures of OTM-51 and U.S. EPA Method 21, except in the case(s) that the site is unable to monitor the locations due to inaccessibility or dangerous conditions. Report details include: coordinate locations of SnifferDRONE leaks and manual verifications, associated location descriptions (where applicable), date and time of verified readings, SnifferDRONE identified and manually verified PPM values, additional notes, map(s) displaying locations of leaks, and photographic documentation of leaks.

Key

Manual Verification ≥ 500 ppm
Manual Verification < 500 ppm

This daily report is not meant for compliance purposes and only intended for customer review.

WEATHER CONDITIONS	
Date:	**9-Sep**
Sky:	Clear Sky
Ground:	Dry
Temperature:	103 °F
Wind Direction:	E
Wind Speed:	3 MPH
Barometric Pressure:	30.45"
Humidity:	24%

LOCATION DETAILS						INSPECTION RESULTS						
Ref	SnifferDRONE Lat	SnifferDRONE Long	Verified Lat	Verified Long	Location Description	SnifferDRONE Date (UTC)	SnifferDRONE Time (UTC)	SnifferDRONE PPM	Verified Date (UTC)	Verified Time (UTC)	Verified PPM	Notes
1	34.431356	-118.644862	34.431329	-118.644939	-	9/9/2026	18:21	1,750	9/9/2026	18:40	***7,000***	
2	34.428376	-118.649743	34.428391	-118.649674	-	9/9/2026	16:39	204	9/9/2026	17:04	***3,000***	
3	34.431341	-118.645547	34.431335	-118.645611	-	9/9/2026	16:51	638	9/9/2026	17:59	***2,000***	
4	34.431438	-118.650474	34.431381	-118.650533	-	9/9/2026	16:05	978	9/9/2026	16:19	***1,000***	
5	34.430101	-118.648205	34.430178	-118.648160	-	9/9/2026	16:45	237	9/9/2026	17:12	***1,000***	
6	34.432901	-118.646718	34.432870	-118.646765	-	9/9/2026	17:21	463	9/9/2026	17:44	***1,000***	
7	34.431731	-118.643666	34.431678	-118.643671	-	9/9/2026	18:20	273	9/9/2026	18:47	***720***	
8	34.432612	-118.646320	34.432593	-118.646358	-	9/9/2026	17:23	213	9/9/2026	17:48	***690***	
9	34.429896	-118.650613	34.429839	-118.650621	-	9/9/2026	16:07	395	9/9/2026	16:25	***680***	
10	34.428326	-118.649260	34.428289	-118.649302	-	9/9/2026	16:39	205	9/9/2026	17:00	***570***	
11	34.432851	-118.646249	34.432805	-118.646226	-	9/9/2026	17:23	338	9/9/2026	17:46	***550***	
12	34.430179	-118.644929	34.430221	-118.644883	-	9/9/2026	18:17	278	9/9/2026	18:34	***520***	
13	34.430349	-118.644776	34.430363	-118.644707	-	9/9/2026	18:17	255	9/9/2026	18:31	***500***	
14	34.432080	-118.650958	-	-	-	9/9/2026	14:57	540	-	-	-	Unable to verify - unsafe conditions
15	34.432235	-118.651145	-	-	-	9/9/2026	14:57	202	-	-	-	Unable to verify - unsafe conditions

Peak Verification Map

Project: 2026 09 Week 37 Emission Study
Job: Emission Study
Report Submitted Sep 10, 2026



Legend

Peak Verification	Drone Flight Peaks
0 – 499 PPM	200 - 499 PPM
500+ PPM	500 + PPM


This map provides an overview of all increased meter readings of methane, or "Drone Flight Peaks", over the course of the inspection and the manual verification measurements taken at each peak.

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 250 500 1,000

Feet

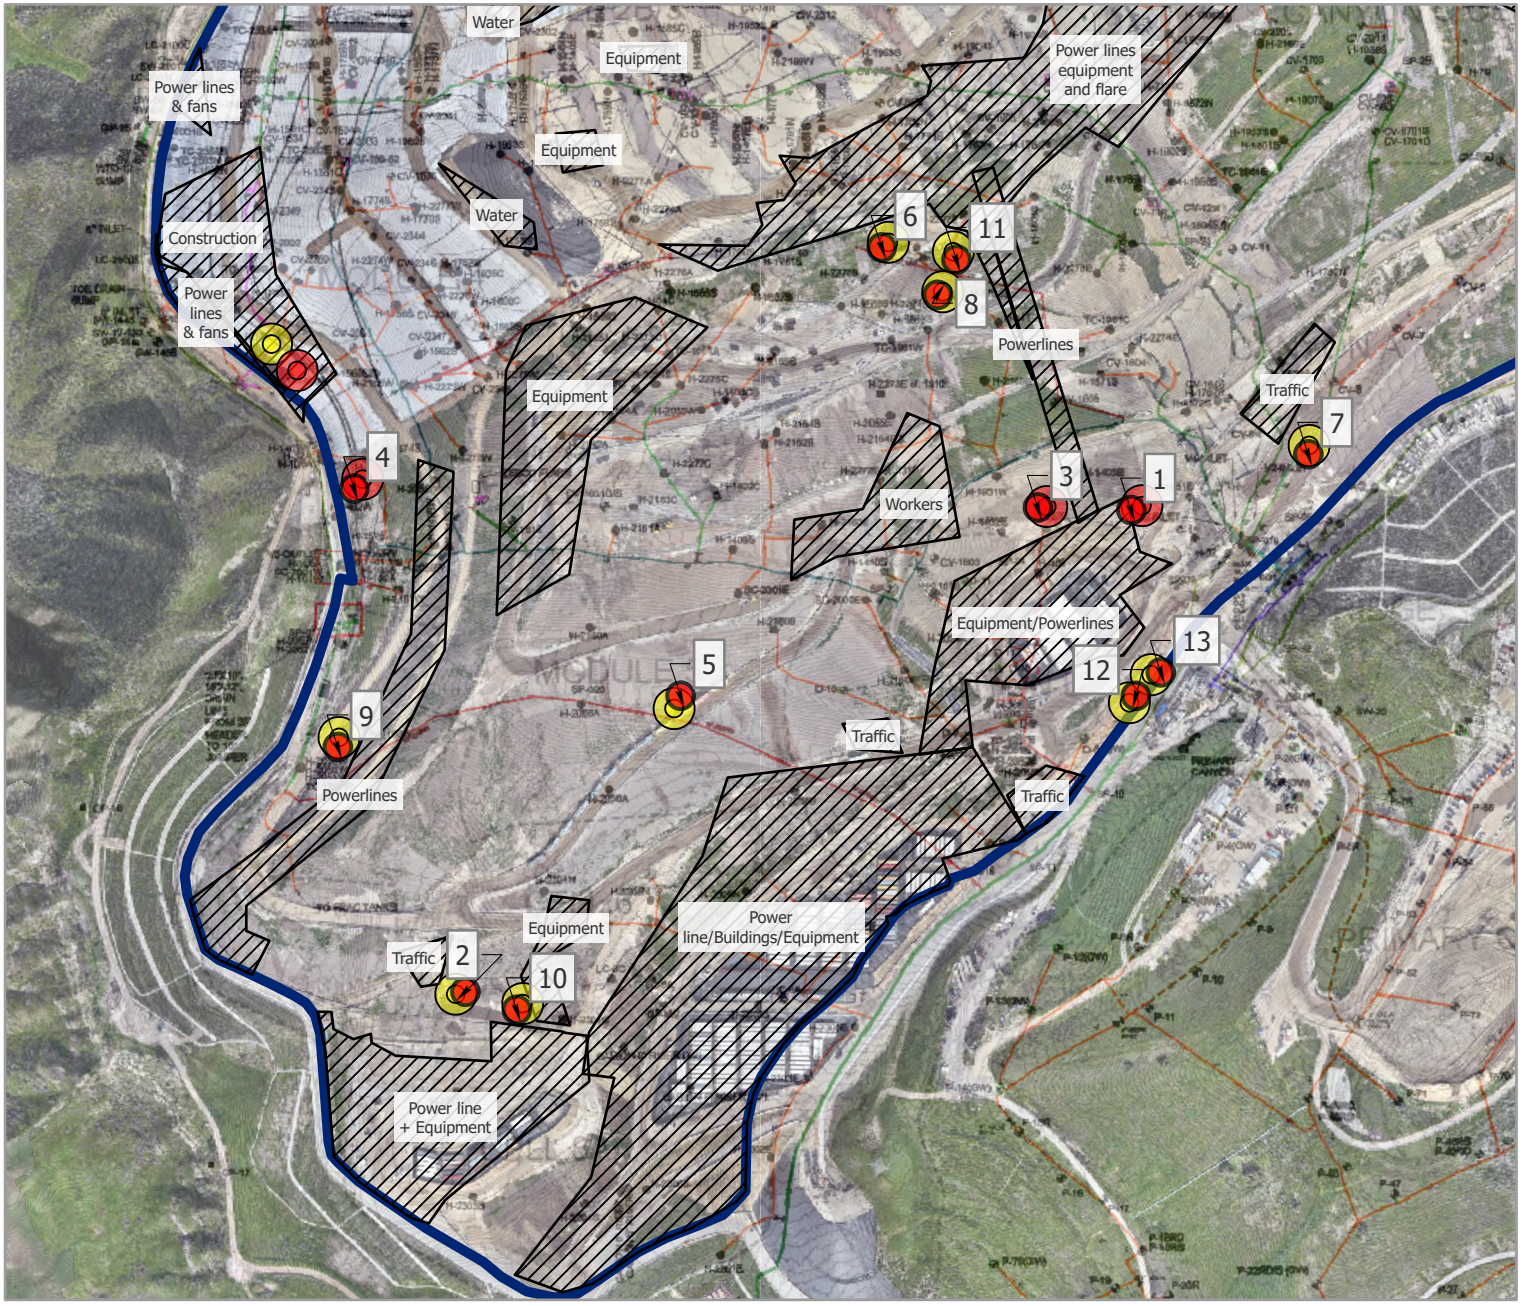


Vantor



1. SnifferDRONE Verification




2. SnifferDRONE Verification

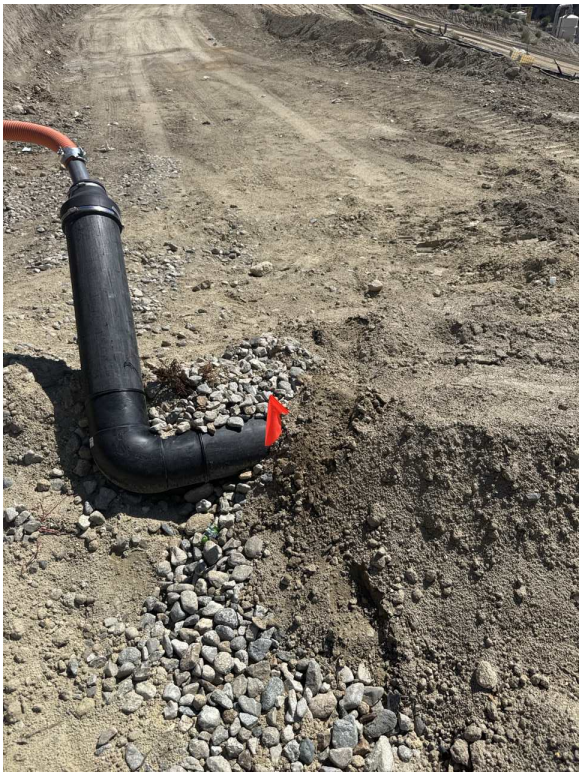

3. SnifferDRONE Verification




4. SnifferDRONE Verification

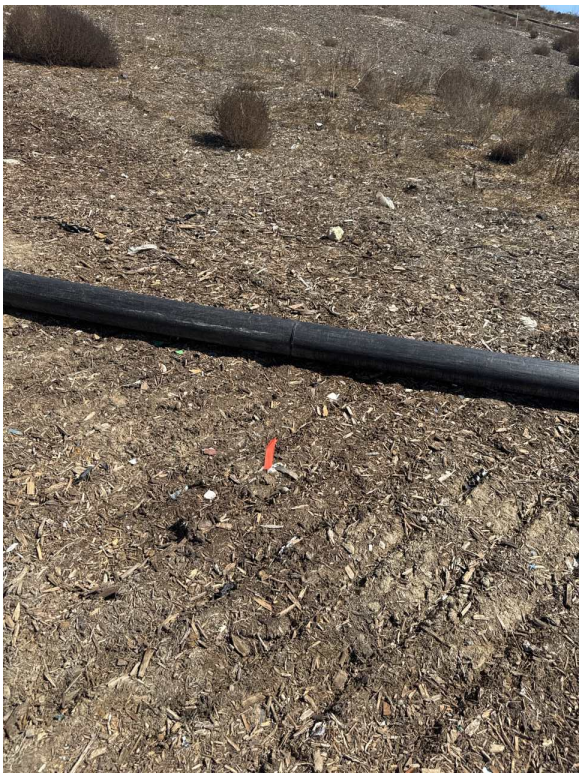

5. SnifferDRONE Verification




6. SnifferDRONE Verification

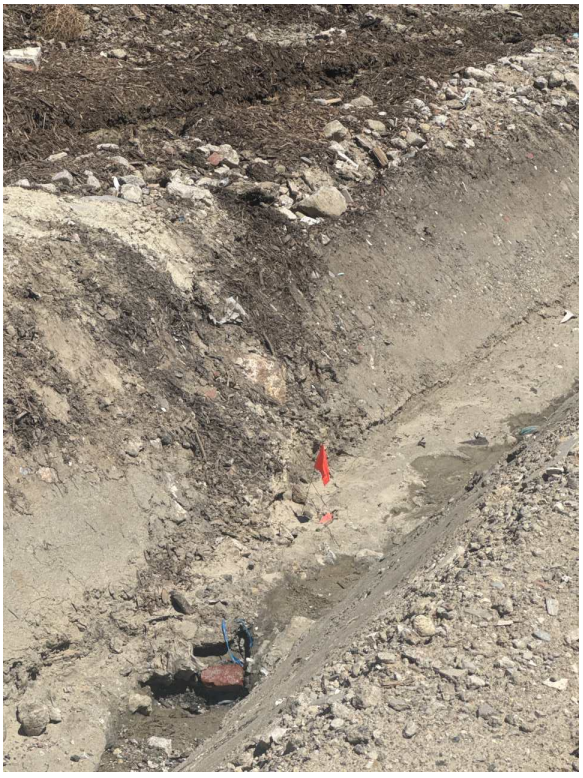

7. SnifferDRONE Verification



8. SnifferDRONE Verification

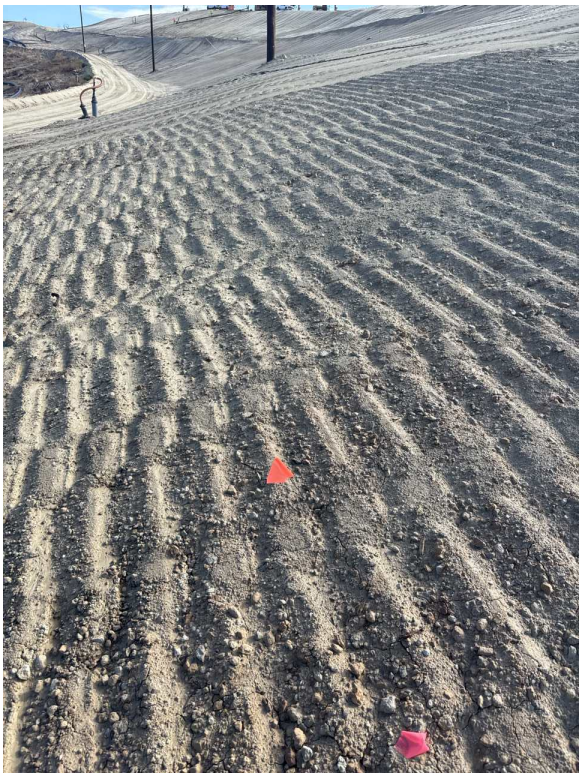

9. SnifferDRONE Verification



10. SnifferDRONE Verification



11. SnifferDRONE Verification



12. SnifferDRONE Verification



13. SnifferDRONE Verification



Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
9-Sep	Clear Sky	103 °F	3 MPH	E	24%	30.45"

sniffer

Chiquita Canyon Interpolated Methane Emissions Change as Recorded by the SnifferDRONE™, Sep 2026 to Sep 2026

9/1/26 - 9/9/26

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N
3. Mean change from Sep. 2026 to Sep. 2026 was a 1.01 PPM decrease. Colors represent standard deviations from the mean. PPMs within one standard deviation are not shown.
4. PRIVILEGED AND CONFIDENTIAL

Legend

- 280 - 45 PPM Decrease
- 44 - 27 PPM Decrease
- 26 - 10 PPM Decrease
- 9 PPM Decrease - 8 PPM Increase
- 9 - 25 PPM Increase
- 26 - 43 PPM Increase
- 44 - 1,022 PPM Increase



Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
9-Sep	Clear Sky	103 °F	3 MPH	E	24%	30.45"

Chiquita Canyon Landfill Interpolated Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing & High-Res Image

Sep 9, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N


N

0 200 400 800
Feet

Legend

CH4 PPM

200
156.64
117.58
78.52
39.45
0

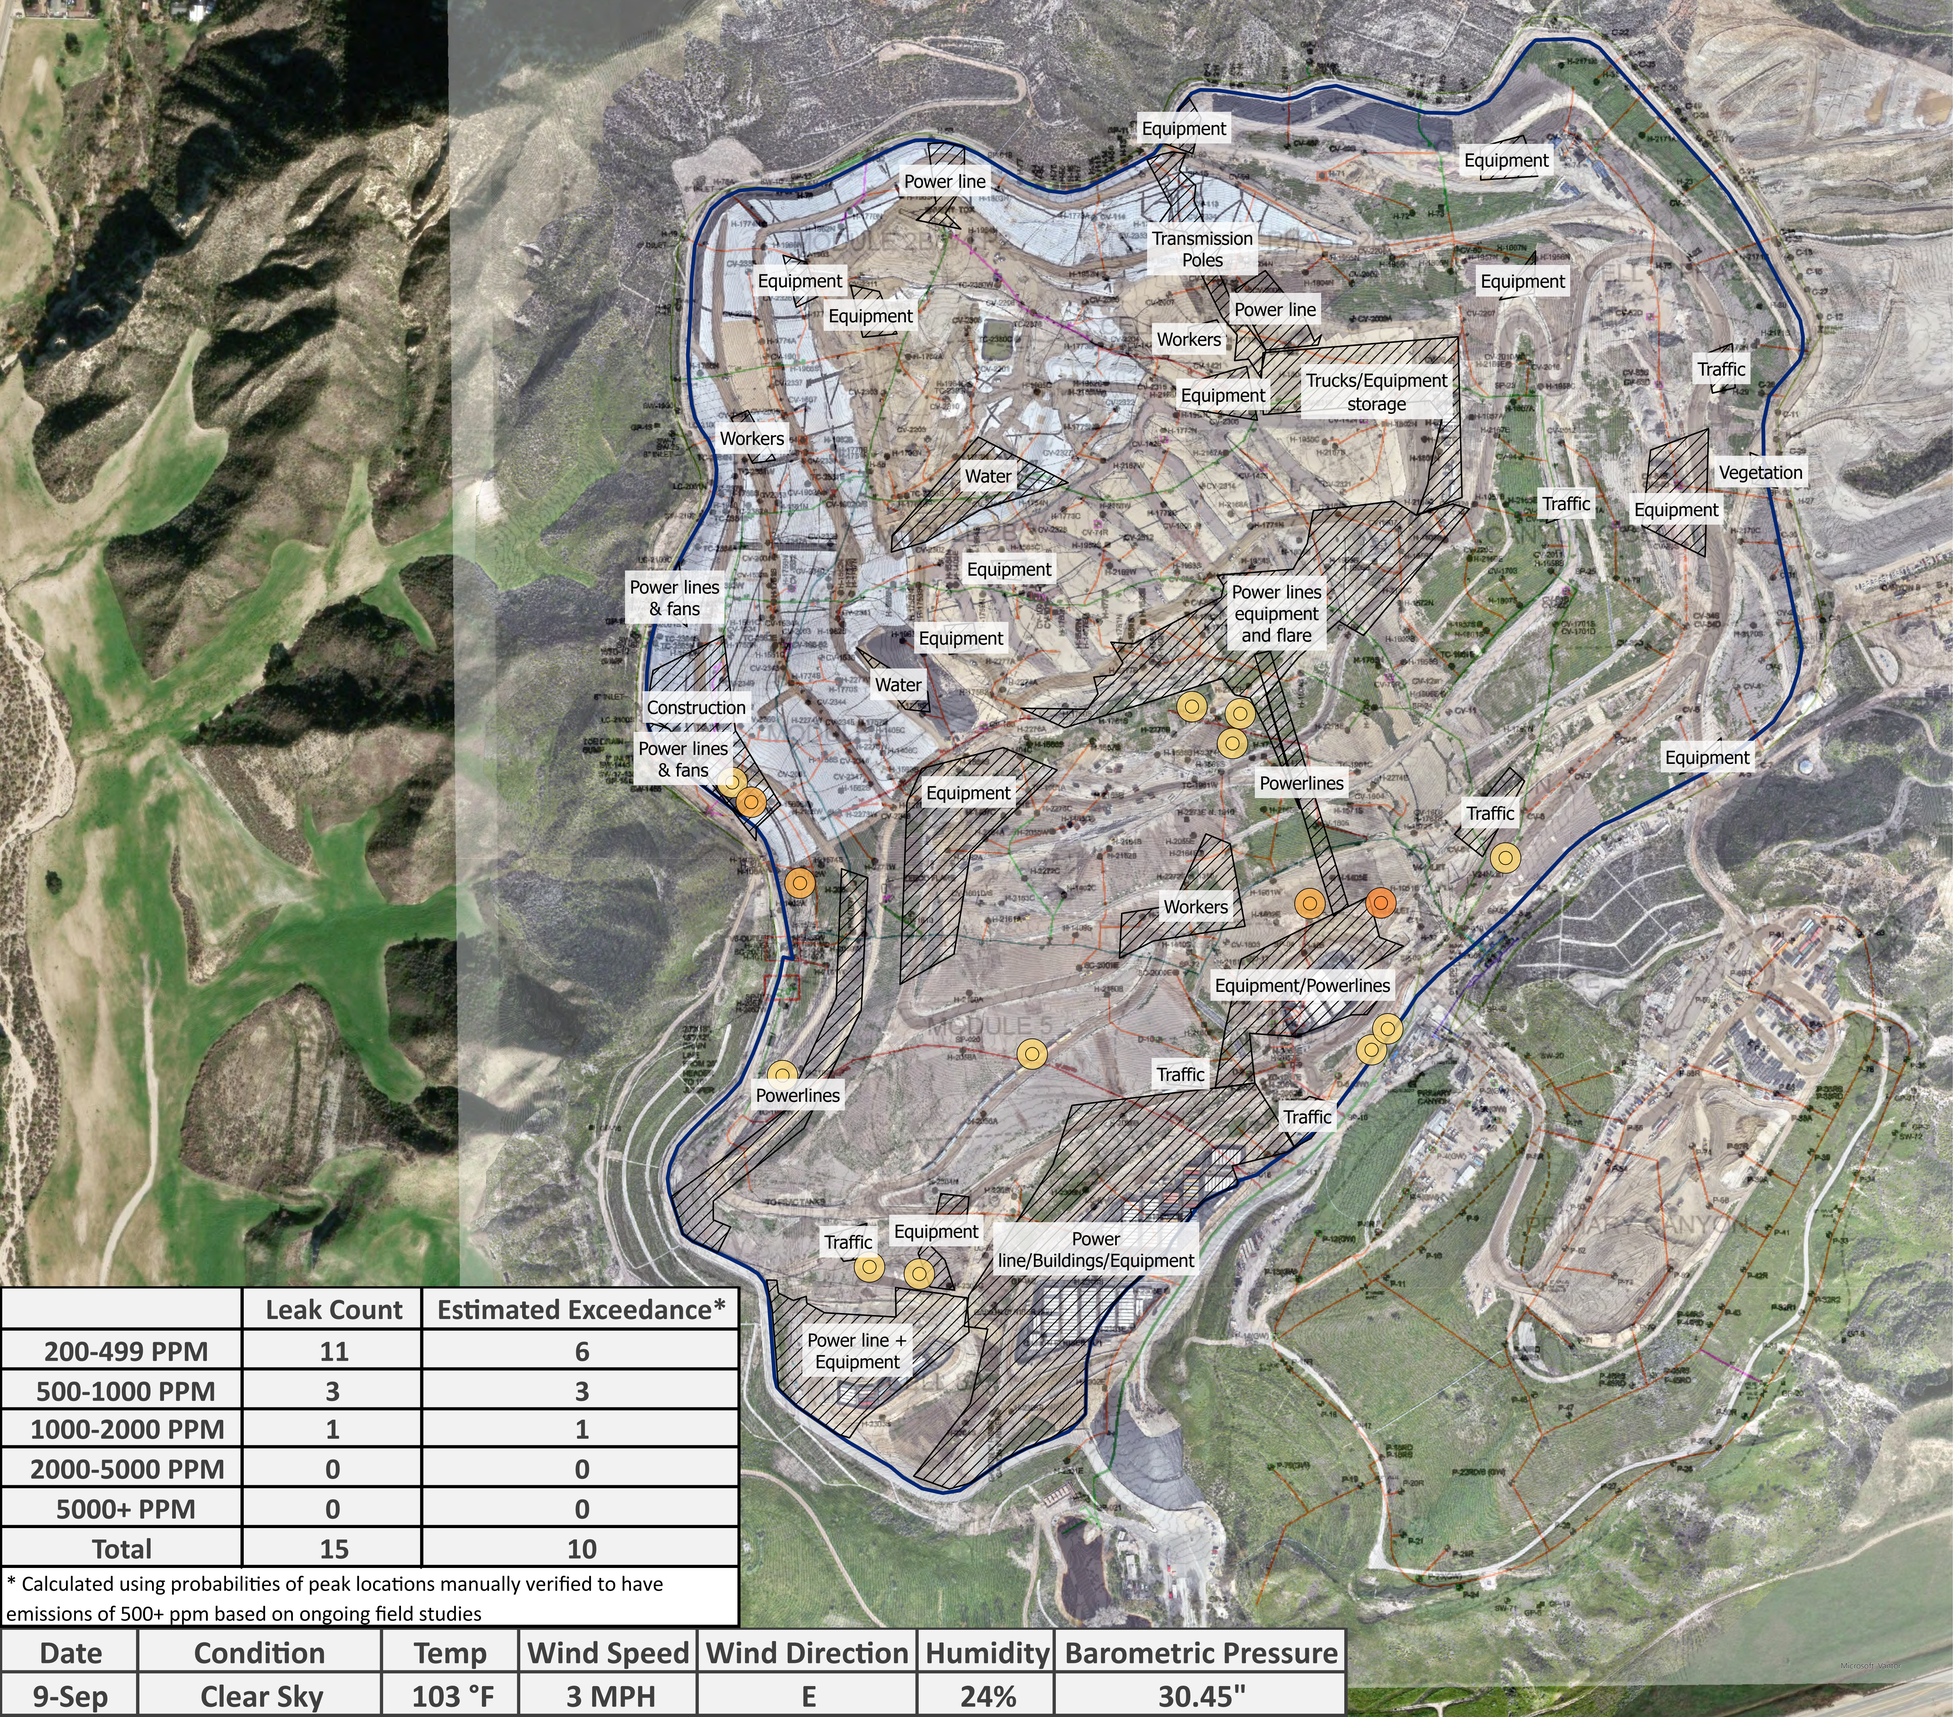

	Leak Count	Estimated Exceedance*
200-499 PPM	11	6
500-1000 PPM	3	3
1000-2000 PPM	1	1
2000-5000 PPM	0	0
5000+ PPM	0	0
Total	15	10

* Calculated using probabilities of peak locations manually verified to have emissions of 500+ ppm based on ongoing field studies

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
9-Sep	Clear Sky	103 °F	3 MPH	E	24%	30.45"

Chiquita Canyon Landfill Methane Emissions Local Peak Values as Recorded by the SnifferDRONE™, over As-Built Drawing & High-Res Image

Sep 9, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 4,999 PPM
- 5000 + PPM

N

0 200 400 800

Feet



Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
9-Sep	Clear Sky	103 °F	3 MPH	E	24%	30.45"

Chiquita Canyon Landfill Point Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing & High-Res Image

Sep 9, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 200 400 800
Feet

Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 5,000 PPM
- 5,000 + PPM

Week 38 (September 15-16, 2026)

Waste Connections - Chiquita Canyon Landfill
Project: 2026 09 Emission Study
Job: Non-Compliance Emission Study
Report Submitted Sept 17, 2026

Emission Study Daily Peaks Verification Report

Information presented within provides results from the emissions monitoring inspection performed by technicians with Sniffer Robotics, Inc. associated with the emission study site and date listed herein. Following the inspection, this report will be updated and disseminated by no later than 12:00 PM local time the next morning.

This report provides details of methane leak locations as determined by the SnifferDRONE™ and manual verification of those leak locations as determined by handheld methane detectors. When an aerial surveillance reading reaches or exceeds 200 PPM methane, a follow-up ground-based surface emissions monitoring field inspection is conducted according to the procedures of OTM-51 and U.S. EPA Method 21, except in the case(s) that the site is unable to monitor the locations due to inaccessibility or dangerous conditions. Report details include: coordinate locations of SnifferDRONE leaks and manual verifications, associated location descriptions (where applicable), date and time of verified readings, SnifferDRONE identified and manually verified PPM values, additional notes, map(s) displaying locations of leaks, and photographic documentation of leaks.

Key

Manual Verification ≥ 500 ppm
Manual Verification < 500 ppm

This daily report is not meant for compliance purposes and only intended for customer review.

WEATHER CONDITIONS	Date:	15-Sep	16-Sep
	Sky:	Clear Sky	Overcast Clouds
	Ground:	Dry	Dry
	Temperature:	83 F	69 F
	Wind Direction:	S	S
	Wind Speed:	9 MPH	4 MPH
	Barometric Pressure:	30.36"	30.48"
	Humidity:	42%	62%

LOCATION DETAILS						INSPECTION RESULTS						
Ref	SnifferDRONE Lat	SnifferDRONE Long	Verified Lat	Verified Long	Location Description	SnifferDRONE Date (UTC)	SnifferDRONE Time (UTC)	SnifferDRONE PPM	Verified Date (UTC)	Verified Time (UTC)	Verified PPM	Notes
1	34.430353	-118.64477	34.430356	-118.644772		9/16/2026	16:36	213	9/16/2026	16:52	***2,000***	
2	34.433217	-118.64558	34.433216	-118.645576		9/16/2026	15:57	208	9/16/2026	17:09	***2,000***	
3	34.428319	-118.64918	34.428322	-118.649210		9/16/2026	18:27	217	9/16/2026	18:46	***990***	
4	34.431265	-118.64439	34.431208	-118.644461		9/16/2026	16:40	425	9/16/2026	16:56	***570***	
5	34.431689	-118.64413	34.431707	-118.644087		9/16/2026	16:41	260	9/16/2026	16:59	***540***	

Peak Verification Map

Project: 2026 09 Week 38 Emission Study
Job: Emission Study
Report Submitted Sept 17, 2026





Legend

Peak Verification	Drone Flight Peaks
0 – 499 PPM	200 - 499 PPM
500+ PPM	500 + PPM

This map provides an overview of all increased meter readings of methane, or "Drone Flight Peaks", over the course of the inspection and the manual verification measurements taken at each peak.

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Dec 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N



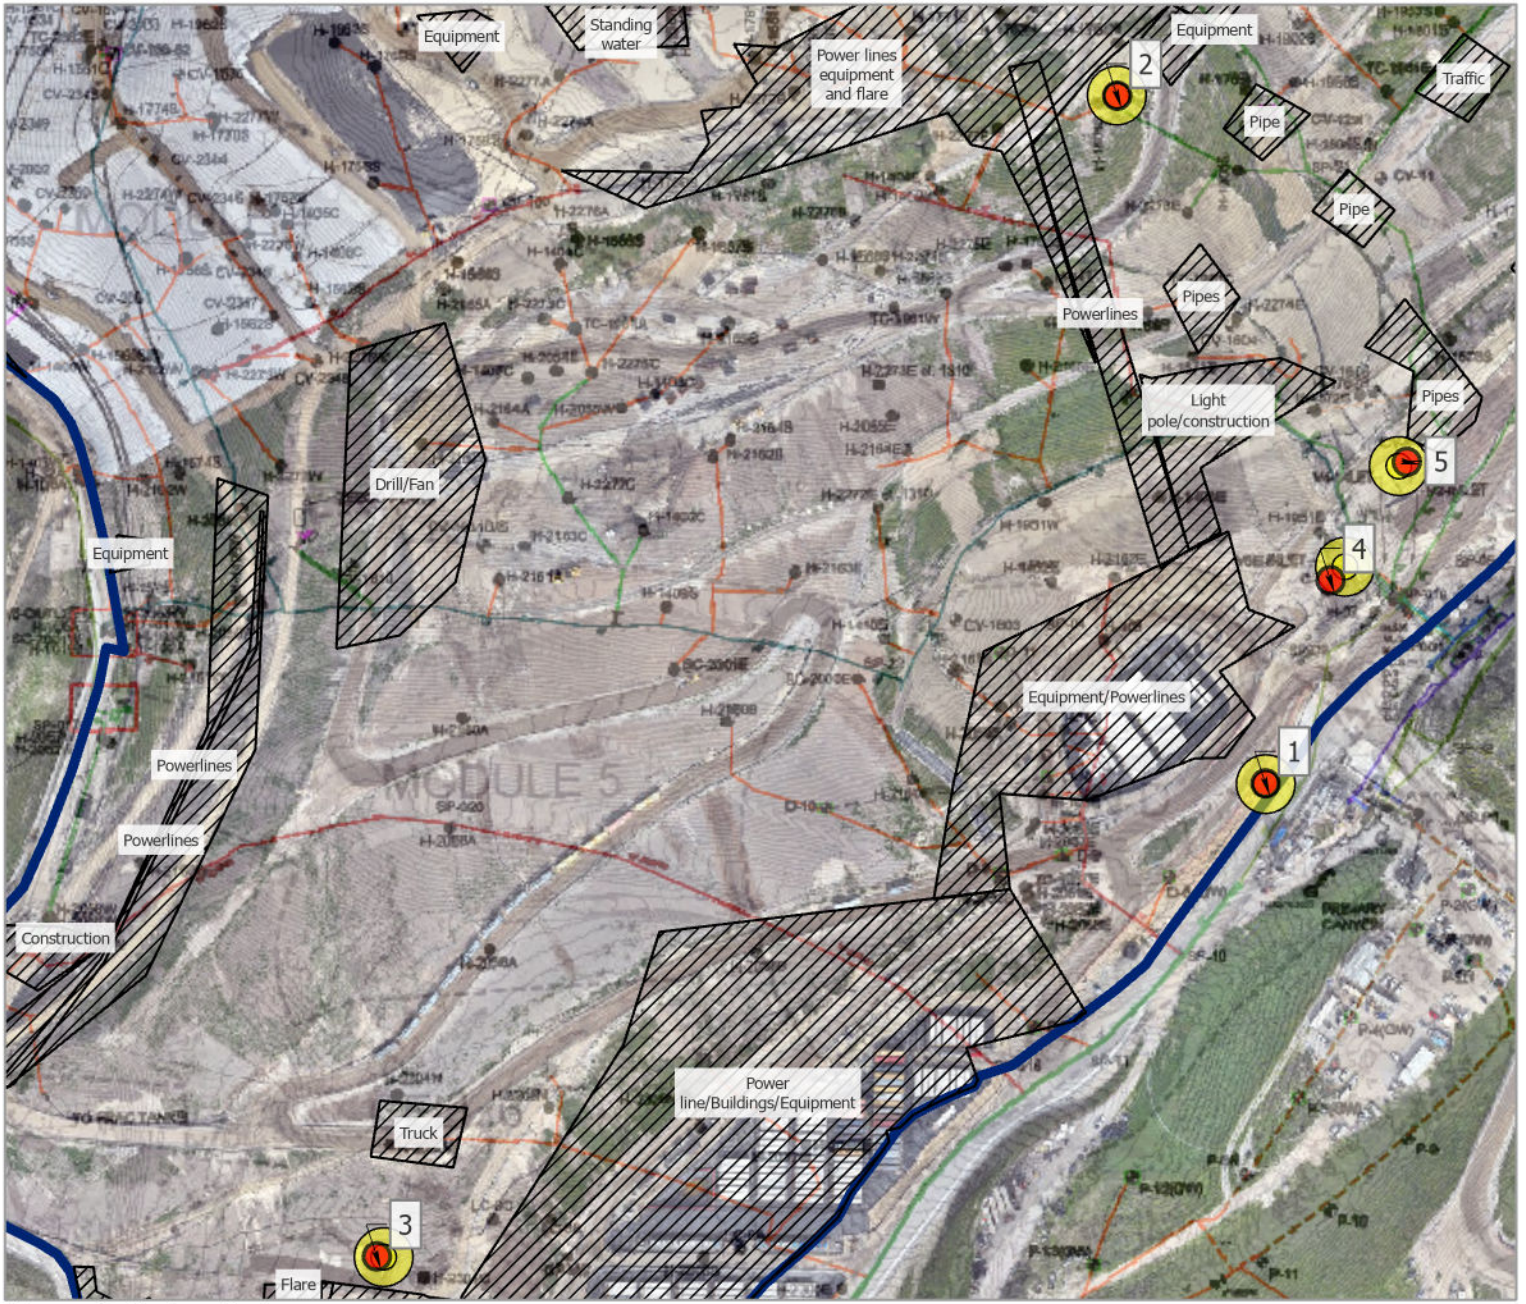



1. SnifferDRONE Verification



2. SnifferDRONE Verification




3. SnifferDRONE Verification



4. SnifferDRONE Verification



5. SnifferDRONE Verification

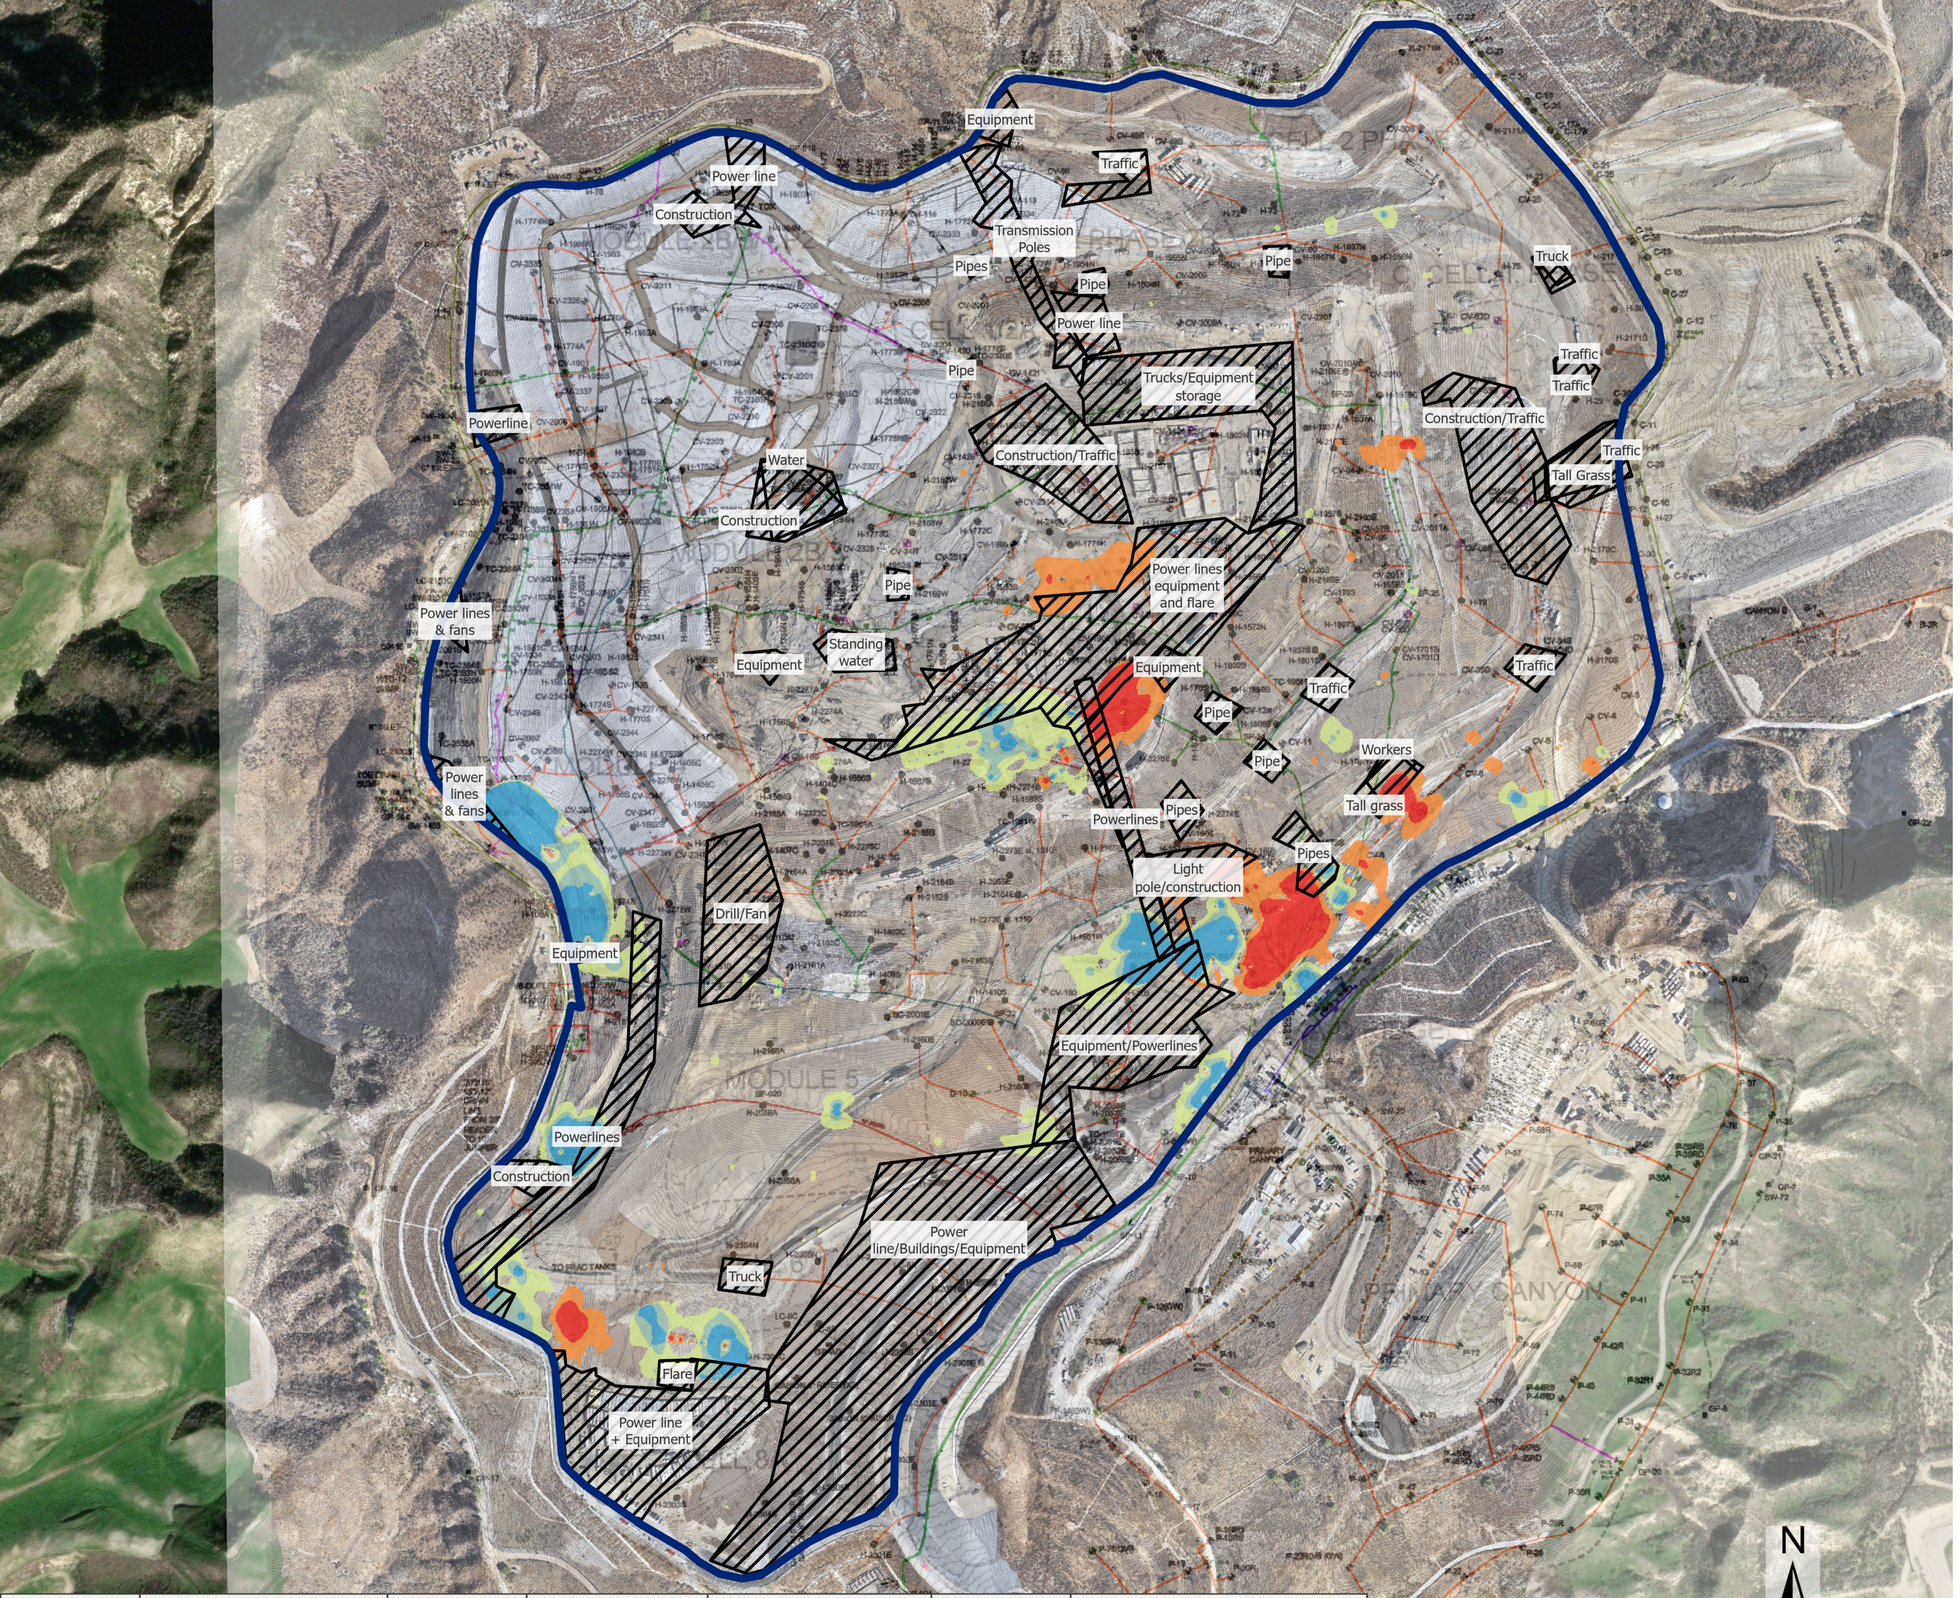

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
15-Sep	Clear Sky	83 F	9 MPH	S	42%	30.36"
16-Sep	Overcast Clouds	69 F	4 MPH	S	62%	30.48"


SITE Interpolated Methane Emissions Change as Recorded by the SnifferDRONE™, Sept 2026 to Sept 2026

09/09/26- 09/15/26

Notes:
1. Basemap: As-built drawing provided by Franklin Engineers & Consultants, LLC dated May 2023; high resolution RGB imagery provided by Waste Connections dated Feb 2023.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N
3. Mean change from Sept. 2026 to Sept. 2026 was a 2.14 PPM decrease. Colors represent standard deviations from the mean. PPMs within one standard deviation are not shown.

Legend

- 954 - 45 PPM Decrease
- 44 - 28 PPM Decrease
- 27 - 11 PPM Decrease
- 10 PPM Decrease - 6 PPM Increase
- 25 - 396 PPM Increase
- 75 - 445 PPM Increase

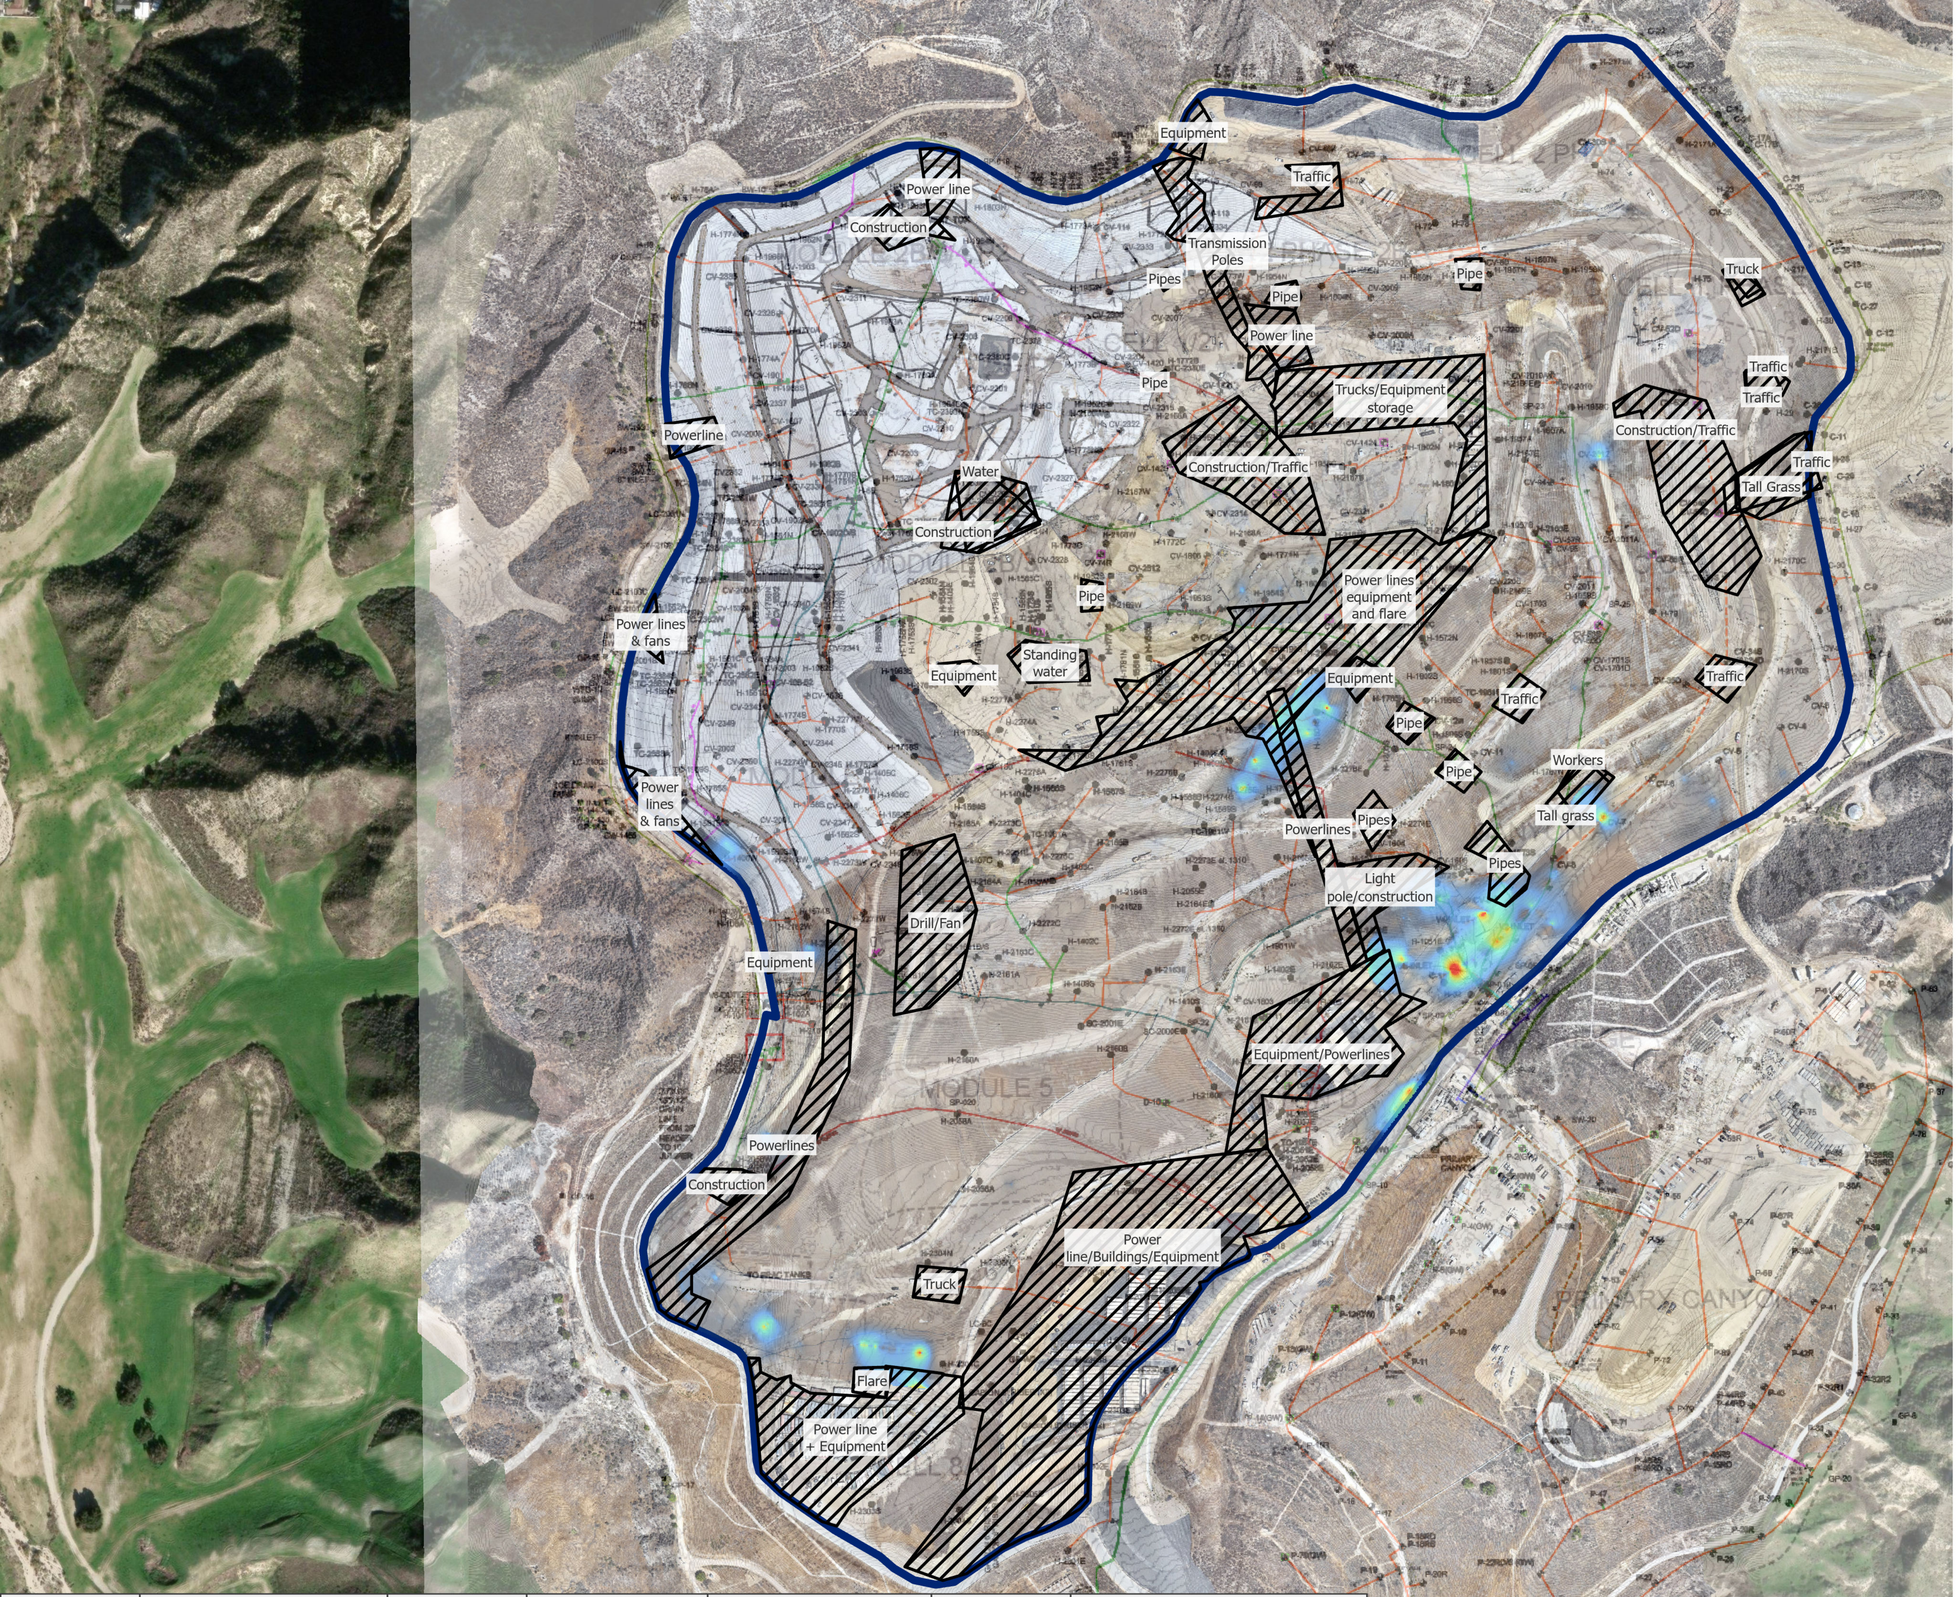

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
15-Sep	Clear Sky	83 F	9 MPH	S	42%	30.36"
16-Sep	Overcast Clouds	69 F	4 MPH	S	62%	30.48"

sniffer

Chiquita Canyon Landfill Interpolated Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing

Sept 15-16, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections dated Aug 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N


N

0 150 300 600
Feet

Legend

CH4 PPM

200
156.64
117.58
78.52
39.45
0

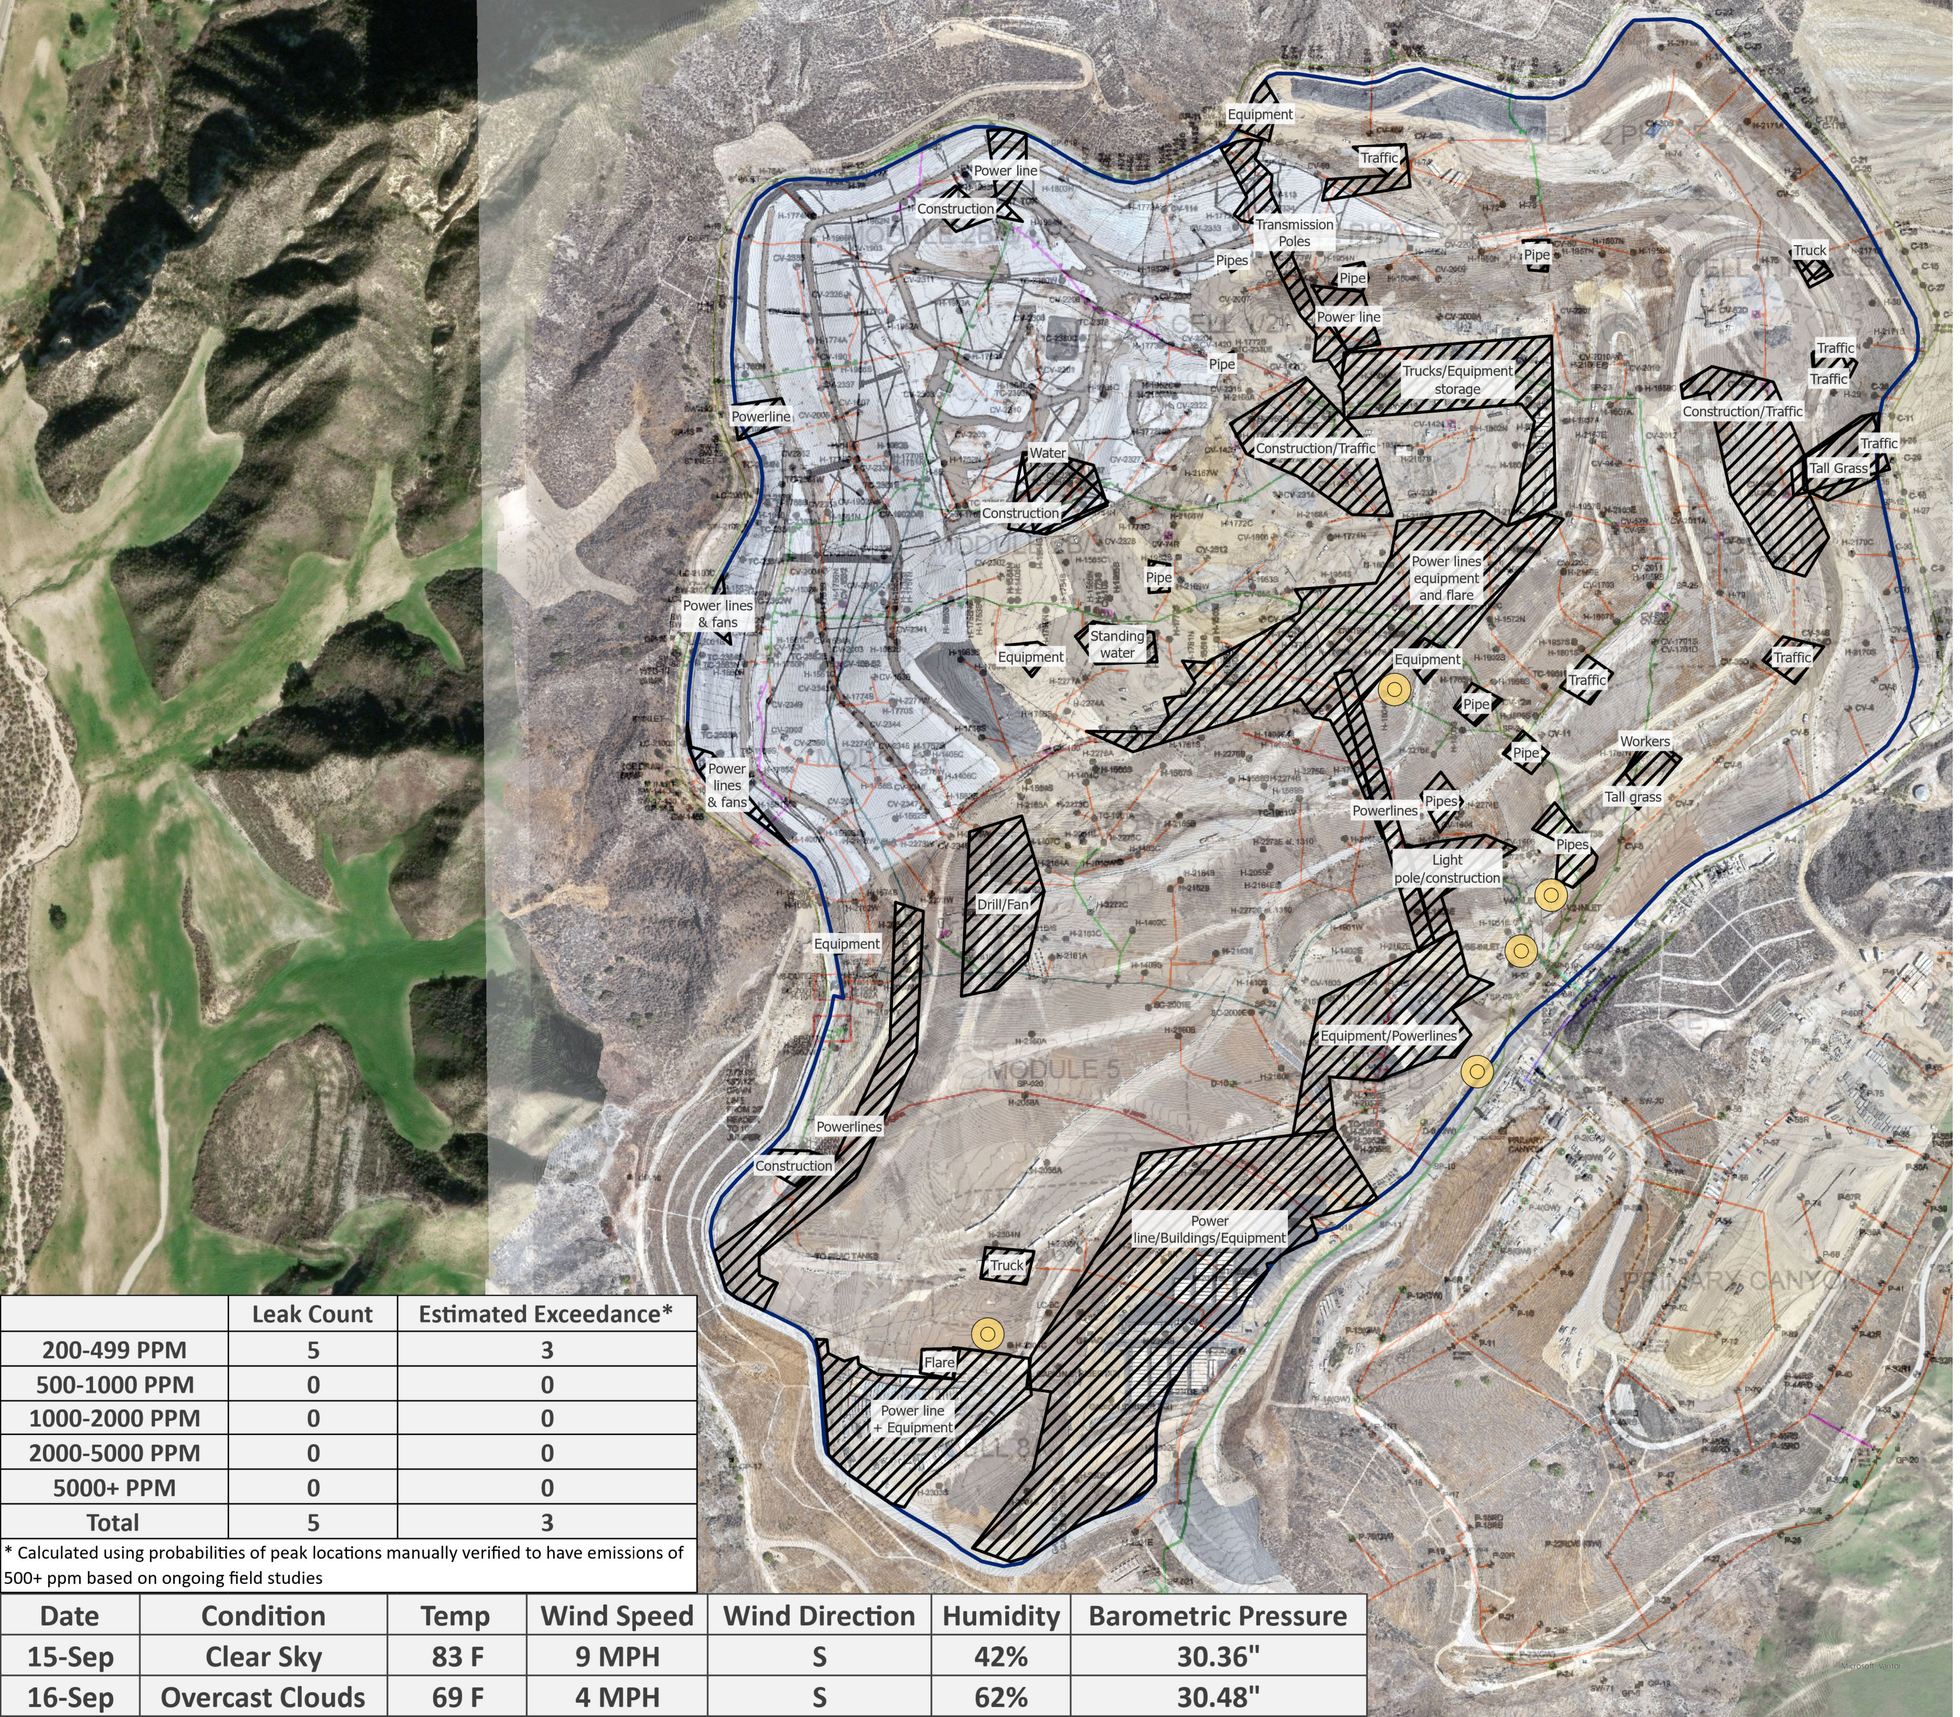

	Leak Count	Estimated Exceedance*
200-499 PPM	5	3
500-1000 PPM	0	0
1000-2000 PPM	0	0
2000-5000 PPM	0	0
5000+ PPM	0	0
Total	5	3

* Calculated using probabilities of peak locations manually verified to have emissions of 500+ ppm based on ongoing field studies

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
15-Sep	Clear Sky	83 F	9 MPH	S	42%	30.36"
16-Sep	Overcast Clouds	69 F	4 MPH	S	62%	30.48"

sniffer

Chiquita Canyon Landfill Methane Emissions Local Peak Values as Recorded by the SnifferDRONE™, over As-Built Drawing

Sep 15-16, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jul 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N


Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 4,999 PPM
- 5000 + PPM

N

0 150 300 600

Feet

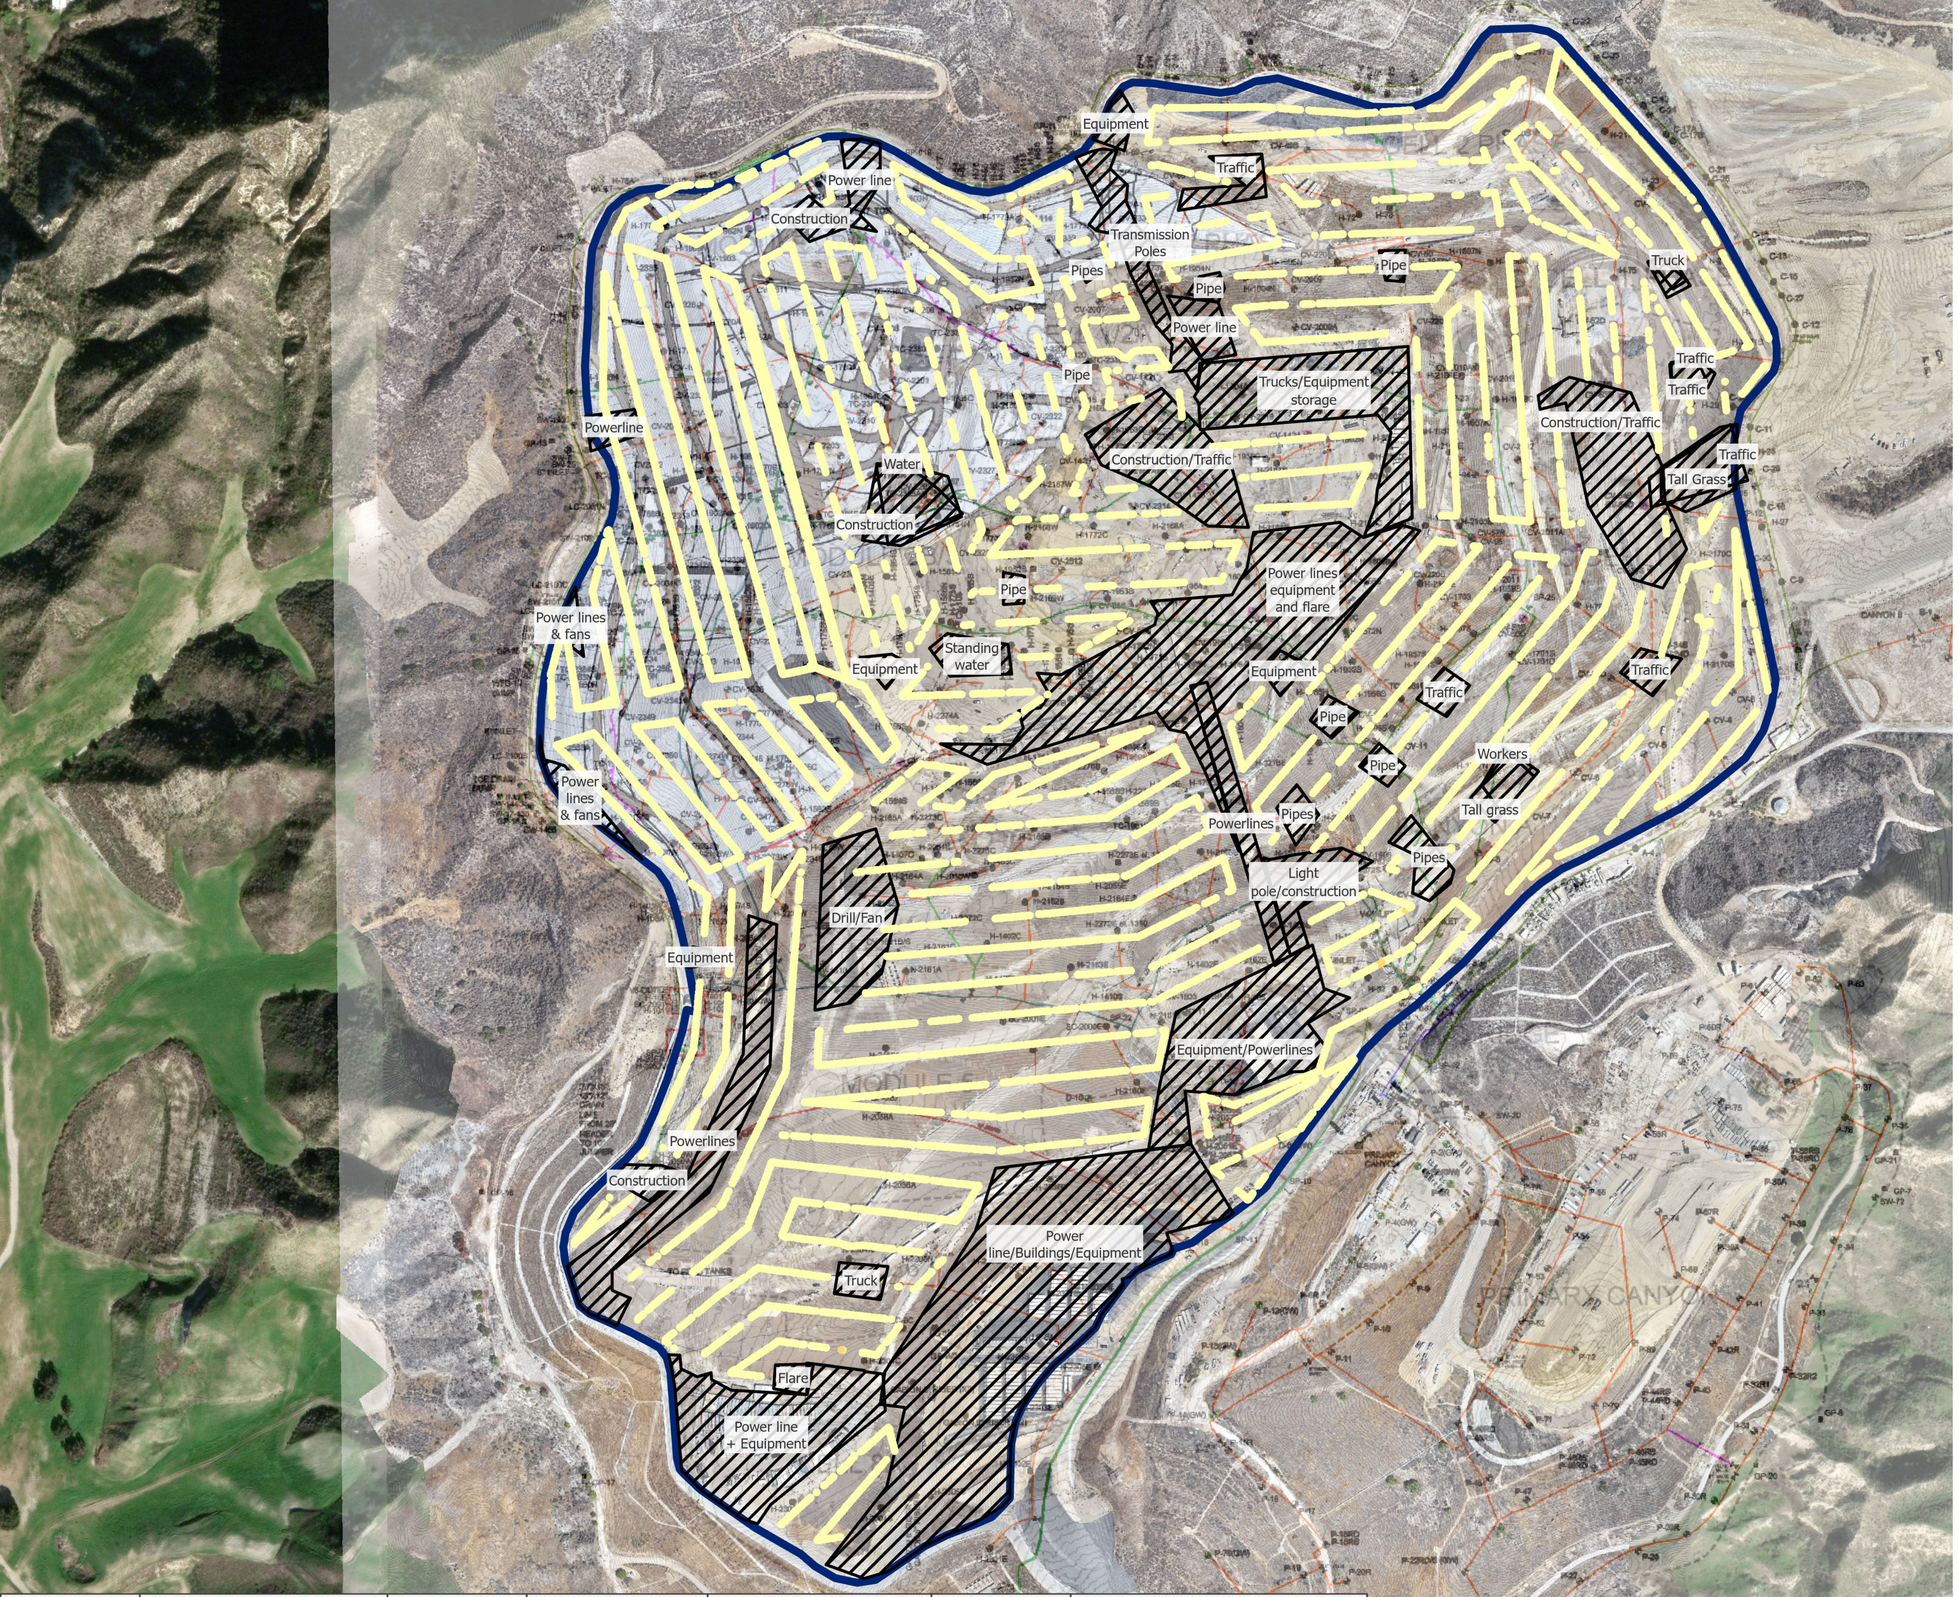

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
15-Sep	Clear Sky	83 F	9 MPH	S	42%	30.36"
16-Sep	Overcast Clouds	69 F	4 MPH	S	62%	30.48"

sniffer

Chiquita Canyon Landfill Point Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing

Sept 15-16, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Aug 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 150 300 600
Feet

Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 5,000 PPM
- 5,000 + PPM

Week 39 (September 22-23, 2026)

Waste Connections - Chiquita Canyon Landfill
Project: 2026 09 Week 39 Emission Study
Job: Non-Compliance Emission Study
Report Submitted Sep 24, 2026

Emission Study Daily Peaks Verification Report

Information presented within provides results from the emissions monitoring inspection performed by technicians with Sniffer Robotics, Inc. associated with the emission study site and date listed herein. Following the inspection, this report will be updated and disseminated by no later than 12:00 PM local time the next morning.

This report provides details of methane leak locations as determined by the SnifferDRONE™ and manual verification of those leak locations as determined by handheld methane detectors. When an aerial surveillance reading reaches or exceeds 200 PPM methane, a follow-up ground-based surface emissions monitoring field inspection is conducted according to the procedures of OTM-51 and U.S. EPA Method 21, except in the case(s) that the site is unable to monitor the locations due to inaccessibility or dangerous conditions. Report details include: coordinate locations of SnifferDRONE leaks and manual verifications, associated location descriptions (where applicable), date and time of verified readings, SnifferDRONE identified and manually verified PPM values, additional notes, map(s) displaying locations of leaks, and photographic documentation of leaks.

Key

Manual Verification ≥ 500 ppm
Manual Verification < 500 ppm


This daily report is not meant for compliance purposes and only intended for customer review.

WEATHER CONDITIONS	Date:	**22-Sep**	**23-Sep**
	Sky:	Few Clouds	Clear Sky
	Ground:	Dry	Dry
	Temperature:	62 °F	70 °F
	Wind Direction:	E	N
	Wind Speed:	1 MPH	7 MPH
	Barometric Pressure:	30.42"	30.33"
	Humidity:	84%	69%

LOCATION DETAILS						INSPECTION RESULTS						
Ref	**SnifferDRONE Lat**	**SnifferDRONE Long**	**Verified Lat**	**Verified Long**	**Location Description**	**SnifferDRONE Date (UTC)**	**SnifferDRONE Time (UTC)**	**SnifferDRONE PPM**	**Verified Date (UTC)**	**Verified Time (UTC)**	**Verified PPM**	**Notes**
1	34.431652	-118.644208	34.431695	-118.644223	-	9/22/2026	16:28	202	9/22/2026	16:59	***800***	

Peak Verification Map

Project: 2026 09 Week 39 Emission Study
Job: Emission Study
Report Submitted Sept 24, 2026

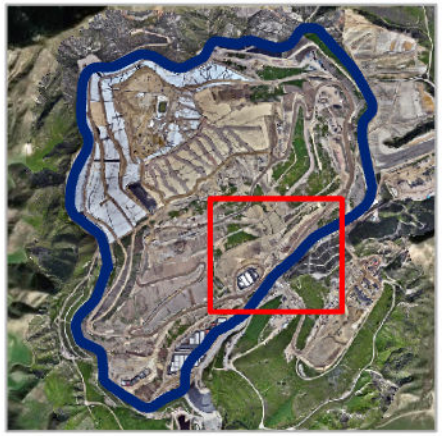

Legend

Peak Verification	Drone Flight Peaks
0 – 499 PPM	200 - 499 PPM
500+ PPM	500 + PPM

This map provides an overview of all increased meter readings of methane, or "Drone Flight Peaks", over the course of the inspection and the manual verification measurements taken at each peak.

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Dec 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 100 200 400


Feet



Microsoft, Vantor, Vantor



1. SnifferDRONE Verification

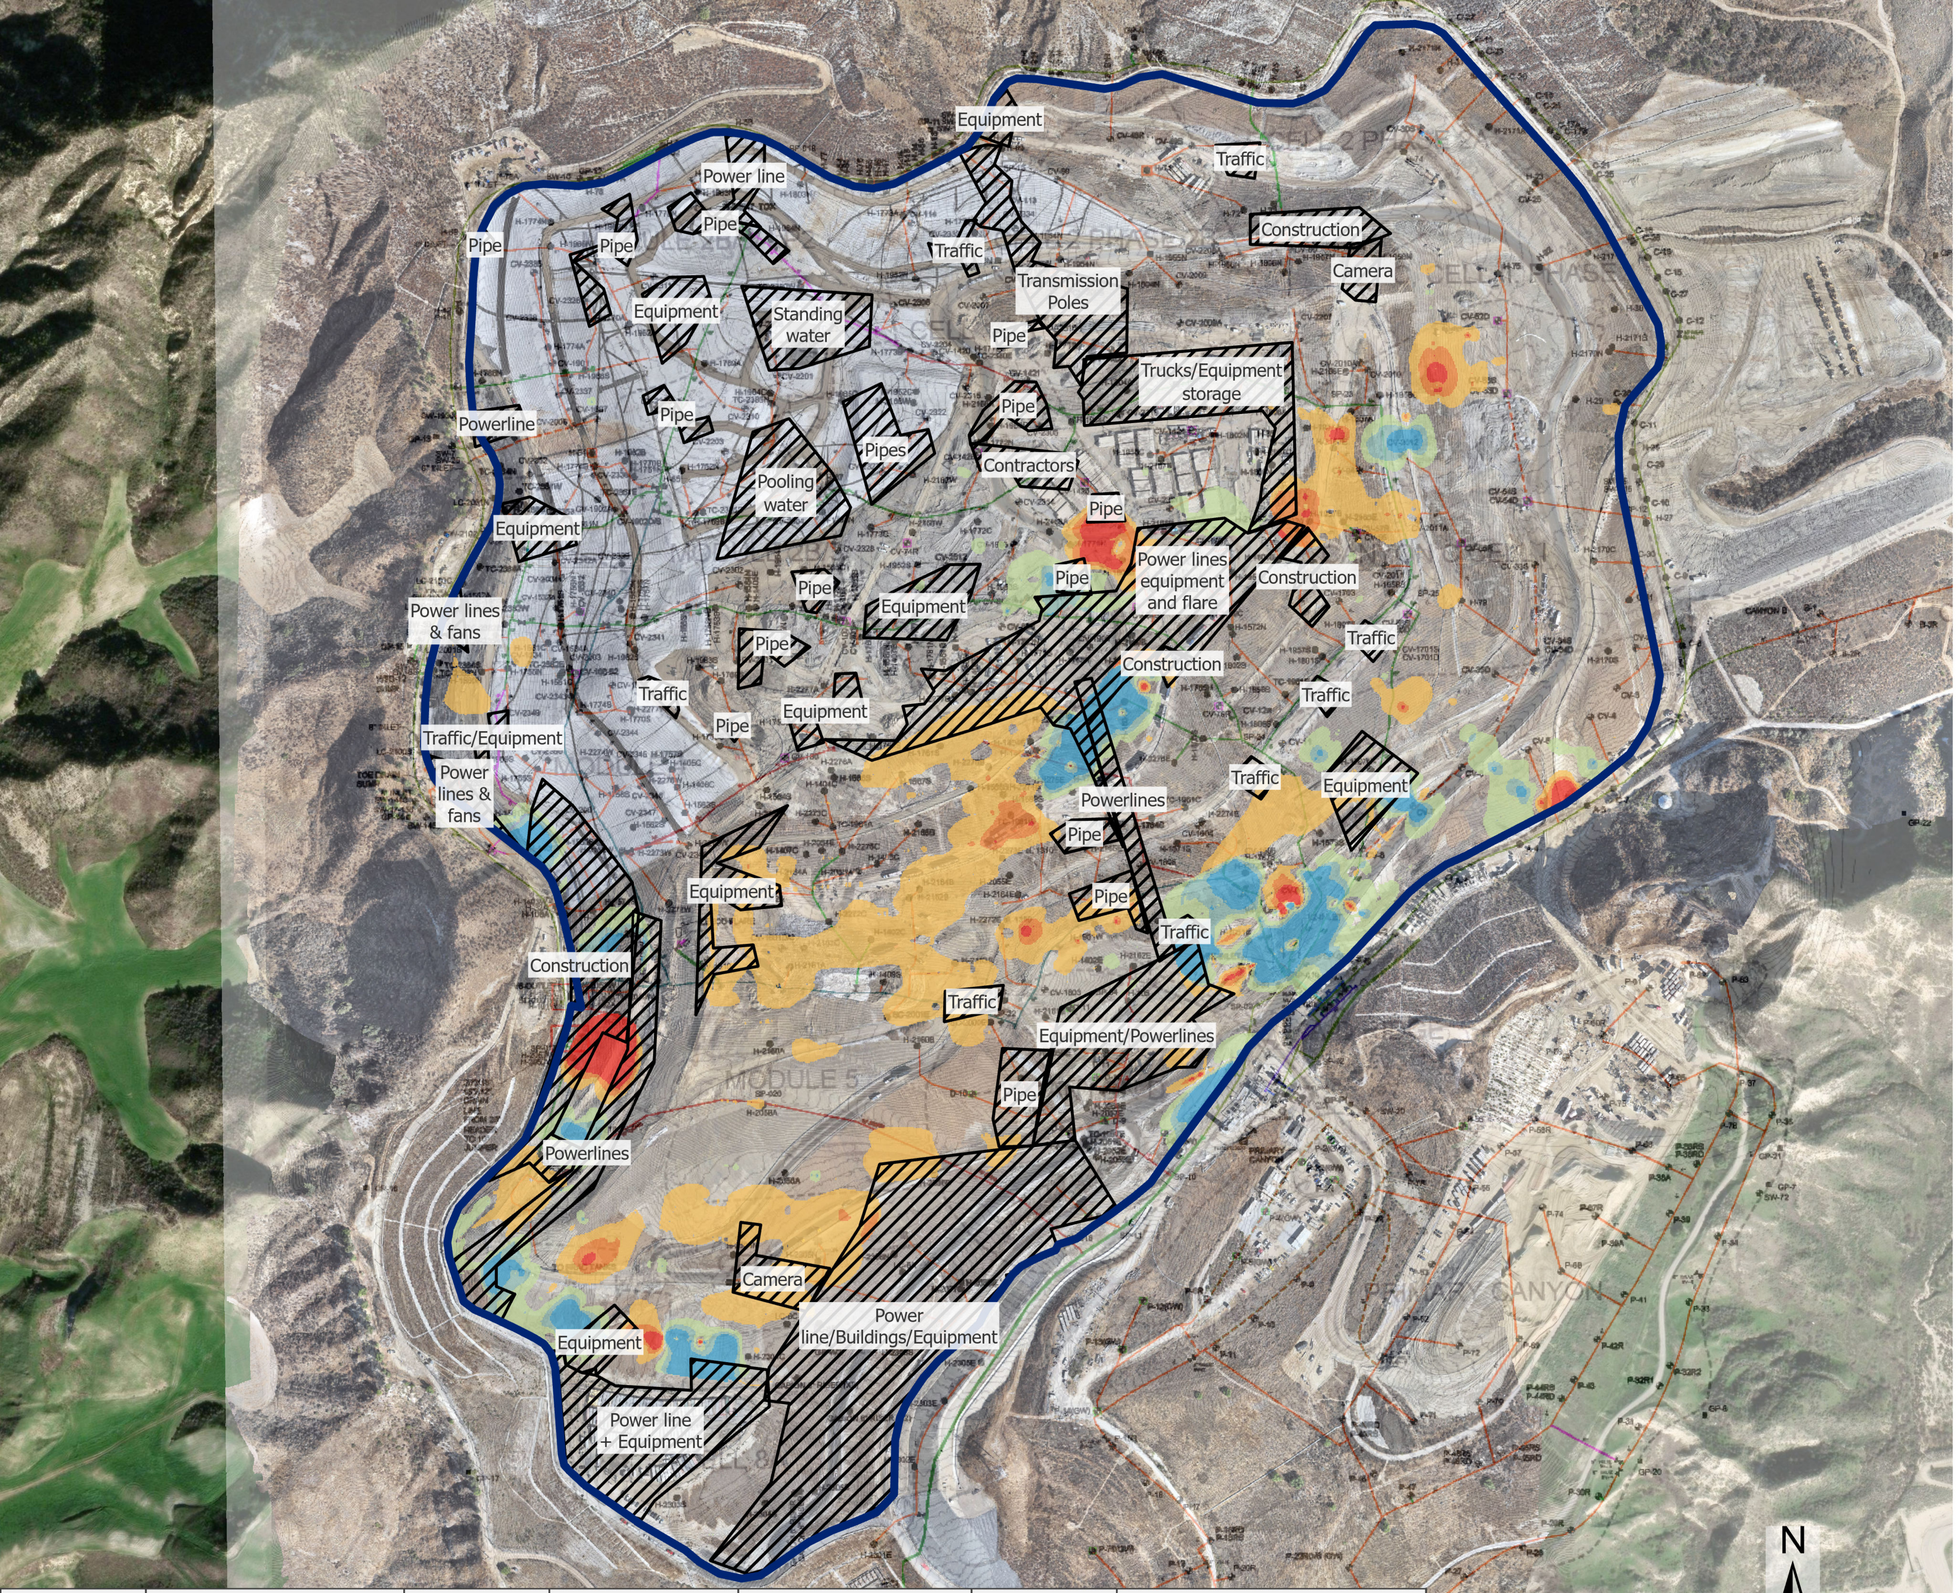

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
22-Sep	Scattered Clouds	66 °F	3 MPH	SW	79%	30.42"
23-Sep	Clear Sky	74 °F	4 MPH	S	82%	30.33"


Interpolated Methane Emissions Change as Recorded by the SnifferDRONE™, Sept 2026 to Sept 2026

09/15/26 - 09/23/26

Notes:
1. Basemap: As-built drawing provided by Franklin Engineers & Consultants, LLC dated May 2023; high resolution RGB imagery provided by Waste Connections dated Feb 2023.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N
3. Mean change from Sept. 2026 to Sept. 2026 was a 2.14 PPM decrease. Colors represent standard deviations from the mean. PPMs within one standard deviation are not shown.

Legend

- 328 - 20 PPM Decrease
- 19 -12 PPM Decrease
- 11 -4 PPM Decrease
- 3 PPM Decrease - 4 PPM Increase
- 13 - 21 PPM Increase
- 22 - 160 PPM Increase

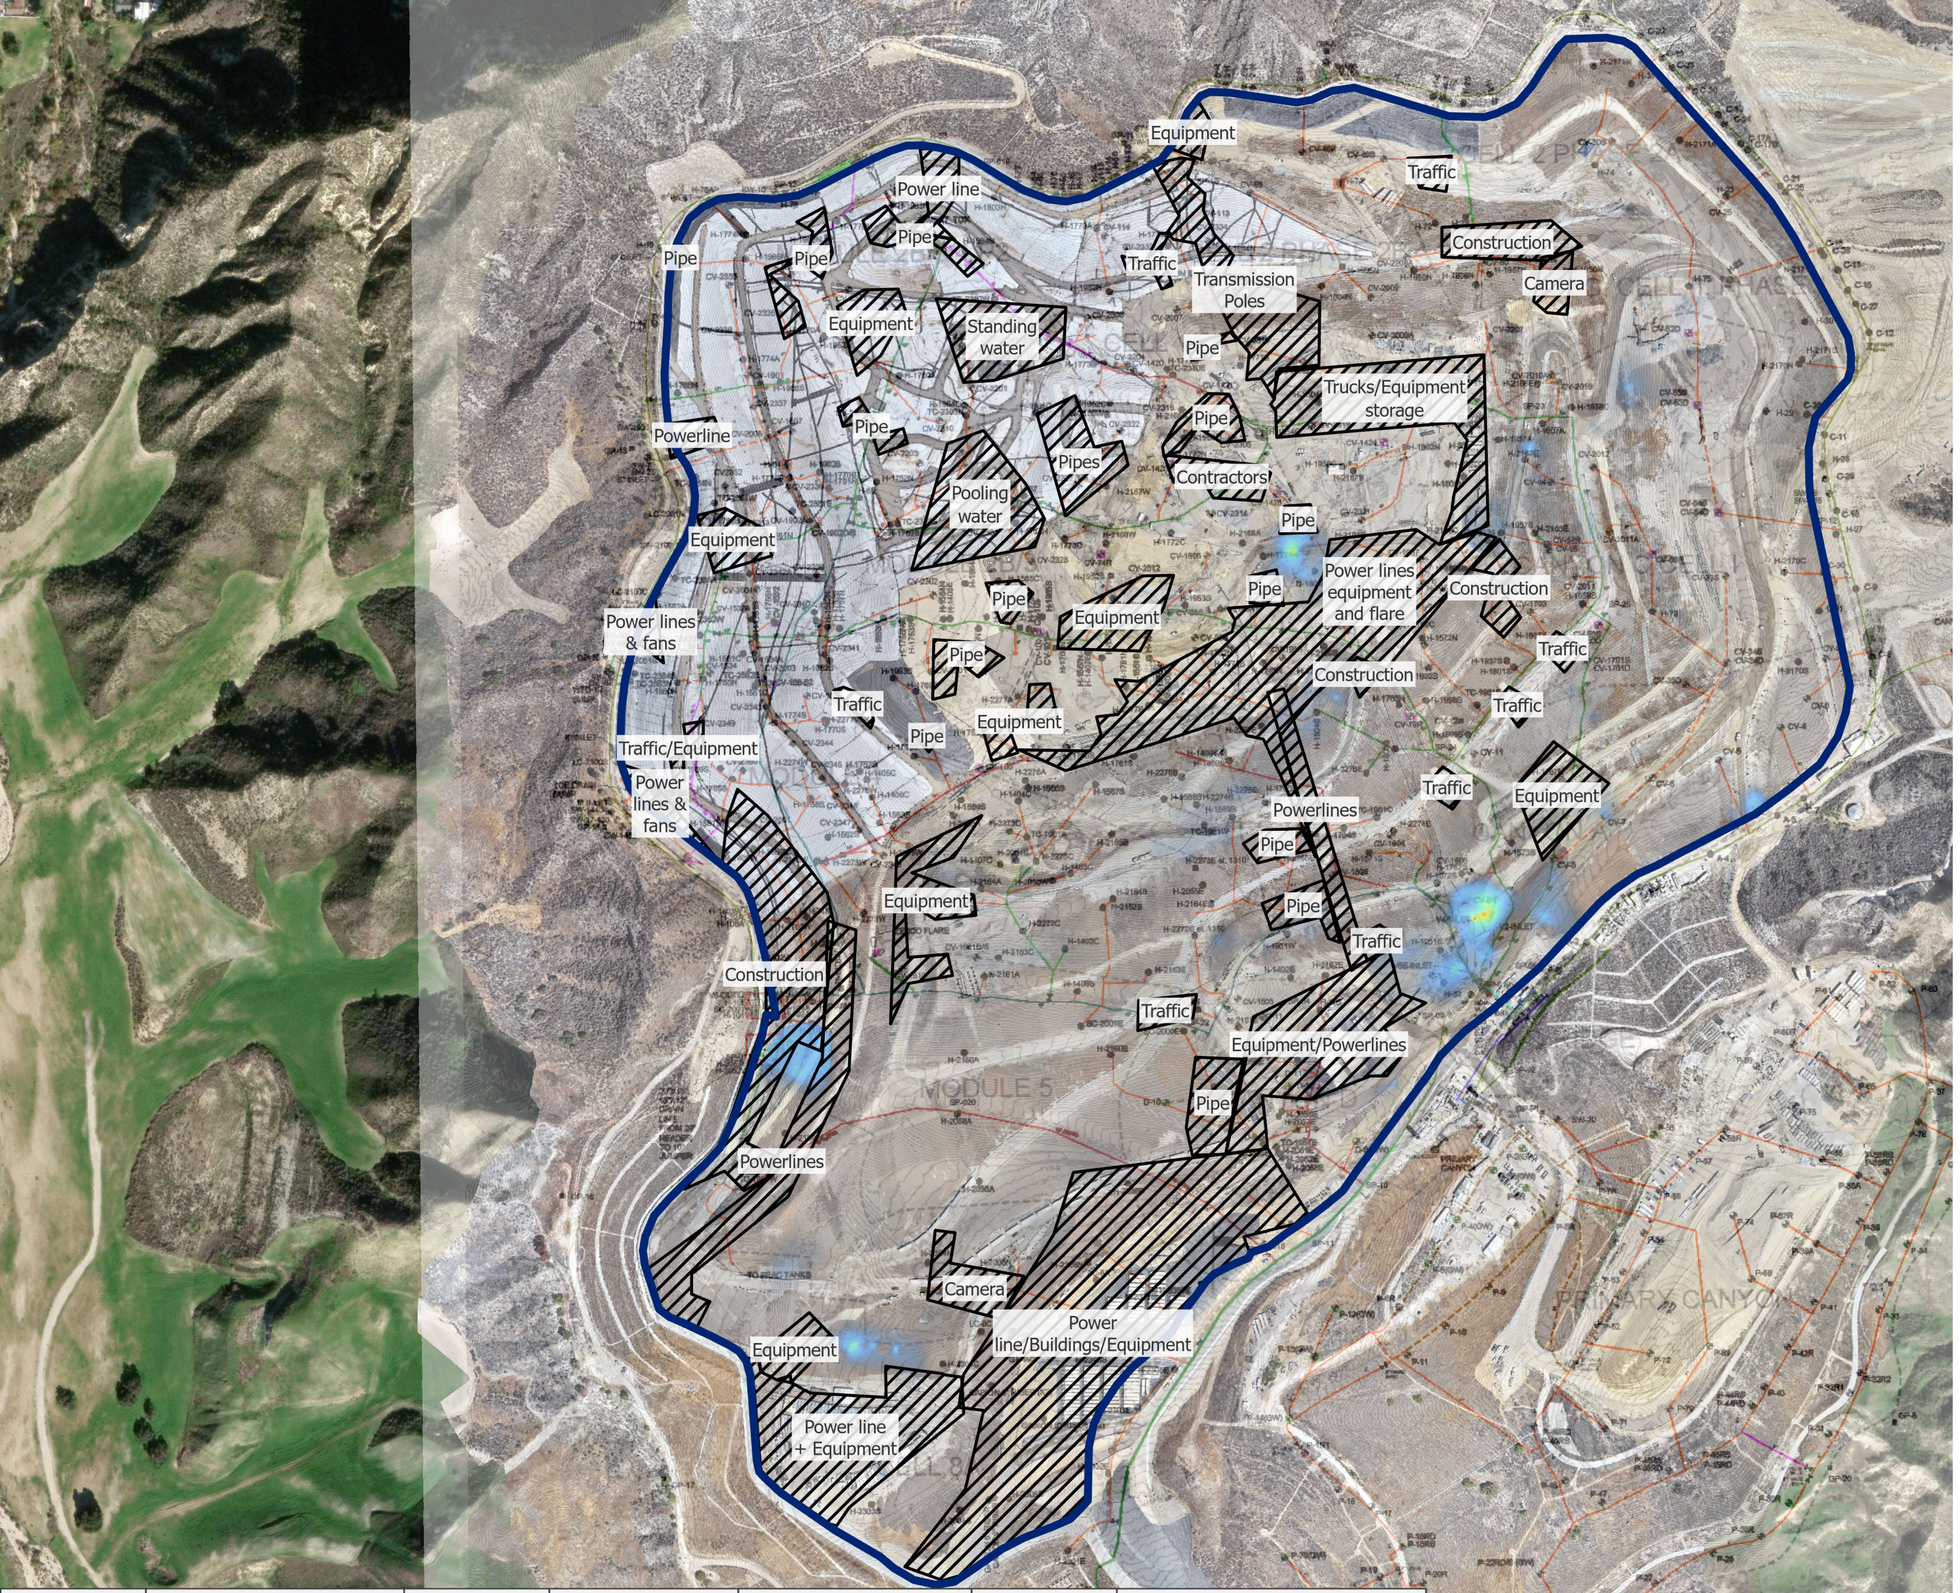

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
22-Sep	Scattered Clouds	66 °F	3 MPH	SW	79%	30.42"
23-Sep	Clear Sky	74 °F	4 MPH	S	82%	30.33"

Chiquita Canyon Landfill Interpolated Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing

Sept 22-23, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections dated Aug 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N


N

0 150 300 600
Feet

Legend

CH4 PPM

200
156.64
117.58
78.52
39.45
0

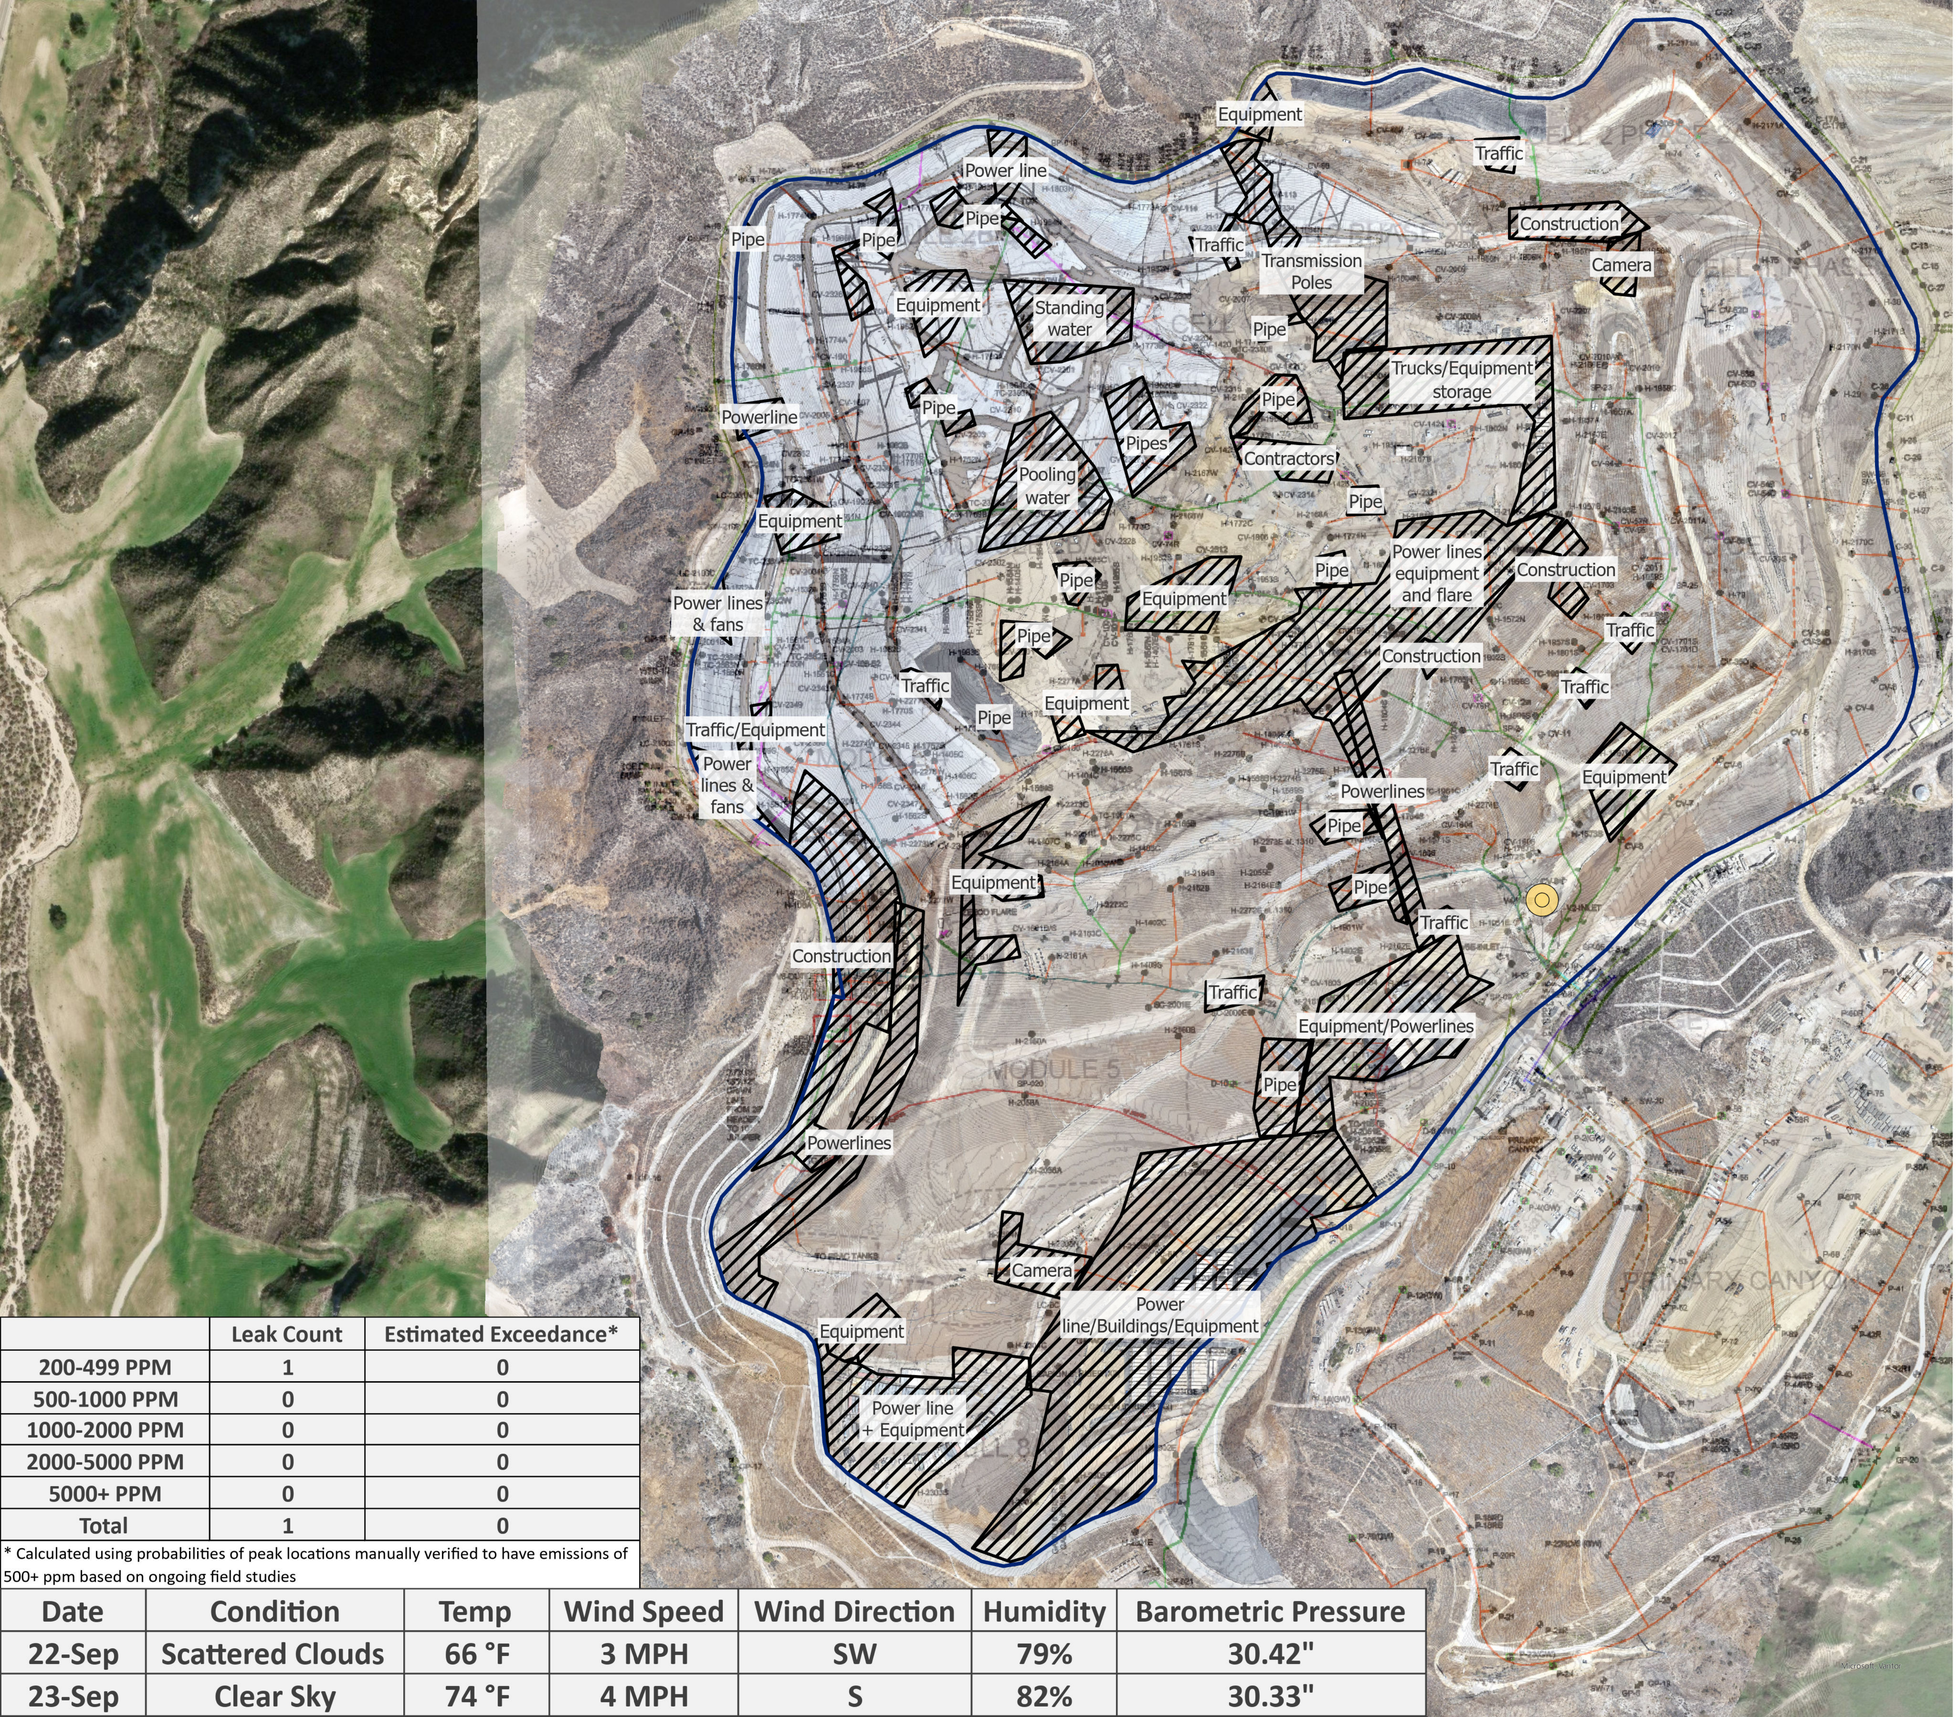

	Leak Count	Estimated Exceedance*
200-499 PPM	1	0
500-1000 PPM	0	0
1000-2000 PPM	0	0
2000-5000 PPM	0	0
5000+ PPM	0	0
Total	1	0

* Calculated using probabilities of peak locations manually verified to have emissions of 500+ ppm based on ongoing field studies

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
22-Sep	Scattered Clouds	66 °F	3 MPH	SW	79%	30.42"
23-Sep	Clear Sky	74 °F	4 MPH	S	82%	30.33"

sniffer

Chiquita Canyon Landfill Methane Emissions Local Peak Values as Recorded by the SnifferDRONE™, over As-Built Drawing

Sep 22-23, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jul 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N


Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 4,999 PPM
- 5000 + PPM

N

0 150 300 600

Feet

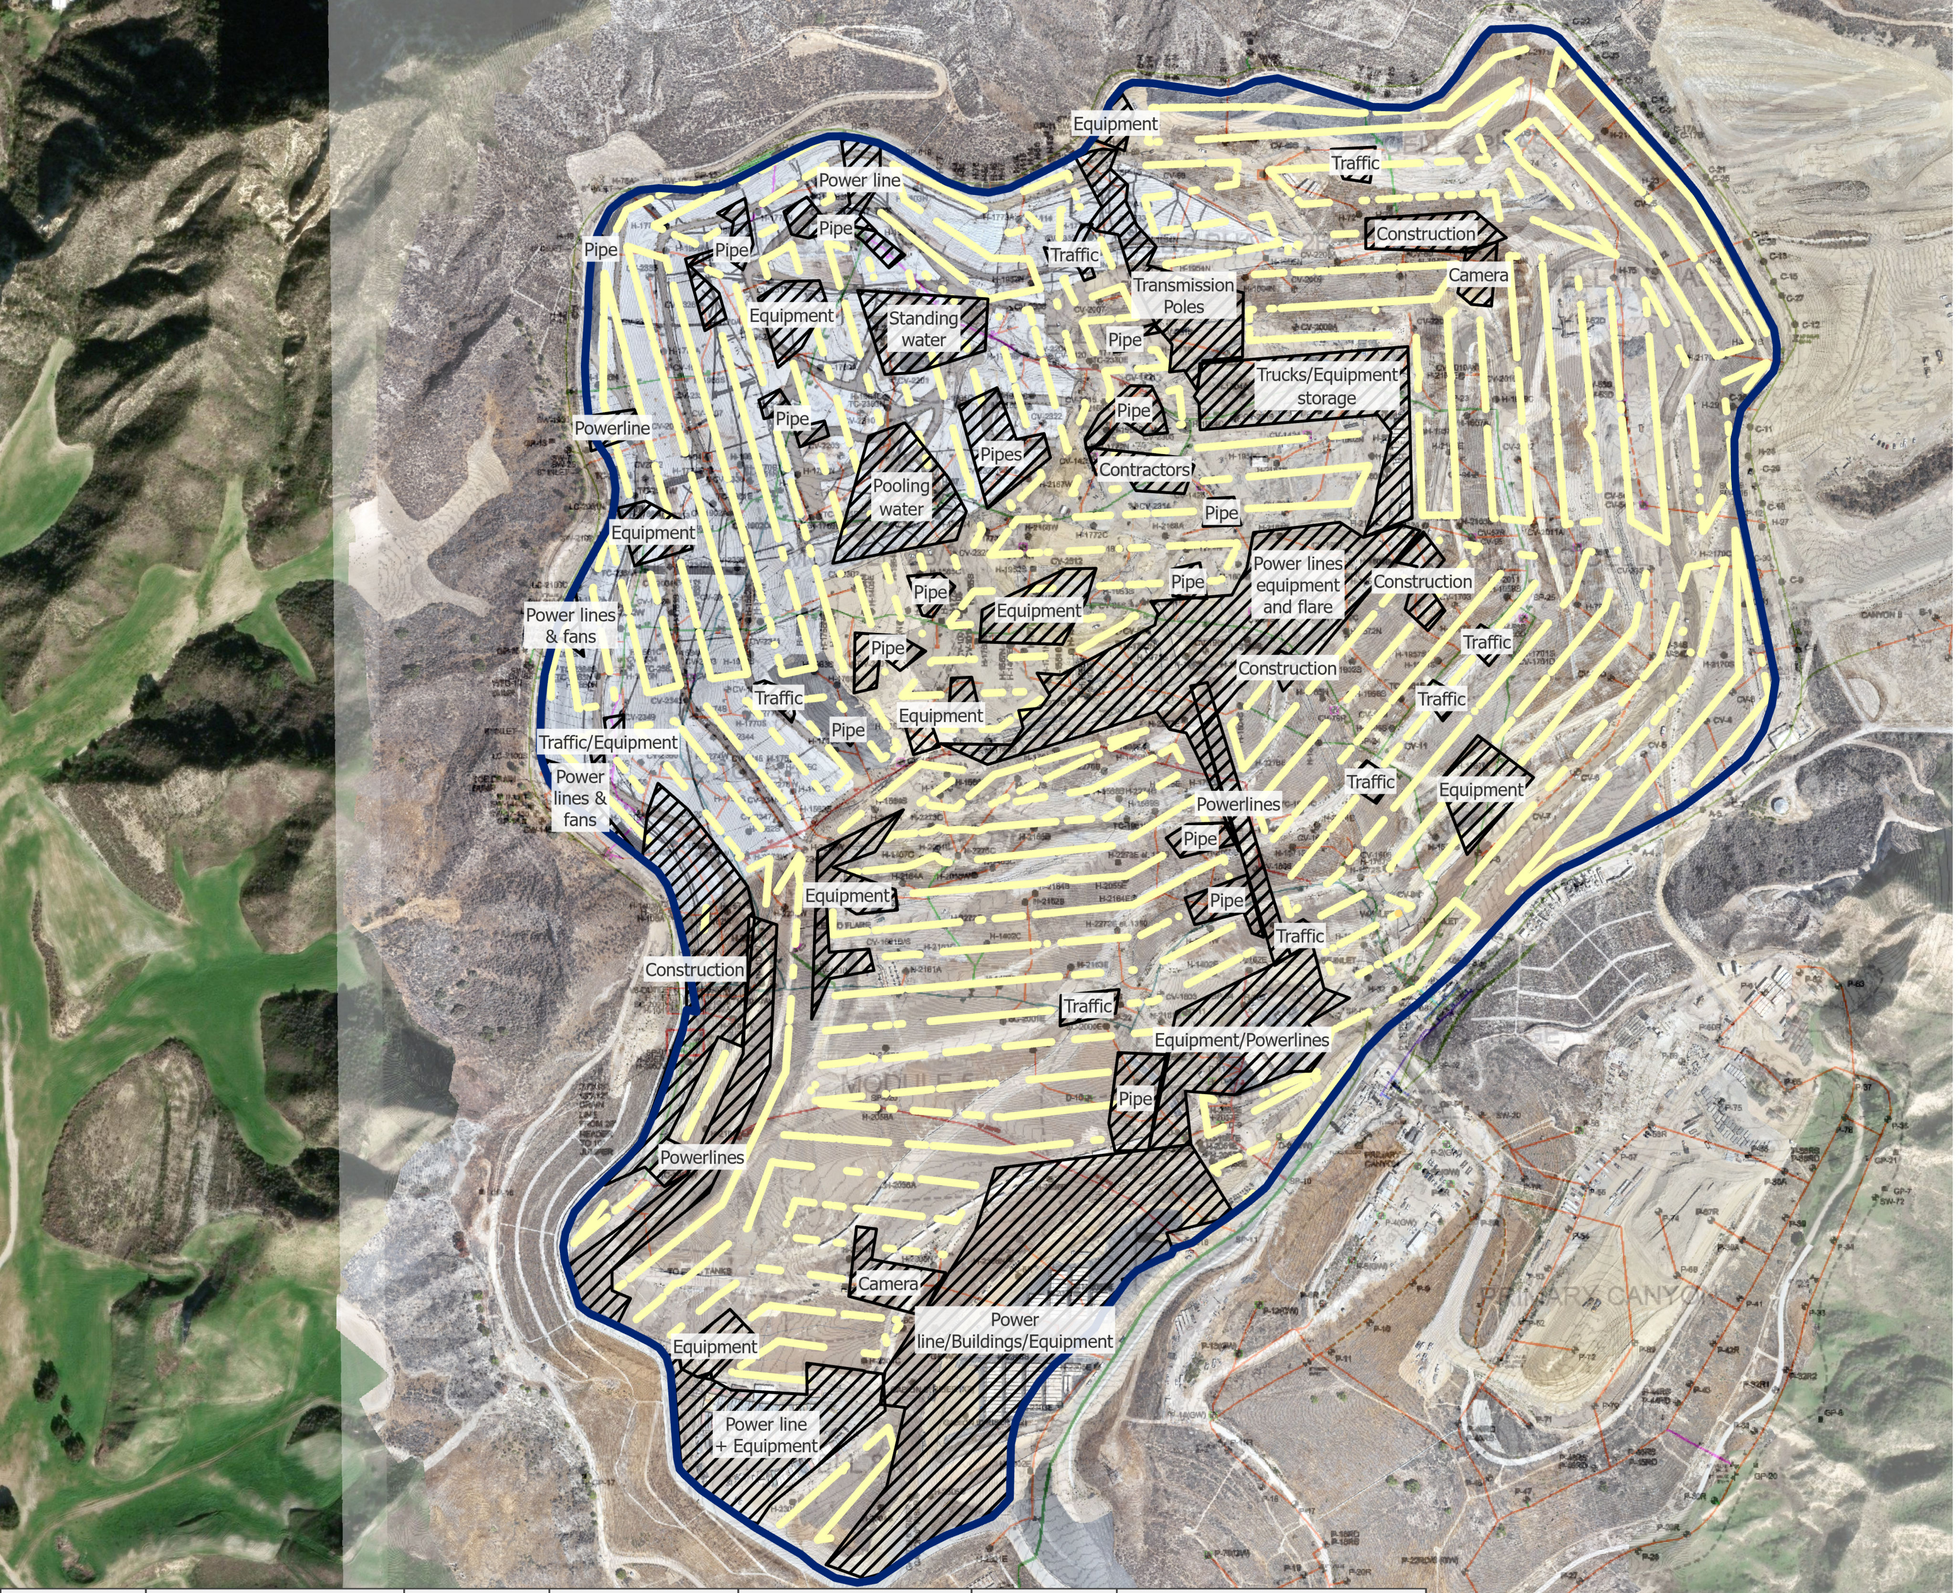

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
22-Sep	Scattered Clouds	66 °F	3 MPH	SW	79%	30.42"
23-Sep	Clear Sky	74 °F	4 MPH	S	82%	30.33"

Chiquita Canyon Landfill Point Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing

Sept 22-23, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Aug 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 150 300 600
Feet

Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 5,000 PPM
- 5,000 + PPM

Week 40 (September 30-October 1, 2026)

Waste Connections - Chiquita Canyon Landfill
Project: 2026 09 Week 40 Emission Study
Job: Non-Compliance Emission Study
Report Submitted Oct 2, 2026

Emission Study Daily Peaks Verification Report

Information presented within provides results from the emissions monitoring inspection performed by technicians with Sniffer Robotics, Inc. associated with the emission study site and date listed herein. Following the inspection, this report will be updated and disseminated by no later than 12:00 PM local time the next morning.

This report provides details of methane leak locations as determined by the SnifferDRONE™ and manual verification of those leak locations as determined by handheld methane detectors. When an aerial surveillance reading reaches or exceeds 200 PPM methane, a follow-up ground-based surface emissions monitoring field inspection is conducted according to the procedures of OTM-51 and U.S. EPA Method 21, except in the case(s) that the site is unable to monitor the locations due to inaccessibility or dangerous conditions. Report details include: coordinate locations of SnifferDRONE leaks and manual verifications, associated location descriptions (where applicable), date and time of verified readings, SnifferDRONE identified and manually verified PPM values, additional notes, map(s) displaying locations of leaks, and photographic documentation of leaks.

Key

Manual Verification ≥ 500 ppm
Manual Verification < 500 ppm

This daily report is not meant for compliance purposes and only intended for customer review.

WEATHER CONDITIONS	Date:	**30-Sep**	**1-Oct**
	Sky:	Clear Sky	Clear Sky
	Ground:	Dry	Dry
	Temperature:	93 °F	90 °F
	Wind Direction:	S	S
	Wind Speed:	6 MPH	5 MPH
	Barometric Pressure:	30.27"	30.33"
	Humidity:	19%	27%

LOCATION DETAILS						**INSPECTION RESULTS**						
Ref	**SnifferDRONE Lat**	**SnifferDRONE Long**	**Verified Lat**	**Verified Long**	**Location Description**	**SnifferDRONE Date (UTC)**	**SnifferDRONE Time (UTC)**	**SnifferDRONE PPM**	**Verified Date (UTC)**	**Verified Time (UTC)**	**Verified PPM**	**Notes**
1	34.432708	-118.646153	34.43260531	-118.646176		10/1/2026	15:07	644	10/1/2026	15:54	***2,000***	
2	34.433045	-118.641169	34.43299234	-118.641168		10/1/2026	17:03	777	10/1/2026	17:32	***2,000***	
3	34.432828	-118.647155	34.43283746	-118.647273		10/1/2026	15:05	331	10/1/2026	15:34	***1,000***	
4	34.431677	-118.644787	34.43164433	-118.644736		10/1/2026	18:11	256	10/1/2026	18:31	***1,000***	
5	34.430027	-118.650541	34.43009589	-118.650497		10/1/2026	20:36	205	10/1/2026	20:52	***1,000***	
6	34.431555	-118.650236	34.43154158	-118.650099		10/1/2026	20:37	421	10/1/2026	20:55	***1,000***	Trench
7	34.431491	-118.644564	34.43142662	-118.644640		10/1/2026	18:11	231	10/1/2026	18:24	***920***	
8	34.431427	-118.644705	34.43137359	-118.644704		10/1/2026	18:11	738	10/1/2026	18:26	***910***	
9	34.432700	-118.646649	34.4327456	-118.646749		10/1/2026	15:07	614	10/1/2026	15:38	***900***	Trench
10	34.432633	-118.646279	34.43259916	-118.646372		10/1/2026	15:08	231	10/1/2026	15:49	***780***	
11	34.432513	-118.646510	34.43255072	-118.646407		10/1/2026	15:08	348	10/1/2026	15:47	***770***	
12	34.432529	-118.642958	34.43255188	-118.643049		10/1/2026	16:56	2,360	10/1/2026	17:46	***750***	
13	34.428228	-118.650005	34.42826382	-118.649996		10/1/2026	19:50	204	10/1/2026	20:13	34	
14	34.430118	-118.648539	34.43007134	-118.648508		10/1/2026	18:49	234	10/1/2026	19:19	20	

Peak Verification Map


Project: 2026 09 Week 40 Emission Study
Job: Emission Study
Report Submitted Oct 2, 2026




Legend

Peak Verification	Drone Flight Peaks
0 – 499 PPM	200 - 499 PPM
500+ PPM	500 + PPM

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N



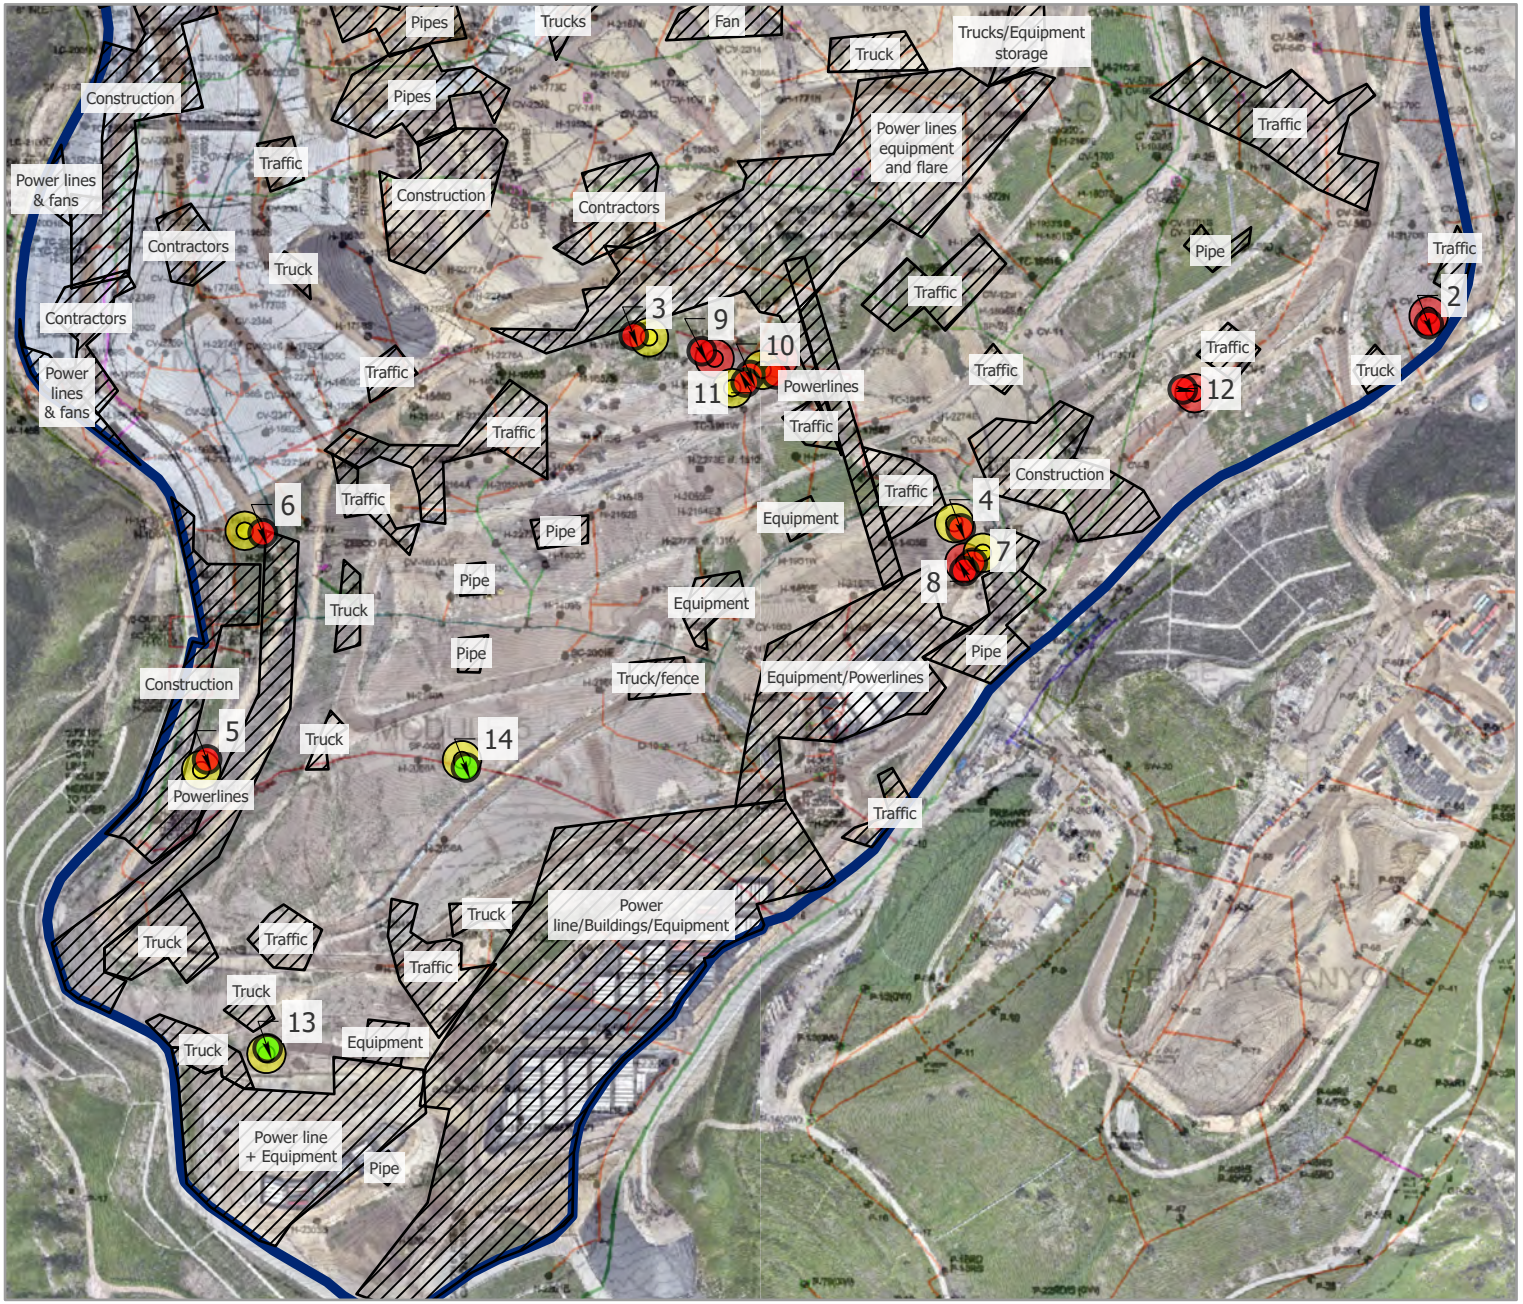

Vantor

Peak Verification Map


Project: 2026 09 Week 40 Emission Study
Job: Emission Study
Report Submitted Oct 2, 2026




Legend

Peak Verification	Drone Flight Peaks
0 – 499 PPM	200 - 499 PPM
500+ PPM	500 + PPM

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jan 2026.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N



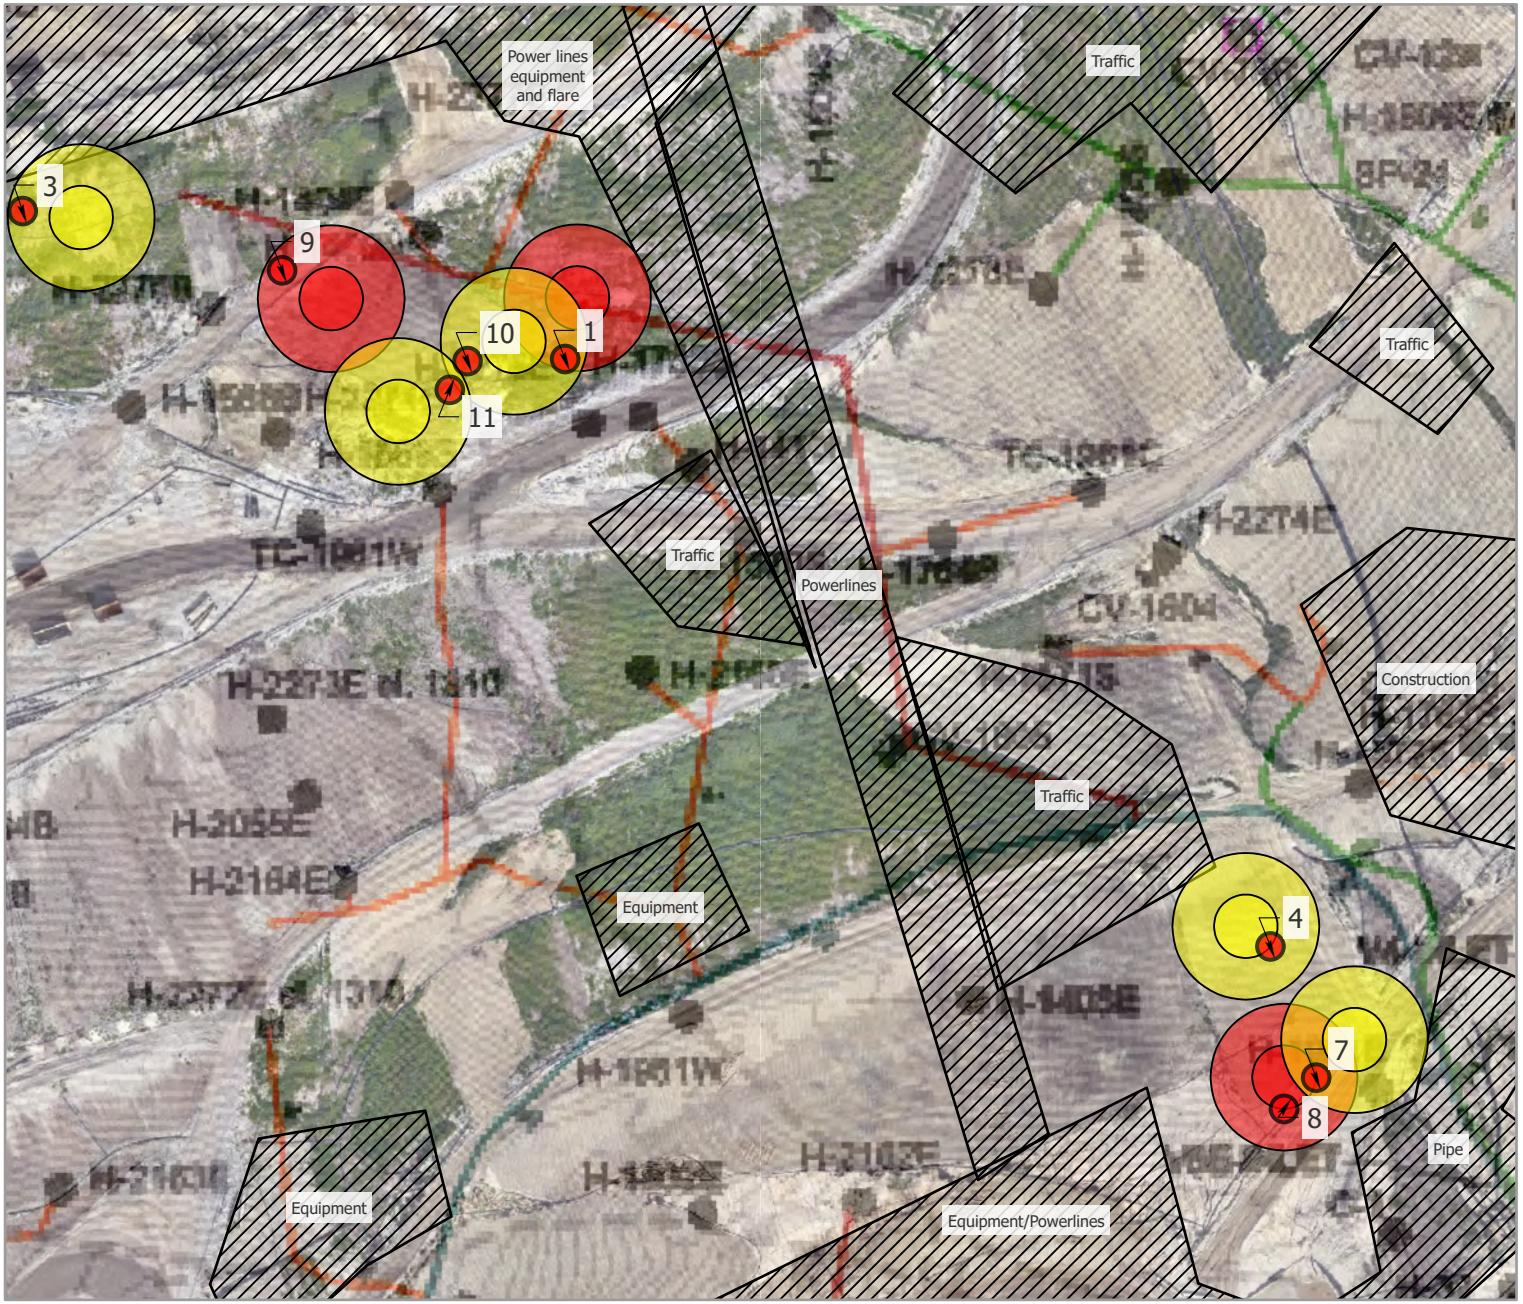

Vantor



1. SnifferDRONE Verification



2. SnifferDRONE Verification



3. SnifferDRONE Verification



4. SnifferDRONE Verification



5. SnifferDRONE Verification



6. SnifferDRONE Verification



7. SnifferDRONE Verification



8. SnifferDRONE Verification



9. SnifferDRONE Verification



10. SnifferDRONE Verification



11. SnifferDRONE Verification




12. SnifferDRONE Verification



13. SnifferDRONE Verification



14. SnifferDRONE Verification

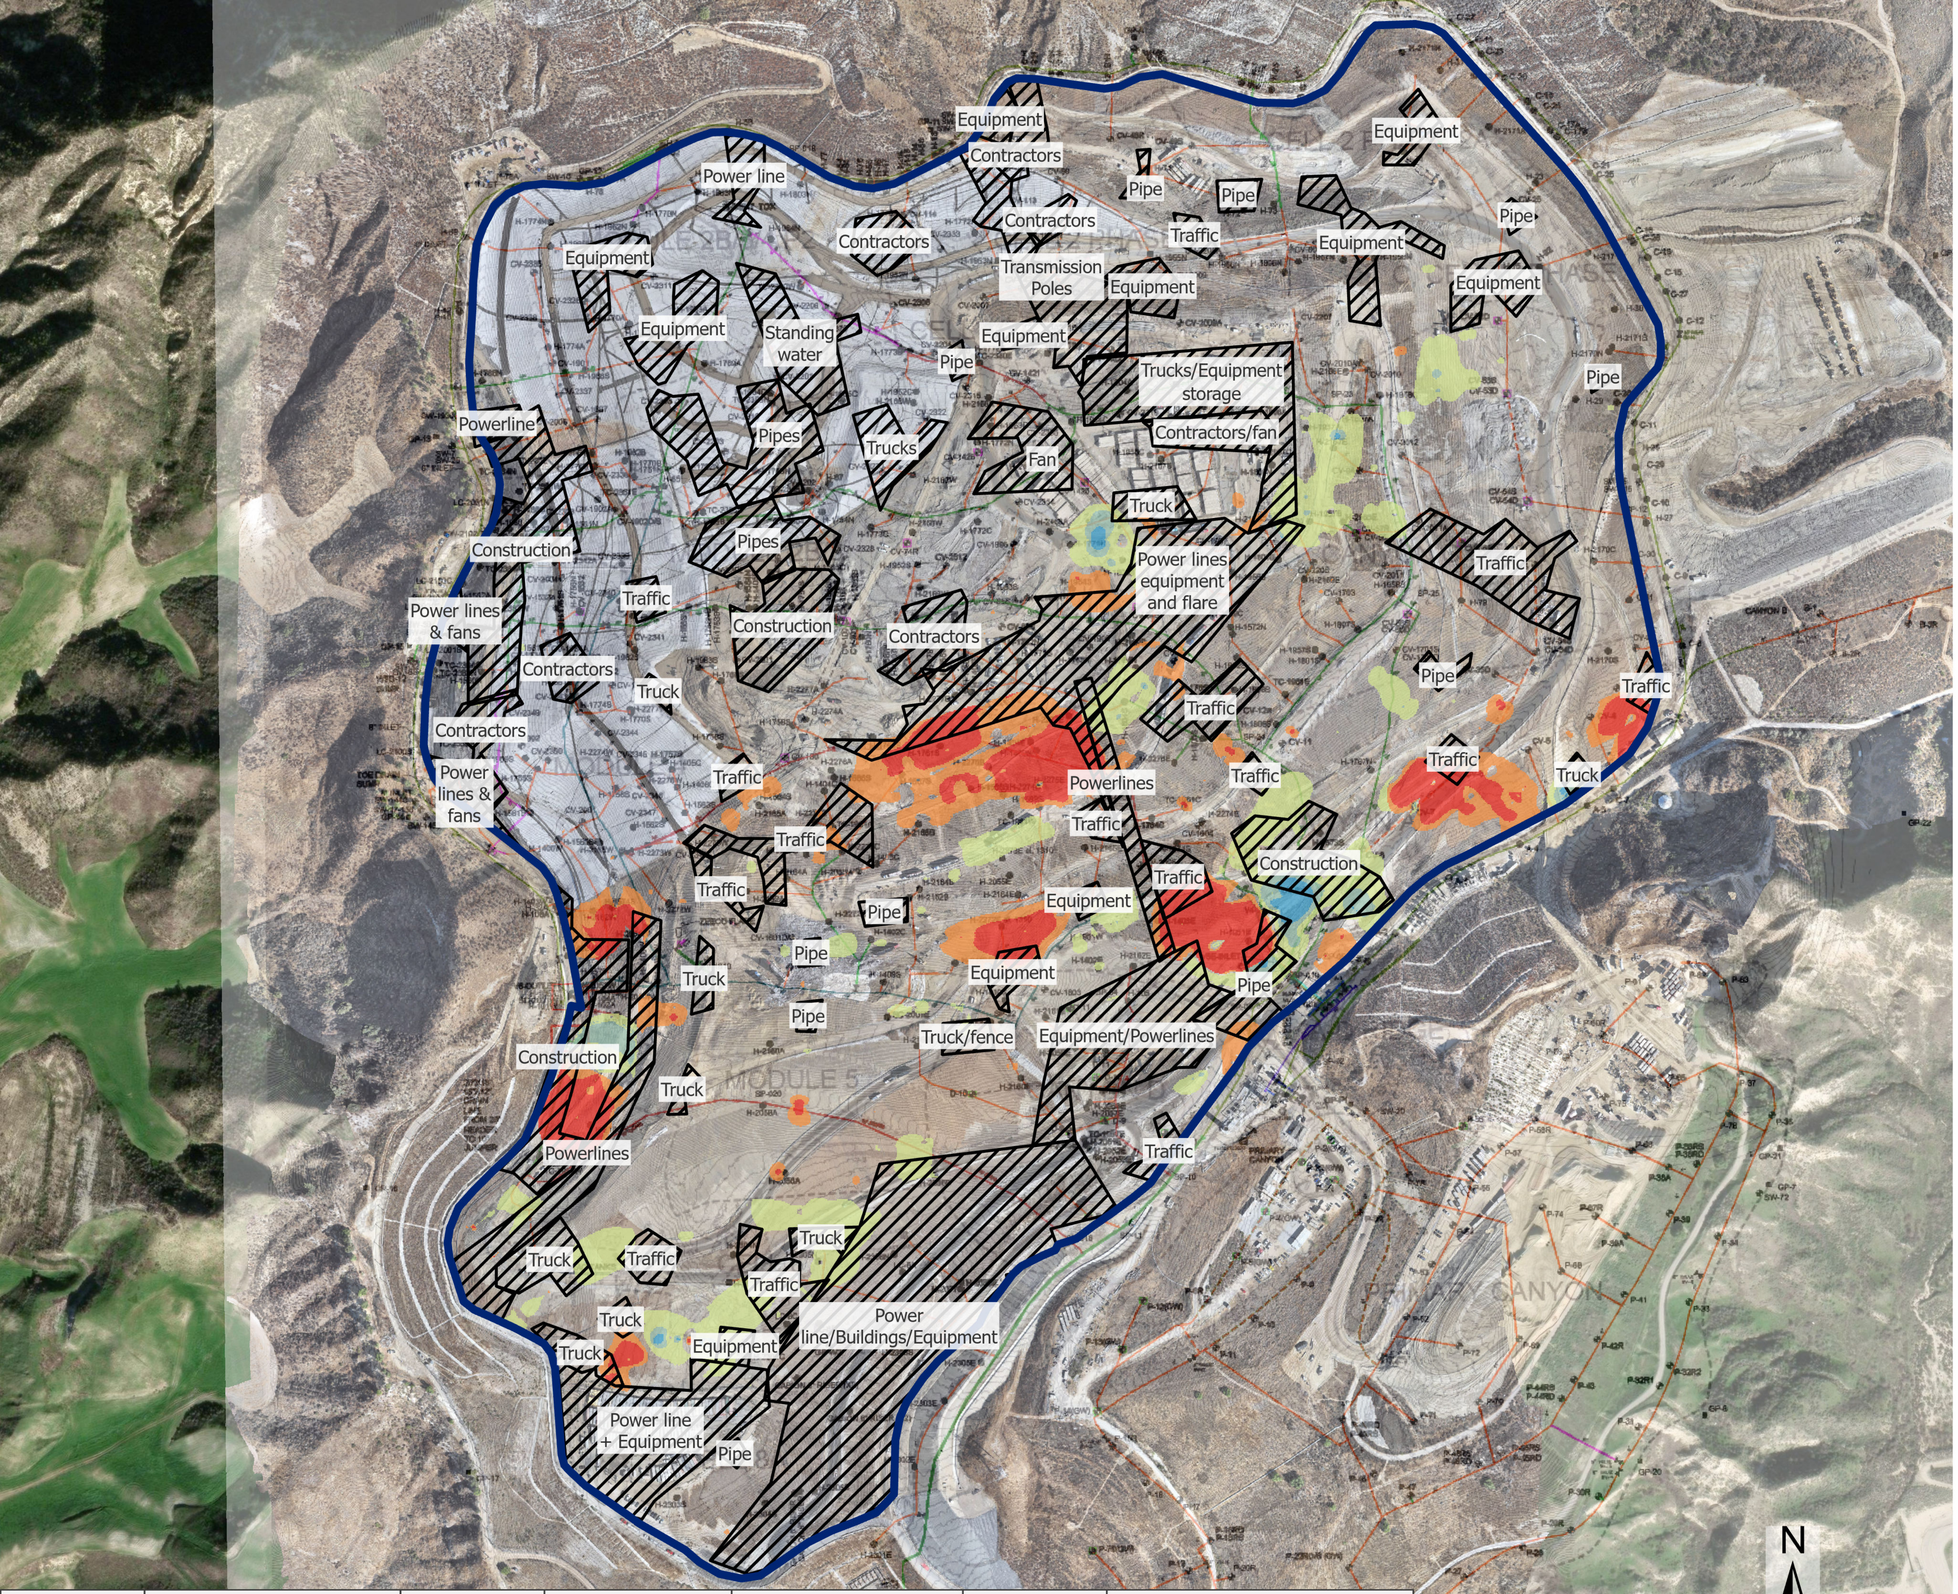

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
30-Sep	Clear Sky	93 °F	6 MPH	S	19%	30.27"
1-Oct	Clear Sky	90 °F	5 MPH	S	27%	30.33"

sniffer


Interpolated Methane Emissions Change as Recorded by the SnifferDRONE™, Sept 2026 to Oct 2026

09/22/26 - 10/01/26

Notes:
1. Basemap: As-built drawing provided by Franklin Engineers & Consultants, LLC dated May 2023; high resolution RGB imagery provided by Waste Connections dated Feb 2023.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N
3. Mean change from Sept. 2026 to Sept. 2026 was a 2.07 PPM Increase. Colors represent standard deviations from the mean. PPMs within one standard deviation are not shown.

Legend

- 186 - 43 PPM Decrease
- 42 -25 PPM Decrease
- 24 -7 PPM Decrease
- 6 PPM Decrease - 11 PPM Increase
- 12 - 29 PPM Increase
- 30 - 2,125 PPM Increase

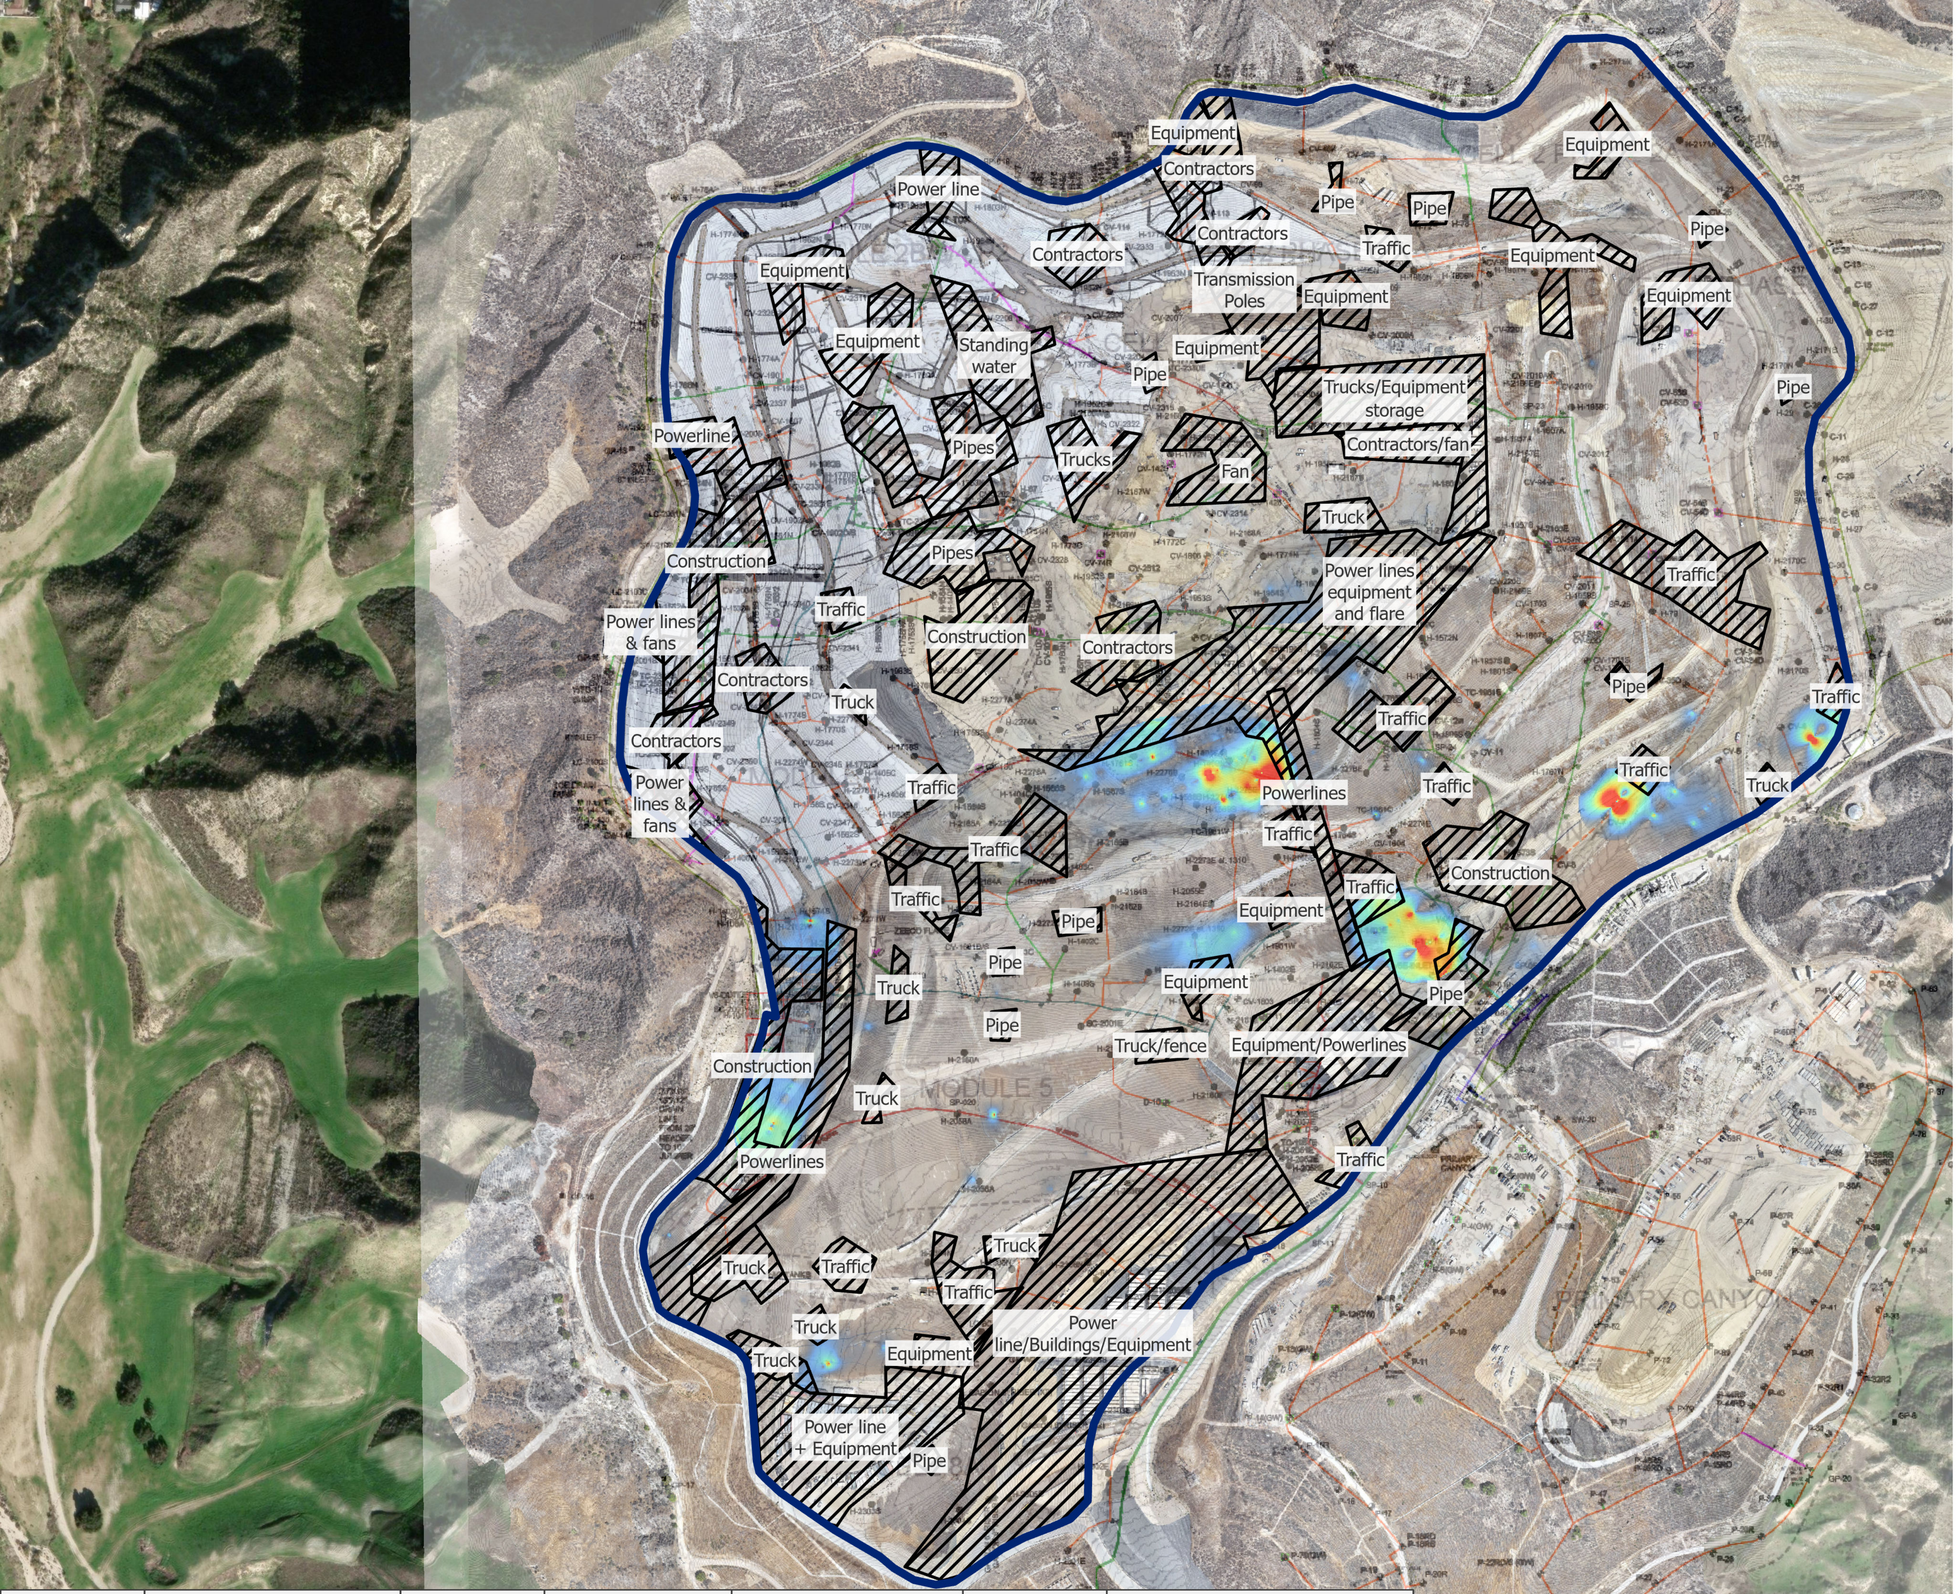

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
30-Sep	Clear Sky	93 °F	6 MPH	S	19%	30.27"
1-Oct	Clear Sky	90 °F	5 MPH	S	27%	30.33"

Chiquita Canyon Landfill Interpolated Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing

Sept 30 - Oct 1, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections dated Aug 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 150 300 600
Feet

Legend

CH4 PPM

200
156.64
117.58
78.52
39.45
0

Chiquita Canyon Landfill Methane Emissions Local Peak Values as Recorded by the SnifferDRONE™, over As-Built Drawing

Sep 30 - Oct 1, 2026

	Leak Count	Estimated Exceedance*
200-499 PPM	9	5
500-1000 PPM	4	4
1000-2000 PPM	0	0
2000-5000 PPM	1	1
5000+ PPM	0	0
Total	14	10

* Calculated using probabilities of peak locations manually verified to have emissions of 500+ ppm based on ongoing field studies


Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
30-Sep	Clear Sky	93 °F	6 MPH	S	19%	30.27"
1-Oct	Clear Sky	90 °F	5 MPH	S	27%	30.33"

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Jul 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

Legend
- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 4,999 PPM
- 5000 + PPM

N

0 150 300 600
Feet

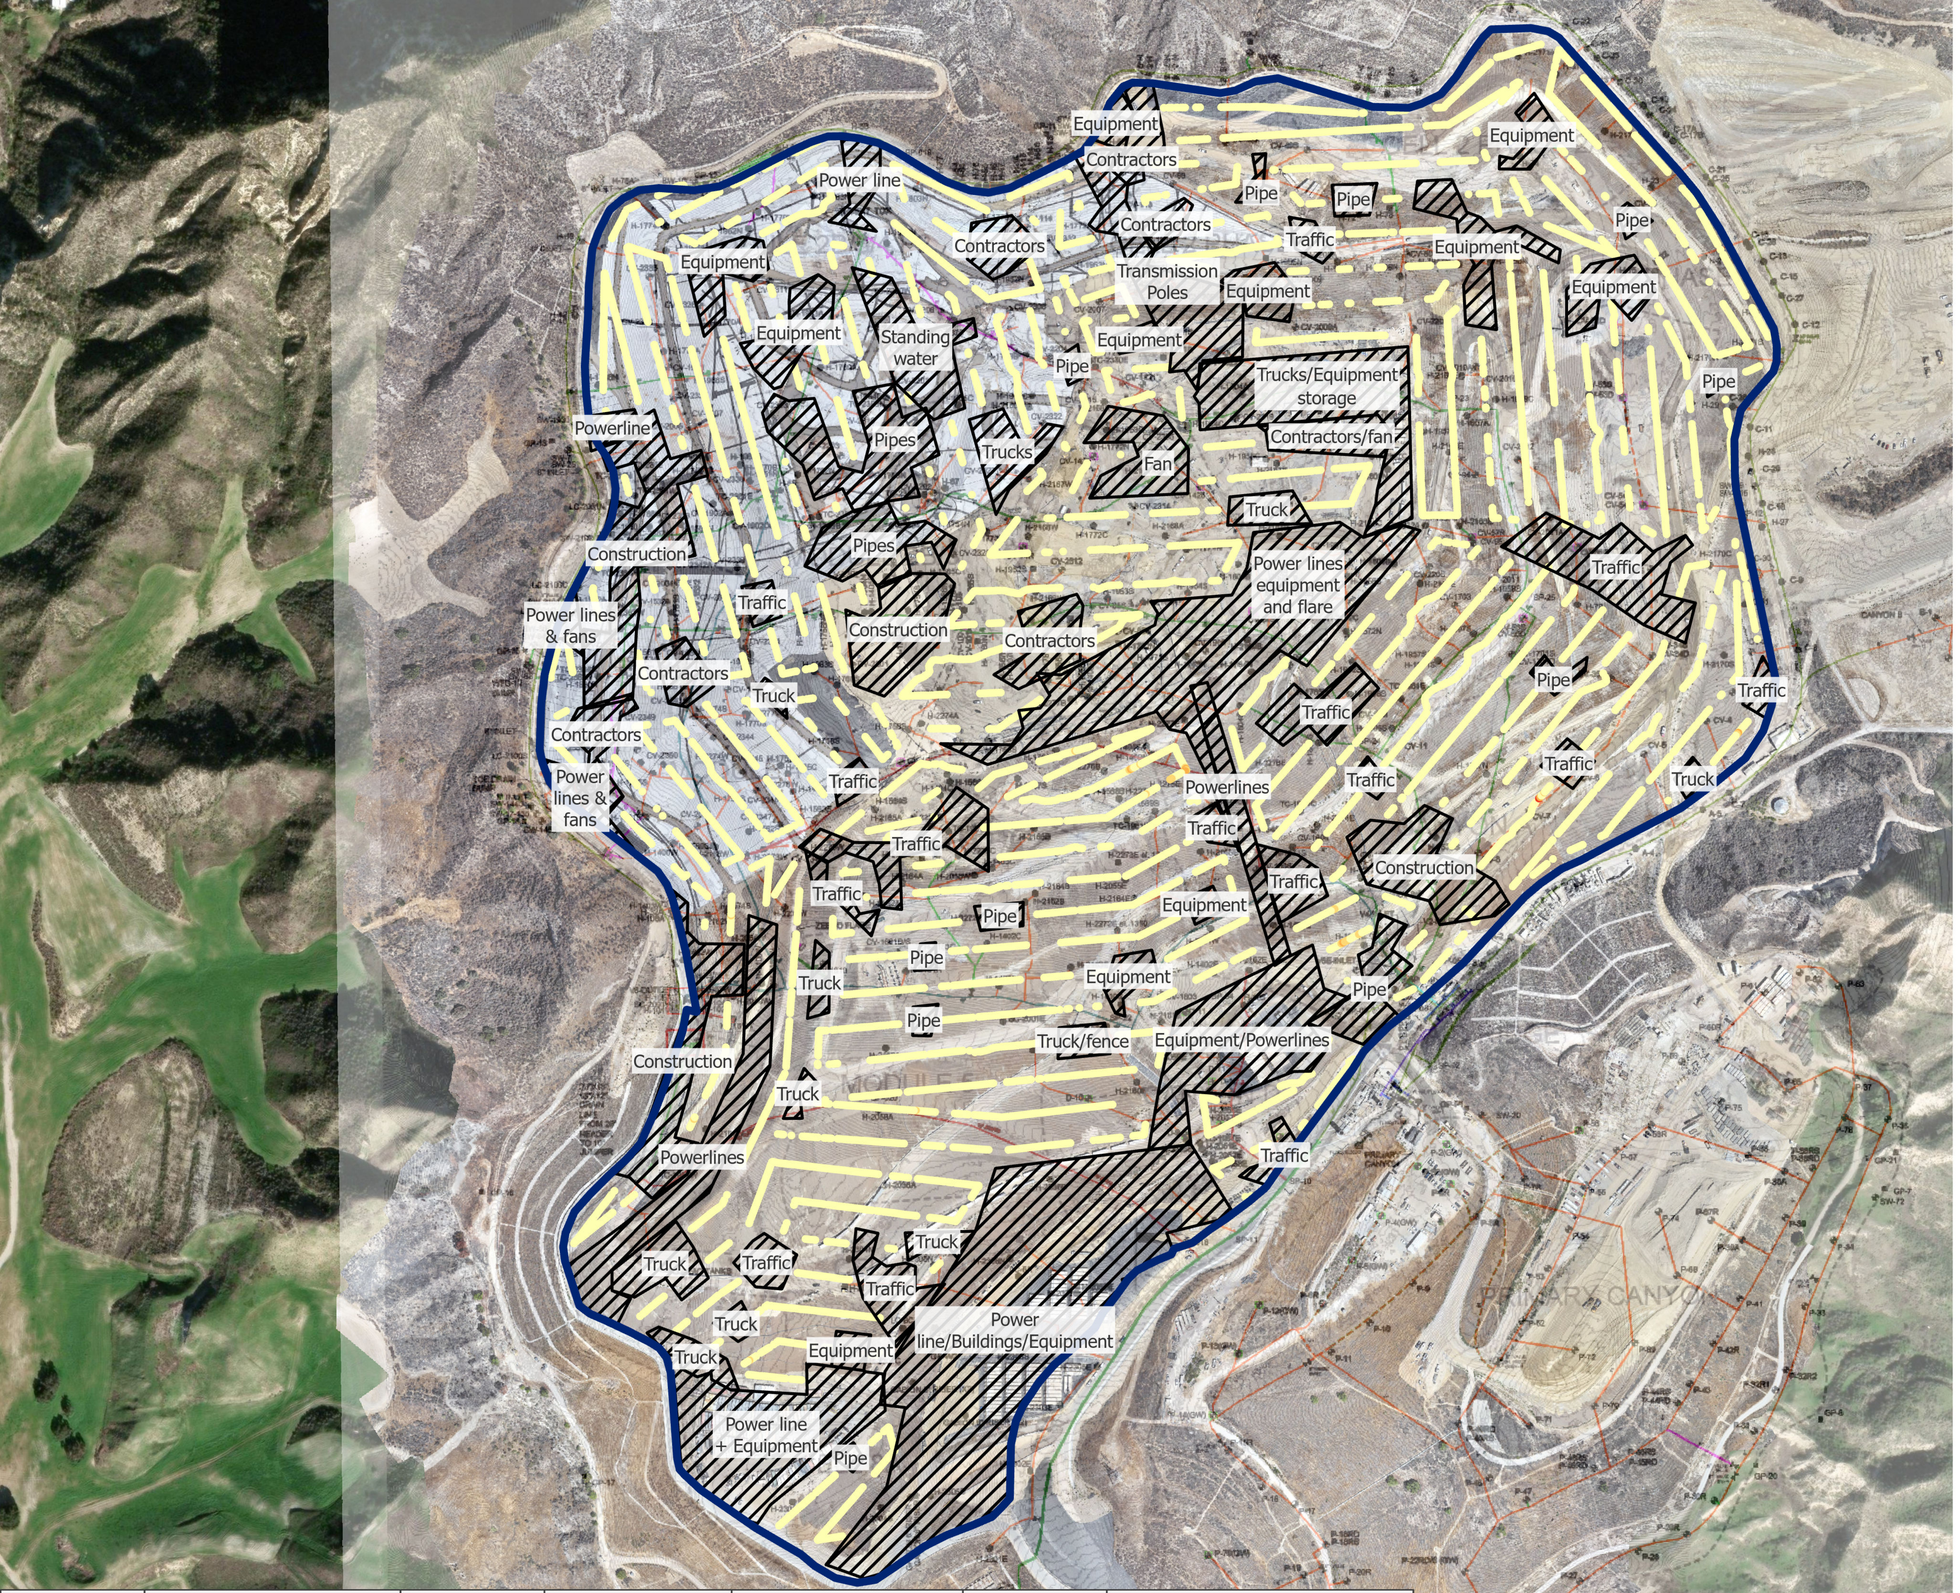

Date	Condition	Temp	Wind Speed	Wind Direction	Humidity	Barometric Pressure
30-Sep	Clear Sky	93 °F	6 MPH	S	19%	30.27"
1-Oct	Clear Sky	90 °F	5 MPH	S	27%	30.33"

Chiquita Canyon Landfill Point Methane Emissions as Recorded by the SnifferDRONE™, over As-Built Drawing

Sept 30 - Oct 1, 2026

Notes:
1. Basemap: As-built drawing provided by SCS Engineers, dated Dec 2023; high resolution RGB imagery provided by Waste Connections, dated Aug 2025.
2. Projected Coordinate System: WGS 1984 UTM Zone 11N

N

0 150 300 600
Feet

Legend

- < 200 PPM
- 200 - 499 PPM
- 500 - 999 PPM
- 1,000 - 1,999 PPM
- 2,000 - 5,000 PPM
- 5,000 + PPM

Attachment D

Daily Inlet Temperatures

Attachment D - LFGTS Vessel Inlet Temperatures

September 2026

	Inlet Temperature (F)			
Date Time	ST-1	ST-2	ST-3	ST-4
09/01/26 07:39	99	59	55	96
09/02/26 07:27	96	57	53	90
09/03/26 07:13	101	61	56	96
09/04/26 07:27	102	60	57	88
09/05/26 08:29	103	61	59	87
09/06/26 08:50	103	73	71	92
09/07/26 08:02	119	71	68	88*
09/08/26 07:09	111	72	70	90
09/09/26 07:51	122	73	71	92
09/10/26 08:00	115	80	77	94
09/11/26 07:43	115	76	72	100
09/12/26 09:35	123	78	79	99
09/13/26 08:08	111	67	65	94
09/14/26 07:49	110	64	62	89
09/15/26 08:03	121	69	66	92
09/16/26 07:56	108	69	66	92
09/17/26 08:13	106	68	66	91
09/18/26 07:57	120	60	55	85
09/19/26 11:42	86	78	91	89
09/20/26 09:16	119	67	64	90
09/21/26 07:16	116	67	65	88
09/22/26 09:54	121	68	69	98
09/23/26 07:28	111	64	63	86
09/24/26 10:40	109	78	82	106
09/25/26 08:08	114	65	62	90
09/26/26 09:23	114	65	65	98
09/27/26 10:24	132	82	83	106
09/28/26 07:43	112	62	57	86
09/29/26 14:02	141	101	103	110
09/30/26 10:58	135	77	80	100

*Outlet temp on ST-4 for 09/07 as inlet temperature recording malfunctioned

Attachment E

Well Temperature and CO Concentration Data

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIWA001	A-01	9/17/2026 7:39:23 AM	57.7	40.3	0.0	2.0			84.5		1.4
CHIWA002	A-02	9/17/2026 7:48:47 AM	57.5	40.7	0.0	1.8			90.9	91.0	1.4
CHIWA003	A-03	9/17/2026 8:00:42 AM	48.1	38.3	1.9	11.7			80.0	80.1	1.3
CHIWA004	A-04	9/17/2026 8:10:05 AM	56.4	41.2	0.0	2.4			95.5	95.5	1.4
CHIWA005	A-05	9/28/2026 8:50:32 AM	58.5	40.0	0.0	1.5			88.1	88.1	1.5
CHIWB001	B-01	9/17/2026 9:22:43 AM	5.5	20.4	0.0	74.1			76.1	76.2	0.3
CHIWB02R	B-02R	9/17/2026 9:16:57 AM	30.3	29.4	0.0	40.3			75.0	75.0	1.0
CHIWB03R	B-03R	9/16/2026 1:51:26 PM	21.9	26.7	0.0	51.4			87.2	87.1	0.8
CHIWB005	B-05	9/16/2026 2:03:40 PM	11.9	25.0	0.3	62.8			92.5	92.6	0.5
CHIWB006	B-06	9/17/2026 8:53:22 AM	21.9	27.2	0.0	50.9			79.2	79.3	0.8
CHIWB07R	B-07R	9/16/2026 10:45:52 AM	26.7	26.9	1.6	44.8			89.0	90.0	1.0
CHIWB07R	B-07R	9/16/2026 10:52:10 AM	32.0	29.4	0.5	38.1			94.8	94.9	1.1
CHIWB008	B-08	9/17/2026 8:39:40 AM	0.4	1.7	20.5	77.4			69.6	69.8	0.2
CHIWB008	B-08	9/17/2026 8:44:20 AM	4.2	6.3	15.3	74.2			68.1	68.3	0.7
CHIWB009	B-09	9/16/2026 9:27:25 AM	34.0	32.8	0.0	33.2			93.0	93.0	1.0
CHIWB010	B-10	9/16/2026 9:20:22 AM	26.4	29.1	0.0	44.5			90.5	90.9	0.9
CHIWB011	B-11	9/16/2026 8:54:56 AM	26.3	30.0	0.3	43.4			106.2	106.2	0.9
CHIWB012	B-12	9/16/2026 1:43:21 PM	15.2	26.0	0.0	58.8			96.1	96.3	0.6
CHIWB013	B-13	9/16/2026 1:37:34 PM	28.6	30.6	0.1	40.7			93.8	93.8	0.9
CHIWB014	B-14	9/16/2026 8:34:59 AM	14.4	27.4	0.0	58.2			104.6	105.1	0.5
CHIWC003	C-03	9/14/2026 1:58:34 PM	54.2	38.4	0.5	6.9			97.3	97.3	1.4
CHIWC007	C-07	9/30/2026 3:03:49 PM	50.5	41.1	0.0	8.4			98.0	97.9	1.2
CHIWC008	C-08	9/17/2026 10:13:25 AM	26.8	25.5	6.9	40.8			84.8	85.0	1.1
CHIWC008	C-08	9/17/2026 10:15:37 AM	30.4	28.3	4.9	36.4			84.9	85.1	1.1
CHIWC010	C-10	9/17/2026 10:44:49 AM	55.6	40.5	0.2	3.7			93.0	93.0	1.4
CHIWC011	C-11	9/3/2026 11:22:35 AM	56.7	40.3	0.0	3.0			98.8	98.9	1.4
CHIWC012	C-12	9/3/2026 11:48:07 AM	55.7	40.6	0.0	3.7			95.3	96.2	1.4
CHIWC015	C-15	9/3/2026 11:44:12 AM	49.1	37.1	2.3	11.5			97.8	97.9	1.3
CHIWC17B	C-17B	9/29/2026 9:29:28 AM	54.2	42.1	0.0	3.7			110.2	110.2	1.3



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIWC018	C-18	9/29/2026 10:05:18 AM	53.0	41.7	0.2	5.1			114.8	114.8	1.3
CHIWC019	C-19	9/29/2026 9:49:37 AM	55.2	41.6	0.0	3.2			98.8	98.9	1.3
CHIWC020	C-20	9/29/2026 9:55:47 AM	55.2	41.5	0.0	3.4			110.7	111.0	1.3
CHIWC024	C-24	9/29/2026 9:39:17 AM	35.6	32.8	5.2	26.4			102.3	102.8	1.1
CHIWC024	C-24	9/29/2026 9:44:02 AM	36.9	33.6	4.5	25.1			103.7	103.6	1.1
CHIWC025	C-25	9/25/2026 12:09:01 PM	0.1	0.6	21.0	78.3			124.3	124.5	0.2
CHIWC025	C-25	9/25/2026 12:10:05 PM	0.2	0.5	20.9	78.4			125.1	125.3	0.4
CHIWC026	C-26	9/25/2026 12:01:24 PM	47.6	44.1	0.0	8.3			110.0	110.0	1.1
CHIWC027	C-27	9/3/2026 11:37:39 AM	0.9	2.4	20.3	76.4			95.3	95.4	0.4
CHIWC027	C-27	9/3/2026 11:38:33 AM	0.1	0.8	20.6	78.5			95.8	95.8	0.1
CHIWC028	C-28	9/3/2026 11:18:29 AM	56.3	39.8	0.0	3.9			103.6	103.6	1.4
CHIWC029	C-29	9/21/2026 8:03:56 AM	47.0	49.8	0.0	3.2			109.4	109.2	0.9
CHIWC030	C-30	9/17/2026 10:25:51 AM	0.0	0.1	20.8	79.1			82.4	82.4	0.0
CHIWC030	C-30	9/17/2026 10:32:06 AM	48.9	39.4	1.1	10.6			112.3	113.3	1.2
CHIWCV02	CV-02	9/21/2026 10:39:51 AM	25.5	29.4	0.0	45.1			120.8	122.4	0.9
CHIWCV03	CV-03	9/21/2026 12:58:06 PM	38.7	36.2	0.0	25.1			120.7	120.7	1.1
CHIWCV04	CV-04	9/30/2026 8:15:05 AM	37.2	36.6	0.7	25.6			118.1	118.0	1.0
CHIWCV05	CV-05	9/4/2026 8:19:06 AM	55.5	40.8	0.0	3.8			106.0	106.0	1.4
CHIWCV06	CV-06	9/28/2026 3:58:30 PM	47.6	46.4	0.0	6.0			100.5	100.4	1.0
CV108-52	CV-108-52	9/1/2026 7:25:00 AM					450				
CV108-52	CV-108-52	9/1/2026 7:25:00 AM						130000			
CV108-52	CV-108-52	9/2/2026 7:35:40 AM	15.6	69.0	0.0	15.4			61.0	60.7	0.2
CV108-52	CV-108-52	9/2/2026 7:36:35 AM	15.6	71.2	0.0	13.2			59.0	59.0	0.2
CV108-52	CV-108-52	9/10/2026 3:44:09 PM	48.6	51.3	0.0	0.1			107.3	108.9	0.9
CV108-52	CV-108-52	9/10/2026 3:44:53 PM	49.6	50.4	0.0	0.0			108.7	108.6	1.0
CV108-52	CV-108-52	9/22/2026 11:11:22 AM	40.7	35.6	4.5	19.2			97.8	97.9	1.1
CHWCV113	CV-113	9/4/2026 7:00:00 AM					37				
CHWCV113	CV-113	9/4/2026 7:00:00 AM						0			
CHWCV113	CV-113	9/14/2026 9:34:21 AM	0.3	1.6	18.7	79.4			97.6	97.8	0.2



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHWCV113	CV-113	9/14/2026 9:35:35 AM	2.4	1.9	18.0	77.7			98.9	98.9	1.3
CHWCV113	CV-113	9/25/2026 10:33:54 AM	12.8	19.1	13.0	55.1			106.0	106.1	0.7
CHWCV114	CV-114	9/4/2026 8:22:00 AM					2200				
CHWCV114	CV-114	9/4/2026 8:22:00 AM						180000			
CHWCV114	CV-114	9/8/2026 9:33:48 AM	0.8	81.3	0.0	17.9			189.9	189.8	0.0
CHWCV114	CV-114	9/8/2026 9:39:00 AM					3460				
CHWCV114	CV-114	9/14/2026 8:28:09 AM	1.5	82.9	0.0	15.6			188.9	189.0	0.0
CHWCV114	CV-114	9/14/2026 8:30:00 AM					3730				
CHWCV114	CV-114	9/21/2026 8:22:00 AM	3.0	79.4	0.0	17.6			189.0	189.0	0.0
CHWCV114	CV-114	9/21/2026 8:25:00 AM					3480				
CHWCV114	CV-114	9/28/2026 8:16:00 AM	2.6	0.0	0.0	97.4			188.8	188.8	
CHWCV114	CV-114	9/28/2026 8:20:00 AM					3070				
CHWCV114	CV-114	9/28/2026 8:20:00 AM					3070				
CHCV1424	CV-1424	9/3/2026 1:47:43 PM	49.0	40.3	0.0	10.7			106.5	106.6	1.2
CCV1532A	CV-1532A	9/1/2026 7:30:00 AM						230000			
CCV1532A	CV-1532A	9/1/2026 7:30:00 AM					1400				
CCV1532A	CV-1532A	9/1/2026 1:33:46 PM	1.2	70.8	1.1	26.9			101.4	102.1	0.0
CCV1532A	CV-1532A	9/30/2026 3:06:52 PM	0.7	75.5	0.9	22.9			167.0	167.2	0.0
CCV1534A	CV-1534A-PLR	9/2/2026 10:23:59 AM	7.9	78.1	0.0	14.0			135.3	131.1	0.1
CCV1534A	CV-1534A-PLR	9/30/2026 3:09:20 PM	0.0	16.8	18.6	64.6			121.9	121.8	0.0
CHCV1535	CV-1535	9/1/2026 9:18:24 AM	45.5	48.3	0.0	6.2			105.4	105.5	0.9
CHCV1535	CV-1535	9/4/2026 7:22:00 AM					2800				
CHCV1535	CV-1535	9/4/2026 7:22:00 AM						180000			
CHCV1535	CV-1535	9/22/2026 11:06:11 AM	28.1	36.2	0.0	35.7			125.6	125.5	0.8
CHCV1535	CV-1535	9/24/2026 2:43:07 PM	29.6	40.2	0.0	30.2			126.1	125.8	0.7
CCV1601D	CV-1601D	9/15/2026 11:02:56 AM	51.2	42.2	0.0	6.6			112.2	113.5	1.2
CCV1601D	CV-1601D	9/21/2026 11:29:39 AM	44.9	43.8	0.0	11.3			115.5	115.1	1.0
CCV1601S	CV-1601S	9/15/2026 11:06:57 AM	50.1	42.8	0.0	7.1			113.2	115.2	1.2
CCV1601S	CV-1601S	9/21/2026 11:25:45 AM	43.0	45.8	0.0	11.2			118.7	117.7	0.9



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV1604	CV-1604	9/24/2026 10:50:44 AM	50.8	44.5	0.0	4.7			115.0	115.0	1.1
CCV1701D	CV-1701D	9/1/2026 8:45:21 AM	9.3	69.0	0.0	21.7			104.8	104.6	0.1
CCV1701S	CV-1701S	9/1/2026 8:41:19 AM	22.5	65.0	0.0	12.5			130.8	130.5	0.3
CHCV1901	CV-1901	9/14/2026 9:48:47 AM	23.1	68.2	0.1	8.6			117.4	117.2	0.3
CHCV1901	CV-1901	9/16/2026 2:06:50 PM	16.9	73.8	0.2	9.1			109.6	108.1	0.2
CCV1902A	CV-1902A	9/1/2026 7:35:00 AM					310				
CCV1902A	CV-1902A	9/1/2026 7:35:00 AM						43000			
CCV1902A	CV-1902A	9/8/2026 10:47:01 AM	2.5	75.0	0.2	22.3			158.4	159.4	0.0
CCV1902A	CV-1902A	9/8/2026 10:50:00 AM					1290				
CCV1902A	CV-1902A	9/16/2026 2:31:00 PM					869.5				
CCV1902A	CV-1902A	9/16/2026 2:32:50 PM	12.4	72.3	1.3	14.0			157.7	157.8	0.2
CCV1902A	CV-1902A	9/23/2026 2:32:08 PM	10.3	77.5	0.0	12.2			182.5	181.6	0.1
CCV1902A	CV-1902A	9/23/2026 2:37:00 PM					1210				
CCV1902A	CV-1902A	9/30/2026 2:35:00 PM					719				
CCV1902A	CV-1902A	9/30/2026 2:40:44 PM	9.6	64.4	2.6	23.4			154.5	155.0	0.1
CHCV1905	CV-1905	9/14/2026 1:14:41 PM	15.0	11.0	14.8	59.2			100.4	89.1	1.4
CHCV1905	CV-1905	9/22/2026 9:36:40 AM	42.3	33.7	4.1	19.9			78.9	89.6	1.3
CHCV1905	CV-1905	9/24/2026 2:08:39 PM	53.1	45.7	0.0	1.2			111.3	111.4	1.2
CHCV2001	CV-2001	9/2/2026 8:39:57 AM	9.5	69.9	2.0	18.6			79.4	79.5	0.1
CHCV2001	CV-2001	9/9/2026 7:20:00 AM					1100				
CHCV2001	CV-2001	9/9/2026 7:20:00 AM						100000			
CHCV2001	CV-2001	9/23/2026 8:47:00 AM	4.6	54.5	7.5	33.4			85.7	86.5	0.1
CHCV2002	CV-2002	9/1/2026 2:10:00 PM						117100			
CHCV2002	CV-2002	9/1/2026 2:10:00 PM					3900				
CHCV2002	CV-2002	9/1/2026 2:10:13 PM	12.4	71.4	0.3	15.9			185.8	185.8	0.2
CHCV2002	CV-2002	9/8/2026 1:42:58 PM	15.2	73.0	0.6	11.2			185.6	185.6	0.2
CHCV2002	CV-2002	9/8/2026 1:45:00 PM					4130				
CHCV2002	CV-2002	9/9/2026 7:25:00 AM					2900				
CHCV2002	CV-2002	9/9/2026 7:25:00 AM						140000			

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2002	CV-2002	9/17/2026 8:11:35 AM	24.9	67.9	0.4	6.8			183.5	183.4	0.4
CHCV2002	CV-2002	9/17/2026 8:13:00 AM					2270				
CHCV2002	CV-2002	9/24/2026 9:58:49 AM	9.8	72.3	0.0	17.9			184.2	184.3	0.1
CHCV2002	CV-2002	9/24/2026 10:10:00 AM					2900				
CHCV2003	CV-2003	9/2/2026 7:38:27 AM	15.0	69.9	0.0	15.1			99.9	101.4	0.2
CHCV2003	CV-2003	9/2/2026 7:41:22 AM	15.3	71.9	0.0	12.8			98.4	98.8	0.2
CHCV2003	CV-2003	9/10/2026 3:49:41 PM	48.3	51.7	0.0	0.0			123.9	123.9	0.9
CHCV2003	CV-2003	9/10/2026 3:50:31 PM	24.9	68.6	0.0	6.5			123.9	123.8	0.4
CHCV2003	CV-2003	9/22/2026 11:14:52 AM	16.0	73.2	0.0	10.8			113.2	113.2	0.2
CHCV2006	CV-2006	9/8/2026 10:53:00 AM	2.8	76.5	0.0	20.7			185.6	185.8	0.0
CHCV2006	CV-2006	9/8/2026 11:05:00 AM					2560				
CHCV2006	CV-2006	9/16/2026 2:22:00 PM					3660				
CHCV2006	CV-2006	9/16/2026 2:23:56 PM	12.8	77.6	0.0	9.6			186.3	186.2	0.2
CHCV2006	CV-2006	9/23/2026 2:26:56 PM	12.7	66.8	0.0	20.5			185.0	185.0	0.2
CHCV2006	CV-2006	9/23/2026 2:29:00 PM					3680				
CHCV2006	CV-2006	9/30/2026 2:25:00 PM					4140				
CHCV2006	CV-2006	9/30/2026 2:27:51 PM	8.5	78.2	0.0	13.3			185.9	185.9	0.1
CHCV2007	CV-2007	9/3/2026 10:00:55 AM	16.8	76.7	0.0	6.5			126.2	126.3	0.2
CHCV2007	CV-2007	9/4/2026 7:48:00 AM					470				
CHCV2007	CV-2007	9/4/2026 7:48:00 AM						62000			
CHCV2007	CV-2007	9/25/2026 2:05:13 PM	9.6	40.3	2.3	47.8			147.0	147.2	0.2
CHCV2007	CV-2007	9/28/2026 10:15:15 AM	8.3	37.5	2.7	51.5			152.5	152.5	0.2
CHCV2007	CV-2007	9/30/2026 10:12:39 AM	8.3	36.1	3.0	52.6			150.5	148.3	0.2
CHCV2007	CV-2007	9/30/2026 10:14:47 AM	8.0	36.4	3.3	52.3			146.5	146.4	0.2
CHCV2008	CV-2008	9/3/2026 9:55:07 AM	45.9	54.1	0.0	0.0			96.3	96.4	0.8
CHCV2008	CV-2008	9/25/2026 2:19:23 PM	41.2	57.0	0.0	1.8			101.7	101.7	0.7
CHCV2009	CV-2009	9/10/2026 1:22:30 PM	41.0	58.4	0.6	0.0			138.0	138.0	0.7
CCV2009A	CV-2009A	9/14/2026 1:25:59 PM	35.5	61.1	0.0	3.4			149.9	150.4	0.6
CCV2009A	CV-2009A	9/14/2026 1:27:41 PM	32.5	63.7	0.0	3.8			150.2	150.3	0.5



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV2009A	CV-2009A	9/14/2026 2:27:00 PM					913				
CCV2009A	CV-2009A	9/14/2026 2:28:48 PM	30.1	63.9	0.0	6.0			151.4	151.3	0.5
CCV2009A	CV-2009A	9/21/2026 1:44:33 PM	35.2	64.5	0.0	0.3			151.5	151.6	0.5
CCV2009A	CV-2009A	9/21/2026 1:45:00 PM					1300				
CHCV2010	CV-2010	9/22/2026 9:53:51 AM	41.3	51.2	0.1	7.4			89.1	89.2	0.8
CCV2010A	CV-2010A	9/22/2026 9:49:39 AM	43.1	44.1	0.3	12.5			85.1	85.4	1.0
CHCV2011	CV-2011	9/1/2026 10:17:28 AM	47.1	37.6	0.0	15.3			128.3	127.6	1.3
CCV2011A	CV-2011A	9/2/2026 2:08:11 PM	30.8	56.0	0.0	13.2			152.0	152.0	0.6
CCV2011A	CV-2011A	9/2/2026 2:10:00 PM					1005				
CCV2011A	CV-2011A	9/2/2026 2:10:00 PM						201200			
CCV2011A	CV-2011A	9/10/2026 9:14:08 AM	41.1	51.5	0.0	7.4			152.6	152.6	0.8
CCV2011A	CV-2011A	9/10/2026 9:16:00 AM					719.5				
CCV2011A	CV-2011A	9/11/2026 9:29:31 AM	28.1	46.4	0.0	25.5			152.7	152.7	0.6
CCV2011A	CV-2011A	9/17/2026 10:27:00 AM					1250				
CCV2011A	CV-2011A	9/17/2026 10:27:38 AM	36.0	50.8	0.0	13.2			151.4	151.3	0.7
CCV2011A	CV-2011A	9/24/2026 2:22:16 PM	39.1	52.3	0.1	8.5			151.9	151.9	0.7
CCV2011A	CV-2011A	9/24/2026 2:25:00 PM					800				
CHCV2012	CV-2012	9/28/2026 1:57:34 PM	39.0	55.2	0.0	5.8			137.9	134.1	0.7
CHCV2201	CV-2201-PLR	9/3/2026 7:56:39 AM	2.8	76.4	1.0	19.8			139.1	138.6	0.0
CHCV2201	CV-2201-PLR	9/3/2026 7:57:44 AM	2.8	77.0	0.9	19.3			138.5	139.8	0.0
CHCV2201	CV-2201-PLR	9/21/2026 8:20:29 AM	2.9	77.1	0.9	19.1			143.8	143.6	0.0
CHCV2201	CV-2201-PLR	9/21/2026 8:21:42 AM	3.0	76.6	0.8	19.6			144.3	144.8	0.0
CHCV2204	CV-2204-PLR	9/8/2026 2:13:18 PM	9.4	64.6	0.0	26.0			192.2	192.4	0.1
CHCV2204	CV-2204-PLR	9/8/2026 2:17:00 PM					1640				
CHCV2204	CV-2204-PLR	9/14/2026 10:19:07 AM	11.8	69.4	0.0	18.8			191.9	191.9	0.2
CHCV2204	CV-2204-PLR	9/14/2026 10:26:00 AM					1540				
CHCV2204	CV-2204-PLR	9/21/2026 10:25:45 AM	19.2	71.2	0.0	9.6			189.8	190.3	0.3
CHCV2204	CV-2204-PLR	9/21/2026 10:28:00 AM					1330				
CHCV2204	CV-2204-PLR	9/28/2026 10:21:59 AM	15.3	72.1	0.0	12.6			192.6	193.5	0.2



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2204	CV-2204-PLR	9/28/2026 10:25:00 AM					1320				
CHCV2205	CV-2205	9/22/2026 10:12:14 AM	10.1	71.8	0.0	18.1			136.1	136.1	0.1
CHCV2205	CV-2205	9/22/2026 10:43:00 AM	12.2	66.9	0.0	20.9			136.8	148.0	0.2
CHCV2205	CV-2205	9/22/2026 10:44:32 AM	10.1	72.7	0.0	17.2			148.6	148.5	0.1
CHCV2205	CV-2205	9/22/2026 1:55:00 PM					2840				
CHCV2207	CV-2207	9/3/2026 1:27:19 PM	46.3	53.4	0.0	0.3			125.7	125.5	0.9
CCV2208A	CV-2208A	9/10/2026 9:58:00 AM					1150				
CCV2208A	CV-2208A	9/11/2026 6:08:06 PM	20.2	61.2	0.0	18.6			149.8	152.6	0.3
CCV2208A	CV-2208A	9/14/2026 1:18:15 PM	34.8	60.1	0.1	5.0			156.8	156.9	0.6
CCV2208A	CV-2208A	9/14/2026 1:19:00 PM					1090				
CCV2208A	CV-2208A	9/24/2026 2:05:00 PM					896				
CCV2208A	CV-2208A	9/24/2026 2:07:36 PM	27.3	64.5	0.1	8.1			156.7	156.9	0.4
CHCV2301	CV-2301	9/2/2026 9:11:34 AM	20.2	64.6	0.0	15.2			179.1	179.0	0.3
CHCV2301	CV-2301	9/2/2026 9:13:00 AM					775				
CHCV2301	CV-2301	9/2/2026 9:13:00 AM						55700			
CHCV2301	CV-2301	9/3/2026 6:40:00 AM					470				
CHCV2301	CV-2301	9/3/2026 6:40:00 AM						55000			
CHCV2301	CV-2301	9/8/2026 9:59:02 AM	22.0	48.9	3.9	25.2			167.1	167.3	0.4
CHCV2301	CV-2301	9/8/2026 10:00:00 AM					1170				
CHCV2301	CV-2301	9/16/2026 1:43:00 PM					830				
CHCV2301	CV-2301	9/16/2026 1:46:53 PM	25.4	69.6	0.0	5.0			179.6	177.6	0.4
CHCV2301	CV-2301	9/23/2026 1:27:45 PM	44.1	55.9	0.0	0.0			175.3	174.9	0.8
CHCV2301	CV-2301	9/23/2026 1:31:00 PM					552				
CHCV2301	CV-2301	9/30/2026 10:14:35 AM	43.3	46.5	10.2	0.0			174.4	174.6	0.9
CHCV2301	CV-2301	9/30/2026 10:15:00 AM					495				
CHCV2302	CV-2302	9/2/2026 8:56:46 AM	43.0	45.2	1.1	10.7			125.8	125.7	1.0
CHCV2302	CV-2302	9/3/2026 6:45:00 AM					0				
CHCV2302	CV-2302	9/3/2026 6:45:00 AM						35000			
CHCV2302	CV-2302	9/17/2026 10:41:57 AM	44.5	45.0	1.1	9.4			113.0	113.3	1.0



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2303	CV-2303	9/3/2026 6:50:00 AM					1700				
CHCV2303	CV-2303	9/3/2026 6:50:00 AM						190000			
CHCV2303	CV-2303	9/3/2026 7:49:00 AM						187500			
CHCV2303	CV-2303	9/3/2026 7:49:00 AM					2165				
CHCV2303	CV-2303	9/3/2026 7:52:16 AM	2.1	73.6	0.0	24.3			190.5		0.0
CHCV2303	CV-2303	9/3/2026 7:53:05 AM	3.2	79.0	0.0	17.8			188.1	189.1	0.0
CHCV2303	CV-2303	9/9/2026 8:46:47 AM	8.8	39.4	0.2	51.6			188.7	188.8	0.2
CHCV2303	CV-2303	9/9/2026 8:50:00 AM					2470				
CHCV2303	CV-2303	9/15/2026 9:24:00 AM	9.7	61.8	0.0	28.5			188.5	189.6	0.2
CHCV2303	CV-2303	9/15/2026 9:25:00 AM					2620				
CHCV2303	CV-2303	9/22/2026 9:19:07 AM	6.4	78.9	0.0	14.7			192.6	193.1	0.1
CHCV2303	CV-2303	9/22/2026 9:21:00 AM					275				
CHCV2304	CV-2304-PLR	9/3/2026 8:30:11 AM	4.0	74.2	0.1	21.7			173.4	173.7	0.1
CHCV2304	CV-2304-PLR	9/3/2026 8:32:00 AM						190200			
CHCV2304	CV-2304-PLR	9/3/2026 8:32:00 AM					1980				
CHCV2304	CV-2304-PLR	9/9/2026 9:38:00 AM					1980				
CHCV2304	CV-2304-PLR	9/9/2026 9:42:30 AM	8.4	73.1	0.0	18.5			177.5	177.4	0.1
CHCV2304	CV-2304-PLR	9/11/2026 2:24:49 PM	2.6	74.4	0.0	23.0			173.4	173.3	0.0
CHCV2304	CV-2304-PLR	9/11/2026 2:25:38 PM	2.7	72.8	0.0	24.5			172.5	172.9	0.0
CHCV2304	CV-2304-PLR	9/15/2026 10:21:48 AM	15.9	69.0	0.0	15.1			176.0	176.8	0.2
CHCV2304	CV-2304-PLR	9/15/2026 10:22:00 AM					1620				
CHCV2304	CV-2304-PLR	9/22/2026 10:45:24 AM	15.0	72.1	0.0	12.9			175.7	176.4	0.2
CHCV2304	CV-2304-PLR	9/22/2026 10:46:00 AM					1470				
CHCV2304	CV-2304-PLR	9/29/2026 9:11:59 AM	26.1	60.7	0.0	13.2			177.6	178.0	0.4
CHCV2304	CV-2304-PLR	9/29/2026 9:20:00 AM					1930				
CHCV2305	CV-2305	9/1/2026 10:04:00 AM						50300			
CHCV2305	CV-2305	9/1/2026 10:04:00 AM					2310				
CHCV2305	CV-2305	9/1/2026 10:04:41 AM	36.5	59.2	0.0	4.3			158.7	158.8	0.6
CHCV2305	CV-2305	9/9/2026 8:05:00 AM						47000			



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2305	CV-2305	9/9/2026 8:05:00 AM					1200				
CHCV2305	CV-2305	9/9/2026 10:42:39 AM	27.0	71.2	0.0	1.8			155.5	155.6	0.4
CHCV2305	CV-2305	9/9/2026 10:43:11 AM	35.9	57.4	0.0	6.7			155.7	155.7	0.6
CHCV2305	CV-2305	9/9/2026 11:00:00 AM					2760				
CHCV2305	CV-2305	9/15/2026 2:00:00 PM					2740				
CHCV2305	CV-2305	9/15/2026 2:02:20 PM	26.5	73.5	0.0	0.0			163.4	163.8	0.4
CHCV2305	CV-2305	9/15/2026 2:04:55 PM	26.3	73.7	0.0	0.0			163.6	163.7	0.4
CHCV2305	CV-2305	9/22/2026 2:28:38 PM	16.0	81.6	0.0	2.4			157.9	157.9	0.2
CHCV2305	CV-2305	9/22/2026 2:31:00 PM					1530				
CHCV2305	CV-2305	9/29/2026 1:49:58 PM	35.5	60.1	0.0	4.4			158.9	159.0	0.6
CHCV2305	CV-2305	9/30/2026 10:00:00 AM					1380				
CHCV2305	CV-2305	9/30/2026 10:01:12 AM	20.9	51.5	0.0	27.6			157.5	157.6	0.4
CHCV2306	CV-2306-PLR	9/8/2026 1:31:32 PM	2.9	76.3	0.4	20.4			182.1	182.0	0.0
CHCV2306	CV-2306-PLR	9/8/2026 1:32:00 PM					1390				
CHCV2306	CV-2306-PLR	9/14/2026 10:15:56 AM	13.0	71.2	0.4	15.4			144.5	144.9	0.2
CHCV2306	CV-2306-PLR	9/14/2026 10:16:00 AM					1530				
CHCV2306	CV-2306-PLR	9/28/2026 10:16:32 AM	18.1	71.2	0.4	10.3			131.7	132.0	0.3
CHCV2306	CV-2306-PLR	9/28/2026 10:20:00 AM					1080				
CHCV2308	CV-2308-PLR	9/3/2026 8:03:28 AM	3.4	77.8	0.5	18.3			121.3	120.6	0.0
CHCV2308	CV-2308-PLR	9/21/2026 8:50:45 AM	4.4	76.6	0.6	18.4			118.8	117.4	0.1
CHCV2310	CV-2310-PLR	9/3/2026 7:36:11 AM	2.1	70.2	0.0	27.7			197.6	198.2	0.0
CHCV2310	CV-2310-PLR	9/3/2026 7:40:00 AM						172000			
CHCV2310	CV-2310-PLR	9/3/2026 7:40:00 AM					1770				
CHCV2310	CV-2310-PLR	9/9/2026 8:56:24 AM	6.3	84.5	0.0	9.2			192.2	192.6	0.1
CHCV2310	CV-2310-PLR	9/9/2026 8:59:00 AM					1680				
CHCV2310	CV-2310-PLR	9/15/2026 9:36:20 AM	6.6	72.7	0.0	20.7			190.5	190.6	0.1
CHCV2310	CV-2310-PLR	9/15/2026 9:38:00 AM					1250				
CHCV2310	CV-2310-PLR	9/22/2026 9:28:31 AM	6.7	70.6	0.0	22.7			191.6	191.7	0.1
CHCV2310	CV-2310-PLR	9/22/2026 9:31:00 AM					1060				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2310	CV-2310-PLR	9/29/2026 8:57:01 AM	12.2	76.1	0.0	11.7			190.2	147.2	0.2
CHCV2310	CV-2310-PLR	9/29/2026 9:00:00 AM					1630				
CHCV2311	CV-2311	9/8/2026 3:18:24 PM	17.6	61.0	0.0	21.4			164.5	166.2	0.3
CHCV2311	CV-2311	9/8/2026 3:20:00 PM					1310				
CHCV2311	CV-2311	9/15/2026 8:20:03 AM	24.8	66.9	0.0	8.3			169.4	169.6	0.4
CHCV2311	CV-2311	9/15/2026 8:21:00 AM					766				
CHCV2311	CV-2311	9/21/2026 2:22:27 PM	28.9	65.5	0.0	5.6			164.2		0.4
CHCV2311	CV-2311	9/21/2026 2:26:00 PM					1400				
CHCV2311	CV-2311	9/28/2026 3:16:00 PM					1380				
CHCV2311	CV-2311	9/28/2026 3:16:22 PM	26.6	64.8	0.0	8.6			154.6	156.5	0.4
CHCV2312	CV-2312-PLR	9/2/2026 8:09:16 AM	3.5	83.0	0.0	13.5			168.3	168.3	0.0
CHCV2312	CV-2312-PLR	9/3/2026 7:00:00 AM					2600				
CHCV2312	CV-2312-PLR	9/3/2026 7:00:00 AM						160000			
CHCV2312	CV-2312-PLR	9/9/2026 1:24:41 PM	17.4	71.0	0.1	11.5			169.7	169.6	0.2
CHCV2312	CV-2312-PLR	9/9/2026 1:35:00 PM					3410				
CHCV2312	CV-2312-PLR	9/16/2026 10:30:00 AM					3530				
CHCV2312	CV-2312-PLR	9/16/2026 10:44:19 AM	5.0	79.9	0.0	15.1			169.6	169.5	0.1
CHCV2312	CV-2312-PLR	9/23/2026 10:29:16 AM	43.9	53.5	2.6	0.0			170.0	170.1	0.8
CHCV2312	CV-2312-PLR	9/23/2026 10:31:00 AM					2893				
CHCV2312	CV-2312-PLR	9/23/2026 1:10:56 PM	6.8	79.1	0.0	14.1			169.8	169.8	0.1
CHCV2312	CV-2312-PLR	9/30/2026 9:44:29 AM	6.4	79.0	0.0	14.6			169.9	170.0	0.1
CHCV2312	CV-2312-PLR	9/30/2026 9:50:00 AM					2700				
CHCV2314	CV-2314-PLR	9/1/2026 1:32:37 PM	11.3	76.9	0.0	11.8			187.2	187.3	0.1
CHCV2314	CV-2314-PLR	9/1/2026 1:38:00 PM						120100			
CHCV2314	CV-2314-PLR	9/1/2026 1:38:00 PM					4010				
CHCV2314	CV-2314-PLR	9/4/2026 7:56:00 AM					2700				
CHCV2314	CV-2314-PLR	9/4/2026 7:56:00 AM						130000			
CHCV2314	CV-2314-PLR	9/9/2026 1:40:13 PM	23.0	76.3	0.0	0.7			188.1	188.1	0.3
CHCV2314	CV-2314-PLR	9/9/2026 1:46:00 PM					2810				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2314	CV-2314-PLR	9/16/2026 9:36:00 AM					3550				
CHCV2314	CV-2314-PLR	9/16/2026 9:39:58 AM	6.1	84.0	0.1	9.8			187.9	187.8	0.1
CHCV2314	CV-2314-PLR	9/23/2026 9:37:50 AM	9.3	79.1	0.6	11.0			186.3	186.2	0.1
CHCV2314	CV-2314-PLR	9/23/2026 9:40:00 AM					2960				
CHCV2314	CV-2314-PLR	9/30/2026 8:54:14 AM	5.1	82.0	0.2	12.7			185.5	185.5	0.1
CHCV2314	CV-2314-PLR	9/30/2026 9:00:00 AM					4010				
CHCV2315	CV-2315	9/3/2026 9:13:05 AM	14.8	74.0	0.1	11.1			184.9	185.1	0.2
CHCV2315	CV-2315	9/3/2026 9:17:00 AM						123800			
CHCV2315	CV-2315	9/3/2026 9:17:00 AM					2450				
CHCV2315	CV-2315	9/4/2026 8:04:00 AM					2200				
CHCV2315	CV-2315	9/4/2026 8:04:00 AM						170000			
CHCV2315	CV-2315	9/8/2026 1:48:37 PM	4.4	79.7	0.0	15.9			179.1	180.6	0.1
CHCV2315	CV-2315	9/8/2026 1:51:00 PM					2730				
CHCV2315	CV-2315	9/14/2026 10:40:35 AM	17.7	69.7	0.0	12.6			191.7	191.8	0.3
CHCV2315	CV-2315	9/14/2026 10:44:00 AM					1710				
CHCV2315	CV-2315	9/21/2026 10:37:20 AM	29.6	64.3	0.0	6.1			187.2	187.3	0.5
CHCV2315	CV-2315	9/21/2026 10:41:00 AM					1530				
CHCV2315	CV-2315	9/28/2026 10:36:48 AM	23.8	66.4	0.0	9.8			187.5	187.5	0.4
CHCV2315	CV-2315	9/28/2026 10:40:00 AM					1360				
CHCV2316	CV-2316	9/2/2026 1:39:54 PM	27.5	68.8	0.0	3.7			149.9	150.0	0.4
CHCV2316	CV-2316	9/2/2026 1:45:00 PM					2030				
CHCV2316	CV-2316	9/2/2026 1:45:00 PM						88600			
CHCV2316	CV-2316	9/3/2026 9:48:34 AM	20.4	69.4	0.0	10.2			149.7	149.8	0.3
CHCV2316	CV-2316	9/10/2026 10:21:00 AM					2370				
CHCV2316	CV-2316	9/10/2026 10:23:35 AM	29.7	67.3	0.0	3.0			150.3	150.3	0.4
CHCV2316	CV-2316	9/14/2026 1:56:00 PM					1625				
CHCV2316	CV-2316	9/14/2026 2:22:00 PM	27.0	66.3	0.0	6.7			149.9	150.0	0.4
CHCV2316	CV-2316	9/21/2026 1:35:00 PM					2270				
CHCV2316	CV-2316	9/21/2026 1:37:31 PM	34.4	65.5	0.0	0.1			150.0	150.1	0.5



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2319	CV-2319	9/2/2026 1:50:00 PM					4290				
CHCV2319	CV-2319	9/2/2026 1:50:00 PM						80200			
CHCV2319	CV-2319	9/2/2026 1:58:16 PM	12.6	83.0	0.0	4.4			161.1	161.2	0.2
CHCV2319	CV-2319	9/2/2026 1:59:13 PM	12.9	80.8	0.0	6.3			161.2	161.2	0.2
CHCV2319	CV-2319	9/9/2026 12:48:41 PM	47.6	52.3	0.1	0.0			160.6	160.6	0.9
CHCV2319	CV-2319	9/9/2026 1:00:00 PM					2990				
CHCV2319	CV-2319	9/15/2026 2:22:47 PM	36.4	63.6	0.0	0.0			167.3	167.3	0.6
CHCV2319	CV-2319	9/15/2026 2:25:00 PM					3030				
CHCV2319	CV-2319	9/22/2026 9:40:58 AM	10.1	81.4	0.1	8.4			172.8	173.6	0.1
CHCV2319	CV-2319	9/22/2026 2:35:00 PM					48.9				
CHCV2319	CV-2319	9/22/2026 2:40:31 PM	26.3	72.7	0.0	1.0			174.7	173.3	0.4
CHCV2319	CV-2319	9/22/2026 2:41:24 PM	19.4	78.4	0.0	2.2			173.1	173.1	0.2
CHCV2319	CV-2319	9/29/2026 1:53:56 PM	35.3	64.7	0.0	0.0			171.8	171.8	0.5
CHCV2319	CV-2319	9/29/2026 2:00:00 PM					4180				
CHCV2321	CV-2321	9/1/2026 8:55:00 AM						76600			
CHCV2321	CV-2321	9/1/2026 8:55:00 AM					3590				
CHCV2321	CV-2321	9/1/2026 8:56:13 AM	18.1	78.9	0.3	2.7			148.2	148.2	0.2
CHCV2321	CV-2321	9/9/2026 10:11:41 AM	33.7	66.3	0.0	0.0			145.3	145.3	0.5
CHCV2321	CV-2321	9/9/2026 10:15:00 AM					3130				
CHCV2321	CV-2321	9/15/2026 1:25:04 PM	39.1	60.5	0.4	0.0			139.3	139.2	0.6
CHCV2321	CV-2321	9/22/2026 9:56:29 AM	13.7	77.0	0.4	8.9			147.2	147.4	0.2
CHCV2321	CV-2321	9/29/2026 1:15:00 PM					2840				
CHCV2321	CV-2321	9/29/2026 1:21:59 PM	24.4	75.3	0.2	0.1			148.4	147.8	0.3
CHCV2321	CV-2321	9/29/2026 1:22:57 PM	30.9	68.9	0.2	0.0			147.7	147.7	0.4
CHCV2322	CV-2322	9/1/2026 1:56:33 PM	9.6	77.3	0.0	13.1			165.0	165.2	0.1
CHCV2322	CV-2322	9/1/2026 2:00:00 PM						109200			
CHCV2322	CV-2322	9/1/2026 2:00:00 PM					2140				
CHCV2322	CV-2322	9/10/2026 8:31:00 AM					2640				
CHCV2322	CV-2322	9/10/2026 8:31:01 AM	6.2	85.1	0.0	8.7			167.5	168.6	0.1



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2322	CV-2322	9/17/2026 12:50:31 PM	14.1	80.5	0.1	5.3			118.6	119.3	0.2
CHCV2324	CV-2324	9/3/2026 1:08:01 PM	45.8	51.9	0.0	2.3			124.9	125.2	0.9
CHCV2326	CV-2326	9/3/2026 9:35:00 AM						153800			
CHCV2326	CV-2326	9/3/2026 9:35:00 AM					3110				
CHCV2326	CV-2326	9/3/2026 9:35:50 AM	12.9	69.3	0.3	17.5			175.7	84.1	0.2
CHCV2326	CV-2326	9/3/2026 1:14:03 PM	57.8	40.7	0.0	1.5			91.5	95.7	1.4
CHCV2326	CV-2326	9/8/2026 3:25:00 PM					3480				
CHCV2326	CV-2326	9/8/2026 3:25:03 PM	16.6	62.7	0.0	20.7			168.8	168.8	0.3
CHCV2326	CV-2326	9/15/2026 8:24:00 AM					3020				
CHCV2326	CV-2326	9/15/2026 8:25:39 AM	20.9	62.6	0.0	16.5			175.6	175.7	0.3
CHCV2326	CV-2326	9/21/2026 2:28:46 PM	25.7	64.7	0.0	9.6			173.1	173.1	0.4
CHCV2326	CV-2326	9/21/2026 2:31:00 PM					3000				
CHCV2326	CV-2326	9/28/2026 3:18:43 PM	26.2	62.1	0.0	11.7			169.8	169.8	0.4
CHCV2326	CV-2326	9/28/2026 3:20:00 PM					2350				
CHCV2327	CV-2327	9/14/2026 10:24:05 AM	3.0	81.5	0.0	15.5			181.5	181.5	0.0
CHCV2327	CV-2327	9/14/2026 10:26:47 AM	2.7	81.7	0.0	15.6			180.4	180.9	0.0
CHCV2327	CV-2327	9/14/2026 1:30:00 PM					2360				
CHCV2327	CV-2327	9/21/2026 8:50:00 AM					1280				
CHCV2327	CV-2327	9/21/2026 8:58:34 AM	1.1	40.8	10.2	47.9			181.0	182.4	0.0
CHCV2327	CV-2327	9/21/2026 9:11:07 AM	1.8	81.4	0.3	16.5			179.4	179.7	0.0
CHCV2327	CV-2327	9/30/2026 9:14:10 AM	24.3	75.7	0.0	0.0			128.3	128.0	0.3
CHCV2328	CV-2328	9/1/2026 2:21:10 PM	43.1	56.9	0.0	0.0			152.5	152.9	0.8
CHCV2328	CV-2328	9/1/2026 2:25:00 PM						2600			
CHCV2328	CV-2328	9/1/2026 2:25:00 PM					1690				
CHCV2328	CV-2328	9/9/2026 7:45:00 AM					630				
CHCV2328	CV-2328	9/9/2026 7:45:00 AM						62000			
CHCV2328	CV-2328	9/9/2026 1:45:59 PM	50.5	49.5	0.0	0.0			119.1	119.1	1.0
CHCV2328	CV-2328	9/24/2026 10:56:47 AM	37.6	56.8	0.1	5.5			151.3	151.3	0.7
CHCV2328	CV-2328	9/24/2026 10:58:35 AM	36.2	57.1	0.0	6.7			151.1	151.3	0.6

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2328	CV-2328	9/28/2026 2:24:07 PM	35.2	63.1	0.0	1.7			148.1	148.4	0.6
CHCV2328	CV-2328	9/30/2026 8:52:17 AM	38.1	55.8	0.0	6.1			145.4	145.4	0.7
CHCV2328	CV-2328	9/30/2026 8:55:00 AM					887				
CHCV2333	CV-2333	9/3/2026 7:45:00 AM					2700				
CHCV2333	CV-2333	9/3/2026 7:45:00 AM						190000			
CHCV2333	CV-2333	9/8/2026 9:30:41 AM	1.2	65.8	0.0	33.0			184.2	184.4	0.0
CHCV2333	CV-2333	9/8/2026 9:35:00 AM					4040				
CHCV2333	CV-2333	9/14/2026 8:23:05 AM	1.9	84.2	0.0	13.9			186.5	186.6	0.0
CHCV2333	CV-2333	9/14/2026 8:25:00 AM					5050				
CHCV2333	CV-2333	9/21/2026 8:18:24 AM	2.4	80.9	0.0	16.7			187.9	187.9	0.0
CHCV2333	CV-2333	9/21/2026 8:21:00 AM					4470				
CHCV2333	CV-2333	9/28/2026 8:05:00 AM					4280				
CHCV2333	CV-2333	9/28/2026 8:08:07 AM	1.0	78.3	0.0	20.7			189.0	189.0	0.0
CHCV2334	CV-2334	9/3/2026 7:50:00 AM					2600				
CHCV2334	CV-2334	9/3/2026 7:50:00 AM						140000			
CHCV2334	CV-2334	9/9/2026 12:10:26 PM	9.0	77.9	0.2	12.9			145.6	145.6	0.1
CHCV2334	CV-2334	9/9/2026 12:10:43 PM	8.5	79.4	0.3	11.8			145.6	145.6	0.1
CHCV2334	CV-2334	9/17/2026 12:59:56 PM	13.2	73.2	0.0	13.6			147.7	147.7	0.2
CHCV2334	CV-2334	9/17/2026 1:03:00 PM					3390				
CHCV2334	CV-2334	9/24/2026 1:25:00 PM					3530				
CHCV2334	CV-2334	9/24/2026 1:44:17 PM	13.3	77.9	0.0	8.8			154.5	154.5	0.2
CHCV2334	CV-2334	9/24/2026 1:45:33 PM	11.5	74.4	0.0	14.1			154.7	154.7	0.2
CHCV2335	CV-2335	9/14/2026 9:41:03 AM	51.2	45.1	0.4	3.3			91.5	91.6	1.1
CHCV2335	CV-2335	9/16/2026 2:27:40 PM	54.4	45.4	0.1	0.1			100.0	100.2	1.2
CHCV2336	CV-2336	9/14/2026 9:45:07 AM	21.0	55.0	4.2	19.8			76.5	76.4	0.4
CHCV2336	CV-2336	9/16/2026 2:20:41 PM	18.7	63.8	2.5	15.0			87.0	87.1	0.3
CHCV2337	CV-2337	9/8/2026 10:57:52 AM	4.7	79.0	0.1	16.2			153.3	153.4	0.1
CHCV2337	CV-2337	9/8/2026 11:00:00 AM					4780				
CHCV2337	CV-2337	9/10/2026 9:00:00 AM					2000				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2337	CV-2337	9/10/2026 9:00:00 AM						100000			
CHCV2337	CV-2337	9/16/2026 2:13:00 PM					4360				
CHCV2337	CV-2337	9/16/2026 2:19:44 PM	15.3	0.0	0.0	84.7			153.7	153.8	
CHCV2337	CV-2337	9/23/2026 2:21:00 PM					3390				
CHCV2337	CV-2337	9/23/2026 2:21:55 PM	13.4	75.9	0.0	10.7			144.7	144.6	0.2
CHCV2337	CV-2337	9/30/2026 2:15:00 PM					4335				
CHCV2337	CV-2337	9/30/2026 2:20:16 PM	7.9	76.1	0.0	16.0			138.8	138.7	0.1
CHCV2338	CV-2338	9/8/2026 11:13:27 AM	2.7	71.9	0.5	24.9			149.9	152.5	0.0
CHCV2338	CV-2338	9/8/2026 11:15:00 AM					891				
CHCV2338	CV-2338	9/16/2026 2:23:00 PM					1140				
CHCV2338	CV-2338	9/16/2026 2:28:52 PM	10.7	76.9	0.0	12.4			175.6	176.3	0.1
CHCV2338	CV-2338	9/23/2026 2:29:15 PM	10.2	77.7	0.0	12.1			173.6	175.6	0.1
CHCV2338	CV-2338	9/23/2026 2:34:00 PM					1040				
CHCV2338	CV-2338	9/30/2026 2:30:00 PM					616				
CHCV2338	CV-2338	9/30/2026 2:35:34 PM	8.0	77.2	0.0	14.8			146.0	149.1	0.1
CHCV2339	CV-2339	9/14/2026 2:04:24 PM	3.7	17.1	15.3	63.9			99.8	99.8	0.2
CHCV2339	CV-2339	9/14/2026 2:06:28 PM	3.8	13.9	16.1	66.2			99.4	99.4	0.3
CHCV2339	CV-2339	9/30/2026 3:45:57 PM	0.5	35.4	11.2	52.9			132.6	130.4	0.0
CHCV2341	CV-2341	9/10/2026 8:29:15 AM	1.5	75.0	0.1	23.4			87.3	87.7	0.0
CHCV2341	CV-2341	9/10/2026 8:30:27 AM	1.4	75.5	0.0	23.1			88.0	88.0	0.0
CHCV2341	CV-2341	9/10/2026 8:45:00 AM					1500				
CHCV2341	CV-2341	9/10/2026 8:45:00 AM						220000			
CHCV2341	CV-2341	9/24/2026 2:48:06 PM	5.5	69.3	0.4	24.8			102.0	102.0	0.1
CCV2342A	CV-2342A-PLR	9/1/2026 1:37:03 PM	4.0	63.3	0.0	32.7			136.7	136.8	0.1
CCV2342A	CV-2342A-PLR	9/8/2026 2:08:22 PM	9.3	74.2	0.0	16.5			159.7	158.3	0.1
CCV2342A	CV-2342A-PLR	9/8/2026 2:17:58 PM	11.3	75.3	0.0	13.4			156.2	151.2	0.2
CCV2342A	CV-2342A-PLR	9/8/2026 2:20:00 PM					672				
CCV2342A	CV-2342A-PLR	9/14/2026 1:57:27 PM	6.1	66.8	0.1	27.1			189.8	189.9	0.1
CCV2342A	CV-2342A-PLR	9/14/2026 2:10:00 PM					1250				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV2342A	CV-2342A-PLR	9/24/2026 9:32:37 AM	8.8	69.5	0.0	21.7			182.3	182.1	0.1
CCV2342A	CV-2342A-PLR	9/24/2026 9:35:00 AM					1070				
CHCV2343	CV-2343-PLR	9/1/2026 1:05:42 PM	2.3	75.8	0.0	21.9			156.4	156.7	0.0
CHCV2343	CV-2343-PLR	9/1/2026 1:25:00 PM						157700			
CHCV2343	CV-2343-PLR	9/1/2026 1:25:00 PM					3600				
CHCV2343	CV-2343-PLR	9/8/2026 1:57:49 PM	4.6	82.2	0.2	13.0			160.7	160.7	0.1
CHCV2343	CV-2343-PLR	9/8/2026 1:59:45 PM	5.0	79.0	0.0	16.0			161.7	162.0	0.1
CHCV2343	CV-2343-PLR	9/8/2026 2:00:00 PM					3810				
CHCV2343	CV-2343-PLR	9/14/2026 1:47:19 PM	3.9	66.9	0.1	29.1			100.6	99.7	0.1
CHCV2343	CV-2343-PLR	9/14/2026 1:50:00 PM					4970				
CHCV2343	CV-2343-PLR	9/16/2026 12:27:21 PM	0.9	72.6	0.3	26.2			180.6	178.9	0.0
CHCV2343	CV-2343-PLR	9/24/2026 9:22:03 AM	13.7	68.1	0.0	18.2			189.4	189.6	0.2
CHCV2343	CV-2343-PLR	9/24/2026 9:25:00 AM					3890				
CHCV2344	CV-2344	9/1/2026 7:15:00 AM					1500				
CHCV2344	CV-2344	9/1/2026 12:55:13 PM	10.7	76.2	0.0	13.1			141.6	142.2	0.1
CHCV2344	CV-2344	9/1/2026 7:15:00 PM						110000			
CHCV2344	CV-2344	9/8/2026 1:49:02 PM	12.4	80.3	0.0	7.3			150.4	150.5	0.2
CHCV2344	CV-2344	9/8/2026 1:50:00 PM					2700				
CHCV2344	CV-2344	9/8/2026 1:50:10 PM	12.1	80.1	0.0	7.8			150.8	150.8	0.2
CHCV2344	CV-2344	9/14/2026 10:26:52 AM	12.3	67.3	0.0	20.4			147.1	147.4	0.2
CHCV2344	CV-2344	9/14/2026 10:32:00 AM					2050				
CHCV2344	CV-2344	9/24/2026 9:12:30 AM	11.1	69.4	0.0	19.5			158.7	158.9	0.2
CHCV2344	CV-2344	9/24/2026 9:15:00 AM					1700				
CHCV2345	CV-2345	9/1/2026 7:10:00 AM					450				
CHCV2345	CV-2345	9/1/2026 7:10:00 AM						33000			
CHCV2345	CV-2345	9/2/2026 7:32:38 AM	19.8	65.4	0.0	14.8			93.5	93.6	0.3
CHCV2345	CV-2345	9/22/2026 11:32:10 AM	17.6	65.8	0.3	16.3			109.5	109.5	0.3
CHCV2346	CV-2346	9/1/2026 7:05:00 AM					540				
CHCV2346	CV-2346	9/1/2026 7:05:00 AM						53000			

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2346	CV-2346	9/1/2026 10:35:00 AM						16600			
CHCV2346	CV-2346	9/1/2026 10:35:00 AM					532				
CHCV2346	CV-2346	9/1/2026 10:36:56 AM	2.2	78.3	0.0	19.5			180.8	180.2	0.0
CHCV2346	CV-2346	9/8/2026 2:30:00 PM					2740				
CHCV2346	CV-2346	9/8/2026 2:32:55 PM	11.4	81.2	0.1	7.3			179.4	179.6	0.1
CHCV2346	CV-2346	9/14/2026 10:07:15 AM	2.2	74.4	0.0	23.5			184.5	184.6	0.0
CHCV2346	CV-2346	9/14/2026 10:09:25 AM	1.6	76.0	0.0	22.4			184.7	184.6	0.0
CHCV2346	CV-2346	9/14/2026 10:10:00 AM					1720				
CHCV2346	CV-2346	9/24/2026 9:05:00 AM					1525				
CHCV2346	CV-2346	9/24/2026 9:07:33 AM	4.5	81.8	0.0	13.7			187.3	187.2	0.1
CHCV2347	CV-2347	9/1/2026 6:55:00 AM					610				
CHCV2347	CV-2347	9/1/2026 6:55:00 AM						46000			
CHCV2347	CV-2347	9/2/2026 7:17:45 AM	14.4	48.6	0.2	36.8			91.2	91.0	0.3
CHCV2347	CV-2347	9/22/2026 12:05:58 PM	14.6	47.0	1.1	37.3			117.6	117.7	0.3
CHCV2348	CV-2348	9/1/2026 6:50:00 AM						28000			
CHCV2348	CV-2348	9/1/2026 6:50:00 PM					380				
CHCV2348	CV-2348	9/2/2026 7:12:27 AM	19.9	51.5	0.1	28.5			131.4	131.4	0.4
CHCV2348	CV-2348	9/2/2026 7:13:13 AM	19.9	51.7	0.1	28.3			131.4	131.5	0.4
CHCV2348	CV-2348	9/22/2026 12:12:09 PM	19.0	51.4	0.0	29.6			137.6	137.6	0.4
CHCV2348	CV-2348	9/22/2026 12:13:11 PM	18.8	53.3	0.0	27.9			137.9	137.9	0.4
CHCV2349	CV-2349	9/1/2026 2:05:00 AM						151900			
CHCV2349	CV-2349	9/1/2026 2:02:58 PM	3.1	71.2	0.7	25.0			162.2	161.7	0.0
CHCV2349	CV-2349	9/1/2026 2:05:00 PM					2770				
CHCV2349	CV-2349	9/2/2026 7:50:00 AM					2900				
CHCV2349	CV-2349	9/2/2026 7:50:00 AM						200000			
CHCV2349	CV-2349	9/8/2026 1:35:00 PM					3020				
CHCV2349	CV-2349	9/8/2026 1:37:23 PM	9.1	77.3	0.7	12.9			164.0	163.8	0.1
CHCV2349	CV-2349	9/8/2026 1:38:01 PM	9.5	80.8	0.3	9.4			163.4	163.5	0.1
CHCV2349	CV-2349	9/17/2026 9:37:56 AM	10.3	75.6	0.0	14.1			176.9	178.0	0.1



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2349	CV-2349	9/17/2026 9:40:00 AM					2410				
CHCV2349	CV-2349	9/24/2026 9:55:30 AM	10.2	72.1	0.0	17.7			181.6	181.7	0.1
CHCV2349	CV-2349	9/24/2026 10:05:00 AM					2680				
CHCV2350	CV-2350	9/1/2026 7:20:00 AM					3400				
CHCV2350	CV-2350	9/1/2026 7:20:00 AM						170000			
CHCV2350	CV-2350	9/2/2026 8:27:52 AM	6.2	69.6	1.0	23.2			75.8	75.6	0.1
CHCV2350	CV-2350	9/23/2026 9:06:15 AM	5.1	79.7	0.3	14.9			117.3	117.4	0.1
CHCV2351	CV-2351	9/2/2026 7:15:00 AM					220				
CHCV2351	CV-2351	9/2/2026 7:15:00 AM						27000			
CHCV2351	CV-2351	9/10/2026 12:26:23 PM	19.0	47.9	5.4	27.7			118.4	118.2	0.4
CHCV2351	CV-2351	9/10/2026 12:27:25 PM	18.2	45.7	5.5	30.6			118.0	117.9	0.4
CHCV2351	CV-2351	9/23/2026 9:53:22 AM	0.0	9.2	19.0	71.8			96.7	96.6	0.0
CHCV2352	CV-2352	9/2/2026 7:20:00 AM					820				
CHCV2352	CV-2352	9/2/2026 7:20:00 AM						190000			
CHCV2352	CV-2352	9/10/2026 11:57:24 AM	3.8	73.5	0.6	22.1			146.1	144.6	0.1
CHCV2352	CV-2352	9/10/2026 11:59:11 AM	3.7	74.6	0.2	21.5			144.6	144.6	0.0
CHCV2352	CV-2352	9/30/2026 3:26:31 PM	18.1	68.1	0.1	13.7			189.3	190.5	0.3
CHCV2353	CV-2353-PLR	9/2/2026 7:54:07 AM	4.1	68.4	1.0	26.5			90.4	91.2	0.1
CHCV2353	CV-2353-PLR	9/10/2026 8:40:00 AM					560				
CHCV2353	CV-2353-PLR	9/10/2026 8:40:00 AM						230000			
CHCV2353	CV-2353-PLR	9/30/2026 4:20:22 PM	1.9	39.9	8.9	49.3			140.6	142.2	0.0
CHCV2354	CV-2354	9/2/2026 7:45:00 AM					1400				
CHCV2354	CV-2354	9/2/2026 7:45:00 AM						150000			
CHCV2354	CV-2354	9/2/2026 8:05:50 AM	7.2	73.8	0.0	19.0			163.2	163.4	0.1
CHCV2354	CV-2354	9/2/2026 8:06:24 AM	7.4	74.5	0.1	18.0			162.5	162.2	0.1
CHCV2354	CV-2354	9/8/2026 8:08:52 AM	5.4	74.5	0.0	20.1			187.3	188.2	0.1
CHCV2354	CV-2354	9/8/2026 8:10:05 AM	5.3	70.3	0.0	24.4			188.7	188.0	0.1
CHCV2354	CV-2354	9/8/2026 9:08:00 AM					1530				
CHCV2354	CV-2354	9/17/2026 9:46:30 AM	11.4	75.6	0.0	13.0			187.6	188.0	0.2



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2354	CV-2354	9/17/2026 9:50:00 AM					2210				
CHCV2354	CV-2354	9/24/2026 9:34:17 AM	9.4	72.7	0.0	17.9			182.2	182.3	0.1
CHCV2354	CV-2354	9/24/2026 9:47:15 AM	7.7	71.3	0.3	20.7			110.3	110.5	0.1
CHCV2354	CV-2354	9/24/2026 9:50:00 AM					1210				
CCV24001	CV-24001	9/10/2026 9:02:39 AM	53.4	44.3	0.0	2.3			105.6	106.3	1.2
CCV24001	CV-24001	9/16/2026 2:35:59 PM	51.9	45.1	0.1	2.9			97.2	97.4	1.2
CCV24002	CV-24002	9/10/2026 8:53:47 AM	35.4	49.0	0.0	15.6			112.6	111.9	0.7
CCV24002	CV-24002	9/16/2026 2:44:36 PM	35.4	49.1	0.1	15.4			111.0	110.3	0.7
CCV24003	CV-24003	9/14/2026 9:33:43 AM	26.1	40.5	0.6	32.8			104.8	105.0	0.6
CCV24003	CV-24003	9/16/2026 2:48:11 PM	30.2	54.6	0.2	15.0			106.5	106.6	0.6
CCV24004	CV-24004	9/1/2026 11:16:57 AM	38.7	53.1	0.0	8.2			122.3	122.4	0.7
CCV24004	CV-24004	9/16/2026 12:39:13 PM	31.8	52.3	0.0	15.9			121.3	121.2	0.6
CCV24006	CV-24006	9/1/2026 11:38:09 AM	20.5	66.6	1.5	11.4			132.3	130.8	0.3
CCV24006	CV-24006	9/1/2026 11:38:58 AM	19.2	67.4	1.8	11.6			130.2	130.4	0.3
CCV24006	CV-24006	9/16/2026 1:53:51 PM	11.4	77.0	1.6	10.0			111.5	111.6	0.1
CCV24007	CV-24007	9/1/2026 1:41:17 PM	26.5	46.2	0.1	27.2			145.5	145.7	0.6
CCV24007	CV-24007	9/3/2026 7:10:00 AM					400				
CCV24007	CV-24007	9/3/2026 7:10:00 AM						51000			
CCV24007	CV-24007	9/8/2026 3:13:15 PM	16.2	67.7	0.0	16.1			166.8	166.8	0.2
CCV24007	CV-24007	9/8/2026 3:15:00 PM					1040				
CCV24007	CV-24007	9/15/2026 8:10:00 AM					283				
CCV24007	CV-24007	9/15/2026 8:12:16 AM	28.1	41.7	0.0	30.2			144.4	144.3	0.7
CCV24007	CV-24007	9/29/2026 9:01:50 AM	20.3	40.7	0.1	38.9			145.4	145.5	0.5
CCV24007	CV-24007	9/29/2026 9:03:57 AM	13.4	65.5	0.0	21.1			146.3	146.5	0.2
CCV24007	CV-24007	9/29/2026 9:55:00 AM					1690				
CCV24008	CV-24008	9/8/2026 3:07:24 PM	12.6	67.9	0.0	19.5			185.4	185.5	0.2
CCV24008	CV-24008	9/8/2026 3:09:00 PM					1840				
CCV24008	CV-24008	9/14/2026 2:57:03 PM	17.1	65.8	0.0	17.1			185.2	185.4	0.3
CCV24008	CV-24008	9/14/2026 2:59:00 PM					1650				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24008	CV-24008	9/21/2026 2:19:31 PM	23.0	70.9	0.0	6.1			182.8	182.8	0.3
CCV24008	CV-24008	9/21/2026 2:20:00 PM					1250				
CCV24008	CV-24008	9/28/2026 3:12:00 PM					756				
CCV24008	CV-24008	9/28/2026 3:12:04 PM	26.6	63.0	0.0	10.4			181.5	181.6	0.4
CCV24009	CV-24009	9/8/2026 3:00:41 PM	6.4	77.4	0.0	16.2			172.4	172.2	0.1
CCV24009	CV-24009	9/8/2026 3:03:00 PM					1480				
CCV24009	CV-24009	9/14/2026 2:51:55 PM	15.3	72.6	0.2	11.9			167.3	167.3	0.2
CCV24009	CV-24009	9/14/2026 2:52:00 PM					1120				
CCV24009	CV-24009	9/21/2026 2:14:38 PM	15.1	74.0	0.3	10.6			173.3	173.0	0.2
CCV24009	CV-24009	9/21/2026 2:15:00 PM					1460				
CCV24009	CV-24009	9/28/2026 2:54:10 PM	13.9	74.5	0.0	11.6			161.2	161.3	0.2
CCV24009	CV-24009	9/28/2026 3:05:00 PM					1280				
CCV24010	CV-24010	9/14/2026 1:20:33 PM	34.8	54.3	0.5	10.4			103.5	103.6	0.6
CCV24010	CV-24010	9/23/2026 1:13:43 PM	0.0	1.9	20.0	78.1			104.5	104.5	0.0
CCV24011	CV-24011	9/10/2026 1:14:00 PM					2600				
CCV24011	CV-24011	9/10/2026 1:15:42 PM	18.7	69.7	0.0	11.6			189.4	189.5	0.3
CCV24011	CV-24011	9/15/2026 8:34:00 AM					2610				
CCV24011	CV-24011	9/15/2026 8:38:24 AM	19.0	67.0	0.0	14.0			185.6	185.6	0.3
CCV24011	CV-24011	9/22/2026 8:35:45 AM	18.9	68.4	0.0	12.7			183.9	183.8	0.3
CCV24011	CV-24011	9/22/2026 8:37:00 AM					1880				
CCV24011	CV-24011	9/29/2026 8:04:57 AM	18.1	65.5	0.0	16.4			181.9	181.8	0.3
CCV24011	CV-24011	9/29/2026 8:10:00 AM					2250				
CCV24012	CV-24012	9/10/2026 1:34:00 PM					2600				
CCV24012	CV-24012	9/10/2026 1:36:19 PM	8.6	79.7	0.0	11.7			182.7	181.8	0.1
CCV24012	CV-24012	9/15/2026 8:57:47 AM	5.6	60.0	0.0	34.4			187.7	187.7	0.1
CCV24012	CV-24012	9/15/2026 8:59:00 AM					1450				
CCV24012	CV-24012	9/22/2026 8:52:16 AM	5.3	78.7	0.0	16.0			181.8	183.2	0.1
CCV24012	CV-24012	9/22/2026 8:55:00 AM					1740				
CCV24012	CV-24012	9/29/2026 8:25:00 AM					2020				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24012	CV-24012	9/29/2026 8:26:34 AM	3.5	78.5	0.0	18.0			175.0	174.6	0.0
CCV24012	CV-24012	9/29/2026 8:27:45 AM	4.3	81.9	0.0	13.8			175.5	175.2	0.1
CCV24013	CV-24013	9/8/2026 2:55:00 PM					2320				
CCV24013	CV-24013	9/8/2026 2:55:38 PM	3.8	75.7	0.2	20.3			189.7	190.1	0.1
CCV24013	CV-24013	9/14/2026 2:41:00 PM					1700				
CCV24013	CV-24013	9/14/2026 2:45:29 PM	8.9	73.4	0.3	17.4			189.6	188.7	0.1
CCV24013	CV-24013	9/21/2026 2:06:00 PM					1605				
CCV24013	CV-24013	9/21/2026 2:06:42 PM	9.4	73.9	0.3	16.4			189.6	190.6	0.1
CCV24013	CV-24013	9/22/2026 9:07:43 AM	7.2	78.3	0.0	14.5			185.8	186.0	0.1
CCV24013	CV-24013	9/28/2026 2:25:03 PM	6.4	46.3	6.6	40.7			190.6	190.2	0.1
CCV24013	CV-24013	9/28/2026 2:34:21 PM	6.9	52.6	5.0	35.5			190.2	189.5	0.1
CCV24013	CV-24013	9/28/2026 2:46:14 PM	7.1	53.1	4.1	35.7			190.8	190.0	0.1
CCV24013	CV-24013	9/28/2026 3:05:00 PM					105.5				
CCV24014	CV-24014	9/8/2026 10:27:00 AM					1580				
CCV24014	CV-24014	9/8/2026 10:29:18 AM	1.9	73.6	0.0	24.5			182.9	182.9	0.0
CCV24014	CV-24014	9/14/2026 9:42:29 AM	13.6	71.7	0.4	14.3			183.6	183.7	0.2
CCV24014	CV-24014	9/14/2026 9:47:00 AM					1560				
CCV24014	CV-24014	9/21/2026 9:59:00 AM					1540				
CCV24014	CV-24014	9/21/2026 10:01:34 AM	14.2	69.3	0.8	15.7			183.8	183.8	0.2
CCV24014	CV-24014	9/28/2026 9:50:00 AM					1370				
CCV24014	CV-24014	9/28/2026 9:51:51 AM	12.1	66.5	1.4	20.0			183.0	183.0	0.2
CCV24015	CV-24015	9/8/2026 10:15:00 AM					1390				
CCV24015	CV-24015	9/8/2026 10:15:01 AM	1.5	66.3	0.0	32.2			187.9	188.3	0.0
CCV24015	CV-24015	9/14/2026 9:33:41 AM	11.0	73.9	0.0	15.1			179.6	179.9	0.1
CCV24015	CV-24015	9/14/2026 9:37:00 AM					2390				
CCV24015	CV-24015	9/21/2026 9:43:08 AM	9.4	73.0	0.0	17.6			189.6	189.8	0.1
CCV24015	CV-24015	9/21/2026 9:47:00 AM					1690				
CCV24015	CV-24015	9/28/2026 9:20:40 AM	10.3	76.3	0.0	13.4			163.2	163.3	0.1
CCV24015	CV-24015	9/28/2026 9:25:00 AM					1660				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24016	CV-24016	9/10/2026 1:20:58 PM	24.6	49.0	0.2	26.2			167.3	167.9	0.5
CCV24016	CV-24016	9/10/2026 1:23:00 PM					1270				
CCV24016	CV-24016	9/15/2026 8:42:34 AM	18.1	64.5	0.0	17.4			161.4	161.6	0.3
CCV24016	CV-24016	9/15/2026 8:46:00 AM					418				
CCV24016	CV-24016	9/22/2026 8:41:38 AM	16.7	54.7	0.0	28.6			176.5	176.4	0.3
CCV24016	CV-24016	9/22/2026 8:43:00 AM					959				
CCV24016	CV-24016	9/29/2026 8:07:47 AM	14.9	56.7	0.0	28.4			167.6	167.5	0.3
CCV24016	CV-24016	9/29/2026 8:15:00 AM					1410				
CCV24017	CV-24017	9/9/2026 7:35:00 AM					1400				
CCV24017	CV-24017	9/9/2026 7:35:00 AM						160000			
CCV24017	CV-24017	9/9/2026 8:19:35 AM	20.9	71.3	0.4	7.4			176.0	176.4	0.3
CCV24017	CV-24017	9/9/2026 8:21:00 AM					1095				
CCV24017	CV-24017	9/15/2026 8:47:21 AM	17.7	52.5	0.0	29.8			186.7	186.8	0.3
CCV24017	CV-24017	9/15/2026 8:51:00 AM					1110				
CCV24017	CV-24017	9/22/2026 8:31:00 AM					1250				
CCV24017	CV-24017	9/22/2026 8:31:48 AM	19.7	69.8	0.7	9.8			174.5	174.0	0.3
CCV24017	CV-24017	9/29/2026 8:02:00 AM	19.2	66.5	0.9	13.4			167.3	167.1	0.3
CCV24017	CV-24017	9/29/2026 8:05:00 AM					1275				
CCV24018	CV-24018	9/1/2026 1:52:46 PM	11.0	65.9	0.2	22.9			132.4	131.9	0.2
CCV24018	CV-24018	9/1/2026 1:53:33 PM	10.9	66.1	0.2	22.8			131.6	131.7	0.2
CCV24018	CV-24018	9/15/2026 9:11:09 AM	5.1	72.5	0.0	22.4			133.9	133.8	0.1
CCV24018	CV-24018	9/24/2026 8:57:40 AM	11.0	60.8	0.0	28.2			140.1	135.3	0.2
CCV24018	CV-24018	9/24/2026 8:58:59 AM	9.0	65.8	0.0	25.2			134.8	134.6	0.1
CCV24019	CV-24019	9/3/2026 7:27:00 AM						158000			
CCV24019	CV-24019	9/3/2026 7:27:00 AM					2300				
CCV24019	CV-24019	9/3/2026 7:27:22 AM	4.0	82.5	0.1	13.4			181.6	181.8	0.0
CCV24019	CV-24019	9/9/2026 8:36:17 AM	6.5	77.9	0.4	15.2			180.7	181.9	0.1
CCV24019	CV-24019	9/9/2026 8:39:00 AM					1740				
CCV24019	CV-24019	9/15/2026 9:06:46 AM	4.5	75.6	0.0	19.9			184.0	183.7	0.1



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24019	CV-24019	9/15/2026 9:09:00 AM					1600				
CCV24019	CV-24019	9/22/2026 9:08:00 AM					1980				
CCV24019	CV-24019	9/24/2026 10:45:00 AM					2050				
CCV24019	CV-24019	9/24/2026 10:45:17 AM	9.9	73.1	0.0	17.0			190.5	190.8	0.1
CCV24019	CV-24019	9/29/2026 8:43:49 AM	8.8	70.1	2.1	19.0			175.6	175.3	0.1
CCV24019	CV-24019	9/29/2026 8:45:00 AM					1970				
CCV24020	CV-24020	9/3/2026 8:44:20 AM	0.6	8.1	16.6	74.7			80.5	81.2	0.1
CCV24020	CV-24020	9/3/2026 8:45:27 AM	0.6	10.0	16.1	73.3			81.7	81.7	0.1
CCV24020	CV-24020	9/21/2026 8:32:06 AM	0.0	9.2	17.2	73.6			69.4	69.4	0.0
CCV24020	CV-24020	9/21/2026 8:33:17 AM	0.1	10.1	16.5	73.3			69.4	69.3	0.0
CCV24021	CV-24021	9/3/2026 8:33:42 AM	9.0	66.0	3.5	21.5			147.1	147.1	0.1
CCV24021	CV-24021	9/3/2026 8:39:22 AM	11.7	64.4	3.3	20.6			145.9	146.0	0.2
CCV24021	CV-24021	9/3/2026 1:27:00 PM						83000			
CCV24021	CV-24021	9/3/2026 1:27:00 PM					260				
CCV24021	CV-24021	9/10/2026 1:38:53 PM	8.5	76.5	0.0	15.0			109.6	109.8	0.1
CCV24021	CV-24021	9/21/2026 8:38:36 AM	0.0	1.0	19.2	79.8			75.4	76.4	0.0
CCV24021	CV-24021	9/21/2026 8:39:59 AM	0.1	0.3	19.3	80.3			76.4	76.3	0.3
CCV24022	CV-24022-PLR	9/8/2026 10:34:00 AM					1860				
CCV24022	CV-24022-PLR	9/8/2026 10:34:57 AM	2.4	71.9	0.0	25.7			194.7	194.8	0.0
CCV24022	CV-24022-PLR	9/14/2026 9:47:06 AM	10.2	70.7	0.4	18.7			194.7	194.8	0.1
CCV24022	CV-24022-PLR	9/17/2026 1:14:16 PM	14.6	74.2	0.0	11.2			194.5	194.7	0.2
CCV24022	CV-24022-PLR	9/17/2026 1:15:00 PM					2220				
CCV24022	CV-24022-PLR	9/21/2026 10:04:00 AM					2060				
CCV24022	CV-24022-PLR	9/21/2026 10:05:58 AM	11.8	67.0	0.0	21.2			194.4	194.4	0.2
CCV24022	CV-24022-PLR	9/28/2026 9:56:17 AM	9.4	68.2	0.5	21.9			194.6	194.7	0.1
CCV24022	CV-24022-PLR	9/28/2026 10:05:00 AM					1970				
CCV24023	CV-24023	9/8/2026 10:21:52 AM	1.5	66.5	0.0	32.0			196.3	196.4	0.0
CCV24023	CV-24023	9/8/2026 10:23:00 AM					1530				
CCV24023	CV-24023	9/14/2026 9:37:06 AM	10.5	74.6	0.0	14.9			196.1	196.2	0.1

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24023	CV-24023	9/14/2026 9:41:00 AM					1210				
CCV24023	CV-24023	9/21/2026 9:52:32 AM	11.2	58.9	3.3	26.6			185.2	188.3	0.2
CCV24023	CV-24023	9/21/2026 9:53:00 AM					1080				
CCV24023	CV-24023	9/28/2026 9:32:30 AM	15.3	63.8	0.0	20.9			196.4	196.4	0.2
CCV24023	CV-24023	9/28/2026 9:33:25 AM	15.0	70.4	0.0	14.6			196.4	196.5	0.2
CCV24023	CV-24023	9/28/2026 9:35:00 AM					1570				
CCV24024	CV-24024-PLR	9/14/2026 1:05:56 PM	1.5	72.6	0.5	25.4			162.8	165.5	0.0
CCV24024	CV-24024-PLR	9/14/2026 1:07:36 PM	1.4	73.8	0.2	24.6			165.6	163.3	0.0
CCV24024	CV-24024-PLR	9/14/2026 2:45:00 PM					1440				
CCV24024	CV-24024-PLR	9/21/2026 9:33:56 AM	10.8	72.7	0.0	16.5			139.0	139.0	0.1
CCV24025	CV-24025	9/3/2026 7:56:02 AM	3.6	80.6	0.0	15.8			174.3	174.4	0.0
CCV24025	CV-24025	9/3/2026 8:00:00 AM						127300			
CCV24025	CV-24025	9/3/2026 8:00:00 AM					2190				
CCV24025	CV-24025	9/9/2026 8:43:21 AM	12.2	51.5	0.3	36.0			168.6	167.7	0.2
CCV24025	CV-24025	9/9/2026 8:45:00 AM					1460				
CCV24025	CV-24025	9/15/2026 9:18:02 AM	13.0	68.1	0.0	18.9			178.2	178.6	0.2
CCV24025	CV-24025	9/15/2026 9:19:00 AM					1970				
CCV24025	CV-24025	9/22/2026 9:13:58 AM	8.7	64.0	0.0	27.3			184.0	184.1	0.1
CCV24025	CV-24025	9/22/2026 9:16:00 AM					2110				
CCV24025	CV-24025	9/29/2026 8:49:38 AM	10.8	60.2	0.0	29.0			170.7	171.0	0.2
CCV24025	CV-24025	9/29/2026 8:50:00 AM					2010				
CCV24026	CV-24026	9/3/2026 7:33:18 AM	2.7	81.2	0.0	16.1			179.6	179.5	0.0
CCV24026	CV-24026	9/3/2026 7:34:00 AM						196700			
CCV24026	CV-24026	9/3/2026 7:34:00 AM					1990				
CCV24026	CV-24026	9/9/2026 8:31:27 AM	7.3	70.0	0.0	22.7			142.6	142.2	0.1
CCV24026	CV-24026	9/21/2026 8:25:41 AM	1.0	79.9	0.0	19.1			184.9	184.5	0.0
CCV24026	CV-24026	9/21/2026 8:26:47 AM	1.0	79.6	0.0	19.4			184.3	184.4	0.0
CCV24026	CV-24026	9/28/2026 10:42:46 AM	0.9	87.7	0.0	11.4			184.4	184.5	0.0
CCV24026	CV-24026	9/29/2026 8:35:00 AM					2320				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24026	CV-24026	9/29/2026 8:35:11 AM	3.7	78.8	0.0	17.5			179.6	179.4	0.0
CCV24027	CV-24027	9/9/2026 11:08:00 AM	7.9	37.8	7.9	46.4			117.6	117.7	0.2
CCV24027	CV-24027	9/21/2026 8:45:43 AM	0.2	11.2	16.2	72.4			82.3	84.5	0.0
CCV24027	CV-24027	9/21/2026 8:46:35 AM	0.2	11.0	16.2	72.6			83.2	83.9	0.0
CCV24028	CV-24028	9/8/2026 10:39:56 AM	1.8	70.7	0.0	27.5			198.6	198.5	0.0
CCV24028	CV-24028	9/8/2026 10:45:00 AM					1330				
CCV24028	CV-24028	9/14/2026 9:52:00 AM					1110				
CCV24028	CV-24028	9/14/2026 9:59:11 AM	11.4	69.4	0.0	19.2			195.6	195.7	0.2
CCV24028	CV-24028	9/21/2026 10:10:45 AM	11.2	70.5	0.0	18.3			195.8	195.4	0.2
CCV24028	CV-24028	9/21/2026 10:13:00 AM					1110				
CCV24028	CV-24028	9/28/2026 10:02:58 AM	11.8	69.7	0.0	18.5			196.6	196.4	0.2
CCV24028	CV-24028	9/28/2026 10:10:00 AM					1080				
CCV24029	CV-24029	9/9/2026 10:30:51 AM	2.3	66.1	3.7	27.9			117.9	118.3	0.0
CCV24029	CV-24029	9/25/2026 10:15:36 AM	0.1	3.1	19.2	77.6			97.0	96.7	0.0
CCV24030	CV-24030	9/8/2026 9:51:00 AM					244				
CCV24030	CV-24030	9/8/2026 9:52:46 AM	1.1	66.4	3.6	28.9			86.2	91.1	0.0
CCV24030	CV-24030	9/14/2026 8:52:00 AM					1680				
CCV24030	CV-24030	9/14/2026 9:02:11 AM	3.8	63.6	4.5	28.1			185.0	185.0	0.1
CCV24030	CV-24030	9/14/2026 9:08:34 AM	4.3	64.8	3.6	27.3			187.0	75.3	0.1
CCV24030	CV-24030	9/21/2026 9:12:52 AM	5.2	68.1	3.7	23.0			186.0	71.9	0.1
CCV24030	CV-24030	9/21/2026 9:15:00 AM					1370				
CCV24030	CV-24030	9/21/2026 9:21:19 AM	10.1	69.8	1.9	18.2			186.0	76.3	0.1
CCV24030	CV-24030	9/28/2026 8:35:00 AM					1870				
CCV24030	CV-24030	9/28/2026 8:36:53 AM	5.1	68.0	3.2	23.7			88.0	75.3	0.1
CCV24031	CV-24031	9/1/2026 2:26:16 PM	26.8	62.4	0.2	10.6			141.5	141.3	0.4
CCV24031	CV-24031	9/3/2026 8:12:54 AM	3.4	80.3	0.0	16.3			146.7	147.4	0.0
CCV24031	CV-24031	9/3/2026 8:17:00 AM						78250			
CCV24031	CV-24031	9/3/2026 8:17:00 AM					670.5				
CCV24031	CV-24031	9/9/2026 9:07:06 AM	19.1	73.2	0.0	7.7			157.9	158.1	0.3



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24031	CV-24031	9/9/2026 9:10:00 AM					712.5				
CCV24031	CV-24031	9/15/2026 9:52:53 AM	31.2	68.8	0.0	0.0			162.0	162.5	0.5
CCV24031	CV-24031	9/15/2026 9:57:00 AM					1030				
CCV24031	CV-24031	9/22/2026 9:40:37 AM	24.7	60.7	0.0	14.6			157.0	157.6	0.4
CCV24031	CV-24031	9/22/2026 9:44:00 AM					818				
CCV24031	CV-24031	9/29/2026 9:04:40 AM	42.3	57.7	0.0	0.0			155.9	155.7	0.7
CCV24031	CV-24031	9/29/2026 9:10:00 AM					781				
CCV24032	CV-24032	9/3/2026 7:35:00 AM					2000				
CCV24032	CV-24032	9/3/2026 8:05:00 AM						139400			
CCV24032	CV-24032	9/3/2026 8:05:26 AM	3.4	78.5	0.0	18.1			195.9	196.2	0.0
CCV24032	CV-24032	9/3/2026 8:06:12 AM	4.1	65.4	0.0	30.5			196.4	196.6	0.1
CCV24032	CV-24032	9/9/2026 9:02:42 AM	6.3	76.2	0.0	17.5			195.4	195.3	0.1
CCV24032	CV-24032	9/9/2026 9:04:00 AM					1280				
CCV24032	CV-24032	9/15/2026 9:43:54 AM	7.4	74.8	0.0	17.8			195.9	195.9	0.1
CCV24032	CV-24032	9/15/2026 9:47:00 AM					1380				
CCV24032	CV-24032	9/22/2026 9:35:52 AM	19.9	69.0	0.0	11.1			192.5	192.3	0.3
CCV24032	CV-24032	9/22/2026 9:38:00 AM					887				
CCV24032	CV-24032	9/29/2026 9:01:56 AM	39.2	60.8	0.0	0.0			181.8	181.4	0.6
CCV24032	CV-24032	9/29/2026 9:05:00 AM					887				
CCV24033	CV-24033	9/3/2026 7:35:00 AM						191400			
CCV24033	CV-24033	9/3/2026 7:35:00 AM					2500				
CCV24033	CV-24033	9/3/2026 7:42:08 AM	2.4	79.6	0.0	18.0			193.6	194.1	0.0
CCV24033	CV-24033	9/9/2026 8:52:55 AM	6.3	69.9	0.0	23.8			193.3	193.5	0.1
CCV24033	CV-24033	9/9/2026 8:55:00 AM					2210				
CCV24033	CV-24033	9/15/2026 9:28:55 AM	5.1	65.3	0.0	29.6			196.9	196.7	0.1
CCV24033	CV-24033	9/15/2026 9:32:00 AM					2480				
CCV24033	CV-24033	9/22/2026 9:22:23 AM	5.7	76.4	0.0	17.9			194.7	194.4	0.1
CCV24033	CV-24033	9/22/2026 9:27:00 AM					2060				
CCV24033	CV-24033	9/29/2026 8:53:18 AM	11.3	74.0	0.0	14.7			193.8	193.3	0.2



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24033	CV-24033	9/29/2026 8:55:00 AM					1675				
CCV24034	CV-24034	9/8/2026 1:21:00 PM					1040				
CCV24034	CV-24034	9/8/2026 1:24:32 PM	2.2	78.9	0.7	18.2			153.4	153.9	0.0
CCV24034	CV-24034	9/14/2026 10:06:34 AM	10.7	69.9	0.0	19.4			163.6	163.2	0.2
CCV24034	CV-24034	9/14/2026 10:09:00 AM					960				
CCV24034	CV-24034	9/21/2026 10:18:00 AM					994				
CCV24034	CV-24034	9/21/2026 10:19:16 AM	13.5	71.4	0.0	15.1			182.8	197.3	0.2
CCV24034	CV-24034	9/21/2026 10:20:16 AM	12.1	69.9	0.0	18.0			196.8	196.4	0.2
CCV24034	CV-24034	9/28/2026 10:07:28 AM	12.8	70.6	0.0	16.6			177.0	177.6	0.2
CCV24034	CV-24034	9/28/2026 10:15:00 AM					1110				
CCV24035	CV-24035-PLR	9/8/2026 9:27:31 AM	1.4	75.1	0.0	23.5			189.3	190.0	0.0
CCV24035	CV-24035-PLR	9/8/2026 9:29:00 AM					1980				
CCV24035	CV-24035-PLR	9/14/2026 8:17:00 AM					1520				
CCV24035	CV-24035-PLR	9/14/2026 8:17:07 AM	2.2	83.6	0.1	14.1			176.6	174.6	0.0
CCV24035	CV-24035-PLR	9/21/2026 8:14:30 AM	3.7	80.9	0.0	15.4			187.0	186.7	0.0
CCV24035	CV-24035-PLR	9/21/2026 8:15:00 AM					1395				
CCV24035	CV-24035-PLR	9/28/2026 7:53:30 AM	1.8	80.8	0.0	17.4			184.8	183.9	0.0
CCV24035	CV-24035-PLR	9/28/2026 7:55:00 AM					1915				
CCV24036	CV-24036	9/1/2026 2:33:35 PM	52.4	40.8	0.9	5.9			101.4	101.5	1.3
CCV24036	CV-24036	9/11/2026 2:07:19 PM	61.3	37.8	0.9	0.0			110.0	110.2	1.6
CCV24036	CV-24036	9/11/2026 2:08:24 PM	60.7	38.4	0.9	0.0			110.0	109.8	1.6
CCV24036	CV-24036	9/24/2026 11:11:10 AM	52.3	40.8	0.7	6.2			107.8	108.0	1.3
CCV24037	CV-24037	9/1/2026 3:35:53 PM	19.6	59.1	2.8	18.5			117.9	117.8	0.3
CCV24037	CV-24037	9/24/2026 11:22:54 AM	40.6	40.3	3.5	15.6			122.1	120.0	1.0
CCV24038	CV-24038	9/14/2026 11:13:08 AM	5.0	77.7	0.0	17.3			185.2	185.2	0.1
CCV24038	CV-24038	9/14/2026 11:14:07 AM	4.6	78.0	0.0	17.4			185.6	185.6	0.1
CCV24038	CV-24038	9/14/2026 2:15:00 PM					1820				
CCV24038	CV-24038	9/21/2026 10:10:47 AM	3.0	77.7	0.0	19.3			194.9	195.1	0.0
CCV24038	CV-24038	9/21/2026 10:20:00 AM					1610				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24038	CV-24038	9/22/2026 10:40:33 AM	18.8	68.5	0.0	12.7			197.1	197.1	0.3
CCV24038	CV-24038	9/29/2026 9:21:20 AM	16.8	72.2	0.0	11.0			194.0	194.3	0.2
CCV24038	CV-24038	9/29/2026 9:30:00 AM					1690				
CCV24039	CV-24039	9/3/2026 8:43:35 AM	1.1	6.2	17.9	74.8			94.7	94.5	0.2
CCV24039	CV-24039	9/3/2026 8:45:09 AM	1.1	6.8	17.8	74.3			94.3	94.5	0.2
CCV24039	CV-24039	9/29/2026 9:17:59 AM	0.0	1.5	17.8	80.7			97.3	95.8	0.0
CCV24039	CV-24039	9/29/2026 9:18:59 AM	0.1	1.3	17.5	81.1			98.6	97.5	0.1
CCV24040	CV-24040	9/3/2026 8:50:25 AM	3.9	72.4	1.1	22.6			172.8	172.5	0.1
CCV24040	CV-24040	9/3/2026 8:52:00 AM						197000			
CCV24040	CV-24040	9/3/2026 8:52:00 AM					1960				
CCV24040	CV-24040	9/9/2026 9:53:48 AM	15.1	74.3	0.0	10.6			176.2	176.6	0.2
CCV24040	CV-24040	9/9/2026 9:55:00 AM					2690				
CCV24040	CV-24040	9/15/2026 10:32:00 AM					2370				
CCV24040	CV-24040	9/15/2026 10:35:47 AM	4.0	65.0	2.3	28.7			145.3	146.1	0.1
CCV24040	CV-24040	9/15/2026 10:38:31 AM	3.5	67.5	1.2	27.8			143.0	143.5	0.1
CCV24040	CV-24040	9/21/2026 8:14:52 AM	0.5	11.5	16.5	71.5			74.6	75.1	0.0
CCV24040	CV-24040	9/21/2026 8:16:09 AM	0.5	12.5	16.5	70.5			75.5	75.8	0.0
CCV24041	CV-24041	9/9/2026 11:11:38 AM	3.3	22.3	15.7	58.7			114.6	114.8	0.1
CCV24041	CV-24041	9/23/2026 1:19:53 PM	0.0	0.3	20.3	79.4			108.2	108.1	0.0
CCV24042	CV-24042	9/8/2026 1:36:57 PM	5.4	73.9	0.0	20.7			180.9	180.4	0.1
CCV24042	CV-24042	9/8/2026 1:37:00 PM					1400				
CCV24042	CV-24042	9/14/2026 10:23:07 AM	12.8	75.5	0.0	11.7			181.5	182.9	0.2
CCV24042	CV-24042	9/14/2026 10:27:00 AM					1540				
CCV24042	CV-24042	9/21/2026 10:29:12 AM	25.0	65.8	0.0	9.2			176.1	175.2	0.4
CCV24042	CV-24042	9/21/2026 10:32:00 AM					1040				
CCV24042	CV-24042	9/28/2026 10:28:10 AM	16.0	72.8	0.0	11.2			182.3	179.2	0.2
CCV24042	CV-24042	9/28/2026 10:30:00 AM					1850				
CCV24043	CV-24043	9/14/2026 2:27:14 PM	42.7	57.3	0.0	0.0			104.9	105.0	0.7
CCV24043	CV-24043	9/30/2026 4:24:40 PM	37.9	56.9	0.1	5.1			122.0	122.0	0.7



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24044	CV-24044	9/3/2026 8:17:38 AM	23.0	69.9	0.0	7.1			149.0	149.4	0.3
CCV24044	CV-24044	9/3/2026 8:23:00 AM						67000			
CCV24044	CV-24044	9/3/2026 8:23:00 AM					596				
CCV24044	CV-24044	9/9/2026 9:15:54 AM	29.2	69.2	0.0	1.6			151.3	152.4	0.4
CCV24044	CV-24044	9/9/2026 9:17:00 AM					596				
CCV24044	CV-24044	9/14/2026 9:52:00 AM					2440				
CCV24044	CV-24044	9/15/2026 10:10:54 AM	33.3	66.0	0.0	0.7			157.9	159.7	0.5
CCV24044	CV-24044	9/15/2026 10:12:00 AM					584				
CCV24044	CV-24044	9/22/2026 9:50:00 AM					530				
CCV24044	CV-24044	9/22/2026 9:56:36 AM	36.8	63.1	0.0	0.1			158.2	157.7	0.6
CCV24044	CV-24044	9/29/2026 9:08:25 AM	36.6	63.4	0.0	0.0			154.6	154.9	0.6
CCV24044	CV-24044	9/29/2026 9:15:00 AM					577				
CCV24045	CV-24045	9/3/2026 8:23:14 AM	25.5	70.7	0.0	3.8			185.3	185.5	0.4
CCV24045	CV-24045	9/3/2026 8:27:00 AM						161100			
CCV24045	CV-24045	9/3/2026 8:27:00 AM					1750				
CCV24045	CV-24045	9/9/2026 9:26:00 AM					458				
CCV24045	CV-24045	9/9/2026 9:29:21 AM	15.0	65.6	1.3	18.1			188.3	188.6	0.2
CCV24045	CV-24045	9/15/2026 10:14:44 AM	33.2	66.7	0.0	0.1			187.7	187.9	0.5
CCV24045	CV-24045	9/15/2026 10:18:00 AM					1150				
CCV24045	CV-24045	9/22/2026 10:34:00 AM					1600				
CCV24045	CV-24045	9/22/2026 10:37:26 AM	18.9	71.5	0.4	9.2			190.1	189.4	0.3
CCV24045	CV-24045	9/29/2026 9:16:50 AM	18.4	70.5	0.5	10.6			184.9	185.3	0.3
CCV24045	CV-24045	9/29/2026 9:17:31 AM	18.2	70.8	0.4	10.6			185.8	186.0	0.3
CCV24045	CV-24045	9/29/2026 9:25:00 AM					1910				
CCV24046	CV-24046	9/14/2026 10:32:13 AM	1.0	73.1	0.3	25.6			180.2	180.4	0.0
CCV24046	CV-24046	9/14/2026 10:32:44 AM	1.1	74.5	0.4	24.0			182.1	182.3	0.0
CCV24046	CV-24046	9/21/2026 9:20:00 AM					1830				
CCV24046	CV-24046	9/21/2026 9:25:30 AM	0.2	72.2	1.1	26.5			184.8	185.5	0.0
CCV24046	CV-24046	9/21/2026 9:27:21 AM	0.2	73.0	0.1	26.7			184.0	184.7	0.0



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24046	CV-24046	9/22/2026 1:28:16 PM	8.8	75.2	0.0	16.0			147.0	146.9	0.1
CCV24046	CV-24046	9/22/2026 1:32:00 PM	8.9	73.2	0.2	17.7			147.0	146.8	0.1
CCV24046	CV-24046	9/29/2026 9:35:00 AM					1740				
CCV24046	CV-24046	9/29/2026 9:38:38 AM	10.4	71.9	0.0	17.7			172.7	173.5	0.1
CCV24048	CV-24048	9/9/2026 11:14:18 AM	4.4	29.0	11.7	54.9			120.2	120.5	0.2
CCV24048	CV-24048	9/23/2026 1:23:23 PM	6.5	76.6	0.1	16.8			106.2	107.2	0.1
CCV24049	CV-24049	9/10/2026 9:20:00 AM					1700				
CCV24049	CV-24049	9/10/2026 9:20:00 AM						150000			
CCV24049	CV-24049	9/14/2026 9:39:50 AM	4.0	77.2	0.0	18.8			183.4	183.4	0.1
CCV24049	CV-24049	9/14/2026 9:40:16 AM	4.2	78.7	0.0	17.1			183.8	183.8	0.1
CCV24049	CV-24049	9/14/2026 10:45:00 AM					2200				
CCV24049	CV-24049	9/21/2026 9:35:00 AM					1820				
CCV24049	CV-24049	9/21/2026 9:40:32 AM	4.5	71.0	0.0	24.5			187.6	188.7	0.1
CCV24049	CV-24049	9/21/2026 9:41:36 AM	4.5	74.2	0.0	21.3			189.2	189.3	0.1
CCV24049	CV-24049	9/28/2026 2:11:38 PM	8.0	78.8	0.0	13.2			187.9	187.8	0.1
CCV24049	CV-24049	9/28/2026 2:40:00 PM					1750				
CCV24050	CV-24050	9/14/2026 2:38:57 PM	47.5	41.7	0.0	10.8			121.8	121.8	1.1
CCV24050	CV-24050	9/30/2026 2:26:44 PM	27.6	36.5	0.0	35.9			119.4	118.7	0.8
CCV24051	CV-24051	9/14/2026 11:02:47 AM	28.6	47.6	3.4	20.4			107.7	108.0	0.6
CCV24051	CV-24051	9/24/2026 11:45:13 AM	25.4	62.0	2.4	10.2			111.8	114.0	0.4
CCV24052	CV-24052	9/14/2026 10:13:38 AM	21.9	42.1	4.2	31.8			126.3	126.3	0.5
CCV24052	CV-24052	9/14/2026 10:14:40 AM	26.9	49.8	1.8	21.5			127.4	127.5	0.5
CCV24052	CV-24052	9/23/2026 1:29:49 PM	32.5	39.7	0.5	27.3			113.0	115.7	0.8
CCV24053	CV-24053	9/8/2026 7:40:00 AM					58				
CCV24053	CV-24053	9/8/2026 7:40:00 AM						8800			
CCV24053	CV-24053	9/14/2026 10:03:36 AM	31.7	46.1	0.0	22.2			106.3	106.7	0.7
CCV24053	CV-24053	9/23/2026 1:26:37 PM	28.6	49.0	0.2	22.2			118.6	119.2	0.6
CCV24054	CV-24054	9/8/2026 1:44:40 PM	8.9	77.3	0.0	13.8			171.5	171.4	0.1
CCV24054	CV-24054	9/8/2026 1:48:00 PM					894.5				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24054	CV-24054	9/14/2026 10:33:37 AM	28.0	0.0	0.0	72.0			167.8	167.9	
CCV24054	CV-24054	9/14/2026 10:34:00 AM					1080				
CCV24054	CV-24054	9/21/2026 10:34:28 AM	27.3	59.7	0.0	13.0			177.0	177.0	0.5
CCV24054	CV-24054	9/21/2026 10:37:00 AM					977				
CCV24054	CV-24054	9/28/2026 10:42:38 AM	22.8	65.3	0.0	11.9			161.1	161.9	0.3
CCV24054	CV-24054	9/28/2026 10:45:00 AM					1360				
CCV24055	CV-24055	9/10/2026 9:25:00 AM					1400				
CCV24055	CV-24055	9/10/2026 9:25:00 AM						85000			
CCV24055	CV-24055	9/14/2026 9:36:06 AM	4.9	55.9	3.0	36.2			122.0	122.3	0.1
CCV24055	CV-24055	9/30/2026 8:16:47 AM	4.6	41.3	5.3	48.8			151.0	151.0	0.1
CCV24055	CV-24055	9/30/2026 8:17:55 AM	4.5	41.9	5.1	48.5			151.0	151.0	0.1
CCV24055	CV-24055	9/30/2026 10:20:00 AM					322				
CCV24056	CV-24056	9/1/2026 9:14:34 AM	23.1	66.2	0.0	10.7			99.1	99.2	0.3
CCV24056	CV-24056	9/22/2026 11:03:33 AM	25.0	45.7	0.0	29.3			117.8	117.7	0.5
CCV24057	CV-24057	9/14/2026 2:15:25 PM	34.7	58.8	0.0	6.5			147.4	146.9	0.6
CCV24057	CV-24057	9/14/2026 2:16:28 PM	34.2	65.8	0.0	0.0			145.7	145.5	0.5
CCV24057	CV-24057	9/14/2026 3:00:00 PM					1540				
CCV24057	CV-24057	9/17/2026 10:27:01 AM	14.3	74.9	0.1	10.7			148.9	148.6	0.2
CCV24057	CV-24057	9/21/2026 10:46:29 AM	19.4	72.3	0.0	8.3			149.3	152.4	0.3
CCV24057	CV-24057	9/21/2026 10:47:11 AM	19.3	72.3	0.0	8.4			152.7	152.8	0.3
CCV24057	CV-24057	9/21/2026 10:50:00 AM					1250				
CCV24058	CV-24058	9/11/2026 1:53:52 PM	45.8	37.2	0.1	16.9			111.4	112.8	1.2
CCV24058	CV-24058	9/11/2026 1:55:09 PM	44.2	35.8	0.0	20.0			111.7	112.0	1.2
CCV24058	CV-24058	9/17/2026 10:38:59 AM	30.9	36.0	0.3	32.8			100.9	101.0	0.9
CCV24059	CV-24059	9/2/2026 9:05:00 AM					684				
CCV24059	CV-24059	9/2/2026 9:05:00 AM						150200			
CCV24059	CV-24059	9/2/2026 9:06:09 AM	20.6	65.5	0.0	13.9			156.5	156.6	0.3
CCV24059	CV-24059	9/8/2026 9:49:40 AM	13.0	66.7	0.3	20.0			154.3	155.9	0.2
CCV24059	CV-24059	9/8/2026 9:50:00 AM					489.5				

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24059	CV-24059	9/8/2026 9:51:20 AM	12.6	69.0	0.1	18.3			155.5	155.9	0.2
CCV24059	CV-24059	9/16/2026 1:37:00 PM					691				
CCV24059	CV-24059	9/16/2026 1:42:42 PM	25.8	71.4	0.0	2.8			160.2	159.9	0.4
CCV24059	CV-24059	9/23/2026 1:24:51 PM	29.7	70.3	0.0	0.0			156.7	156.9	0.4
CCV24059	CV-24059	9/23/2026 1:27:00 PM					431				
CCV24059	CV-24059	9/30/2026 10:05:00 AM					339				
CCV24059	CV-24059	9/30/2026 10:08:00 AM	45.3	54.7	0.0	0.0			155.4	155.4	0.8
CCV24060	CV-24060	9/2/2026 9:45:32 AM	31.8	61.7	0.2	6.3			133.0	130.7	0.5
CCV24060	CV-24060	9/17/2026 11:02:39 AM	29.4	62.2	0.3	8.1			126.1	126.7	0.5
CCV24061	CV-24061	9/2/2026 9:52:58 AM	44.6	54.6	0.0	0.8			102.4	102.5	0.8
CCV24061	CV-24061	9/28/2026 10:31:48 AM	7.2	80.4	0.0	12.4			147.6	147.3	0.1
CCV24062	CV-24062	9/1/2026 2:14:11 PM	35.7	64.2	0.0	0.1			175.4	175.7	0.6
CCV24062	CV-24062	9/1/2026 2:15:00 PM						102100			
CCV24062	CV-24062	9/1/2026 2:15:00 PM					942.5				
CCV24062	CV-24062	9/3/2026 7:20:00 AM					840				
CCV24062	CV-24062	9/3/2026 7:20:00 AM						110000			
CCV24062	CV-24062	9/10/2026 8:48:00 AM					1200				
CCV24062	CV-24062	9/16/2026 10:09:38 AM	29.5	65.0	0.0	5.5			173.3	173.7	0.5
CCV24062	CV-24062	9/16/2026 10:13:00 AM					940.5				
CCV24062	CV-24062	9/23/2026 10:16:47 AM	40.6	59.4	0.0	0.0			178.3	178.8	0.7
CCV24062	CV-24062	9/23/2026 10:19:00 AM					175				
CCV24062	CV-24062	9/30/2026 9:17:26 AM	19.7	75.5	0.0	4.8			170.1	170.4	0.3
CCV24062	CV-24062	9/30/2026 9:20:00 AM					1800				
CCV24063	CV-24063	9/1/2026 2:00:39 PM	8.4	79.6	0.0	12.0			186.3	186.3	0.1
CCV24063	CV-24063	9/1/2026 2:05:00 PM						96900			
CCV24063	CV-24063	9/1/2026 2:05:00 PM					1970				
CCV24063	CV-24063	9/3/2026 7:20:00 AM					1400				
CCV24063	CV-24063	9/3/2026 7:20:00 AM						110000			
CCV24063	CV-24063	9/10/2026 8:38:00 AM					1230				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24063	CV-24063	9/10/2026 8:38:14 AM	17.9	79.7	0.0	2.4			188.1	185.2	0.2
CCV24063	CV-24063	9/10/2026 8:39:09 AM	17.9	76.6	0.0	5.5			184.9	184.7	0.2
CCV24063	CV-24063	9/14/2026 2:32:38 PM	11.5	76.5	0.0	12.0			183.6	183.7	0.2
CCV24063	CV-24063	9/15/2026 10:47:20 AM	11.5	74.0	0.0	14.5			183.9	184.0	0.2
CCV24063	CV-24063	9/17/2026 12:22:16 PM	9.6	75.9	0.0	14.5					0.1
CCV24063	CV-24063	9/17/2026 1:33:24 PM	21.7	70.2	0.0	8.1			167.8	167.7	0.3
CCV24063	CV-24063	9/17/2026 1:34:00 PM					1190				
CCV24063	CV-24063	9/23/2026 10:11:45 AM	32.2	67.7	0.0	0.1			167.4	167.5	0.5
CCV24063	CV-24063	9/23/2026 10:13:00 AM					1410				
CCV24063	CV-24063	9/30/2026 9:08:35 AM	24.7	75.3	0.0	0.0			133.5	133.1	0.3
CCV24063	CV-24063	9/30/2026 9:15:00 AM					731.5				
CCV24064	CV-24064-PLR	9/1/2026 1:18:43 PM	37.6	58.3	0.0	4.1			191.4	191.5	0.6
CCV24064	CV-24064-PLR	9/1/2026 1:25:00 PM						121100			
CCV24064	CV-24064-PLR	9/1/2026 1:25:00 PM					2350				
CCV24064	CV-24064-PLR	9/3/2026 7:30:00 AM					1600				
CCV24064	CV-24064-PLR	9/3/2026 7:30:00 AM						140000			
CCV24064	CV-24064-PLR	9/9/2026 1:28:11 PM	47.8	52.2	0.0	0.0			191.7	192.6	0.9
CCV24064	CV-24064-PLR	9/9/2026 1:32:00 PM					1940				
CCV24064	CV-24064-PLR	9/10/2026 8:45:01 AM	18.7	75.7	0.0	5.6			175.2	175.6	0.2
CCV24064	CV-24064-PLR	9/16/2026 9:05:32 AM	35.8	64.2	0.0	0.0			190.2	191.1	0.6
CCV24064	CV-24064-PLR	9/16/2026 9:14:00 AM					2030				
CCV24064	CV-24064-PLR	9/23/2026 9:22:59 AM	46.5	53.5	0.0	0.0			188.2	189.7	0.9
CCV24064	CV-24064-PLR	9/23/2026 9:25:00 AM					1340				
CCV24064	CV-24064-PLR	9/30/2026 8:25:00 AM					2020				
CCV24064	CV-24064-PLR	9/30/2026 8:38:49 AM	37.9	56.7	0.0	5.4			188.1	188.5	0.7
CCV24065	CV-24065-TP17	9/3/2026 8:57:02 AM	12.8	53.4	2.0	31.8			113.3	113.3	0.2
CCV24065	CV-24065-TP17	9/8/2026 7:50:00 AM					290				
CCV24065	CV-24065-TP17	9/8/2026 7:50:00 AM						15000			
CCV24065	CV-24065-TP17	9/22/2026 10:39:59 AM	14.0	42.9	0.9	42.2			126.3	126.5	0.3

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24066	CV-24066	9/1/2026 9:11:21 AM	21.0	41.6	0.1	37.3			89.1	89.3	0.5
CCV24066	CV-24066	9/10/2026 8:15:00 AM					250				
CCV24066	CV-24066	9/10/2026 8:15:00 AM						23000			
CCV24066	CV-24066	9/22/2026 11:00:28 AM	16.9	44.9	0.0	38.2			102.6	103.9	0.4
CCV24066	CV-24066	9/24/2026 2:36:50 PM	18.0	42.6	0.0	39.4			123.0	122.8	0.4
CCV24067	CV-24067	9/29/2026 2:12:24 PM	16.4	47.7	0.0	36.0			156.2	156.7	0.3
CCV24067	CV-24067	9/29/2026 2:14:48 PM	16.9	45.9	0.0	37.1			156.8	156.8	0.4
CCV24068	CV-24068	9/3/2026 10:45:39 AM	38.9	49.3	0.2	11.6			151.1	151.2	0.8
CCV24068	CV-24068	9/3/2026 10:47:00 AM						42300			
CCV24068	CV-24068	9/3/2026 10:47:00 AM					644				
CCV24068	CV-24068	9/8/2026 10:05:00 AM					545				
CCV24068	CV-24068	9/8/2026 10:06:07 AM	25.6	50.6	0.2	23.6			145.2	145.3	0.5
CCV24068	CV-24068	9/17/2026 1:41:53 PM	24.9	72.0	0.0	3.1			140.0	139.9	0.3
CCV24069	CV-24069	9/2/2026 8:53:53 AM	21.7	49.7	0.1	28.5			117.5	116.7	0.4
CCV24069	CV-24069	9/8/2026 7:00:00 AM					580				
CCV24069	CV-24069	9/8/2026 7:00:00 AM						64000			
CCV24069	CV-24069	9/28/2026 10:46:59 AM	11.9	44.8	0.2	43.1			126.3	126.4	0.3
CCV24070	CV-24070	9/2/2026 8:55:00 AM						64200			
CCV24070	CV-24070	9/2/2026 8:55:00 AM					1590				
CCV24070	CV-24070	9/2/2026 8:55:24 AM	29.3	64.5	0.0	6.2			149.4	149.4	0.5
CCV24070	CV-24070	9/8/2026 7:10:00 AM					1000				
CCV24070	CV-24070	9/8/2026 7:10:00 AM						82000			
CCV24070	CV-24070	9/9/2026 1:57:00 PM	32.2	67.7	0.1	0.0			119.1	119.1	0.5
CCV24070	CV-24070	9/9/2026 1:57:46 PM	30.7	69.2	0.1	0.0			119.1	119.1	0.4
CCV24070	CV-24070	9/10/2026 1:57:00 PM					1370				
CCV24070	CV-24070	9/10/2026 1:59:57 PM	33.6	66.4	0.0	0.0			150.7	150.7	0.5
CCV24070	CV-24070	9/16/2026 1:23:00 PM					1360				
CCV24070	CV-24070	9/16/2026 1:30:24 PM	42.9	57.1	0.0	0.0			144.7	144.7	0.8
CCV24071	CV-24071	9/2/2026 9:40:06 AM	24.9	68.0	0.0	7.1			138.4	138.3	0.4



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24071	CV-24071	9/8/2026 7:15:00 AM					550				
CCV24071	CV-24071	9/8/2026 7:15:00 AM						74000			
CCV24071	CV-24071	9/17/2026 2:19:48 PM	33.7	60.4	0.0	5.9			134.7	134.0	0.6
CCV24072	CV-24072	9/2/2026 1:30:58 PM	42.9	57.1	0.0	0.0			111.0	110.0	0.8
CCV24072	CV-24072	9/17/2026 2:25:11 PM	25.5	69.4	0.0	5.1			110.9	111.6	0.4
CCV24073	CV-24073-TP13	9/1/2026 2:25:19 PM	47.3	52.7	0.0	0.0			157.5	157.6	0.9
CCV24073	CV-24073-TP13	9/1/2026 2:30:00 PM						47600			
CCV24073	CV-24073-TP13	9/1/2026 2:30:00 PM					1420				
CCV24073	CV-24073-TP13	9/9/2026 1:21:38 PM	47.0	52.9	0.1	0.0			138.4	138.4	0.9
CCV24073	CV-24073-TP13	9/21/2026 2:25:32 PM	24.1	71.1	0.2	4.6			153.9	154.4	0.3
CCV24073	CV-24073-TP13	9/30/2026 9:00:28 AM	29.2	65.1	0.0	5.7			153.5	153.5	0.4
CCV24073	CV-24073-TP13	9/30/2026 9:01:24 AM	27.9	64.9	0.0	7.2			153.5	153.7	0.4
CCV24073	CV-24073-TP13	9/30/2026 9:05:00 AM					1170				
CCV24074	CV-24074	9/2/2026 2:20:20 PM	1.5	83.5	0.1	14.9			118.3	118.8	0.0
CCV24074	CV-24074	9/21/2026 2:20:48 PM	1.1	80.4	0.2	18.3			127.9	127.3	0.0
CCV24075	CV-24075-TP15	9/1/2026 1:27:41 PM	25.5	71.0	1.0	2.5			178.5	178.4	0.4
CCV24075	CV-24075-TP15	9/1/2026 1:34:00 PM						67500			
CCV24075	CV-24075-TP15	9/1/2026 1:34:00 PM					1740				
CCV24075	CV-24075-TP15	9/9/2026 1:36:18 PM	31.9	66.8	1.3	0.0			181.5	181.6	0.5
CCV24075	CV-24075-TP15	9/9/2026 1:41:00 PM					2030				
CCV24075	CV-24075-TP15	9/16/2026 9:26:05 AM	10.8	82.6	0.0	6.6			182.3	182.3	0.1
CCV24075	CV-24075-TP15	9/16/2026 9:28:00 AM					2100				
CCV24075	CV-24075-TP15	9/23/2026 9:31:50 AM	37.0	62.2	0.8	0.0			181.4	181.5	0.6
CCV24075	CV-24075-TP15	9/23/2026 9:35:00 AM					770				
CCV24075	CV-24075-TP15	9/30/2026 8:50:15 AM	27.7	66.7	1.3	4.3			179.1	179.2	0.4
CCV24075	CV-24075-TP15	9/30/2026 8:55:00 AM					1710				
CCV24076	CV-24076	9/1/2026 1:45:00 PM						41400			
CCV24076	CV-24076	9/1/2026 1:45:00 PM					1040				
CCV24076	CV-24076	9/1/2026 1:45:11 PM	24.0	44.9	3.8	27.3			167.6	167.4	0.5



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24076	CV-24076	9/1/2026 1:49:10 PM	23.4	45.1	3.9	27.6			172.5	172.2	0.5
CCV24076	CV-24076	9/9/2026 1:57:00 PM					818				
CCV24076	CV-24076	9/9/2026 1:58:23 PM	24.4	43.2	4.1	28.3			172.5	174.2	0.6
CCV24076	CV-24076	9/16/2026 9:59:57 AM	5.9	82.1	0.0	12.0			171.0	171.8	0.1
CCV24076	CV-24076	9/16/2026 10:02:00 AM					1010				
CCV24076	CV-24076	9/23/2026 9:57:00 AM	29.0	37.9	2.4	30.7			168.5	168.0	0.8
CCV24076	CV-24076	9/30/2026 9:00:43 AM	23.1	39.3	2.8	34.8			160.5	160.0	0.6
CCV24076	CV-24076	9/30/2026 9:05:00 AM					881				
CCV24077	CV-24077	9/1/2026 9:39:47 AM	22.7	57.4	0.0	19.9			143.9	140.9	0.4
CCV24077	CV-24077	9/1/2026 11:02:58 AM	21.6	66.2	0.0	12.2			136.0	136.1	0.3
CCV24077	CV-24077	9/1/2026 2:25:00 PM						40000			
CCV24077	CV-24077	9/1/2026 2:25:00 PM					1330				
CCV24077	CV-24077	9/1/2026 2:29:54 PM	26.5	69.3	0.0	4.2			154.1	153.7	0.4
CCV24077	CV-24077	9/8/2026 10:33:07 AM	13.8	68.9	0.0	17.3			157.3	157.6	0.2
CCV24077	CV-24077	9/8/2026 10:35:00 AM					1800				
CCV24077	CV-24077	9/14/2026 9:40:00 AM					1290				
CCV24077	CV-24077	9/14/2026 9:41:46 AM	15.5	60.1	0.0	24.4			157.7	157.8	0.3
CCV24077	CV-24077	9/14/2026 10:22:00 AM	14.6	65.1	0.0	20.3			157.5	157.3	0.2
CCV24077	CV-24077	9/22/2026 12:59:33 PM	11.5	75.8	0.0	12.7			154.3	154.5	0.2
CCV24077	CV-24077	9/22/2026 1:00:24 PM	12.5	78.5	0.0	9.0			155.1	155.1	0.2
CCV24077	CV-24077	9/23/2026 1:52:00 PM					950				
CCV24077	CV-24077	9/23/2026 1:52:12 PM	25.8	60.5	0.0	13.7			156.0	156.2	0.4
CCV24077	CV-24077	9/30/2026 1:55:00 PM					1370				
CCV24077	CV-24077	9/30/2026 1:57:09 PM	24.7	63.6	0.0	11.7			156.0	156.0	0.4
CCV24078	CV-24078	9/1/2026 11:05:35 AM	7.9	63.9	3.2	25.0			108.7	108.8	0.1
CCV24078	CV-24078	9/22/2026 10:57:51 AM	15.2	62.6	3.2	19.0			113.9	113.9	0.2
CCV24079	CV-24079-TP8	9/1/2026 10:56:25 AM	0.8	83.0	0.0	16.2			94.4	94.4	0.0
CCV24079	CV-24079-TP8	9/21/2026 11:00:53 AM	18.8	68.1	0.1	13.0			170.4	169.1	0.3
CCV24079	CV-24079-TP8	9/21/2026 11:03:19 AM	8.1	76.6	0.1	15.2			169.1	170.4	0.1



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24079	CV-24079-TP8	9/28/2026 10:34:01 AM	19.0	75.6	0.0	5.4			166.5	166.1	0.3
CCV24079	CV-24079-TP8	9/30/2026 9:15:00 AM					1100				
CCV24079	CV-24079-TP8	9/30/2026 9:17:09 AM	20.2	64.4	0.0	15.4			162.3	163.3	0.3
CCV24080	CV-24080	9/1/2026 10:50:48 AM	18.9	68.8	0.0	12.3			123.5	123.6	0.3
CCV24080	CV-24080	9/9/2026 2:19:31 PM	31.2	48.7	0.0	20.1			128.3	128.4	0.6
CCV24080	CV-24080	9/17/2026 10:09:09 AM	41.2	56.1	0.0	2.7			119.7	119.5	0.7
CCV24081	CV-24081-TP10	9/2/2026 9:06:17 AM	25.0	73.7	0.1	1.2			104.7	104.7	0.3
CCV24081	CV-24081-TP10	9/17/2026 1:48:26 PM	27.7	71.4	0.0	0.9			107.8	107.9	0.4
CCV24082	CV-24082	9/2/2026 9:30:43 AM	43.2	54.8	0.0	2.0			122.8	122.5	0.8
CCV24082	CV-24082	9/17/2026 1:53:48 PM	43.3	53.8	0.0	2.9			126.1	125.2	0.8
CCV24083	CV-24083	9/2/2026 8:49:34 AM	30.6	66.2	0.0	3.2			157.9	158.8	0.5
CCV24083	CV-24083	9/2/2026 8:50:00 AM					1430				
CCV24083	CV-24083	9/2/2026 8:50:00 AM						76700			
CCV24083	CV-24083	9/8/2026 10:18:45 AM	19.3	68.8	0.1	11.8			152.8	153.8	0.3
CCV24083	CV-24083	9/8/2026 10:20:00 AM					1360				
CCV24083	CV-24083	9/17/2026 1:55:13 PM	40.8	59.2	0.0	0.0			154.0	152.8	0.7
CCV24083	CV-24083	9/17/2026 1:57:00 PM					703.5				
CCV24083	CV-24083	9/23/2026 1:21:00 PM					1060				
CCV24083	CV-24083	9/23/2026 1:23:41 PM	7.6	74.2	0.0	18.2			149.5	148.0	0.1
CCV24083	CV-24083	9/30/2026 10:01:53 AM	39.9	60.1	0.0	0.0			137.8	138.2	0.7
CCV24084	CV-24084-TP11	9/2/2026 8:41:51 AM	28.3	71.2	0.0	0.5			185.2	185.4	0.4
CCV24084	CV-24084-TP11	9/2/2026 8:45:00 AM					2215				
CCV24084	CV-24084-TP11	9/2/2026 8:45:00 AM						106300			
CCV24084	CV-24084-TP11	9/8/2026 10:20:41 AM	2.3	80.9	0.0	16.8			187.2	187.4	0.0
CCV24084	CV-24084-TP11	9/8/2026 10:25:00 AM					3620				
CCV24084	CV-24084-TP11	9/17/2026 1:59:08 PM	39.8	60.2	0.0	0.0			186.2	186.0	0.7
CCV24084	CV-24084-TP11	9/17/2026 2:02:00 PM					3220				
CCV24084	CV-24084-TP11	9/23/2026 1:13:00 PM					2770				
CCV24084	CV-24084-TP11	9/23/2026 1:16:20 PM	7.0	79.8	0.0	13.2			186.1	186.3	0.1



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24084	CV-24084-TP11	9/30/2026 9:55:00 AM					2810				
CCV24084	CV-24084-TP11	9/30/2026 9:57:04 AM	8.2	79.0	0.0	12.8			185.3	185.2	0.1
CCV24085	CV-24085	9/1/2026 11:10:02 AM	40.6	51.9	0.0	7.5			93.7	93.6	0.8
CCV24085	CV-24085	9/1/2026 11:10:35 AM	41.7	51.9	0.0	6.4			93.6	93.6	0.8
CCV24085	CV-24085	9/9/2026 2:14:51 PM	27.6	40.0	0.0	32.4			133.8	132.8	0.7
CCV24085	CV-24085	9/9/2026 2:15:24 PM	27.8	39.9	0.0	32.3			132.6	132.6	0.7
CCV24085	CV-24085	9/18/2026 4:38:39 PM	24.4	33.8	0.1	41.7			130.9	129.8	0.7
CCV24086	CV-24086	9/1/2026 10:18:55 AM	39.1	48.2	0.0	12.7			126.2	126.9	0.8
CCV24086	CV-24086	9/17/2026 9:56:01 AM	39.7	46.0	0.1	14.2			127.3	127.4	0.9
CCV24087	CV-24087	9/14/2026 1:57:58 PM	49.2	43.1	0.0	7.7			121.5	121.3	1.1
CCV24087	CV-24087	9/21/2026 9:41:26 AM	44.1	42.0	0.8	13.1			123.4	123.3	1.1
CCV24088	CV-24088	9/2/2026 1:21:22 PM	47.4	52.6	0.0	0.0			112.6	113.1	0.9
CCV24088	CV-24088	9/17/2026 3:03:53 PM	44.8	51.9	0.1	3.2			104.5	104.8	0.9
CCV24089	CV-24089	9/1/2026 2:52:55 PM	44.6	46.2	0.0	9.2			129.3	129.5	1.0
CCV24089	CV-24089	9/22/2026 2:06:04 PM	31.6	40.4	0.1	27.9			129.1	129.2	0.8
CCV24090	CV-24090	9/3/2026 12:03:50 PM	44.6	51.4	0.0	4.0			113.4	113.3	0.9
CCV24090	CV-24090	9/14/2026 1:45:37 PM	42.7	49.3	0.0	8.0			117.0	116.6	0.9
CCV24090	CV-24090	9/21/2026 9:16:50 AM	40.0	49.7	0.0	10.3			108.3	108.4	0.8
CCV24091	CV-24091	9/14/2026 1:37:49 PM	54.6	42.3	0.0	3.1			111.2	111.3	1.3
CCV24091	CV-24091	9/21/2026 8:59:41 AM	56.2	40.7	0.0	3.1			98.8	100.0	1.4
CCV24092	CV-24092	9/14/2026 1:27:47 PM	51.3	45.1	0.0	3.6			119.4	119.5	1.1
CCV24092	CV-24092	9/24/2026 2:16:45 PM	50.9	46.7	0.0	2.4			119.9	119.8	1.1
CCV24093	CV-24093	9/13/2026 9:56:20 AM	29.5	22.6	10.3	37.6			99.4	98.3	1.3
CCV24093	CV-24093	9/13/2026 9:58:10 AM	29.3	21.5	10.2	39.0			100.7	100.8	1.4
CCV24093	CV-24093	9/28/2026 10:16:44 AM	0.2	3.9	20.0	75.9			80.1	80.4	0.1
CCV24094	CV-24094	9/14/2026 1:07:34 PM	19.3	70.0	3.0	7.7			102.9	102.9	0.3
CCV24094	CV-24094	9/22/2026 10:05:46 AM	10.0	73.2	2.2	14.6			99.8	99.8	0.1
CCV24095	CV-24095	9/1/2026 1:57:31 PM	5.3	71.6	0.0	23.1			186.0	186.2	0.1
CCV24095	CV-24095	9/1/2026 2:00:00 PM						159300			

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24095	CV-24095	9/1/2026 2:00:00 PM					2620				
CCV24095	CV-24095	9/8/2026 1:30:00 PM					2940				
CCV24095	CV-24095	9/8/2026 1:31:41 PM	7.6	78.1	0.1	14.2			191.3	191.3	0.1
CCV24095	CV-24095	9/10/2026 8:30:00 AM					2200				
CCV24095	CV-24095	9/10/2026 8:30:00 AM						180000			
CCV24095	CV-24095	9/17/2026 9:42:47 AM	11.4	79.9	0.0	8.7			192.0	192.1	0.1
CCV24095	CV-24095	9/17/2026 9:47:00 AM					3210				
CCV24095	CV-24095	9/24/2026 9:52:08 AM	12.9	68.7	0.0	18.4			191.8	191.6	0.2
CCV24095	CV-24095	9/24/2026 10:00:00 AM					2670				
CCV24096	CV-24096	9/2/2026 8:14:01 AM	32.6	53.7	2.6	11.1			65.8	65.8	0.6
CCV24096	CV-24096	9/23/2026 9:26:01 AM	30.5	40.7	4.5	24.3			87.7	88.4	0.7
CCV24097	CV-24097	9/2/2026 8:18:03 AM	50.5	44.4	0.4	4.7			66.2	66.2	1.1
CCV24097	CV-24097	9/30/2026 3:17:38 PM	41.6	40.3	0.0	18.1			99.3	99.4	1.0
CCV24098	CV-24098	9/2/2026 8:23:38 AM	43.7	51.6	0.3	4.4			72.3	72.3	0.8
CCV24098	CV-24098	9/23/2026 9:16:20 AM	43.9	48.5	1.3	6.3			88.4	89.4	0.9
CCV24099	CV-24099	9/2/2026 8:32:12 AM	23.3	50.2	4.6	21.9			67.0	66.4	0.5
CCV24099	CV-24099	9/23/2026 9:11:30 AM	0.0	4.8	19.5	75.7			79.8	80.5	0.0
CCV24099	CV-24099	9/23/2026 9:13:00 AM	0.1	2.0	19.9	78.0			81.1	81.2	0.1
CCV24100	CV-24100	9/2/2026 8:50:27 AM	44.1	52.5	0.3	3.1			97.3	97.3	0.8
CCV24100	CV-24100	9/2/2026 1:05:00 PM					144				
CCV24100	CV-24100	9/2/2026 1:05:00 PM						5600			
CCV24100	CV-24100	9/2/2026 1:12:10 PM	33.8	66.2	0.0	0.0			151.7	153.7	0.5
CCV24100	CV-24100	9/2/2026 1:16:31 PM	33.4	66.6	0.0	0.0			152.1	152.6	0.5
CCV24100	CV-24100	9/8/2026 7:35:00 AM					38				
CCV24100	CV-24100	9/8/2026 7:35:00 AM						6300			
CCV24100	CV-24100	9/8/2026 2:53:01 PM	29.5	70.4	0.1	0.0			147.6	148.4	0.4
CCV24100	CV-24100	9/8/2026 2:55:00 PM					192				
CCV24100	CV-24100	9/17/2026 2:15:00 PM					348				
CCV24100	CV-24100	9/17/2026 2:19:56 PM	35.9	64.1	0.0	0.0			148.6	148.5	0.6

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24100	CV-24100	9/17/2026 2:21:00 PM	35.6	64.4	0.0	0.0			148.7	149.0	0.6
CCV24100	CV-24100	9/24/2026 10:19:50 AM	29.3	70.3	0.3	0.1			142.1	133.8	0.4
CCV24100	CV-24100	9/24/2026 10:25:00 AM					137				
CCV24100	CV-24100	9/28/2026 1:58:23 PM	17.4	80.9	1.1	0.6			122.3	125.7	0.2
CCV24101	CV-24101	9/8/2026 7:30:00 AM					0				
CCV24101	CV-24101	9/8/2026 7:30:00 AM						1200			
CCV24101	CV-24101	9/8/2026 2:50:19 PM		47.9	1.9				109.7	109.9	
CCV24101	CV-24101	9/28/2026 1:59:13 PM	17.6	80.4	0.5	1.5			127.9	128.1	0.2
CCV24102	CV-24102	9/2/2026 9:21:46 AM	43.1	47.1	0.0	9.8			101.0	101.1	0.9
CCV24102	CV-24102	9/22/2026 12:22:15 PM	40.3	52.4	0.0	7.3			101.9	101.7	0.8
CCV24103	CV-24103	9/1/2026 11:30:43 AM	41.2	42.6	0.0	16.2			111.6	111.7	1.0
CCV24103	CV-24103	9/21/2026 11:54:27 AM	42.1	41.4	0.0	16.5			110.5	110.6	1.0
CCV24104	CV-24104	9/1/2026 1:54:55 PM	44.1	49.9	0.0	6.0			101.7	101.8	0.9
CCV24104	CV-24104	9/3/2026 10:55:10 AM	40.5	53.8	0.0	5.7			101.4	101.6	0.8
CCV24104	CV-24104	9/21/2026 12:21:54 PM	41.8	52.5	0.0	5.7			102.3	102.2	0.8
CCV24105	CV-24105	9/1/2026 2:02:32 PM	45.1	40.6	0.0	14.3			118.3	118.3	1.1
CCV24105	CV-24105	9/22/2026 3:05:41 PM	41.1	41.4	0.0	17.5			118.2	118.3	1.0
CCV24106	CV-24106	9/15/2026 12:21:17 PM	42.4	37.3	0.0	20.3			129.7	129.1	1.1
CCV24106	CV-24106	9/15/2026 12:21:57 PM	41.7	37.7	0.0	20.6			129.1	128.8	1.1
CCV24107	CV-24107	9/9/2026 1:53:59 PM	38.1	43.2	0.0	18.7			126.1	126.9	0.9
CCV24108	CV-24108	9/9/2026 1:16:23 PM	44.9	46.7	0.0	8.4			136.5	135.0	1.0
CCV24108	CV-24108	9/9/2026 1:17:42 PM	45.8	45.8	0.0	8.4			135.0	135.0	1.0
CCV24109	CV-24109	9/9/2026 12:50:32 PM	30.3	44.7	1.4	23.6			124.4	124.6	0.7
CCV24110	CV-24110	9/3/2026 1:03:31 PM	26.9	71.4	0.0	1.7			131.3	131.5	0.4
CCV24111	CV-24111	9/3/2026 1:42:51 PM	41.7	52.5	0.1	5.7			117.9	116.7	0.8
CCV24112	CV-24112	9/3/2026 1:20:04 PM	46.7	39.5	0.0	13.8			130.2	130.2	1.2
CCV24114	CV-24114	9/23/2026 9:58:47 AM	54.2	40.5	0.0	5.3			121.0	122.0	1.3
CCV24116	CV-24116	9/24/2026 1:00:00 PM					20.3				
CCV24116	CV-24116	9/24/2026 1:00:00 PM						3200			



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24116	CV-24116	9/24/2026 1:11:51 PM						58000			
CCV24116	CV-24116	9/24/2026 1:12:29 PM	51.0	43.8	0.0	5.2			118.7	118.3	1.2
CCV24116	CV-24116	9/24/2026 3:03:05 PM					25				
CCV24117	CV-24117	9/24/2026 10:47:16 AM	32.5	38.4	0.0	29.1			107.0	107.0	0.8
CCV24118	CV-24118	9/1/2026 9:00:54 AM	8.2	79.8	0.0	12.0			150.9	150.9	0.1
CCV24118	CV-24118	9/2/2026 2:19:21 PM	31.1	52.0	0.0	16.9			150.5	151.0	0.6
CCV24118	CV-24118	9/2/2026 2:25:00 PM					3750				
CCV24118	CV-24118	9/2/2026 2:25:00 PM						133800			
CCV24118	CV-24118	9/10/2026 9:35:00 AM					3110				
CCV24118	CV-24118	9/10/2026 9:38:23 AM	16.2	73.1	0.0	10.7			151.4	151.6	0.2
CCV24118	CV-24118	9/17/2026 10:36:18 AM	32.1	62.7	0.0	5.2			144.2	144.5	0.5
CCV24118	CV-24118	9/17/2026 10:39:00 AM					2010				
CCV24119	CV-24119	9/28/2026 2:35:12 PM	44.0	46.2	0.0	9.8			137.1	136.0	1.0
CCV24120	CV-24120	9/9/2026 8:10:00 AM					680				
CCV24120	CV-24120	9/9/2026 8:10:00 AM						42000			
CCV24120	CV-24120	9/14/2026 10:25:29 AM	3.3	39.8	10.8	46.1			97.7	97.7	0.1
CCV24120	CV-24120	9/14/2026 10:27:15 AM	2.5	29.5	12.9	55.1			97.7	97.7	0.1
CCV24120	CV-24120	9/25/2026 10:26:04 AM	1.7	18.2	15.1	65.0			92.2	92.0	0.1
CCV24120	CV-24120	9/28/2026 9:41:44 AM	7.8	92.2	0.0	0.0			89.4	84.7	0.1
CCV24120	CV-24120	9/28/2026 9:50:35 AM	6.9	89.6	0.9	2.6			91.6	91.5	0.1
CCV24121	CV-24121	9/3/2026 9:37:51 AM	23.6	52.8	2.6	21.1			99.9	125.5	0.4
CCV24121	CV-24121	9/3/2026 9:43:25 AM	31.6	51.2	3.6	13.7			125.7	125.5	0.6
CCV24121	CV-24121	9/10/2026 9:45:00 AM					25				
CCV24121	CV-24121	9/10/2026 9:45:00 AM						1600			
CCV24121	CV-24121	9/25/2026 10:30:06 AM	31.7	67.5	0.0	0.8			127.2	127.4	0.5
CCV24122	CV-24122	9/8/2026 8:20:00 AM					200				
CCV24122	CV-24122	9/8/2026 8:20:00 AM						15000			
CCV24122	CV-24122	9/15/2026 7:57:25 AM	27.9	24.0	10.3	37.8			67.3	67.4	1.2
CCV24122	CV-24122	9/15/2026 7:58:33 AM	27.9	24.0	10.3	37.8			67.5	67.5	1.2



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24122	CV-24122	9/25/2026 10:38:50 AM	32.8	27.6	7.3	32.3			99.6	100.1	1.2
CCV24123	CV-24123	9/3/2026 9:17:50 AM	45.4	50.6	0.0	3.9			117.1	117.3	0.9
CCV24123	CV-24123	9/11/2026 3:37:45 PM	50.5	49.5	0.0	0.0			117.0		1.0
CCV24123	CV-24123	9/11/2026 3:38:20 PM	50.9	49.1	0.0	0.0			117.0		1.0
CCV24123	CV-24123	9/23/2026 8:27:33 AM	46.6	49.4	0.0	4.0			117.0	116.6	0.9
CCV24124	CV-24124	9/15/2026 10:14:34 AM	6.4	67.4	1.3	24.9			135.9	136.0	0.1
CCV24124	CV-24124	9/15/2026 10:15:20 AM	5.7	71.2	1.3	21.8			135.9	135.9	0.1
CCV24124	CV-24124	9/29/2026 8:14:35 AM	6.2	60.8	2.3	30.7			134.1	133.9	0.1
CCV24124	CV-24124	9/29/2026 8:15:27 AM	6.2	61.0	2.3	30.6			133.4	133.9	0.1
CCV24125	CV-24125-TP20	9/9/2026 8:20:00 AM					0				
CCV24125	CV-24125-TP20	9/9/2026 8:20:00 AM						1400			
CCV24125	CV-24125-TP20	9/14/2026 9:25:49 AM	37.6	48.1	1.5	12.8			124.2	121.4	0.8
CCV24125	CV-24125-TP20	9/29/2026 8:05:16 AM	44.1	51.3	0.0	4.6			90.0	89.9	0.9
CCV24126	CV-24126	9/8/2026 2:01:24 PM	15.0	63.4	0.0	21.6			189.3	189.4	0.2
CCV24126	CV-24126	9/8/2026 2:04:00 PM					3490				
CCV24126	CV-24126	9/14/2026 1:36:52 PM	16.3	40.1	2.3	41.3			177.6	177.7	0.4
CCV24126	CV-24126	9/14/2026 1:40:00 PM					1340				
CCV24126	CV-24126	9/21/2026 1:17:00 PM					1360				
CCV24126	CV-24126	9/21/2026 1:17:21 PM	19.1	34.2	3.2	43.5			174.2	174.1	0.6
CCV24126	CV-24126	9/28/2026 1:36:03 PM	13.4	35.4	2.7	48.5			174.0	174.2	0.4
CCV24126	CV-24126	9/28/2026 1:45:00 PM					1370				
CCV24127	CV-24127	9/8/2026 8:00:00 AM					2600				
CCV24127	CV-24127	9/8/2026 8:00:00 AM						180000			
CCV24127	CV-24127	9/8/2026 2:06:28 PM	8.9	69.4	0.0	21.7			177.2	177.2	0.1
CCV24127	CV-24127	9/8/2026 2:09:00 PM					3930				
CCV24127	CV-24127	9/14/2026 1:33:01 PM	28.2	67.5	0.0	4.3			160.3	160.3	0.4
CCV24127	CV-24127	9/14/2026 1:36:00 PM					1620				
CCV24127	CV-24127	9/21/2026 1:12:42 PM	34.5	65.5	0.0	0.0			164.0	164.3	0.5
CCV24127	CV-24127	9/21/2026 1:13:00 PM					1780				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24127	CV-24127	9/28/2026 1:25:09 PM	26.7	40.6	0.5	32.2			151.6	151.4	0.7
CCV24127	CV-24127	9/28/2026 1:35:00 PM					1760				
CCV24128	CV-24128	9/9/2026 12:13:22 PM	23.5	70.8	0.3	5.4			145.6	123.0	0.3
CCV24128	CV-24128	9/9/2026 12:14:49 PM	24.0	69.7	0.3	6.0			122.3	122.3	0.3
CCV24128	CV-24128	9/10/2026 9:35:00 AM					2700				
CCV24128	CV-24128	9/10/2026 9:35:00 AM						110000			
CCV24128	CV-24128	9/25/2026 9:55:31 AM	23.1	58.8	0.3	17.8			127.8	127.8	0.4
CCV24129	CV-24129	9/9/2026 12:18:22 PM	43.9	55.4	0.7	0.0			130.8	130.8	0.8
CCV24129	CV-24129	9/25/2026 9:45:34 AM	45.6	54.4	0.0	0.0			130.6	130.0	0.8
CCV24130	CV-24130	9/30/2026 2:09:18 PM	18.7	72.0	0.0	9.3			126.1	125.6	0.3
CCV24131	CV-24131	9/10/2026 1:47:00 PM	40.1	58.5	0.2	1.2			127.2	127.3	0.7
CCV24132	CV-24132	9/30/2026 10:16:29 AM	50.4	44.1	0.0	5.5			129.4	129.7	1.1
CCV24133	CV-24133	9/21/2026 8:33:25 AM	48.0	41.7	0.0	10.3			123.9	123.7	1.2
CCV24134	CV-24134-TP19	9/10/2026 1:06:47 PM	21.9	70.2	0.1	7.8			153.2	153.0	0.3
CCV24134	CV-24134-TP19	9/14/2026 1:29:38 PM	25.7	68.2	0.0	6.1			152.3	152.0	0.4
CCV24134	CV-24134-TP19	9/14/2026 1:32:00 PM					2890				
CCV24134	CV-24134-TP19	9/21/2026 1:07:00 PM					3140				
CCV24134	CV-24134-TP19	9/21/2026 1:09:25 PM	36.4	63.5	0.0	0.1			151.7	152.2	0.6
CCV24134	CV-24134-TP19	9/28/2026 1:06:51 PM	25.8	69.5	0.0	4.7			150.0	150.1	0.4
CCV24134	CV-24134-TP19	9/28/2026 1:25:00 PM					2760				
CCV24135	CV-24135	9/3/2026 9:48:00 AM						141700			
CCV24135	CV-24135	9/3/2026 9:48:00 AM					4220				
CCV24135	CV-24135	9/3/2026 10:26:41 AM	21.7	71.0	0.0	7.3			150.4	150.4	0.3
CCV24135	CV-24135	9/10/2026 2:23:00 PM					3960				
CCV24135	CV-24135	9/10/2026 2:26:00 PM	18.0	73.9	0.0	8.1			149.4	149.2	0.2
CCV24135	CV-24135	9/10/2026 2:27:03 PM	16.8	73.4	0.0	9.8			149.3	149.2	0.2
CCV24135	CV-24135	9/14/2026 1:23:45 PM	23.7	67.8	0.0	8.5			150.1	150.2	0.3
CCV24135	CV-24135	9/14/2026 1:27:00 PM					4270				
CCV24135	CV-24135	9/24/2026 1:53:54 PM	20.2	74.8	0.0	5.0			150.4	150.4	0.3



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24135	CV-24135	9/24/2026 1:55:00 PM					4070				
CCV24136	CV-24136	9/10/2026 1:43:56 PM	26.1	64.2	0.2	9.5			135.6	135.7	0.4
CCV24137	CV-24137	9/28/2026 1:45:23 PM	43.7	44.1	0.0	12.2			105.6	104.2	1.0
CCV24138	CV-24138	9/2/2026 7:35:00 AM					160				
CCV24138	CV-24138	9/2/2026 7:35:00 AM						25000			
CCV24138	CV-24138	9/2/2026 7:58:13 AM	0.5	10.2	17.4	71.9			65.6	65.5	0.0
CCV24138	CV-24138	9/2/2026 7:59:07 AM	0.5	10.2	17.3	72.0			65.3	65.3	0.0
CCV24138	CV-24138	9/30/2026 2:54:56 PM	2.3	72.3	0.2	25.2			162.2	161.4	0.0
CCV24139	CV-24139	9/1/2026 1:45:00 PM						180100			
CCV24139	CV-24139	9/1/2026 1:45:00 PM					1070				
CCV24139	CV-24139	9/1/2026 1:48:41 PM	5.5	70.8	0.4	23.3			145.4	145.4	0.1
CCV24139	CV-24139	9/2/2026 7:30:00 AM					720				
CCV24139	CV-24139	9/2/2026 7:30:00 AM						210000			
CCV24139	CV-24139	9/8/2026 1:22:11 PM	8.7	58.3	4.3	28.7			110.5	110.5	0.1
CCV24139	CV-24139	9/10/2026 2:55:48 PM	1.9	2.1	20.3	75.7			132.1	129.5	0.9
CCV24139	CV-24139	9/10/2026 3:13:23 PM	9.3	16.2	15.6	58.9			127.2	125.3	0.6
CCV24139	CV-24139	9/10/2026 3:15:24 PM	8.9	18.3	15.0	57.8			125.4	125.4	0.5
CCV24139	CV-24139	9/30/2026 2:51:42 PM	4.2	53.0	7.8	35.0			128.4	129.2	0.1
CCV24140	CV-24140	9/1/2026 1:40:00 PM						182800			
CCV24140	CV-24140	9/1/2026 1:40:00 PM					2160				
CCV24140	CV-24140	9/1/2026 1:44:48 PM	3.8	74.8	0.0	21.4			164.0	164.0	0.1
CCV24140	CV-24140	9/2/2026 7:25:00 AM					1400				
CCV24140	CV-24140	9/2/2026 7:25:00 AM						210000			
CCV24140	CV-24140	9/8/2026 1:16:52 PM	3.4	73.7	0.6	22.3			165.9	166.0	0.0
CCV24140	CV-24140	9/8/2026 1:20:00 PM					2140				
CCV24140	CV-24140	9/17/2026 9:53:55 AM	7.1	72.3	0.3	20.3			154.7	153.3	0.1
CCV24140	CV-24140	9/17/2026 9:55:00 AM					2120				
CCV24140	CV-24140	9/24/2026 9:42:13 AM	7.8	72.8	0.3	19.1			145.3	145.5	0.1
CCV24140	CV-24140	9/24/2026 9:45:00 AM					1290				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24141	CV-24141	9/2/2026 7:10:00 AM					26				
CCV24141	CV-24141	9/2/2026 7:10:00 AM						1900			
CCV24141	CV-24141	9/15/2026 9:57:58 AM	2.1	6.4	17.6	73.9			90.4	91.6	0.3
CCV24141	CV-24141	9/15/2026 9:59:24 AM	2.1	5.6	17.7	74.6			92.2	92.1	0.4
CCV24141	CV-24141	9/23/2026 9:57:06 AM	0.9	6.1	18.4	74.6			95.9	94.6	0.1
CCV24142	CV-24142	9/1/2026 1:54:21 PM	4.0	65.9	2.7	27.4			128.0	128.2	0.1
CCV24142	CV-24142	9/2/2026 7:40:00 AM					1200				
CCV24142	CV-24142	9/2/2026 7:40:00 AM						170000			
CCV24142	CV-24142	9/30/2026 2:58:57 PM	1.6	52.9	7.2	38.3			130.5	130.5	0.0
CCV24143	CV-24143	9/1/2026 7:40:00 AM					660				
CCV24143	CV-24143	9/1/2026 7:40:00 AM						94000			
CCV24143	CV-24143	9/10/2026 12:19:01 PM	4.8	62.0	5.2	28.0			125.2	124.2	0.1
CCV24143	CV-24143	9/10/2026 12:20:07 PM	3.9	61.0	5.3	29.8			123.9	124.1	0.1
CCV24143	CV-24143	9/23/2026 9:50:14 AM	1.7	71.2	2.9	24.2			100.3	100.4	0.0
CCV24144	CV-24144	9/2/2026 8:20:25 AM	55.9	41.0	0.0	3.1			68.7	68.8	1.4
CCV24145	CV-24145	9/9/2026 8:26:12 AM	14.9	59.4	0.0	25.7			187.7	188.0	0.3
CCV24145	CV-24145	9/9/2026 8:28:00 AM					1620				
CCV24145	CV-24145	9/15/2026 8:52:56 AM	14.4	58.4	0.0	27.2			187.1	187.2	0.2
CCV24145	CV-24145	9/15/2026 8:55:00 AM					1770				
CCV24145	CV-24145	9/22/2026 8:48:58 AM	12.6	40.1	0.0	47.3			187.6	187.6	0.3
CCV24145	CV-24145	9/22/2026 8:50:00 AM					1100				
CCV24145	CV-24145	9/29/2026 8:14:25 AM	8.7	72.8	0.0	18.5			187.9	187.6	0.1
CCV24145	CV-24145	9/29/2026 8:20:00 AM					2250				
CCV24146	CV-24146	9/11/2026 3:43:00 PM	54.5	45.5	0.0	0.0			115.0		1.2
CCV24146	CV-24146	9/11/2026 3:43:31 PM	58.8	41.2	0.0	0.0					1.4
CCV24146	CV-24146	9/23/2026 8:23:00 AM	54.1	40.1	0.0	5.8			113.9	113.9	1.3
CCV24146	CV-24146	9/29/2026 7:46:29 AM	52.8	41.6	0.0	5.6			113.9	114.1	1.3
CCV24146	CV-24146	9/29/2026 7:48:05 AM	52.6	42.0	0.0	5.4			114.2	114.2	1.3
CCV24147	CV-24147	9/14/2026 8:55:38 AM	52.0	42.3	0.0	5.7			115.3	115.3	1.2



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24147	CV-24147	9/29/2026 7:53:08 AM	49.6	41.1	0.0	9.3			113.1	113.2	1.2
CCV24148	CV-24148	9/1/2026 1:15:45 PM	32.5	61.0	0.0	6.5			167.1	167.2	0.5
CCV24148	CV-24148	9/1/2026 1:21:00 PM						49050			
CCV24148	CV-24148	9/1/2026 1:21:00 PM					983				
CCV24148	CV-24148	9/9/2026 1:24:00 PM					1250				
CCV24148	CV-24148	9/9/2026 1:25:02 PM	47.4	52.6	0.0	0.0			172.7	172.6	0.9
CCV24148	CV-24148	9/16/2026 9:01:24 AM	31.5	67.5	0.0	1.0			176.9	177.4	0.5
CCV24148	CV-24148	9/16/2026 9:06:00 AM					1580				
CCV24148	CV-24148	9/23/2026 9:17:16 AM	42.1	57.9	0.0	0.0			174.7	174.6	0.7
CCV24148	CV-24148	9/23/2026 9:21:00 AM					861				
CCV24148	CV-24148	9/30/2026 8:20:00 AM					1060				
CCV24148	CV-24148	9/30/2026 8:33:02 AM	32.0	61.7	0.0	6.3			166.2	166.4	0.5
CCV24149	CV-24149	9/2/2026 2:26:43 PM	35.9	54.8	0.0	9.3			128.5	128.4	0.7
CCV24149	CV-24149	9/28/2026 10:08:01 AM	31.9	63.3	0.0	4.8			129.0	129.2	0.5
CCV24150	CV-24150	9/14/2026 1:00:56 PM	41.8	57.7	0.4	0.1			96.0	96.0	0.7
CCV24150	CV-24150	9/22/2026 10:00:08 AM	42.7	57.2	0.1	0.0			111.8	111.7	0.7
CCV24151	CV-24151	9/2/2026 1:38:48 PM	45.9	46.4	0.3	7.4			116.4	116.9	1.0
CCV24151	CV-24151	9/28/2026 10:24:52 AM	39.9	55.5	0.0	4.6			121.9	122.9	0.7
CCV24152	CV-24152	9/2/2026 2:13:03 PM	19.3	76.5	0.0	4.2			142.5	142.6	0.3
CCV24152	CV-24152	9/2/2026 2:14:21 PM	19.5	76.3	0.0	4.2			142.7	142.7	0.3
CCV24152	CV-24152	9/21/2026 2:17:53 PM	18.6	72.6	0.2	8.6			144.3	144.3	0.3
CCV24153	CV-24153	9/2/2026 2:35:08 PM	38.0	61.9	0.0	0.1			116.9	116.7	0.6
CCV24153	CV-24153	9/28/2026 10:19:05 AM	36.3	63.7	0.0	0.0			129.6	129.7	0.6
CCV24154	CV-24154	9/3/2026 12:57:36 PM	44.2	52.3	0.0	3.4			108.8	109.0	0.8
CCV24154	CV-24154	9/24/2026 1:45:55 PM	40.3	58.9	0.0	0.8			113.7	113.2	0.7
CCV24155	CV-24155	9/2/2026 2:32:05 PM	33.5	61.8	0.0	4.7			123.9	124.4	0.5
CCV24155	CV-24155	9/28/2026 10:12:48 AM	37.7	56.9	0.0	5.4			128.5	128.6	0.7
CCV24156	CV-24156	9/2/2026 8:34:18 AM	25.8	69.6	0.0	4.6			137.1	137.2	0.4
CCV24156	CV-24156	9/2/2026 8:35:16 AM	27.2	71.7	0.0	1.1			136.9	137.0	0.4



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24156	CV-24156	9/17/2026 2:44:43 PM	22.3	70.0	1.1	6.6			137.1	137.1	0.3
CCV24157	CV-24157	9/2/2026 1:17:03 PM	45.6	54.0	0.4	0.0			108.1	108.4	0.8
CCV24157	CV-24157	9/17/2026 2:54:47 PM	47.9	51.1	0.0	1.0			103.0	103.3	0.9
CCV24158	CV-24158	9/2/2026 1:50:00 PM	44.0	56.0	0.0	0.0			127.9	127.9	0.8
CCV24158	CV-24158	9/18/2026 9:48:59 AM	41.7	58.3	0.0	0.0			126.2	126.1	0.7
CCV24159	CV-24159	9/13/2026 10:18:12 AM	46.6	49.3	0.0	4.0			128.6	128.5	0.9
CCV24159	CV-24159	9/13/2026 10:19:02 AM	46.0	49.2	0.0	4.8			128.2	128.3	0.9
CCV24159	CV-24159	9/25/2026 11:34:39 AM	28.9	68.1	0.0	3.0			126.8	130.8	0.4
CCV24159	CV-24159	9/25/2026 11:37:32 AM	30.6	66.7	0.0	2.7			136.5	135.7	0.5
CCV24159	CV-24159	9/25/2026 11:38:14 AM	31.1	65.6	0.0	3.3			135.7	135.4	0.5
CCV24160	CV-24160	9/13/2026 10:07:13 AM	49.0	47.9	0.0	3.1			127.3	127.3	1.0
CCV24160	CV-24160	9/13/2026 10:08:00 AM	48.7	47.3	0.0	4.0			127.4	127.4	1.0
CCV24160	CV-24160	9/24/2026 2:00:04 PM	47.8	52.2	0.0	0.0			127.3	127.2	0.9
CCV24161	CV-24161	9/14/2026 1:18:54 PM	37.6	49.9	0.0	12.5			128.8	128.2	0.8
CCV24162	CV-24162	9/9/2026 1:08:06 PM	36.5	38.9	0.3	24.3			120.5	120.5	0.9
CCV24162	CV-24162	9/14/2026 1:22:08 PM	48.6	48.2	0.0	3.2			105.2	105.6	1.0
CCV24163	CV-24163	9/1/2026 9:47:08 AM	27.6	69.9	0.0	2.5			136.1	136.5	0.4
CCV24164	CV-24164	9/2/2026 9:23:46 AM	32.4	67.6	0.0	0.0			127.1	126.6	0.5
CCV24164	CV-24164	9/2/2026 9:26:17 AM	33.6	66.4	0.0	0.0			127.6	83.7	0.5
CCV24164	CV-24164	9/17/2026 2:06:22 PM	32.1	67.9	0.0	0.0			132.0	132.4	0.5
CCV24164	CV-24164	9/17/2026 2:07:38 PM	34.2	64.2	0.0	1.6			132.0	131.3	0.5
CCV24165	CV-24165	9/15/2026 1:44:17 PM	26.1	69.3	0.1	4.5			122.1	122.1	0.4
CCV24165	CV-24165	9/30/2026 1:54:12 PM	21.2	68.0	0.0	10.8			130.2	131.3	0.3
CCV24165	CV-24165	9/30/2026 2:18:26 PM	40.9	52.0	0.1	7.0			122.7	123.1	0.8
CCV24166	CV-24166	9/13/2026 10:25:03 AM	52.8	43.4	0.0	3.8			113.2	111.9	1.2
CCV24166	CV-24166	9/13/2026 10:25:58 AM	52.1	43.6	0.0	4.3			112.0	112.1	1.2
CCV24166	CV-24166	9/21/2026 8:17:14 AM	57.3	39.8	0.1	2.8			107.1	107.4	1.4
CCV24167	CV-24167	9/15/2026 9:35:57 AM	38.5	45.4	0.0	16.1			113.1	113.1	0.8
CCV24167	CV-24167	9/30/2026 1:45:26 PM	53.4	42.6	0.0	4.0			120.8	121.4	1.3

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24167	CV-24167	9/30/2026 1:46:57 PM	52.1	43.2	0.0	4.7			122.2	122.0	1.2
CCV24168	CV-24168	9/14/2026 2:05:52 PM	32.5	62.4	0.0	5.1			135.0	89.3	0.5
CCV24168	CV-24168	9/21/2026 9:52:58 AM	37.2	60.1	0.0	2.7			131.2	133.4	0.6
CCV24169	CV-24169	9/14/2026 2:01:29 PM	41.0	42.0	0.0	17.0			119.5	119.2	1.0
CCV24169	CV-24169	9/28/2026 10:50:36 AM	33.9	42.5	0.0	23.6			119.4	119.4	0.8
CCV24170	CV-24170	9/2/2026 9:09:47 AM	6.7	87.4	0.0	5.9			125.9	125.9	0.1
CCV24170	CV-24170	9/17/2026 1:45:21 PM	7.5	82.5	0.1	9.9			129.8	129.8	0.1
CCV24171	CV-24171	9/14/2026 1:31:04 PM	53.3	42.5	0.0	4.2			125.4	125.5	1.3
CCV24171	CV-24171	9/21/2026 8:30:41 AM	53.4	45.4	0.0	1.2			123.8	124.4	1.2
CCV24172	CV-24172	9/14/2026 1:41:43 PM	50.9	41.7	0.2	7.2			127.2	127.2	1.2
CCV24172	CV-24172	9/21/2026 9:04:18 AM	49.4	39.7	0.8	10.1			125.9	125.8	1.2
CCV24173	CV-24173	9/14/2026 1:49:58 PM	9.4	84.7	0.0	5.9			136.2	136.1	0.1
CCV24173	CV-24173	9/21/2026 9:21:07 AM	8.2	90.2	0.0	1.6			134.6	134.7	0.1
CCV24174	CV-24174	9/15/2026 1:52:08 PM	32.5	56.0	0.0	11.5			111.5	111.5	0.6
CCV24174	CV-24174	9/24/2026 8:32:37 AM	32.4	41.9	0.0	25.7			128.2	125.5	0.8
CCV24175	CV-24175	9/15/2026 9:24:45 AM	41.3	51.1	0.0	7.6			110.9	111.0	0.8
CCV24175	CV-24175	9/30/2026 8:57:29 AM	14.8	80.4	0.0	4.8			114.4	77.5	0.2
CCV24176	CV-24176	9/1/2026 11:15:56 AM	28.1	65.0	0.0	6.9			94.8	95.6	0.4
CCV24176	CV-24176	9/1/2026 11:16:38 AM	28.0	65.9	0.0	6.1			95.9	95.9	0.4
CCV24176	CV-24176	9/3/2026 10:17:38 AM	30.3	62.8	0.0	7.0			89.4	90.3	0.5
CCV24176	CV-24176	9/30/2026 9:16:05 AM	19.0	33.6	2.5	44.9			79.0	79.0	0.6
CCV24177	CV-24177	9/2/2026 7:09:30 AM	9.2	76.9	0.7	13.2			100.1	100.3	0.1
CCV24177	CV-24177	9/22/2026 12:56:38 PM	7.7	87.8	1.0	3.5			110.4	110.4	0.1
CCV24178	CV-24178	9/1/2026 2:59:57 PM	23.4	72.8	0.0	3.8			94.2	94.1	0.3
CCV24178	CV-24178	9/1/2026 3:02:27 PM	26.6	72.4	0.0	1.0			94.5	94.5	0.4
CCV24178	CV-24178	9/3/2026 10:29:19 AM	26.6	66.5	0.0	6.9			92.0	93.0	0.4
CCV24178	CV-24178	9/9/2026 2:38:51 PM	28.2	56.4	0.0	15.4			134.4	134.4	0.5
CCV24178	CV-24178	9/9/2026 2:41:36 PM	28.3	57.0	0.0	14.7			134.4	134.5	0.5
CCV24178	CV-24178	9/22/2026 1:58:45 PM	27.2	47.8	0.2	24.8			134.0	133.6	0.6

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24179	CV-24179	9/1/2026 11:22:17 AM	13.5	76.5	0.0	10.0			117.2	117.6	0.2
CCV24179	CV-24179	9/30/2026 11:41:43 AM	12.0	70.8	1.9	15.3			100.3	100.6	0.2
CCV24179	CV-24179	9/30/2026 11:42:38 AM	11.8	72.8	1.8	13.6			101.8	102.0	0.2
CCV24180	CV-24180	9/1/2026 3:04:20 PM	23.8	76.2	0.0	0.0			91.6	91.6	0.3
CCV24180	CV-24180	9/1/2026 3:05:55 PM	17.2	79.9	0.0	2.9			91.8	91.8	0.2
CCV24180	CV-24180	9/18/2026 4:27:56 PM	26.9	43.3	0.0	29.8			129.4	128.5	0.6
CCV24180	CV-24180	9/22/2026 3:35:15 PM	28.6	48.8	0.0	22.6			126.2	126.2	0.6
CCV24181	CV-24181	9/1/2026 2:56:29 PM	18.4	78.9	0.0	2.7			97.8	97.7	0.2
CCV24181	CV-24181	9/1/2026 2:57:27 PM	17.1	78.3	0.0	4.6			97.4	97.4	0.2
CCV24181	CV-24181	9/9/2026 2:02:35 PM	32.6	55.6	0.0	11.8			123.6	123.6	0.6
CCV24181	CV-24181	9/22/2026 3:27:56 PM	39.9	51.3	0.0	8.8			119.2	119.3	0.8
CCV24182	CV-24182	9/1/2026 2:49:50 PM	42.7	42.4	0.0	14.9			101.6	101.6	1.0
CCV24182	CV-24182	9/22/2026 3:17:59 PM	33.4	38.7	1.2	26.7			113.5	113.7	0.9
CCV24183	CV-24183	9/1/2026 2:44:48 PM	45.4	40.5	0.0	14.1			98.2	98.2	1.1
CCV24183	CV-24183	9/22/2026 2:15:06 PM	31.4	25.5	0.4	42.7			96.2	95.0	1.2
CCV24184	CV-24184	9/1/2026 2:29:37 PM	50.0	41.1	0.0	8.9			131.1	131.3	1.2
CCV24184	CV-24184	9/1/2026 2:34:21 PM	51.8	42.2	0.0	6.0			136.3	136.5	1.2
CCV24184	CV-24184	9/3/2026 12:22:14 PM	47.8	44.0	1.0	7.3			137.6	138.3	1.1
CCV24184	CV-24184	9/3/2026 12:23:03 PM	47.4	43.8	1.1	7.7			138.4	138.3	1.1
CCV24184	CV-24184	9/22/2026 2:21:19 PM	30.8	28.5	4.9	35.8			129.7	130.0	1.1
CCV24185	CV-24185	9/1/2026 2:19:32 PM	51.2	45.6	0.0	3.2			125.9	127.5	1.1
CCV24185	CV-24185	9/1/2026 2:20:58 PM	48.4	51.6	0.0	0.0			127.6	127.6	0.9
CCV24185	CV-24185	9/3/2026 12:38:20 PM	49.0	48.5	0.0	2.5			125.4	125.3	1.0
CCV24185	CV-24185	9/22/2026 2:34:09 PM	30.2	27.8	7.9	34.1			124.2	124.1	1.1
CCV24185	CV-24185	9/22/2026 2:35:54 PM	48.4	42.6	0.1	8.9			124.1	124.1	1.1
CCV24186	CV-24186	9/15/2026 10:32:27 AM	45.1	34.9	1.7	18.3			125.0	124.9	1.3
CCV24186	CV-24186	9/22/2026 2:42:35 PM	49.9	39.4	0.5	10.2			125.5	126.2	1.3
CCV24187	CV-24187	9/2/2026 9:24:10 AM	50.2	45.5	0.0	4.3			124.3	124.4	1.1
CCV24187	CV-24187	9/22/2026 12:48:46 PM	45.0	53.1	0.0	1.9			126.5	126.6	0.8

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24187	CV-24187	9/22/2026 2:45:38 PM	50.2	40.7	0.1	9.0			107.3	107.5	1.2
CCV24188	CV-24188	9/2/2026 8:53:02 AM	49.3	45.6	0.0	5.1			117.4	117.5	1.1
CCV24188	CV-24188	9/22/2026 10:14:23 AM	51.4	44.0	0.0	4.6			117.1	117.9	1.2
CCV24189	CV-24189	9/2/2026 8:58:47 AM	43.5	34.4	3.5	18.6			108.9	108.2	1.3
CCV24189	CV-24189	9/22/2026 10:07:55 AM	54.3	41.7	0.0	4.0			100.0	104.3	1.3
CCV24189	CV-24189	9/22/2026 10:08:53 AM	53.0	41.3	0.3	5.4			105.0	105.6	1.3
CCV24190	CV-24190	9/2/2026 9:15:42 AM	52.9	42.9	0.0	4.2			123.1	123.6	1.2
CCV24190	CV-24190	9/22/2026 12:45:58 PM	46.2	53.3	0.5	0.0			122.3	119.9	0.9
CCV24192	CV-24192	9/2/2026 9:12:33 AM	54.5	41.4	0.0	4.1			119.7	119.8	1.3
CCV24192	CV-24192	9/4/2026 1:39:12 PM	52.3	41.0	0.0	6.7			121.5	121.4	1.3
CCV24192	CV-24192	9/22/2026 12:39:10 PM	54.4	44.1	1.5	0.0			118.9	119.7	1.2
CCV24193	CV-24193	9/1/2026 11:28:13 AM	44.2	42.8	0.0	13.0			117.6	117.7	1.0
CCV24193	CV-24193	9/21/2026 11:49:20 AM	50.8	42.7	0.0	6.5			119.3	119.3	1.2
CCV24194	CV-24194	9/1/2026 1:49:41 PM	53.0	38.0	0.3	8.7			106.3	106.3	1.4
CCV24194	CV-24194	9/3/2026 10:43:30 AM	49.6	47.6	0.0	2.9			107.5	107.6	1.0
CCV24194	CV-24194	9/21/2026 12:40:02 PM	50.4	44.9	0.0	4.7			106.0	106.1	1.1
CCV24194	CV-24194	9/21/2026 12:42:15 PM	51.6	44.6	0.0	3.8			106.6	106.5	1.2
CCV24195	CV-24195	9/1/2026 1:57:58 PM	51.7	44.9	0.0	3.4			118.6	118.7	1.2
CCV24195	CV-24195	9/3/2026 11:04:13 AM	41.2	42.6	0.1	16.1			118.1	118.1	1.0
CCV24195	CV-24195	9/21/2026 12:26:17 PM	49.5	46.2	0.0	4.3			119.7	119.8	1.1
CCV24195	CV-24195	9/22/2026 3:15:01 PM	51.2	44.8	0.0	4.0			117.6	118.1	1.1
CCV24196	CV-24196	9/1/2026 2:06:39 PM	46.4	48.4	0.2	5.0			123.6	123.6	1.0
CCV24196	CV-24196	9/22/2026 3:03:17 PM	46.2	52.6	0.0	1.2			123.9	123.7	0.9
CCV24197	CV-24197	9/1/2026 2:10:01 PM	44.9	42.7	0.0	12.4			124.4	124.4	1.1
CCV24197	CV-24197	9/22/2026 2:56:45 PM	47.1	45.3	0.0	7.6			128.4	126.6	1.0
CCV24198	CV-24198	9/15/2026 12:38:31 PM	35.4	36.4	0.0	28.2			128.2	128.0	1.0
CCV24198	CV-24198	9/15/2026 12:40:21 PM	34.8	36.6	0.0	28.6			127.9	127.7	1.0
CCV24198	CV-24198	9/30/2026 1:17:46 PM	47.5	41.0	0.0	11.5			125.8	126.1	1.2
CCV24199	CV-24199	9/15/2026 12:27:13 PM	46.5	39.6	0.0	13.9			128.5	128.4	1.2

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24199	CV-24199	9/15/2026 12:29:31 PM	46.4	40.6	0.0	13.0			128.4	128.4	1.1
CCV24199	CV-24199	9/30/2026 1:27:46 PM	51.6	44.8	0.0	3.6			127.9	128.8	1.2
CCV24200	CV-24200	9/15/2026 9:58:46 AM	45.0	39.2	0.0	15.8			120.9	120.9	1.1
CCV24200	CV-24200	9/15/2026 9:59:38 AM	45.1	38.6	0.0	16.3			120.9	120.9	1.2
CCV24200	CV-24200	9/30/2026 1:33:17 PM	51.3	40.6	0.0	8.1			121.7	121.8	1.3
CCV24201	CV-24201	9/15/2026 10:10:20 AM	48.3	46.4	0.1	5.2			109.5	124.0	1.0
CCV24201	CV-24201	9/15/2026 10:11:55 AM	49.0	46.3	0.0	4.7			125.4	125.4	1.1
CCV24201	CV-24201	9/15/2026 10:14:30 AM	48.6	46.7	0.0	4.7			126.6	125.0	1.0
CCV24201	CV-24201	9/24/2026 1:50:00 PM					24.3				
CCV24201	CV-24201	9/24/2026 1:50:00 PM						1000			
CCV24201	CV-24201	9/24/2026 1:50:04 PM						23000			
CCV24201	CV-24201	9/24/2026 1:50:55 PM	48.7	47.3	0.0	4.0			119.2	119.0	1.0
CCV24201	CV-24201	9/24/2026 2:48:38 PM					20				
CCV24201	CV-24201	9/28/2026 8:40:33 AM	47.4	47.2	0.0	5.5			93.1	124.2	1.0
CCV24201	CV-24201	9/28/2026 8:44:14 AM	47.9	47.5	0.0	4.6			127.9	128.6	1.0
CCV24202	CV-24202	9/15/2026 4:15:49 PM	26.8	32.7	0.0	40.5			125.4	121.0	0.8
CCV24202	CV-24202	9/15/2026 4:17:09 PM	26.1	32.5	0.0	41.4			119.7	119.9	0.8
CCV24202	CV-24202	9/23/2026 10:59:35 AM	35.4	39.2	0.0	25.4			127.1	127.2	0.9
CCV24202	CV-24202	9/24/2026 1:32:57 PM						16000			
CCV24202	CV-24202	9/24/2026 1:35:00 PM					11.8				
CCV24202	CV-24202	9/24/2026 1:35:00 PM						1000			
CCV24202	CV-24202	9/24/2026 1:35:03 PM	36.3	38.6	0.0	25.0			118.2	118.4	0.9
CCV24202	CV-24202	9/24/2026 3:14:01 PM					10				
CCV24203	CV-24203	9/15/2026 9:25:44 AM	53.3	42.4	0.0	4.3			122.8	123.0	1.3
CCV24203	CV-24203	9/15/2026 9:28:02 AM	53.1	42.4	0.0	4.5			123.3	123.8	1.3
CCV24203	CV-24203	9/24/2026 12:50:00 PM					11.9				
CCV24203	CV-24203	9/24/2026 12:50:00 PM						1400			
CCV24203	CV-24203	9/24/2026 12:53:25 PM						39000			
CCV24203	CV-24203	9/24/2026 12:54:25 PM	51.8	43.9	0.0	4.3			124.1	124.2	1.2

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24203	CV-24203	9/24/2026 2:54:50 PM					25				
CCV24204	CV-24204	9/15/2026 9:12:51 AM	51.7	44.0	0.0	4.3			126.9	126.9	1.2
CCV24204	CV-24204	9/15/2026 9:15:00 AM	50.7	44.6	0.0	4.7			127.0	127.2	1.1
CCV24204	CV-24204	9/15/2026 9:15:53 AM	50.2	45.7	0.0	4.1			127.2	127.2	1.1
CCV24204	CV-24204	9/25/2026 9:17:43 AM	49.5	45.4	0.0	5.1			127.3	127.3	1.1
CCV24205	CV-24205	9/15/2026 9:07:09 AM	54.0	41.1	0.0	4.9			124.0	124.1	1.3
CCV24205	CV-24205	9/15/2026 9:08:01 AM	52.9	41.7	0.0	5.4			124.2	124.1	1.3
CCV24205	CV-24205	9/30/2026 4:14:08 PM	50.3	44.5	0.0	5.2			125.0	125.0	1.1
CCV24206	CV-24206	9/15/2026 9:41:41 AM	36.4	41.1	3.9	18.6			82.1	81.9	0.9
CCV24206	CV-24206	9/15/2026 9:45:15 AM	44.2	48.1	0.2	7.5			82.3	82.3	0.9
CCV24206	CV-24206	9/23/2026 10:43:02 AM	46.1	46.6	0.9	6.4			106.7	107.9	1.0
CCV24206	CV-24206	9/23/2026 10:44:23 AM	49.0	50.1	0.0	0.9			108.9	109.1	1.0
CCV24206	CV-24206	9/24/2026 12:30:00 PM					11.1				
CCV24206	CV-24206	9/24/2026 12:30:00 PM						3700			
CCV24206	CV-24206	9/24/2026 12:33:26 PM						35000			
CCV24206	CV-24206	9/24/2026 12:37:06 PM	46.1	41.2	0.0	12.7			92.7	93.5	1.1
CCV24206	CV-24206	9/24/2026 12:39:33 PM	46.4	39.9	0.0	13.6			101.6	101.8	1.2
CCV24206	CV-24206	9/24/2026 3:07:10 PM					40				
CCV24207	CV-24207	9/3/2026 12:47:00 PM	40.1	56.1	0.0	3.8			127.3	136.1	0.7
CCV24207	CV-24207	9/3/2026 12:48:27 PM	39.0	57.9	0.0	3.1			136.4	136.5	0.7
CCV24207	CV-24207	9/13/2026 1:29:48 PM	47.7	47.2	0.0	5.0			135.8	135.7	1.0
CCV24207	CV-24207	9/13/2026 1:32:35 PM	48.0	47.2	0.0	4.8			135.5	135.3	1.0
CCV24207	CV-24207	9/13/2026 1:35:07 PM	48.1	46.8	0.0	5.1			135.2	134.6	1.0
CCV24207	CV-24207	9/13/2026 1:35:54 PM	47.9	47.2	0.0	4.9			133.9	133.8	1.0
CCV24207	CV-24207	9/21/2026 8:26:11 AM	46.1	53.5	0.0	0.4			126.8	130.2	0.9
CCV24208	CV-24208	9/24/2026 10:14:51 AM	41.7	57.4	0.0	0.9			131.8	131.8	0.7
CCV24208	CV-24208	9/24/2026 10:16:08 AM	41.4	57.6	0.0	1.0			128.4	128.6	0.7
CCV24209	CV-24209	9/30/2026 2:11:34 PM	10.0	73.8	0.0	16.2			131.6	131.9	0.1
CCV24210	CV-24210	9/9/2026 1:42:55 PM	29.9	35.8	0.0	34.3			123.7	124.2	0.8



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24211	CV-24211	9/28/2026 2:53:00 PM	15.8	76.6	0.3	7.3			114.4	99.5	0.2
CCV24212	CV-24212	9/28/2026 2:46:21 PM	9.3	70.2	0.8	19.7			118.1	110.9	0.1
CCV24213	CV-24213	9/4/2026 9:21:22 AM	43.1	47.2	0.0	9.8			111.4	112.8	0.9
CCV24214	CV-24214	9/30/2026 1:49:40 PM	13.7	58.1	0.0	28.2			115.4	115.6	0.2
CCV24215	CV-24215	9/30/2026 1:28:04 PM	44.4	50.1	0.0	5.5			119.7	119.7	0.9
CCV24216	CV-24216	9/16/2026 11:46:26 AM	39.1	40.2	0.0	20.7			124.0	121.6	1.0
CCV24217	CV-24217	9/3/2026 1:30:59 PM	41.0	58.2	0.0	0.8			109.0	109.0	0.7
CCV24218	CV-24218	9/14/2026 1:37:55 PM	44.4	50.1	0.0	5.5			124.9	124.7	0.9
CCV24219	CV-24219	9/1/2026 9:17:40 AM	13.9	82.1	0.0	4.0			183.9	183.8	0.2
CCV24219	CV-24219	9/1/2026 9:23:00 AM						110300			
CCV24219	CV-24219	9/1/2026 9:23:00 AM					3280				
CCV24219	CV-24219	9/9/2026 10:37:30 AM	17.7	74.4	0.0	7.9			185.1	185.2	0.2
CCV24219	CV-24219	9/9/2026 10:37:57 AM	24.9	75.1	0.0	0.0			185.3	185.2	0.3
CCV24219	CV-24219	9/9/2026 10:42:00 AM					2315				
CCV24219	CV-24219	9/15/2026 1:45:00 PM					3440				
CCV24219	CV-24219	9/15/2026 1:50:49 PM	12.3	76.9	0.0	10.8			189.6	189.5	0.2
CCV24219	CV-24219	9/15/2026 1:52:47 PM	15.5	80.2	0.0	4.3			189.5	189.5	0.2
CCV24219	CV-24219	9/22/2026 2:24:19 PM	16.2	83.1	0.0	0.7			187.8	187.7	0.2
CCV24219	CV-24219	9/22/2026 2:26:00 PM					1340				
CCV24219	CV-24219	9/29/2026 1:44:55 PM	22.6	77.1	0.2	0.1			185.6	186.1	0.3
CCV24219	CV-24219	9/29/2026 1:45:41 PM	22.4	76.6	0.0	1.0			187.0	187.5	0.3
CCV24219	CV-24219	9/29/2026 1:50:00 PM					2530				
CCV24220	CV-24220	9/1/2026 9:58:34 AM	21.7	50.7	1.2	26.4			147.3	147.7	0.4
CCV24220	CV-24220	9/8/2026 9:02:20 AM	18.5	43.8	2.2	35.5			140.2	130.5	0.4
CCV24220	CV-24220	9/8/2026 9:07:51 AM	13.9	58.9	0.8	26.4			129.9	129.5	0.2
CCV24221	CV-24221	9/28/2026 2:25:52 PM	30.3	35.9	0.1	33.7			129.3	125.8	0.8
CCV24222	CV-24222	9/30/2026 8:21:47 AM	50.0	40.5	0.0	9.5			121.8	121.8	1.2
CCV24223	CV-24223	9/28/2026 2:38:35 PM	35.3	54.7	0.2	9.8			125.0	125.0	0.6
CCV24224	CV-24224	9/30/2026 9:30:13 AM	47.9	47.9	0.0	4.2			80.5	81.0	1.0

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CCV24224	CV-24224	9/30/2026 9:30:54 AM	48.8	47.6	0.0	3.6			81.5	81.5	1.0
CCV24224	CV-24224	9/30/2026 2:00:06 PM	52.2	42.9	0.0	4.9			111.3	111.4	1.2
CCV24225	CV-24225	9/1/2026 9:07:25 AM	48.4	49.1	0.5	2.0			120.5	120.6	1.0
CCV24226	CV-24226	9/28/2026 2:56:01 PM	50.5	48.6	0.2	0.7			111.7	111.6	1.0
CCV24227	CV-24227	9/2/2026 9:09:03 AM	55.9	42.0	0.0	2.1			117.4	117.6	1.3
CCV24227	CV-24227	9/4/2026 1:33:49 PM	52.9	40.8	0.0	6.3			118.8	118.7	1.3
CCV24227	CV-24227	9/22/2026 12:30:13 PM	51.2	48.8	0.0	0.0			118.0	118.0	1.0
CCV24231	CV-24231	9/30/2026 12:42:54 PM	44.0	44.0	0.0	12.0			127.6	127.5	1.0
CCV24236	CV-24236	9/2/2026 1:22:24 PM	54.2	37.6	0.0	8.2			107.3	107.3	1.4
CCV24237	CV-24237	9/2/2026 1:11:47 PM	59.2	35.9	1.4	3.5			112.1	112.3	1.6
CCV24237	CV-24237	9/4/2026 2:04:02 PM	39.0	40.2	1.3	19.5			112.8	112.9	1.0
CCV24243	CV-24243	9/17/2026 12:16:52 PM	48.3	37.6	1.6	12.5			117.9	120.9	1.3
CCV24243	CV-24243	9/17/2026 12:30:09 PM	27.2	23.9	8.6	40.4			121.2	120.8	1.1
CCV24243	CV-24243	9/17/2026 12:37:43 PM	28.8	25.7	8.5	37.1			120.5	120.6	1.1
CCV24243	CV-24243	9/22/2026 1:52:57 PM	43.0	34.7	3.6	18.7			115.7	115.8	1.2
CCV24244	CV-24244	9/16/2026 8:41:03 AM	49.0	38.8	0.3	11.8			112.8	112.7	1.3
CCV24244	CV-24244	9/16/2026 8:43:19 AM	48.5	39.0	0.5	12.0			112.7	112.6	1.2
CCV24245	CV-24245	9/28/2026 10:15:21 AM	48.2	40.5	0.0	11.3			117.2	117.7	1.2
CCV24245	CV-24245	9/28/2026 10:17:16 AM	47.7	40.9	0.0	11.4			117.8	117.7	1.2
CCV24246	CV-24246	9/4/2026 9:59:35 AM	52.5	44.0	0.0	3.5			117.9	121.5	1.2
CCV24246	CV-24246	9/4/2026 10:00:29 AM	52.0	43.9	0.0	4.1			121.7	121.8	1.2
CCV24253	CV-24253	9/28/2026 9:37:51 AM	50.0	41.3	0.0	8.7			105.9	107.2	1.2
CCV24253	CV-24253	9/28/2026 9:39:46 AM	49.4	41.7	0.0	9.0			105.9	107.5	1.2
CHIWCV25	CV-25	9/21/2026 8:45:49 AM	54.9	42.2	0.0	2.9			89.9	90.2	1.3
CHCV2501	CV-2501	9/4/2026 1:08:58 PM	51.7	43.0	0.0	5.3			128.7	128.6	1.2
CHCV2502	CV-2502	9/11/2026 10:11:06 AM	56.8	35.9	0.0	7.3			114.6	120.3	1.6
CHCV2502	CV-2502	9/11/2026 10:12:18 AM	56.5	39.0	0.0	4.5			122.0	122.0	1.4
CHCV2503	CV-2503	9/11/2026 10:21:39 AM	45.5	32.1	0.0	22.4			130.3	130.4	1.4
CHCV2503	CV-2503	9/23/2026 12:40:37 PM	43.5	37.7	0.0	18.8			130.2	130.2	1.2

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2504	CV-2504	9/23/2026 10:20:47 AM	48.4	40.8	0.0	10.9			129.9	130.1	1.2
CHCV2504	CV-2504	9/23/2026 10:23:26 AM	47.3	41.2	0.0	11.5			130.2	130.1	1.1
CHCV2505	CV-2505	9/23/2026 12:39:50 PM	50.7	42.5	0.0	6.9			127.2	127.3	1.2
CHCV2506	CV-2506	9/23/2026 12:41:42 PM	49.9	42.3	0.0	7.8			127.2	127.2	1.2
CHCV2506	CV-2506	9/23/2026 1:16:38 PM	46.3	41.5	0.0	12.2			123.2	123.2	1.1
CHCV2507	CV-2507	9/23/2026 1:33:01 PM	52.1	42.8	0.0	5.1			126.7	126.6	1.2
CHCV2507	CV-2507	9/23/2026 1:36:04 PM	52.4	42.6	0.0	5.1			126.6	126.6	1.2
CHCV2508	CV-2508	9/23/2026 2:08:04 PM	49.7	41.7	0.0	8.6			121.7	121.7	1.2
CHCV2509	CV-2509	9/4/2026 10:15:57 AM	49.3	42.7	0.0	8.0			117.0	117.0	1.2
CHCV2510	CV-2510	9/4/2026 10:06:27 AM	52.7	43.2	0.0	4.1			116.1	116.1	1.2
CV25100D	CV-25100D	9/3/2026 10:05:34 AM	12.4	64.9	0.1	22.6			147.9	149.5	0.2
CV25100D	CV-25100D	9/3/2026 10:06:21 AM	12.4	64.9	0.3	22.4			148.9	151.1	0.2
CV25100D	CV-25100D	9/3/2026 10:34:00 AM					771				
CV25100D	CV-25100D	9/3/2026 10:34:00 AM						63000			
CV25100D	CV-25100D	9/8/2026 1:58:00 PM					798				
CV25100D	CV-25100D	9/8/2026 1:58:37 PM	13.7	62.5	0.5	23.3			159.4	157.5	0.2
CV25100D	CV-25100D	9/14/2026 1:43:20 PM	30.1	47.6	0.1	22.2			123.5	123.2	0.6
CV25100D	CV-25100D	9/25/2026 2:09:25 PM	11.9	42.0	0.2	45.9			120.2	120.4	0.3
CV25100S	CV-25100S	9/8/2026 1:54:00 PM					2660				
CV25100S	CV-25100S	9/8/2026 1:54:17 PM	3.6	76.2	0.0	20.2			189.0	188.5	0.0
CV25100S	CV-25100S	9/14/2026 1:46:48 PM	19.1	63.9	0.0	17.0			176.4	176.4	0.3
CV25100S	CV-25100S	9/14/2026 1:47:00 PM					3330				
CV25100S	CV-25100S	9/21/2026 1:22:46 PM	11.6	72.0	0.0	16.4			178.4	178.6	0.2
CV25100S	CV-25100S	9/21/2026 1:24:00 PM					2790				
CV25100S	CV-25100S	9/28/2026 1:43:54 PM	8.7	79.9	0.0	11.4			164.0	164.2	0.1
CV25100S	CV-25100S	9/28/2026 1:55:00 PM					1910				
CV25101D	CV-25101D	9/3/2026 9:32:55 AM	23.2	46.3	0.0	30.5			128.9	128.8	0.5
CV25101D	CV-25101D	9/22/2026 10:51:18 AM	18.2	37.7	0.1	44.0			127.5	127.5	0.5
CV25101S	CV-25101S	9/3/2026 9:34:39 AM	5.9	27.5	0.1	66.5			108.8	109.1	0.2

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CV25101S	CV-25101S	9/22/2026 10:53:04 AM	4.5	21.1	1.0	73.4			115.4	115.7	0.2
CV25102_	CV-25102	9/14/2026 9:45:37 AM	1.6	81.6	0.0	16.8			198.1	200.1	0.0
CV25102_	CV-25102	9/14/2026 9:46:33 AM	1.6	81.6	0.0	16.8			200.4	200.4	0.0
CV25102_	CV-25102	9/14/2026 1:20:00 PM					1660				
CV25102_	CV-25102	9/21/2026 9:40:00 AM					1260				
CV25102_	CV-25102	9/21/2026 9:46:14 AM	1.7	77.4	0.3	20.6			179.6	179.4	0.0
CV25102_	CV-25102	9/21/2026 9:48:39 AM	2.1	76.8	0.3	20.8			174.0	174.6	0.0
CV25102_	CV-25102	9/28/2026 10:49:11 AM	15.7	71.1	0.0	13.2			185.8	185.9	0.2
CV25102_	CV-25102	9/28/2026 1:05:00 PM					1810				
CV25102_	CV-25102	9/30/2026 8:30:50 AM	1.9	78.6	0.4	19.1			196.3	196.4	0.0
CV25102_	CV-25102	9/30/2026 8:32:19 AM	1.8	78.5	0.1	19.6			196.5	196.4	0.0
CV25103_	CV-25103	9/3/2026 9:09:00 AM	21.7	32.9	2.7	42.7			116.8	117.3	0.7
CV25103_	CV-25103	9/22/2026 10:46:56 AM	19.1	25.9	4.4	50.6			112.5	111.9	0.7
CV25104D	CV-25104D	9/15/2026 9:02:09 AM	3.7	79.7	0.0	16.6			135.0	129.5	0.0
CV25104D	CV-25104D	9/15/2026 9:02:43 AM	3.6	82.7	0.0	13.7			128.8	128.7	0.0
CV25104D	CV-25104D	9/23/2026 1:35:53 PM	3.6	80.1	0.2	16.1			152.5	155.2	0.0
CV25104S	CV-25104S	9/14/2026 9:28:09 AM	12.0	71.6	0.0	16.4			174.0	174.2	0.2
CV25104S	CV-25104S	9/14/2026 9:28:26 AM	11.9	72.7	0.0	15.4			174.0	174.2	0.2
CV25104S	CV-25104S	9/21/2026 10:03:05 AM	13.6	65.3	0.0	21.1			118.0	118.0	0.2
CV25104S	CV-25104S	9/30/2026 9:51:41 AM	9.5	71.3	0.0	19.2			118.4	118.0	0.1
CV25105D	CV-25105D	9/3/2026 8:36:30 AM	0.4	2.0	20.3	77.3			70.0	70.0	0.2
CV25105D	CV-25105D	9/3/2026 8:39:20 AM	4.6	19.5	14.7	61.2			69.4	68.9	0.2
CV25105D	CV-25105D	9/25/2026 11:09:43 AM	12.0	78.2	0.1	9.7			134.0	134.0	0.2
CV25105D	CV-25105D	9/25/2026 11:12:40 AM	11.4	78.3	0.0	10.3			134.0	134.0	0.1
CV25105S	CV-25105S	9/3/2026 8:42:42 AM	0.0	2.5	20.3	77.2			83.1	83.1	0.0
CV25105S	CV-25105S	9/3/2026 8:43:52 AM	0.0	1.7	20.4	77.9			67.3	67.1	0.0
CV25105S	CV-25105S	9/25/2026 10:57:59 AM	2.1	2.9	16.9	78.1			98.5	98.3	0.7
CV25105S	CV-25105S	9/25/2026 10:59:33 AM	2.1	3.0	17.1	77.8			98.6	98.6	0.7
CV25106D	CV-25106D	9/14/2026 9:16:26 AM	40.0	58.6	0.3	1.1			81.3	81.3	0.7



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CV25106D	CV-25106D	9/21/2026 2:39:29 PM	20.7	62.2	2.8	14.3			108.1	108.3	0.3
CV25106S	CV-25106S	9/15/2026 9:01:26 AM	19.4	34.1	5.8	40.7			77.3	77.3	0.6
CV25106S	CV-25106S	9/15/2026 9:02:41 AM	19.1	34.8	5.5	40.6			77.3	77.1	0.5
CV25106S	CV-25106S	9/21/2026 2:36:58 PM	7.5	14.0	15.8	62.7			96.1	96.1	0.5
CV25107D	CV-25107D	9/1/2026 9:37:00 AM					4190				
CV25107D	CV-25107D	9/1/2026 9:37:00 AM						110100			
CV25107D	CV-25107D	9/1/2026 9:41:08 AM	2.6	0.0	19.7	77.7			169.5	168.9	
CV25107D	CV-25107D	9/1/2026 9:49:48 AM	10.8	53.7	7.0	28.5			168.5	167.7	0.2
CV25107D	CV-25107D	9/1/2026 9:52:33 AM	15.3	76.3	1.4	7.0			167.4	167.5	0.2
CV25107D	CV-25107D	9/1/2026 10:04:00 AM						110100			
CV25107D	CV-25107D	9/9/2026 10:27:10 AM	12.6	80.1	0.0	7.3			172.9	172.7	0.2
CV25107D	CV-25107D	9/9/2026 10:32:44 AM	12.1	59.9	4.2	23.8			173.4	173.3	0.2
CV25107D	CV-25107D	9/9/2026 10:33:42 AM	12.2	63.9	0.8	23.1			173.5	173.8	0.2
CV25107D	CV-25107D	9/9/2026 10:35:00 AM					3410				
CV25107D	CV-25107D	9/15/2026 1:35:00 PM					4090				
CV25107D	CV-25107D	9/15/2026 1:35:50 PM	12.2	79.1	0.0	8.7			173.5	173.2	0.2
CV25107D	CV-25107D	9/15/2026 1:39:57 PM	10.4	76.2	0.0	13.4			175.4	175.9	0.1
CV25107D	CV-25107D	9/22/2026 2:13:00 PM					108				
CV25107D	CV-25107D	9/22/2026 2:20:08 PM	11.8	49.7	2.8	35.7			164.9	165.1	0.2
CV25107D	CV-25107D	9/29/2026 1:39:25 PM	11.1	38.8	7.9	42.2			163.8	167.1	0.3
CV25107D	CV-25107D	9/29/2026 1:40:00 PM					3530				
CV25107S	CV-25107S	9/3/2026 12:53:12 PM	2.4	87.1	0.0	10.5			103.2	103.2	0.0
CV25107S	CV-25107S	9/22/2026 10:17:17 AM	46.2	50.8	0.1	2.9			143.9	142.6	0.9
CV25107S	CV-25107S	9/22/2026 10:19:04 AM	49.2	47.0	0.1	3.7			144.0	143.0	1.0
CHCV2511	CV-2511	9/30/2026 1:02:49 PM	51.1	43.8	0.0	5.1			127.4	127.3	1.2
CHCV2512	CV-2512	9/4/2026 10:31:39 AM	44.0	42.6	0.0	13.4			125.3	125.4	1.0
CHCV2513	CV-2513	9/17/2026 1:56:08 PM	53.7	42.1	0.0	4.2			121.8	121.7	1.3
CHCV2513	CV-2513	9/17/2026 1:59:17 PM	52.8	42.0	0.0	5.2			121.7	121.7	1.3
CHCV2514	CV-2514	9/21/2026 10:01:35 AM	53.7	42.0	0.0	4.3			127.4	127.5	1.3

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2514	CV-2514	9/21/2026 10:07:35 AM	53.4	41.8	0.0	4.8			127.8	127.8	1.3
CHCV2515	CV-2515	9/29/2026 10:32:00 AM	43.7	37.5	0.0	18.9			115.7	115.1	1.2
CHCV2515	CV-2515	9/29/2026 10:36:37 AM	43.4	38.0	0.0	18.6			114.8	115.2	1.1
CHCV2515	CV-2515	9/29/2026 10:37:18 AM	43.5	38.2	0.0	18.4			115.2	115.2	1.1
CHCV2515	CV-2515	9/29/2026 10:40:01 AM	43.5	38.2	0.0	18.4			115.2	115.3	1.1
CHCV2516	CV-2516	9/16/2026 11:55:45 AM	50.1	42.2	0.0	7.7			128.0	127.9	1.2
CHCV2517	CV-2517	9/21/2026 9:13:49 AM	40.0	35.3	0.0	24.7			115.5	116.0	1.1
CHCV2518	CV-2518	9/21/2026 9:35:14 AM	52.5	38.3	0.0	9.2			109.8	110.3	1.4
CHCV2519	CV-2519	9/22/2026 2:34:58 PM	46.4	41.4	0.1	12.1			122.8	122.7	1.1
CHCV2520	CV-2520	9/22/2026 2:46:22 PM	34.1	50.4	0.0	15.5			135.9	134.9	0.7
CHCV2520	CV-2520	9/22/2026 2:48:41 PM	34.2	51.3	0.0	14.5			134.0	134.0	0.7
CHCV2521	CV-2521	9/30/2026 8:54:33 AM	45.7	43.6	0.0	10.7			105.5	105.4	1.0
CHCV2521	CV-2521	9/30/2026 12:10:46 PM	44.0	46.6	0.0	9.4			138.9	138.1	0.9
CHCV2521	CV-2521	9/30/2026 12:11:47 PM	45.0	44.6	0.0	10.4			137.8	138.0	1.0
CHCV2522	CV-2522	9/22/2026 3:06:29 PM	41.8	45.5	0.0	12.7			132.8	131.3	0.9
CHCV2522	CV-2522	9/22/2026 3:07:55 PM	43.6	44.3	0.0	12.1			129.3	129.4	1.0
CHCV2523	CV-2523	9/25/2026 11:36:15 AM	47.8	41.7	0.0	10.5			126.8	126.8	1.1
CHCV2524	CV-2524	9/22/2026 3:14:40 PM	32.2	40.5	1.0	26.3			138.1	126.7	0.8
CHCV2524	CV-2524	9/22/2026 3:18:41 PM	33.0	37.6	0.9	28.5			122.1	121.8	0.9
CHCV2525	CV-2525	9/25/2026 11:17:14 AM	32.3	32.4	0.1	35.2			119.3	119.2	1.0
CHCV2526	CV-2526	9/29/2026 9:14:52 AM	47.4	39.0	0.0	13.5			122.5	122.7	1.2
CHCV2527	CV-2527	9/14/2026 8:36:25 AM	46.4	43.6	0.1	9.9			132.5	132.5	1.1
CHCV2527	CV-2527	9/14/2026 8:37:20 AM	45.8	44.0	0.0	10.2			132.6	132.2	1.0
CHCV2527	CV-2527	9/30/2026 9:05:03 AM	5.7	50.4	0.0	44.0			86.7	86.4	0.1
CHCV2527	CV-2527	9/30/2026 9:07:01 AM	5.4	52.2	0.0	42.4			86.1	86.1	0.1
CHCV2527	CV-2527	9/30/2026 9:11:36 AM	5.0	52.6	0.0	42.4			86.4	84.6	0.1
CHCV2527	CV-2527	9/30/2026 9:12:30 AM	5.1	52.9	0.0	42.1			84.6	84.5	0.1
CHCV2527	CV-2527	9/30/2026 12:24:57 PM	10.0	54.3	0.0	35.7			110.5	113.7	0.2
CHCV2527	CV-2527	9/30/2026 12:26:17 PM	12.2	54.5	0.0	33.3			114.6	114.6	0.2

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2528	CV-2528	9/21/2026 10:33:20 AM	43.4	35.8	0.0	20.8			110.6	110.5	1.2
CHCV2529	CV-2529	9/4/2026 8:05:25 AM	55.1	39.4	0.7	4.7			77.4	80.4	1.4
CHCV2529	CV-2529	9/4/2026 8:07:06 AM	51.6	39.1	1.3	8.0			80.6	80.6	1.3
CHCV2530	CV-2530	9/28/2026 3:53:58 PM	45.3	47.4	0.2	7.1			107.9	109.9	1.0
CHCV2531	CV-2531	9/28/2026 3:43:12 PM	35.2	53.1	0.2	11.5			113.6	113.3	0.7
CHCV2532	CV-2532	9/30/2026 8:40:47 AM	51.5	42.4	0.2	5.9			97.1	97.6	1.2
CHCV2533	CV-2533	9/28/2026 3:24:49 PM	43.0	36.2	3.6	17.2			128.2	127.4	1.2
CHCV2534	CV-2534	9/1/2026 11:25:42 AM	33.8	46.3	0.0	19.9			110.6	110.6	0.7
CHCV2534	CV-2534	9/28/2026 3:16:57 PM	51.6	48.3	0.0	0.1			100.4	100.7	1.1
CHCV2535	CV-2535	9/23/2026 12:53:43 PM	45.5	39.3	0.0	15.3			115.5	115.2	1.2
CHCV2536	CV-2536	9/25/2026 9:51:12 AM	48.1	43.1	1.3	7.5			98.2	98.2	1.1
CHCV2537	CV-2537	9/25/2026 9:09:18 AM	47.0	39.2	0.0	13.8			118.6	118.7	1.2
CHCV2538	CV-2538	9/25/2026 8:54:18 AM	50.2	40.9	0.0	9.0			114.5	114.4	1.2
CHCV2539	CV-2539	9/15/2026 10:51:41 AM	44.0	42.3	0.0	13.7			120.5	120.3	1.0
CHCV2539	CV-2539	9/21/2026 12:01:09 PM	41.3	43.2	0.0	15.5			122.6	122.3	1.0
CHCV2540	CV-2540	9/2/2026 9:19:21 AM	15.9	80.1	0.0	4.0			138.4	138.6	0.2
CHCV2540	CV-2540	9/17/2026 1:58:14 PM	7.6	81.6	0.0	10.8			138.7	138.9	0.1
CHCV2541	CV-2541	9/1/2026 10:53:11 AM	21.9	63.8	0.0	14.3			108.4	108.9	0.3
CHCV2541	CV-2541	9/17/2026 10:16:55 AM	22.7	63.9	0.1	13.3			127.5	128.6	0.4
CHCV2542	CV-2542	9/2/2026 1:13:18 PM	44.3	54.0	0.6	1.1			130.1	130.1	0.8
CHCV2542	CV-2542	9/17/2026 3:00:18 PM	39.4	56.6	0.4	3.6			130.0	130.4	0.7
CHCV2543	CV-2543-PLR	9/2/2026 9:36:06 AM	6.2	55.2	7.1	31.5			95.9	97.9	0.1
CHCV2543	CV-2543-PLR	9/17/2026 2:16:09 PM	13.5	60.1	4.1	22.3			99.7	101.0	0.2
CHCV2544	CV-2544	9/15/2026 9:11:52 AM	6.9	84.9	0.0	8.2			89.8	89.8	0.1
CHCV2544	CV-2544	9/15/2026 9:14:07 AM	7.0	84.7	0.0	8.3			145.2	145.3	0.1
CHCV2544	CV-2544	9/15/2026 9:33:39 AM	6.8	82.3	0.0	10.9			145.4	145.4	0.1
CHCV2544	CV-2544	9/21/2026 10:26:52 AM	10.7	82.2	0.0	7.1			150.1	150.0	0.1
CHCV2544	CV-2544	9/21/2026 10:35:00 AM					2090				
CHCV2545	CV-2545	9/2/2026 1:57:34 PM	27.2	71.1	0.0	1.7			126.5	129.4	0.4

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2545	CV-2545	9/2/2026 2:00:03 PM	29.1	70.9	0.0	0.0			129.3	129.7	0.4
CHCV2545	CV-2545	9/21/2026 1:45:21 PM	33.1	61.0	0.1	5.8			127.9	127.5	0.5
CHCV2546	CV-2546	9/2/2026 2:02:59 PM	22.8	73.0	0.0	4.2			129.8	129.6	0.3
CHCV2546	CV-2546	9/2/2026 2:03:29 PM	22.6	75.0	0.1	2.3			129.1	130.6	0.3
CHCV2546	CV-2546	9/21/2026 2:15:18 PM	18.6	73.6	3.5	4.3			124.4	124.5	0.3
CHCV2547	CV-2547	9/24/2026 1:41:35 PM	51.7	46.6	0.0	1.7			99.9	99.7	1.1
CHCV2548	CV-2548	9/1/2026 12:26:39 PM	6.6	80.2	0.0	13.2			139.7	139.7	0.1
CHCV2548	CV-2548	9/1/2026 12:27:39 PM	6.3	81.7	0.0	12.0			139.6	139.6	0.1
CHCV2548	CV-2548	9/3/2026 1:03:06 PM	7.0	75.8	0.0	17.2			86.3	85.5	0.1
CHCV2548	CV-2548	9/18/2026 2:00:15 PM	7.0	85.6	0.0	7.4			137.8	137.9	0.1
CHCV2548	CV-2548	9/18/2026 2:02:16 PM	6.9	85.9	0.0	7.2			137.9	137.8	0.1
CHCV2548	CV-2548	9/22/2026 9:25:43 AM	6.0	82.2	0.0	11.8			139.0	139.0	0.1
CHCV2549	CV-2549	9/1/2026 12:15:56 PM	40.7	52.3	0.0	7.0			117.2	116.7	0.8
CHCV2549	CV-2549	9/1/2026 12:17:23 PM	40.1	53.0	0.0	6.9			116.9	117.1	0.8
CHCV2549	CV-2549	9/3/2026 1:08:50 PM	40.9	53.8	0.0	5.3			117.0	116.8	0.8
CHCV2549	CV-2549	9/18/2026 1:52:07 PM	14.7	82.2	0.0	3.1			135.7	135.7	0.2
CHCV2549	CV-2549	9/18/2026 1:53:32 PM	14.7	77.3	0.0	8.0			135.9	135.7	0.2
CHCV2550	CV-2550	9/1/2026 1:08:00 PM						113900			
CHCV2550	CV-2550	9/1/2026 1:08:00 PM					2040				
CHCV2550	CV-2550	9/1/2026 1:09:01 PM	8.9	78.5	0.0	12.6			184.3	184.4	0.1
CHCV2550	CV-2550	9/9/2026 1:03:44 PM	23.2	76.8	0.0	0.0			181.1	180.6	0.3
CHCV2550	CV-2550	9/9/2026 1:05:00 PM					3000				
CHCV2550	CV-2550	9/16/2026 9:45:27 AM	5.5	76.9	0.0	17.6			186.2	187.0	0.1
CHCV2550	CV-2550	9/16/2026 9:48:00 AM					3280				
CHCV2550	CV-2550	9/23/2026 9:05:00 AM					347				
CHCV2550	CV-2550	9/23/2026 9:06:42 AM	13.0	84.2	0.1	2.7			186.4	185.6	0.2
CHCV2550	CV-2550	9/30/2026 8:10:00 AM					2460				
CHCV2550	CV-2550	9/30/2026 8:13:11 AM	5.4	85.7	0.0	8.9			179.9	179.3	0.1
CHCV2551	CV-2551	9/1/2026 9:06:00 AM						79300			



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2551	CV-2551	9/1/2026 9:06:00 AM					2970				
CHCV2551	CV-2551	9/9/2026 10:15:15 AM	33.5	66.5	0.0	0.0			169.4	169.5	0.5
CHCV2551	CV-2551	9/9/2026 10:25:00 AM					2910				
CHCV2551	CV-2551	9/15/2026 1:29:53 PM	35.0	65.0	0.0	0.0			166.6	167.9	0.5
CHCV2551	CV-2551	9/15/2026 1:30:00 PM					1540				
CHCV2551	CV-2551	9/22/2026 2:05:45 PM	34.9	64.9	0.1	0.1			164.3	163.1	0.5
CHCV2551	CV-2551	9/22/2026 2:07:00 PM					2190				
CHCV2551	CV-2551	9/29/2026 1:30:00 PM					2660				
CHCV2551	CV-2551	9/29/2026 1:30:09 PM	32.1	67.9	0.0	0.0			155.0	155.7	0.5
CHCV2552	CV-2552	9/1/2026 1:12:06 PM	8.3	81.6	0.0	10.1			171.3	171.3	0.1
CHCV2552	CV-2552	9/1/2026 1:16:00 PM						74500			
CHCV2552	CV-2552	9/1/2026 1:16:00 PM					1800				
CHCV2552	CV-2552	9/9/2026 1:16:00 PM					372				
CHCV2552	CV-2552	9/9/2026 1:17:03 PM	40.3	59.4	0.3	0.0			165.1	165.1	0.7
CHCV2552	CV-2552	9/16/2026 8:55:00 AM					1080				
CHCV2552	CV-2552	9/16/2026 8:55:21 AM	24.8	75.2	0.0	0.0			168.3	168.5	0.3
CHCV2552	CV-2552	9/23/2026 9:14:44 AM	32.3	67.2	0.5	0.0			167.1	167.1	0.5
CHCV2552	CV-2552	9/23/2026 9:15:00 AM					1290				
CHCV2552	CV-2552	9/30/2026 8:15:00 AM					1460				
CHCV2552	CV-2552	9/30/2026 8:27:07 AM	23.4	76.2	0.3	0.1			167.7	167.7	0.3
CHCV2553	CV-2553	9/2/2026 9:50:00 AM	34.8	60.4	0.0	4.8			110.0	110.0	0.6
CHCV2553	CV-2553	9/17/2026 10:55:57 AM	36.0	57.8	0.1	6.1			89.8	76.5	0.6
CHCV2554	CV-2554	9/1/2026 2:17:21 PM	35.4	64.6	0.0	0.0			160.4	160.5	0.5
CHCV2554	CV-2554	9/1/2026 2:20:00 PM						59700			
CHCV2554	CV-2554	9/1/2026 2:20:00 PM					779				
CHCV2554	CV-2554	9/10/2026 8:49:04 AM	36.1	62.6	1.3	0.0			168.2	168.6	0.6
CHCV2554	CV-2554	9/10/2026 8:51:00 AM					816				
CHCV2554	CV-2554	9/16/2026 10:15:07 AM	32.3	65.8	0.0	1.9			164.5	165.1	0.5
CHCV2554	CV-2554	9/16/2026 10:17:00 AM					669				



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2554	CV-2554	9/23/2026 10:20:05 AM	42.0	57.9	0.0	0.1			169.0	169.0	0.7
CHCV2554	CV-2554	9/23/2026 10:25:00 AM					671				
CHCV2554	CV-2554	9/30/2026 9:20:33 AM	33.5	66.5	0.0	0.0			164.0	164.4	0.5
CHCV2554	CV-2554	9/30/2026 9:30:00 AM					582				
CHCV2555	CV-2555	9/14/2026 10:19:23 AM	51.2	47.4	0.0	1.4			119.4	118.3	1.1
CHCV2555	CV-2555	9/21/2026 2:31:09 PM	44.1	55.3	0.1	0.5			127.3	128.8	0.8
CHCV2556	CV-2556-PLR	9/1/2026 1:23:16 PM	21.4	68.0	1.1	9.5			183.7	183.7	0.3
CHCV2556	CV-2556-PLR	9/1/2026 1:29:00 PM						84900			
CHCV2556	CV-2556-PLR	9/1/2026 1:29:00 PM					2270				
CHCV2556	CV-2556-PLR	9/9/2026 1:31:40 PM	47.0	53.0	0.0	0.0			170.7	170.8	0.9
CHCV2556	CV-2556-PLR	9/9/2026 1:37:00 PM					1980				
CHCV2556	CV-2556-PLR	9/16/2026 9:12:40 AM	36.8	63.2	0.0	0.0			186.6	187.1	0.6
CHCV2556	CV-2556-PLR	9/16/2026 9:18:00 AM					2940				
CHCV2556	CV-2556-PLR	9/16/2026 9:20:48 AM	10.7	80.8	0.0	8.5			186.8	187.7	0.1
CHCV2556	CV-2556-PLR	9/16/2026 9:21:53 AM	11.6	81.4	0.0	7.0			187.6	187.6	0.1
CHCV2556	CV-2556-PLR	9/23/2026 9:27:28 AM	41.2	46.9	2.3	9.6			174.8	174.3	0.9
CHCV2556	CV-2556-PLR	9/23/2026 9:30:00 AM					687				
CHCV2556	CV-2556-PLR	9/30/2026 8:45:00 AM					927				
CHCV2556	CV-2556-PLR	9/30/2026 8:45:01 AM	23.6	45.9	2.8	27.7			171.8	171.8	0.5
CHCV2557	CV-2557	9/15/2026 8:51:14 AM	16.8	43.1	0.0	40.1			140.6	140.8	0.4
CHCV2557	CV-2557	9/15/2026 8:52:00 AM	16.8	43.1	0.0	40.1			139.6	140.0	0.4
CHCV2557	CV-2557	9/22/2026 10:25:41 AM	15.6	39.1	2.9	42.4			139.7	139.1	0.4
CHCV2558	CV-2558-PLR	9/1/2026 10:13:00 AM						70000			
CHCV2558	CV-2558-PLR	9/1/2026 10:13:00 AM					1150				
CHCV2558	CV-2558-PLR	9/1/2026 10:28:32 AM	17.3	75.1	0.3	7.3			192.6	193.3	0.2
CHCV2558	CV-2558-PLR	9/9/2026 1:00:56 PM	14.5	69.1	0.1	16.3			189.3	189.3	0.2
CHCV2558	CV-2558-PLR	9/9/2026 1:10:00 PM					2150				
CHCV2558	CV-2558-PLR	9/15/2026 2:10:00 PM					600				
CHCV2558	CV-2558-PLR	9/15/2026 2:11:15 PM	15.3	79.8	0.0	4.9			191.8	191.4	0.2



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2558	CV-2558-PLR	9/23/2026 8:35:00 AM					452.5				
CHCV2558	CV-2558-PLR	9/23/2026 8:42:47 AM	13.3	81.9	0.0	4.8			186.0	186.0	0.2
CHCV2558	CV-2558-PLR	9/29/2026 2:05:00 PM					1700				
CHCV2558	CV-2558-PLR	9/29/2026 2:07:13 PM	17.2	78.5	0.0	4.3			201.2	201.2	0.2
CHCV2559	CV-2559	9/14/2026 1:31:45 PM	10.3	89.7	0.0	0.0			120.2	120.2	0.1
CHCV2559	CV-2559	9/22/2026 9:49:02 AM	12.3	77.9	0.1	9.7			131.4	131.8	0.2
CHCV2560	CV-2560	9/3/2026 9:21:28 AM	9.1	85.3	0.0	5.6			135.0	134.2	0.1
CHCV2560	CV-2560	9/22/2026 10:49:07 AM	14.0	70.0	0.2	15.8			137.3	137.3	0.2
CHCV2561	CV-2561	9/3/2026 9:41:08 AM	12.9	42.3	0.6	44.2			118.0	118.0	0.3
CHCV2561	CV-2561	9/25/2026 2:14:35 PM	12.9	46.8	0.3	40.0			110.0	110.0	0.3
CHCV2562	CV-2562	9/14/2026 1:42:18 PM	30.2	69.8	0.0	0.0			129.2	129.3	0.4
CHCV2563	CV-2563	9/23/2026 8:42:14 AM	38.8	53.8	0.2	7.2			116.3	113.2	0.7
CHCV2564	CV-2564	9/1/2026 10:33:16 AM	30.6	58.0	0.0	11.4			103.9	103.9	0.5
CHCV2564	CV-2564	9/17/2026 10:06:15 AM	39.7	54.3	0.1	5.9			120.1	120.0	0.7
CHCV2565	CV-2565	9/1/2026 11:35:08 AM	38.3	42.2	0.0	19.5			101.4	101.4	0.9
CHCV2565	CV-2565	9/4/2026 1:22:35 PM	43.9	41.2	0.0	14.9			103.7	103.4	1.1
CHCV2565	CV-2565	9/30/2026 11:33:22 AM	41.8	43.0	0.0	15.2			120.4	120.3	1.0
CHCV2566	CV-2566	9/1/2026 11:33:06 AM	43.7	43.6	0.0	12.7			102.1	102.3	1.0
CHCV2566	CV-2566	9/21/2026 11:57:56 AM	48.5	44.8	0.0	6.7			117.0	117.4	1.1
CHCV2567	CV-2567	9/1/2026 1:52:22 PM	51.1	41.0	0.1	7.8			104.3	104.4	1.2
CHCV2567	CV-2567	9/21/2026 12:33:36 PM	50.0	44.3	0.0	5.7			115.9	116.3	1.1
CHCV2568	CV-2568	9/1/2026 2:47:30 PM	41.4	39.9	0.0	18.7			97.3	97.3	1.0
CHCV2568	CV-2568	9/3/2026 11:10:53 AM	42.5	45.7	0.0	11.8			107.7	107.8	0.9
CHCV2568	CV-2568	9/22/2026 3:09:14 PM	38.7	43.3	0.0	18.0			101.7	101.7	0.9
CHCV2569	CV-2569	9/1/2026 2:37:13 PM	45.7	45.7	0.0	8.6			97.2	97.3	1.0
CHCV2569	CV-2569	9/24/2026 12:16:37 PM	41.5	45.6	0.0	12.9			116.7	116.8	0.9
CHCV2570	CV-2570	9/1/2026 2:13:36 PM	52.1	42.4	0.0	5.5			97.1	97.3	1.2
CHCV2570	CV-2570	9/30/2026 1:55:05 PM	52.7	42.8	0.0	4.5			119.5	119.5	1.2
CHCV2571	CV-2571	9/2/2026 10:53:10 AM	54.1	38.5	0.0	7.4			97.3	97.3	1.4

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2572	CV-2572	9/30/2026 10:38:28 AM	54.6	43.3	0.0	2.1			123.0	122.9	1.3
CHCV2602	CV-2602	9/28/2026 9:13:58 AM	48.4	40.7	0.0	10.9			112.1	112.3	1.2
CHCV2603	CV-2603	9/17/2026 1:31:00 PM	49.0	41.4	0.0	9.6			122.3	122.3	1.2
CHCV2603	CV-2603	9/17/2026 1:35:30 PM	48.4	41.3	0.0	10.3			123.0	122.9	1.2
CHCV2603	CV-2603	9/17/2026 1:37:32 PM	48.4	41.9	0.0	9.7			122.9	122.8	1.2
CHCV2605	CV-2605	9/30/2026 9:04:23 AM	46.1	42.0	0.0	11.9			129.1	129.4	1.1
CHCV2606	CV-2606	9/17/2026 1:17:22 PM	53.3	41.4	0.0	5.4			123.9	123.9	1.3
CHCV2606	CV-2606	9/17/2026 1:22:30 PM	53.2	41.6	0.0	5.2			124.3	124.3	1.3
CHCV2606	CV-2606	9/17/2026 1:24:50 PM	52.2	42.2	0.0	5.6			124.3	124.3	1.2
CHCV2608	CV-2608	9/21/2026 9:33:42 AM	53.6	41.2	0.0	5.2			88.4	114.7	1.3
CHCV2608	CV-2608	9/21/2026 9:44:28 AM	53.3	41.9	0.0	4.8			120.2	123.1	1.3
CHCV2610	CV-2610	9/9/2026 10:26:51 AM	56.0	40.7	0.0	3.3			116.6	116.6	1.4
CHCV2610	CV-2610	9/9/2026 10:27:56 AM	54.9	40.6	0.0	4.4			116.7	116.7	1.4
CHCV2611	CV-2611	9/25/2026 8:33:59 AM	58.6	39.4	0.0	2.0			99.7	101.4	1.5
CHCV2611	CV-2611	9/25/2026 8:35:07 AM	57.0	39.5	0.0	3.4			101.8	101.9	1.4
CHCV2612	CV-2612	9/23/2026 10:24:54 AM	56.0	42.9	0.0	1.1			105.9	106.6	1.3
CHCV2613	CV-2613	9/23/2026 9:13:04 AM	53.0	41.1	0.0	5.9			105.4		1.3
CHCV2613	CV-2613	9/23/2026 9:20:54 AM	52.9	41.1	0.0	6.1			106.4	108.7	1.3
CHCV2613	CV-2613	9/23/2026 9:28:02 AM	55.1	40.4	0.0	4.5			109.1	109.2	1.4
CHCV2613	CV-2613	9/23/2026 9:45:38 AM	54.6	40.3	0.0	5.1			108.6	109.3	1.4
CHCV2614	CV-2614	9/21/2026 12:45:34 PM	53.2	42.1	0.0	4.7			124.7	124.6	1.3
CHCV2614	CV-2614	9/21/2026 12:51:30 PM	54.1	41.1	0.0	4.8			125.0	125.7	1.3
CHCV2614	CV-2614	9/21/2026 12:53:19 PM	52.8	42.4	0.0	4.8			125.8	125.9	1.2
CHCV2615	CV-2615	9/21/2026 12:14:18 PM	46.8	44.2	0.0	9.0			108.6	108.6	1.1
CHCV2615	CV-2615	9/21/2026 12:17:00 PM	45.8	45.7	0.0	8.5			109.1	108.5	1.0
CHCV2615	CV-2615	9/21/2026 12:18:55 PM	45.4	45.9	0.0	8.7			108.1	108.0	1.0
CHCV2627	CV-2627	9/11/2026 8:23:45 AM	58.8	38.6	0.0	2.6			113.0	113.2	1.5
CHCV2634	CV-2634	9/4/2026 7:30:48 AM	1.0	2.3	20.8	76.0			68.2	68.3	0.5
CHCV2634	CV-2634	9/11/2026 8:16:30 AM	1.1	5.1	20.5	73.3			88.8	89.5	0.2

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2634	CV-2634	9/23/2026 1:07:00 PM	2.1	7.1	20.4	70.4			106.1	107.1	0.3
CHCV2634	CV-2634	9/24/2026 2:13:35 PM						1000			
CHCV2634	CV-2634	9/24/2026 2:14:26 PM	1.1	2.7	20.1	76.1			102.0	102.1	0.4
CHCV2634	CV-2634	9/24/2026 2:25:00 PM					15.8				
CHCV2634	CV-2634	9/24/2026 2:25:00 PM						1000			
CHCV2634	CV-2634	9/24/2026 2:58:48 PM					30				
CHCV2634	CV-2634	9/24/2026 2:58:48 PM					30				
CHCV2634	CV-2634	9/24/2026 2:58:48 PM					30				
CHCV2638	CV-2638	9/27/2026 11:47:09 AM	18.0	52.3	0.0	29.7			104.4	104.5	0.3
CHCV2663	CV-2663	9/28/2026 1:50:21 PM	25.6	55.1	0.1	19.2			143.1	143.2	0.5
CHCV2676	CV-2676	9/1/2026 8:50:09 AM	15.0	74.6	0.0	10.4			128.4	130.6	0.2
CHCV2680	CV-2680	9/16/2026 11:27:44 AM	41.8	40.6	0.1	17.5			132.4	122.6	1.0
CHCV2680	CV-2680	9/16/2026 11:30:13 AM	38.5	40.6	0.5	20.4			125.8	125.9	0.9
CHCV2680	CV-2680	9/22/2026 2:55:28 PM	39.9	44.0	0.0	16.1			129.1	128.7	0.9
CHCV2681	CV-2681	9/22/2026 3:00:45 PM	14.0	42.9	0.0	43.1			94.2	94.5	0.3
CHCV2681	CV-2681	9/22/2026 3:01:29 PM	13.0	44.8	0.0	42.2			94.6	94.6	0.3
CHCV2683	CV-2683	9/22/2026 3:21:53 PM	24.6	44.1	0.0	31.3			96.9	96.9	0.6
CHCV2684	CV-2684	9/28/2026 2:31:31 PM	28.8	36.1	0.1	35.0			125.7	116.6	0.8
CHCV2687	CV-2687	9/9/2026 1:20:38 PM	49.4	40.2	0.0	10.4			124.6	124.6	1.2
CHCV2688	CV-2688	9/4/2026 8:25:47 AM	55.7	41.3	0.0	3.0			121.1	122.8	1.3
CHCV2688	CV-2688	9/18/2026 3:17:08 PM	55.3	44.7	0.0	0.0			124.3	123.3	1.2
CHCV2689	CV-2689	9/28/2026 3:05:38 PM	0.9	60.7	1.4	37.0			104.8	104.9	0.0
CHCV2689	CV-2689	9/30/2026 11:55:35 AM						282000			
CHCV2689	CV-2689	9/30/2026 11:59:55 AM	0.8	61.1	0.0	38.1			121.3	122.7	0.0
CHCV2689	CV-2689	9/30/2026 12:01:28 PM	0.9	60.8	0.0	38.4			122.2	122.2	0.0
CHCV2690	CV-2690	9/4/2026 8:32:48 AM	54.4	41.4	0.0	4.2			120.8	121.0	1.3
CHCV2691	CV-2691	9/28/2026 7:44:15 AM	55.8	40.2	0.0	4.0			125.7	125.8	1.4
CHCV2692	CV-2692	9/4/2026 7:43:29 AM	55.9	41.0	0.0	3.2			127.0	127.0	1.4
CHCV2692	CV-2692	9/18/2026 3:35:46 PM	54.9	42.2	0.0	2.9			127.2	127.3	1.3



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHCV2695	CV-2695	9/16/2026 1:56:22 PM	54.5	41.8	0.0	3.7			114.4	114.5	1.3
CHCV2695	CV-2695	9/16/2026 2:05:21 PM	53.9	42.1	0.0	4.0			114.4	114.9	1.3
CHCV2695	CV-2695	9/16/2026 2:07:07 PM	53.3	42.9	0.0	3.8			114.9	114.9	1.2
CHWCV48R	CV-48R	9/23/2026 8:32:14 AM	52.1	43.7	0.0	4.2			120.9	121.4	1.2
CHWCV52D	CV-52D	9/22/2026 2:41:30 PM	31.1	51.8	0.0	17.1			102.6	99.2	0.6
CHWCV55R	CV-55R	9/2/2026 2:12:41 PM	29.9	55.0	0.0	15.1			151.6	151.4	0.5
CHWCV55R	CV-55R	9/2/2026 2:15:00 PM					425				
CHWCV55R	CV-55R	9/2/2026 2:15:00 PM						169000			
CHWCV55R	CV-55R	9/10/2026 9:19:10 AM	37.5	49.3	0.1	13.1			152.4	152.5	0.8
CHWCV55R	CV-55R	9/10/2026 9:21:00 AM					207				
CHWCV55R	CV-55R	9/11/2026 9:33:09 AM	30.2	46.9	0.0	22.9			152.9	152.8	0.6
CHWCV55R	CV-55R	9/17/2026 10:30:20 AM	35.1	43.8	0.0	21.1			150.8	151.0	0.8
CHWCV55R	CV-55R	9/17/2026 10:33:00 AM					440				
CHWCV55R	CV-55R	9/24/2026 2:26:06 PM	37.9	50.0	0.0	12.1			151.8	151.4	0.8
CHWCV55R	CV-55R	9/24/2026 2:30:00 PM					249				
CHWCV56D	CV-56D	9/1/2026 8:36:44 AM	36.7	36.0	0.9	26.4			117.8	117.7	1.0
CHWCV56S	CV-56S	9/1/2026 8:31:46 AM	26.4	17.3	4.5	51.8			110.9	110.8	1.5
CHWCV57R	CV-57R	9/1/2026 10:13:04 AM	47.3	38.5	0.0	14.2			105.2	105.4	1.2
CHWCV79R	CV-79R	9/1/2026 9:35:58 AM	51.3	45.7	0.0	3.0			136.8	136.5	1.1
CHWCV79R	CV-79R	9/1/2026 9:37:09 AM	51.0	45.5	0.0	3.5			135.8	135.9	1.1
CHIWCV94	CV-94	9/22/2026 10:04:47 AM	50.1	40.5	0.0	9.4			112.3	112.5	1.2
CHIWCV95	CV-95	9/1/2026 10:09:59 AM	35.7	29.3	2.0	33.0			91.6	91.7	1.2
CHIWCV99	CV-99	9/4/2026 7:05:00 AM					900				
CHIWCV99	CV-99	9/4/2026 7:05:00 AM						64000			
CHIWCV99	CV-99	9/14/2026 9:15:48 AM	3.0	6.5	17.8	72.7			85.9	86.7	0.5
CHIWCV99	CV-99	9/14/2026 9:19:46 AM	31.6	48.3	3.5	16.6			88.0	88.3	0.7
CHIWCV99	CV-99	9/25/2026 10:42:18 AM	40.9	54.1	0.3	4.7			105.0	98.8	0.8
CHIWD002	D-02	9/25/2026 9:39:15 AM	60.3	38.0	0.0	1.7			88.8	89.1	1.6
CHIWD002	D-02	9/28/2026 12:45:58 PM	58.7	38.4	0.0	2.9			92.8	92.6	1.5

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIWD002	D-02	9/28/2026 12:48:09 PM	56.6	40.4	0.0	3.1			92.3	92.3	1.4
CHIWD003	D-03	9/2/2026 10:11:51 AM	51.6	36.6	1.7	10.1			99.5	99.6	1.4
CHIWD004	D-04	9/25/2026 9:43:51 AM	50.4	38.0	0.7	10.8			89.4	89.5	1.3
CHIWD009	D-09	9/25/2026 8:39:40 AM	55.8	40.0	0.0	4.2			115.5	115.6	1.4
CHIWD010	D-10	9/2/2026 10:47:58 AM	54.5	40.0	0.3	5.2			102.9	103.0	1.4
CHIFP001	FP-001	9/9/2026 11:56:26 AM	27.2	24.2	3.6	45.0			114.6	114.6	1.1
CHIFP002	FP-002	9/9/2026 11:59:58 AM	26.5	24.5	4.4	44.6			114.6	114.6	1.1
CHIFP003	FP-003	9/9/2026 12:04:20 PM	45.5	44.9	1.5	8.1			114.6	114.6	1.0
CHIFP005	FP-005	9/25/2026 10:01:13 AM	0.1	2.7	18.5	78.7			89.1	89.2	0.0
CHIFP006	FP-006	9/9/2026 10:42:38 AM	21.8	65.9	0.4	11.9			107.1	107.4	0.3
CHIFP008	FP-008	9/9/2026 10:51:01 AM	4.6	33.3	9.9	52.2			108.4	108.3	0.1
CHIFP009	FP-009	9/9/2026 10:56:29 AM	15.4	66.8	1.6	16.2			114.2	114.2	0.2
CHIFP010	FP-010	9/9/2026 11:00:51 AM	19.9	76.3	0.6	3.2			120.9	120.9	0.3
CHIFP011	FP-011	9/9/2026 11:03:30 AM	24.9	35.6	6.9	32.6			96.1	96.4	0.7
CHIFP012	FP-012	9/1/2026 11:45:24 AM	0.7	4.7	19.0	75.6			95.6	95.8	0.1
CHIFP013	FP-013	9/1/2026 11:33:24 AM	2.4	6.0	17.1	74.5			95.5	95.5	0.4
CHIFP014	FP-014	9/25/2026 10:20:20 AM	4.5	35.5	10.1	49.9			112.4	112.5	0.1
CHIFP015	FP-015	9/9/2026 10:36:14 AM	0.3	0.7	19.3	79.7			114.6	114.7	0.4
CHIFP016	FP-016	9/9/2026 10:39:37 AM	0.3	0.4	19.3	80.0			108.9	109.5	0.8
CHIFP017	FP-017	9/14/2026 11:00:20 AM	54.4	35.0	2.4	8.2			98.8	98.6	1.6
CHIFP018	FP-018	9/1/2026 2:40:24 PM	50.4	38.9	0.6	10.1			96.1	96.1	1.3
CHIFP019	FP-019	9/1/2026 2:44:17 PM	54.4	43.5	0.1	2.0			95.1	95.2	1.3
CHIFP020	FP-020	9/14/2026 11:24:45 AM	5.1	10.6	13.8	70.5			96.0	96.0	0.5
CHIFP021	FP-021	9/14/2026 11:16:23 AM	14.0	28.1	8.7	49.2			106.1	106.1	0.5
CHIFP022	FP-022	9/14/2026 11:21:00 AM	6.1	26.8	1.1	66.0			104.5	104.5	0.2
CHIFP023	FP-023	9/3/2026 8:54:48 AM	18.4	45.5	5.2	30.9			82.0	82.1	0.4
CHIFP024	FP-024	9/9/2026 11:18:04 AM	18.9	40.3	6.1	34.7			103.4	103.7	0.5
CHIFP025	FP-025	9/14/2026 10:07:38 AM	6.9	14.1	14.5	64.5			95.2	95.3	0.5
CHIFP026	FP-026	9/14/2026 10:10:15 AM	11.5	23.0	10.7	54.8			92.6	92.6	0.5

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIFP027	FP-027	9/14/2026 10:53:07 AM	11.9	26.7	8.6	52.8			98.7	98.8	0.4
CHIFP027	FP-027	9/14/2026 2:20:08 PM	13.0	24.9	9.5	52.6			97.0	96.9	0.5
CHIFP027	FP-027	9/15/2026 10:17:45 AM	1.0	18.6	15.1	65.3			93.6	93.7	0.1
CHIFP028	FP-028	9/14/2026 10:55:24 AM	9.2	10.1	15.7	65.0			101.0	101.1	0.9
CHIFP028	FP-028	9/15/2026 10:30:36 AM	0.1	2.1	19.7	78.1			89.1	89.1	0.0
CHIFP028	FP-028	9/15/2026 10:31:51 AM	0.0	0.9	20.6	78.5			89.5	89.5	0.0
CHIFP029	FP-029	9/14/2026 11:04:54 AM	52.2	41.3	0.0	6.5			110.3	110.9	1.3
CHIFP029	FP-029	9/15/2026 10:38:34 AM	13.5	15.2	11.3	60.0			91.1	90.9	0.9
CHIFP030	FP-030	9/1/2026 2:31:04 PM	50.4	40.1	1.2	8.3			94.3	94.3	1.3
CHIFP031	FP-031	9/1/2026 2:28:03 PM	3.9	18.3	17.7	60.1			91.9	92.4	0.2
CHIFP031	FP-031	9/15/2026 10:39:37 AM	13.0	14.3	11.6	61.1			90.6	90.6	0.9
CHIFP032	FP-032	9/1/2026 2:20:55 PM	6.5	13.6	11.2	68.7			94.6	94.9	0.5
CHIFP033	FP-033	9/1/2026 2:17:52 PM	0.0	1.5	19.5	79.0			95.1	95.1	0.0
CHIFP034	FP-034	9/1/2026 2:13:58 PM	0.4	7.7	11.7	80.2			99.7	99.7	0.1
CHIFP035	FP-035	9/1/2026 1:47:39 PM	19.4	39.8	4.9	35.9			91.8	91.8	0.5
CHIFP036	FP-036	9/14/2026 9:56:48 AM	9.7	15.8	12.5	62.0			93.2	93.3	0.6
CHIFP037	FP-037	9/1/2026 1:35:51 PM	1.1	1.1	19.3	78.5			92.9	93.6	1.0
CHIFP038	FP-038	9/14/2026 1:57:24 PM	25.4	17.9	6.6	50.1			98.2	98.7	1.4
CHIFP038	FP-038	9/23/2026 10:03:41 AM	3.4	20.9	16.4	59.3			87.4	87.4	0.2
CHIFP039	FP-039	9/14/2026 1:59:50 PM	51.1	32.9	2.0	14.0			101.6	101.7	1.6
CHIFP040	FP-040	9/23/2026 10:00:51 AM	12.0	43.2	6.4	38.4			103.2	103.2	0.3
CHIFP041	FP-041	9/2/2026 7:45:38 AM	13.4	33.2	4.3	49.1			64.9	65.0	0.4
CHIFP042	FP-042	9/2/2026 8:11:34 AM	6.2	28.7	12.1	53.0			70.4	70.5	0.2
CHIFP043	FP-043	9/2/2026 7:48:43 AM	8.0	26.0	7.6	58.4			82.4	82.5	0.3
CHIFP044	FP-044	9/2/2026 7:51:27 AM	0.5	6.7	19.2	73.6			67.4	67.5	0.1
CHIFP045	FP-045	9/2/2026 1:12:15 PM	0.0	0.1	21.0	78.9			94.1	105.4	0.2
CHIFP046	FP-046	9/25/2026 10:05:05 AM	9.3	36.2	9.1	45.4			93.5	93.4	0.3
CHIFP047	FP-047	9/29/2026 8:20:44 AM	3.3	6.5	15.4	74.8			73.0	73.0	0.5
CHIFP050	FP-050	9/2/2026 2:22:59 PM	25.8	60.0	0.1	14.1			99.9	99.9	0.4



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIFP051	FP-051	9/2/2026 2:17:15 PM	35.9	63.4	0.2	0.5			98.4	98.4	0.6
CHIFP052	FP-052	9/2/2026 1:33:27 PM	9.3	14.1	10.5	66.1			94.0	94.0	0.7
CHIFP053	FP-053	9/2/2026 1:27:21 PM	17.1	19.4	8.6	54.9			100.3	100.6	0.9
CHIFP054	FP-054	9/1/2026 9:06:16 AM	27.3	72.6	0.1	0.0			164.9	165.1	0.4
CHIFP054	FP-054	9/2/2026 2:06:03 PM	37.3	55.0	0.0	7.7			98.1	98.1	0.7
CHIFP055	FP-055	9/28/2026 10:39:01 AM	1.3	14.8	13.4	70.5			94.1	94.2	0.1
CHIFP056	FP-056	9/2/2026 9:03:40 AM	13.5	17.2	10.9	58.4			82.2	82.2	0.8
CHIFP057	FP-057	9/3/2026 12:59:26 PM	40.1	35.9	0.8	23.2			100.0	100.1	1.1
CHIFP058	FP-058	9/3/2026 12:56:21 PM	24.4	35.3	3.1	37.2			97.5	97.6	0.7
CHIFP059	FP-059	9/14/2026 1:04:23 PM	35.5	24.2	8.7	31.6			108.2	108.2	1.5
CHIFP060	FP-060	9/28/2026 10:03:13 AM	0.0	0.0	20.8	79.2			86.5	86.4	
CHIFP061	FP-061	9/9/2026 10:33:21 AM	1.0	14.4	16.0	68.6			112.1		0.1
CHIFP062	FP-062	9/10/2026 12:04:52 PM	9.7	74.4	0.0	15.9			151.0	151.1	0.1
CHIFP063	FP-063	9/10/2026 12:09:15 PM	0.5	3.2	19.4	76.9			112.6	112.8	0.2
CHIFP064	FP-064	9/14/2026 12:54:05 PM	52.9	40.5	0.0	6.6			100.8	101.7	1.3
CHIFP064	FP-064	9/14/2026 12:58:32 PM	51.3	39.0	0.0	9.7			101.6	101.4	1.3
CHIFP064	FP-064	9/15/2026 9:47:50 AM	28.4	27.1	2.3	42.2			92.0	91.9	1.0
CHIFP065	FP-065	9/14/2026 1:10:28 PM	54.6	40.6	0.1	4.7			101.8	103.6	1.3
CHIFP065	FP-065	9/15/2026 9:51:40 AM	32.6	29.9	2.2	35.3			93.0	92.8	1.1
CHIFP066	FP-066	9/14/2026 1:20:35 PM	39.5	30.5	2.2	27.8			103.8	103.8	1.3
CHIFP066	FP-066	9/15/2026 9:55:34 AM	8.1	15.9	9.9	66.1			92.9	92.8	0.5
CHIWH001	H-01 (EXP-01)	9/3/2026 12:08:43 PM	11.3	48.4	0.0	40.3			103.7	104.8	0.2
CHIWH001	H-01 (EXP-01)	9/30/2026 2:26:54 PM	10.2	47.0	0.0	42.9			110.0	110.3	0.2
CHIWH002	H-02 (EXP-02)	9/3/2026 12:33:02 PM	18.1	49.0	0.0	32.9			117.2	117.0	0.4
CHIWH002	H-02 (EXP-02)	9/30/2026 2:29:31 PM	20.5	46.6	0.0	33.0			115.0	115.2	0.4
CHIWH003	H-03 (EXP-03)	9/3/2026 12:29:22 PM	47.9	49.6	0.0	2.5			119.2	117.0	1.0
CHIWH003	H-03 (EXP-03)	9/30/2026 2:35:08 PM	53.2	42.3	0.0	4.6			115.2	115.2	1.3
CHIWH004	H-04 (EXP-04)	9/3/2026 12:23:09 PM	3.4	56.9	0.0	39.7			135.4	131.8	0.1
CHIWH004	H-04 (EXP-04)	9/3/2026 12:24:20 PM	2.5	57.9	0.0	39.6			131.5	131.5	0.0

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIWH004	H-04 (EXP-04)	9/30/2026 2:38:36 PM	1.6	52.7	0.0	45.7			130.6	132.1	0.0
CHIWH004	H-04 (EXP-04)	9/30/2026 2:40:29 PM	1.5	55.3	0.0	43.2			136.6	136.8	0.0
CHIWH008	H-08 (EXP-08)	9/14/2026 8:50:48 AM	50.4	45.3	0.0	4.3			123.3	123.3	1.1
CHIWH008	H-08 (EXP-08)	9/29/2026 8:40:38 AM	51.1	45.8	0.0	3.1			123.3	123.5	1.1
CHIWH008	H-08 (EXP-08)	9/29/2026 8:42:05 AM	50.0	46.8	0.0	3.2			123.5	123.5	1.1
CHIWH010	H-10 (EXP-10)	9/15/2026 8:07:00 AM	11.5	70.4	0.0	18.1			131.2	131.2	0.2
CHIWH010	H-10 (EXP-10)	9/15/2026 8:11:28 AM	10.9	69.6	0.0	19.5			131.3	131.3	0.2
CHIWH010	H-10 (EXP-10)	9/29/2026 8:30:20 AM	11.1	65.7	0.2	23.0			131.0	130.9	0.2
CHIWH010	H-10 (EXP-10)	9/29/2026 8:32:34 AM	11.0	66.3	0.2	22.6			130.8	130.8	0.2
CHH1404C	H-1404C	9/15/2026 9:34:05 AM	12.8	30.3	0.6	56.3			153.8	153.6	0.4
CHH1404C	H-1404C	9/15/2026 9:38:51 AM	12.7	29.9	0.6	56.8			153.4	153.9	0.4
CHH1404C	H-1404C	9/16/2026 10:35:00 AM					201				
CHH1404C	H-1404C	9/16/2026 12:54:05 PM	13.9	31.9	0.5	53.7			151.7	150.8	0.4
CHH1404C	H-1404C	9/16/2026 1:34:20 PM	10.5	26.3	0.5	62.7			151.1	122.2	0.4
CHH1404C	H-1404C	9/16/2026 1:40:19 PM	10.5	26.9	0.5	62.1			106.2	104.6	0.4
CHH1405C	H-1405C	9/1/2026 9:32:25 AM	16.0	49.7	2.9	31.4			90.9	91.2	0.3
CHH1405C	H-1405C	9/22/2026 11:58:24 AM	0.0	0.2	22.8	77.0			101.0	101.0	0.0
CHH1405C	H-1405C	9/22/2026 11:59:05 AM	0.0	0.2	22.8	77.0			100.9	100.8	0.0
CHH1406W	H-1406W	9/2/2026 8:36:20 AM	28.4	59.3	1.9	10.4			71.9	70.8	0.5
CHH1406W	H-1406W	9/4/2026 1:49:40 PM	31.7	55.6	0.6	12.0			93.1	93.5	0.6
CHH1406W	H-1406W	9/10/2026 10:32:49 AM	29.3	63.1	0.3	7.3			93.1	93.2	0.5
CHH1406W	H-1406W	9/23/2026 8:53:49 AM	0.2	7.4	19.4	73.0			83.1	83.1	0.0
CH1408CR	H-1408CR	9/23/2026 12:53:30 PM	42.7	43.2	0.0	14.1			126.1	126.1	1.0
CHH1408E	H-1408E	9/14/2026 2:12:45 PM	54.4	42.0	0.0	3.6			98.1	103.0	1.3
CHH1408E	H-1408E	9/21/2026 10:04:50 AM	55.3	43.0	0.0	1.7			117.6	118.5	1.3
CHH1408W	H-1408W	9/2/2026 9:01:18 AM	36.9	30.5	4.8	27.8			81.6	81.6	1.2
CHH1409N	H-1409N	9/1/2026 2:27:54 PM	42.2	34.8	0.0	23.0			116.8	116.9	1.2
CHH1409N	H-1409N	9/21/2026 9:11:22 AM	57.1	41.2	0.0	1.7			103.6	106.0	1.4
CHH1410S	H-1410S	9/25/2026 9:05:52 AM	50.4	40.9	0.6	8.1			93.3	94.0	1.2

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH1563N	H-1563N	9/14/2026 2:12:22 PM	48.5	36.8	0.3	14.4			126.0	126.0	1.3
CHH1563N	H-1563N	9/17/2026 10:33:10 AM	32.6	37.8	0.5	29.1			126.1	124.6	0.9
CHH1563S	H-1563S	9/1/2026 9:35:22 AM	13.8	27.5	0.4	58.3			90.1	90.1	0.5
CHH1563S	H-1563S	9/22/2026 12:03:36 PM	10.9	23.5	0.3	65.3			94.4	94.4	0.5
CHH1565E	H-1565E	9/14/2026 2:16:08 PM	51.5	39.6	0.0	8.9			104.6	104.6	1.3
CHH1565E	H-1565E	9/21/2026 10:11:59 AM	38.7	36.0	0.0	25.3			91.1	91.2	1.1
CHH1568N	H-1568N	9/14/2026 2:10:12 PM	41.7	38.9	1.2	18.2			116.5	116.4	1.1
CHH1568N	H-1568N	9/21/2026 9:57:33 AM	34.2	38.7	1.5	25.6			116.0	116.0	0.9
CHH1571S	H-1571S	9/24/2026 10:55:12 AM	52.9	42.0	0.0	5.1			94.1	100.2	1.3
CHH1572N	H-1572N	9/22/2026 10:24:00 AM	50.5	42.9	0.0	6.6			108.1	107.3	1.2
CHH1572S	H-1572S	9/24/2026 10:40:13 AM	39.8	35.3	4.2	20.7			94.1	97.2	1.1
CHH1753N	H-1753N	9/1/2026 2:48:08 PM	38.5	30.1	4.8	26.6			96.3	96.3	1.3
CHH1753N	H-1753N	9/24/2026 11:34:35 AM	41.2	33.6	5.3	19.9			94.9	94.7	1.2
CHH1753N	H-1753N	9/24/2026 11:36:18 AM	41.7	33.2	4.9	20.2			94.8	94.7	1.3
CHH1753S	H-1753S	9/14/2026 1:54:43 PM	54.6	41.4	0.0	4.0			108.8	108.9	1.3
CHH1753S	H-1753S	9/17/2026 10:36:17 AM	43.6	39.2	0.0	17.2			106.9	105.5	1.1
CHH1756S	H-1756S	9/2/2026 7:25:00 AM	10.8	25.7	3.5	60.0			68.9	71.3	0.4
CHH1756S	H-1756S	9/22/2026 11:27:30 AM	30.9	41.6	1.9	25.6			111.0	109.4	0.7
CHH1757S	H-1757S	9/1/2026 9:27:22 AM	38.4	46.9	0.0	14.7			93.9	94.1	0.8
CHH1757S	H-1757S	9/22/2026 11:41:50 AM	31.4	42.3	0.0	26.3			109.8	110.1	0.7
CHH1760S	H-1760S	9/14/2026 1:52:17 PM	40.2	58.6	0.0	1.2			122.1	122.1	0.7
CHH1760S	H-1760S	9/21/2026 9:25:24 AM	39.0	55.9	0.0	5.1			117.9	117.9	0.7
CHH1762N	H-1762N	9/13/2026 1:22:53 PM	51.5	39.8	0.0	8.6			115.5	116.1	1.3
CHH1762N	H-1762N	9/13/2026 1:24:07 PM	50.4	39.8	0.0	9.8			116.4	116.5	1.3
CHH1762N	H-1762N	9/21/2026 8:20:33 AM	49.3	38.1	0.0	12.6			113.2	113.4	1.3
CHH1763N	H-1763N	9/14/2026 1:09:46 PM	29.5	29.6	3.1	37.8			121.7	121.5	1.0
CHH1763N	H-1763N	9/24/2026 2:03:05 PM	29.7	41.8	2.3	26.2			124.3	124.3	0.7
CHH1763S	H-1763S	9/9/2026 1:49:39 PM	18.7	27.9	0.0	53.4			127.1	127.1	0.7
CHH1764N	H-1764N	9/9/2026 1:21:26 PM	44.1	39.6	0.0	16.3			122.3	122.1	1.1

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH1764S	H-1764S	9/24/2026 11:03:44 AM	40.8	47.1	0.0	12.1			124.3	123.7	0.9
CHH1767N	H-1767N	9/28/2026 3:02:56 PM	39.6	57.4	0.1	2.9			106.3	106.3	0.7
CHH1769N	H-1769N	9/1/2026 11:12:33 AM	9.7	28.4	3.8	58.1			124.7	123.6	0.3
CHH1769N	H-1769N	9/16/2026 12:33:55 PM	4.7	17.8	7.6	69.9			118.5	117.7	0.3
CHH1769N	H-1769N	9/16/2026 12:34:48 PM	4.6	17.1	7.7	70.6			117.1	117.0	0.3
CHH1770N	H-1770N	9/1/2026 11:22:05 AM	29.2	63.7	0.0	7.1			105.0	105.2	0.5
CHH1770N	H-1770N	9/10/2026 9:10:00 AM					320				
CHH1770N	H-1770N	9/10/2026 9:10:00 AM						23000			
CHH1770N	H-1770N	9/16/2026 2:50:15 PM	27.2	65.6	0.2	7.0			97.3	97.4	0.4
CHH1770S	H-1770S	9/1/2026 9:20:12 AM	40.1	52.8	0.0	7.1			103.4	103.6	0.8
CHH1770S	H-1770S	9/24/2026 2:40:13 PM	27.1	48.3	1.7	22.9			105.7	106.3	0.6
CHH1771A	H-1771A	9/10/2026 1:09:59 PM	33.0	67.0	0.0	0.0			106.7	106.7	0.5
CHH1771B	H-1771B	9/3/2026 8:52:45 AM	13.6	70.2	0.0	16.2			98.8	98.6	0.2
CHH1771B	H-1771B	9/22/2026 10:31:17 AM	25.0	33.2	1.3	40.5			104.0	104.0	0.8
CHH1774N	H-1774N	9/10/2026 8:58:19 AM	38.4	58.6	0.0	3.0			118.9	118.5	0.7
CHH1774N	H-1774N	9/16/2026 2:40:28 PM	37.4	62.4	0.2	0.0			118.5	118.4	0.6
CHH1801S	H-1801S	9/1/2026 9:53:29 AM	0.1	2.6	19.6	77.7			90.5	90.7	0.0
CHH1801S	H-1801S	9/1/2026 9:53:57 AM	0.1	2.3	19.6	78.0			91.6	91.8	0.0
CHH1802S	H-1802S	9/22/2026 10:27:44 AM	53.6	43.7	0.0	2.7			108.4	112.1	1.2
CHH1803N	H-1803N-PLR	9/8/2026 10:07:00 AM					1740				
CHH1803N	H-1803N-PLR	9/8/2026 10:10:29 AM	1.7	77.3	0.0	21.0			198.6	198.5	0.0
CHH1803N	H-1803N-PLR	9/14/2026 9:29:28 AM	11.9	72.8	0.0	15.3			198.3	198.2	0.2
CHH1803N	H-1803N-PLR	9/14/2026 9:32:00 AM					1700				
CHH1803N	H-1803N-PLR	9/21/2026 9:40:35 AM	10.6	74.6	0.0	14.8			198.4	198.4	0.1
CHH1803N	H-1803N-PLR	9/21/2026 9:41:00 AM					1490				
CHH1803N	H-1803N-PLR	9/28/2026 9:10:00 AM					1290				
CHH1803N	H-1803N-PLR	9/28/2026 9:16:43 AM	10.7	74.1	0.0	15.2			198.5	198.7	0.1
CHH1804B	H-1804B	9/14/2026 1:13:24 PM	45.5	54.5	0.0	0.0			112.3	112.3	0.8
CHH1804N	H-1804N	9/25/2026 2:27:02 PM	26.4	70.1	0.1	3.4			130.4	130.4	0.4

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH1804S	H-1804S	9/9/2026 1:23:01 PM	44.0	39.2	0.0	16.8			120.5	120.5	1.1
CHH1805A	H-1805A	9/3/2026 1:50:46 PM	45.9	42.9	0.2	11.0			90.6		1.1
CHH1805B	H-1805B	9/9/2026 1:05:06 PM	24.0	29.0	0.7	46.3			111.1	111.5	0.8
CHH1805S	H-1805S	9/9/2026 1:38:46 PM	44.9	40.8	0.0	14.3			130.6	128.9	1.1
CHH1805S	H-1805S	9/9/2026 1:39:27 PM	45.7	42.3	0.0	12.0			127.9	128.0	1.1
CHH1806A	H-1806A	9/3/2026 1:23:27 PM	49.3	39.0	0.0	11.7			118.2	118.3	1.3
CHH1806B	H-1806B	9/22/2026 10:17:41 AM	41.9	37.6	2.2	18.3			89.6	89.6	1.1
CHH1806B	H-1806B	9/22/2026 10:19:58 AM	46.2	38.6	0.7	14.5			90.6	90.4	1.2
CHH1806N	H-1806N	9/10/2026 1:30:41 PM	42.2	57.7	0.1	0.0			126.2	125.9	0.7
CHH1806S	H-1806S	9/1/2026 9:12:20 AM	17.6	77.3	0.0	5.1			123.3	127.4	0.2
CHH1807A	H-1807A	9/22/2026 10:02:24 AM	52.7	41.7	0.0	5.6			113.7	114.1	1.3
CHH1807N	H-1807N	9/4/2026 9:28:29 AM	29.2	34.3	0.6	35.9			93.9	94.4	0.9
CHH1807N	H-1807N	9/10/2026 1:36:04 PM	47.8	37.2	0.1	14.9			113.3	113.9	1.3
CHH1807S	H-1807S	9/1/2026 10:29:44 AM	45.4	32.9	0.2	21.5			98.0	98.5	1.4
CHH1952S	H-1952S	9/2/2026 1:24:38 PM	52.7	46.5	0.0	0.8			119.2	119.2	1.1
CHH1952S	H-1952S	9/17/2026 2:50:32 PM	53.4	45.1	0.0	1.5			118.3	118.3	1.2
CHH1955C	H-1955C	9/3/2026 1:54:00 PM	24.6	27.2	2.5	45.7			91.7	91.7	0.9
CHH1955N	H-1955N	9/10/2026 1:18:23 PM	40.3	48.4	0.5	10.8			103.1	103.4	0.8
CHH1956B	H-1956B	9/9/2026 12:56:13 PM	14.6	68.6	0.0	16.8			126.4	125.1	0.2
CHH1956B	H-1956B	9/9/2026 12:57:13 PM	17.1	68.7	0.0	14.2			128.5	128.6	0.2
CHH1956N	H-1956N	9/10/2026 1:26:20 PM	54.5	45.4	0.1	0.0			115.3	115.3	1.2
CHH1956S	H-1956S	9/1/2026 9:27:26 AM	44.7	41.2	0.0	14.1			104.1	103.9	1.1
CHH1957B	H-1957B	9/3/2026 1:15:00 PM	57.6	40.4	0.0	2.0			97.3	97.4	1.4
CHH1957N	H-1957N	9/10/2026 1:33:26 PM	52.5	47.4	0.1	0.0			121.9	122.0	1.1
CHH1957S	H-1957S	9/30/2026 9:45:11 AM	45.0	45.2	0.6	9.2			142.6	127.3	1.0
CHH1957S	H-1957S	9/30/2026 9:54:00 AM	44.0	46.0	0.5	9.5			130.5	129.5	1.0
CHH1957S	H-1957S	9/30/2026 2:08:10 PM	41.1	48.6	0.6	9.7			107.8	107.6	0.8
CHH1958C	H-1958C	9/22/2026 9:58:48 AM	41.5	37.7	0.0	20.8			116.2	116.2	1.1
CHH1958N	H-1958N	9/10/2026 1:37:51 PM	48.1	38.1	0.4	13.4			114.2	114.6	1.3

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH1958S	H-1958S	9/1/2026 10:27:20 AM	11.9	16.6	12.1	59.4			96.7	97.5	0.7
CHH1962N	H-1962N	9/1/2026 11:28:27 AM	18.4	33.4	0.9	47.3			134.7	134.7	0.6
CHH1962N	H-1962N	9/1/2026 11:29:39 AM	14.6	27.4	1.7	56.3			134.8	134.8	0.5
CHH1962N	H-1962N	9/16/2026 2:56:18 PM	17.2	36.2	0.9	45.7			136.1	136.9	0.5
CHH1962N	H-1962N	9/16/2026 2:56:46 PM	17.6	33.8	1.5	47.1			136.9	136.7	0.5
CHH1963N	H-1963N	9/1/2026 10:58:20 AM	17.2	60.5	0.8	21.5			145.8	144.1	0.3
CHH1963N	H-1963N	9/1/2026 10:59:34 AM	18.8	66.1	0.2	14.9			144.0	143.8	0.3
CHH1963N	H-1963N	9/16/2026 12:20:55 PM	16.6	65.4	0.9	17.1			143.7	143.5	0.3
CHH1963N	H-1963N	9/16/2026 12:21:46 PM	16.4	66.5	0.9	16.2			143.7	143.7	0.2
CHH1966N	H-1966N	9/10/2026 9:06:20 AM	36.7	41.0	0.0	22.3			110.1	110.2	0.9
CHH1966N	H-1966N	9/16/2026 2:32:58 PM	36.7	43.4	0.1	19.8			110.2	110.1	0.8
CHH1967E	H-1967E	9/2/2026 10:44:57 AM	42.0	35.5	2.0	20.5			101.9	101.6	1.2
CHH1967W	H-1967W	9/2/2026 1:39:12 PM	55.5	37.2	0.0	7.3			102.8	102.8	1.5
CHH2050E	H-2050E	9/30/2026 9:51:30 AM	55.3	42.8	0.2	1.7			101.1	101.2	1.3
CHH2050W	H-2050W	9/21/2026 2:03:14 PM	37.6	37.7	0.0	24.7			98.7	98.6	1.0
CHH2050W	H-2050W	9/21/2026 2:07:51 PM	37.7	37.5	0.0	24.8			98.3	99.8	1.0
CHH2050W	H-2050W	9/21/2026 2:09:57 PM	33.5	36.3	0.0	30.2			100.2	100.2	0.9
CHH2051W	H-2051W	9/2/2026 1:36:38 PM	55.9	39.4	0.0	4.7			103.7	103.8	1.4
CHH2053E	H-2053E	9/2/2026 10:36:42 AM	54.7	39.9	0.0	5.4			119.3	119.4	1.4
CHH2055E	H-2055E	9/15/2026 10:19:32 AM	23.8	33.3	0.0	42.9			92.3	92.6	0.7
CHH2055E	H-2055E	9/24/2026 1:41:22 PM						28000			
CHH2055E	H-2055E	9/24/2026 1:42:43 PM	45.1	41.8	0.0	13.1			104.7	104.7	1.1
CHH2055E	H-2055E	9/24/2026 1:45:00 PM					14.1				
CHH2055E	H-2055E	9/24/2026 1:45:00 PM						3300			
CHH2055E	H-2055E	9/24/2026 2:52:19 PM					20				
CHH2055E	H-2055E	9/28/2026 8:24:51 AM	39.2	36.4	0.0	24.3			71.0	84.3	1.1
CHH2055E	H-2055E	9/28/2026 8:27:27 AM	30.7	34.3	0.0	35.0			86.3	86.4	0.9
CHH2056B	H-2056B	9/30/2026 10:41:17 AM	52.5	42.1	0.0	5.4			113.3	113.3	1.2
CHH2056W	H-2056W	9/2/2026 1:33:36 PM	58.0	38.6	0.0	3.4			106.7	106.7	1.5



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH2057E	H-2057E	9/2/2026 10:33:09 AM	53.5	38.5	1.0	7.0			127.8	127.8	1.4
CHH2058E	H-2058E	9/25/2026 8:43:12 AM	53.5	40.0	0.0	6.5			113.6	113.6	1.3
CHH2058W	H-2058W	9/2/2026 1:31:18 PM	58.3	35.3	0.0	6.4			100.3	100.4	1.7
CHH2059E	H-2059E	9/25/2026 8:48:49 AM	54.6	41.5	0.0	3.9			117.6	117.8	1.3
CHH2059W	H-2059W	9/2/2026 1:18:59 PM	57.5	41.1	0.0	1.4			123.2	123.4	1.4
CHH2161E	H-2161E	9/30/2026 4:18:18 PM	51.4	44.4	0.0	4.2			126.1	126.2	1.2
CHH2161W	H-2161W	9/2/2026 1:15:54 PM	56.7	35.7	0.0	7.6			106.0	106.2	1.6
CHH2163C	H-2163C	9/15/2026 10:57:08 AM	47.1	40.4	0.2	12.3			83.9	83.9	1.2
CHH2163C	H-2163C	9/21/2026 11:35:30 AM	37.7	41.5	0.0	20.8			87.9	87.9	0.9
CHH2163W	H-2163W	9/2/2026 9:04:51 AM	28.7	23.0	9.2	39.1			90.0	92.8	1.2
CHH2163W	H-2163W	9/2/2026 9:05:57 AM	56.5	40.9	0.0	2.6			98.9	99.0	1.4
CHH2163W	H-2163W	9/22/2026 12:25:17 PM	41.6	56.0	0.0	2.4			121.0	121.0	0.7
CHH2164E	H-2164E	9/16/2026 3:11:14 PM	25.3	35.8	0.0	38.9			127.4	127.4	0.7
CHH2164E	H-2164E	9/24/2026 1:20:04 PM						6000			
CHH2164E	H-2164E	9/24/2026 1:23:09 PM	25.6	33.7	0.0	40.8			122.0	122.1	0.8
CHH2164E	H-2164E	9/24/2026 1:25:00 PM					15				
CHH2164E	H-2164E	9/24/2026 1:25:00 PM						1300			
CHH2164E	H-2164E	9/24/2026 3:05:04 PM					28				
CHH2165E	H-2165E	9/25/2026 9:23:57 AM	47.5	47.6	0.0	4.9			125.4	125.4	1.0
CHH2165W	H-2165W	9/2/2026 8:43:14 AM	31.1	65.0	0.1	3.8			139.4	136.6	0.5
CHH2165W	H-2165W	9/2/2026 8:45:08 AM	14.3	76.0	0.0	9.7			135.9	137.6	0.2
CHH2165W	H-2165W	9/9/2026 7:00:00 AM					680				
CHH2165W	H-2165W	9/9/2026 7:00:00 AM						51000			
CHH2165W	H-2165W	9/23/2026 8:49:44 AM	8.9	88.0	0.0	3.1			147.2	147.2	0.1
CHH2165W	H-2165W	9/30/2026 10:38:31 AM	10.1	73.5	0.0	16.4			148.0	146.0	0.1
CHH2165W	H-2165W	9/30/2026 10:39:18 AM	19.4	75.3	0.0	5.3			144.9	145.2	0.3
CHH2165W	H-2165W	9/30/2026 11:35:00 AM					218				
CHH2166E	H-2166E	9/22/2026 10:33:01 AM	50.1	40.4	0.2	9.3			118.0	118.0	1.2
CHH2168C	H-2168C	9/1/2026 12:08:00 PM	54.9	39.4	0.5	5.2			92.8	93.2	1.4

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH2168E	H-2168E	9/22/2026 10:07:45 AM	48.1	39.1	0.1	12.7			114.3	114.3	1.2
CHH2169C	H-2169C	9/9/2026 1:00:48 PM	37.0	37.6	1.2	24.2			120.5	120.7	1.0
CHH2169E	H-2169E	9/22/2026 9:11:45 AM	47.9	48.6	0.0	3.5			77.7	90.1	1.0
CHH2169E	H-2169E	9/22/2026 9:12:40 AM	47.6	47.9	0.0	4.5			92.8	92.9	1.0
CHH2169E	H-2169E	9/22/2026 10:14:12 AM	34.9	60.5	0.0	4.6			110.8	110.9	0.6
CHH2170N	H-2170N	9/25/2026 11:43:20 AM	30.9	35.5	0.0	33.6			121.5	121.5	0.9
CHH2170S	H-2170S	9/21/2026 12:50:35 PM	43.6	38.7	0.1	17.6			106.8	110.6	1.1
CHH2171A	H-2171A	9/29/2026 10:23:57 AM	33.0	35.1	0.0	31.9			100.3	100.3	0.9
CHH2171B	H-2171B	9/21/2026 9:19:40 AM	38.8	34.4	0.0	26.8			119.9	120.0	1.1
CHH2171N	H-2171N	9/29/2026 10:44:58 AM	20.4	31.5	0.0	48.1			113.1	113.1	0.6
CHH2171S	H-2171S	9/25/2026 11:49:39 AM	25.8	33.4	0.0	40.8			121.5	121.7	0.8
CHH2272W	H-2272W	9/2/2026 9:18:52 AM	29.7	35.1	0.0	35.2			123.3	123.3	0.8
CHH2272W	H-2272W	9/22/2026 12:19:10 PM	31.4	35.0	0.0	33.6			122.3	122.1	0.9
CHH2273W	H-2273W	9/2/2026 7:21:33 AM	21.3	40.8	0.0	37.9			120.7	120.7	0.5
CHH2273W	H-2273W	9/4/2026 8:32:00 AM					160				
CHH2273W	H-2273W	9/4/2026 8:32:00 AM						18000			
CHH2273W	H-2273W	9/9/2026 7:10:00 AM					78				
CHH2273W	H-2273W	9/9/2026 7:10:00 AM						10000			
CHH2273W	H-2273W	9/22/2026 12:09:18 PM	31.8	42.0	0.0	26.2			123.2	123.0	0.8
CHH2274B	H-2274B	9/1/2026 2:15:59 PM	54.6	42.3	0.0	3.1			103.9	104.1	1.3
CHH2274B	H-2274B	9/22/2026 2:38:09 PM	53.3	43.6	0.0	3.1			107.5	107.6	1.2
CHH2274W	H-2274W	9/2/2026 7:28:33 AM	19.9	36.3	0.1	43.7			62.0	62.0	0.5
CHH2274W	H-2274W	9/22/2026 11:23:46 AM	13.4	30.2	1.0	55.4			99.8	99.7	0.4
CHH2275E	H-2275E	9/9/2026 1:51:36 PM	46.8	40.9	0.0	12.3			116.4	116.4	1.1
CHH2275W	H-2275W	9/1/2026 11:38:16 AM	10.0	19.6	6.9	63.5			122.3	125.3	0.5
CHH2275W	H-2275W	9/1/2026 11:39:55 AM	27.9	31.8	0.7	39.6			128.3	127.1	0.9
CHH2275W	H-2275W	9/1/2026 11:41:12 AM	34.7	37.5	0.4	27.4			124.5	124.5	0.9
CHH2275W	H-2275W	9/22/2026 12:53:21 PM	8.2	25.1	2.9	63.8			131.8	127.9	0.3
CHH2275W	H-2275W	9/22/2026 12:53:59 PM	8.8	25.7	3.0	62.5			122.6	122.3	0.3



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH2276A	H-2276A	9/14/2026 1:55:11 PM	48.9	42.1	0.2	8.8			113.6	113.7	1.2
CHH2276A	H-2276A	9/21/2026 9:31:10 AM	47.3	41.4	0.2	11.1			112.5	112.3	1.1
CHH2276B	H-2276B	9/1/2026 2:23:18 PM	53.8	44.3	0.0	1.9			116.6	116.9	1.2
CHH2276B	H-2276B	9/21/2026 9:13:01 AM	56.6	41.5	0.0	1.9			119.3	119.4	1.4
CHH2276E	H-2276E	9/9/2026 1:36:12 PM	35.2	34.7	0.0	30.1			120.9	121.0	1.0
CHH2276W	H-2276W	9/1/2026 9:23:11 AM	24.0	44.6	0.0	31.4			101.4	101.6	0.5
CHH2276W	H-2276W	9/22/2026 11:39:01 AM	20.6	41.0	0.0	38.4			100.4	97.7	0.5
CHH2277A	H-2277A	9/1/2026 10:22:08 AM	32.5	37.0	3.6	26.9			91.9	91.9	0.9
CHH2277A	H-2277A	9/17/2026 10:03:32 AM	42.5	42.3	1.8	13.4			79.7	79.9	1.0
CHH2277B	H-2277B	9/14/2026 1:34:55 PM	53.7	42.8	0.0	3.5			95.0	109.9	1.3
CHH2277B	H-2277B	9/21/2026 8:52:57 AM	53.4	40.8	0.0	5.8			110.6	111.4	1.3
CHIWH023	H-23 (EXP-23)	9/21/2026 8:51:57 AM	2.7	80.6	0.0	16.7			75.7	75.8	0.0
CHH2301E	H-2301E	9/24/2026 1:01:31 PM	54.2	40.3	0.0	5.5			102.7	102.7	1.3
CHH2301N	H-2301N	9/16/2026 7:52:01 AM	54.0	35.6	0.0	10.4			89.6	91.2	1.5
CHH2301N	H-2301N	9/23/2026 1:05:15 PM	35.9	32.0	0.0	32.1			98.6	98.6	1.1
CHH2301W	H-2301W	9/28/2026 2:15:49 PM	0.1	0.4	20.8	78.7			92.1	92.4	0.4
CHH2301W	H-2301W	9/28/2026 2:16:39 PM	0.2	0.3	20.8	78.7			94.7	94.8	0.8
CHH2302C	H-2302C	9/17/2026 1:44:50 PM	50.0	39.9	0.0	10.1			122.8	122.8	1.3
CHH2302C	H-2302C	9/17/2026 1:47:40 PM	49.7	39.9	0.0	10.4			122.8	122.8	1.2
CHH2302E	H-2302E	9/24/2026 1:21:07 PM	54.4	42.0	0.0	3.6			110.8	110.9	1.3
CHH2303E	H-2303E	9/24/2026 1:28:29 PM	56.3	39.7	0.0	4.0			101.5	101.8	1.4
CHH2303N	H-2303N	9/21/2026 1:25:13 PM	37.3	33.5	3.5	25.8			107.7	107.9	1.1
CHH2303N	H-2303N	9/21/2026 1:31:23 PM	38.4	34.2	3.3	24.1			108.2	108.2	1.1
CHH2303N	H-2303N	9/21/2026 1:36:02 PM	40.6	35.4	2.7	21.3			108.1	108.0	1.1
CHH2303N	H-2303N	9/21/2026 1:42:20 PM	41.8	35.9	2.6	19.7			107.9	107.9	1.2
CHH2303N	H-2303N	9/21/2026 1:46:07 PM	41.7	35.9	2.7	19.8			108.1	108.3	1.2
CHH2303S	H-2303S	9/30/2026 9:07:20 AM	50.2	41.2	0.0	8.6			107.2	108.2	1.2
CHH2303S	H-2303S	9/30/2026 3:11:43 PM	49.0	38.4	0.0	12.6			110.8	110.8	1.3
CHH2304E	H-2304E	9/24/2026 1:38:49 PM	54.4	41.0	0.0	4.6			98.9	98.8	1.3

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHH2304S	H-2304S	9/30/2026 8:57:47 AM	48.5	40.5	0.0	11.0			112.7	112.7	1.2
CHH2305N	H-2305N	9/21/2026 1:56:13 PM	36.5	36.1	0.0	27.5			101.1	101.2	1.0
CHH2305S	H-2305S	9/30/2026 8:54:12 AM	53.6	43.5	0.0	2.9			127.3	127.2	1.2
CHH2306N	H-2306N	9/30/2026 10:03:45 AM	49.7	44.3	0.0	6.0			119.2	119.2	1.1
CHH2307S	H-2307S	9/28/2026 9:57:33 AM	49.1	41.1	0.2	9.6			108.0	106.9	1.2
CHH2307S	H-2307S	9/28/2026 9:59:24 AM	49.2	40.7	0.2	9.9			108.5	109.0	1.2
CHH2308S	H-2308S	9/28/2026 9:25:41 AM	46.3	40.8	0.0	12.8			98.0	98.6	1.1
CHH2309N	H-2309N	9/23/2026 10:09:11 AM	46.9	39.5	0.0	13.6			103.0	103.5	1.2
CHH2309S	H-2309S	9/28/2026 1:47:35 PM	50.4	41.7	0.0	7.8			120.4	120.4	1.2
CHH2309S	H-2309S	9/28/2026 1:50:05 PM	50.1	42.5	0.0	7.5			120.5	120.5	1.2
CHH2310N	H-2310N	9/21/2026 10:17:15 AM	55.4	41.5	0.0	3.2			110.4	110.5	1.3
CHH2310N	H-2310N	9/21/2026 10:23:24 AM	54.9	41.4	0.0	3.8			111.4	113.5	1.3
CHH2310N	H-2310N	9/21/2026 10:25:58 AM	52.0	43.2	0.0	4.8			113.6	113.7	1.2
CHH2310S	H-2310S	9/30/2026 9:54:34 AM	51.8	43.0	0.0	5.2			99.6	99.6	1.2
CHH2401S	H-2401S	9/17/2026 12:53:46 PM	54.0	40.8	0.0	5.1			112.3	112.3	1.3
CHH2401S	H-2401S	9/17/2026 12:55:27 PM	54.0	40.9	0.0	5.1			112.2	112.3	1.3
CHH2402N	H-2402N	9/16/2026 9:29:50 AM	35.7	36.8	0.0	27.5			111.0	110.4	1.0
CHH2402N	H-2402N	9/16/2026 9:38:17 AM	31.8	35.6	0.0	32.6			109.6	109.8	0.9
CHH2402S	H-2402S	9/17/2026 10:29:36 AM	44.0	40.5	0.0	15.6			112.8	112.8	1.1
CHH2402S	H-2402S	9/17/2026 10:36:31 AM	44.2	40.1	0.0	15.8			112.8	112.8	1.1
CHH2403N	H-2403N	9/16/2026 9:07:19 AM	24.1	28.3	4.2	43.5			118.4	117.3	0.8
CHH2403N	H-2403N	9/16/2026 9:15:02 AM	32.5	33.3	3.2	31.1			116.6	116.5	1.0
CHH2403S	H-2403S	9/17/2026 9:46:50 AM	48.6	41.3	0.5	9.6			77.4	84.4	1.2
CHH2403S	H-2403S	9/17/2026 9:55:54 AM	53.1	43.0	0.0	3.9			88.4	91.0	1.2
CHH2403S	H-2403S	9/17/2026 10:14:23 AM	53.1	42.7	0.0	4.2			95.4	95.8	1.2
CHH2404N	H-2404N	9/4/2026 10:12:11 AM	50.2	43.7	0.0	6.1			116.6	116.6	1.1
CHH2404N	H-2404N	9/17/2026 10:16:28 AM	53.4	42.5	0.0	4.1			96.1	96.2	1.3
CHH2404S	H-2404S	9/17/2026 9:29:43 AM	53.9	41.4	0.0	4.7			114.9	115.0	1.3
CHH2405N	H-2405N	9/30/2026 12:52:28 PM	26.8	35.9	0.0	37.3			125.6	125.5	0.7

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIWH029	H-29	9/25/2026 11:24:23 AM	18.4	44.5	1.8	35.3			104.8	103.6	0.4
CHIWH072	H-72	9/30/2026 1:21:04 PM	41.5	55.7	0.0	2.8			101.4	101.6	0.7
CHIWH074	H-74	9/16/2026 11:51:01 AM	49.7	42.2	0.0	8.1			113.4	113.4	1.2
CHIWH075	H-75	9/22/2026 2:37:52 PM	37.6	39.7	0.0	22.7			96.3	96.5	0.9
CHIWH079	H-79	9/4/2026 9:06:09 AM	47.5	44.1	0.0	8.4			123.7	123.6	1.1
CHIWP02R	P-02R	9/14/2026 10:11:10 AM	26.5	30.3	0.0	43.2			89.7	89.8	0.9
CHIWP03R	P-03R	9/14/2026 1:32:02 PM	40.3	30.0	0.0	29.7			102.9	102.8	1.3
CHIWP004	P-04	9/14/2026 1:26:28 PM	50.2	36.2	0.0	13.6			103.6	103.6	1.4
CHIWP005	P-05	9/14/2026 1:22:06 PM	39.7	33.0	0.0	27.3			106.0	106.0	1.2
CHIWP06R	P-06R	9/14/2026 1:14:43 PM	40.7	32.4	0.0	26.9			113.9	114.9	1.3
CHIWP07R	P-07R	9/14/2026 9:55:22 AM	30.1	26.8	0.0	43.1			89.9	89.8	1.1
CHIWP08R	P-08R	9/14/2026 10:17:08 AM	53.1	37.7	0.0	9.2			100.4	100.4	1.4
CHIWP009	P-09	9/14/2026 10:29:35 AM	48.2	36.0	0.0	15.8			98.1	98.2	1.3
CHIWP010	P-10	9/14/2026 10:34:17 AM	41.5	33.6	0.0	24.9			96.1	96.1	1.2
CHIWP011	P-11	9/14/2026 10:41:27 AM	45.5	35.8	0.0	18.7			106.8	107.1	1.3
CHIWP012	P-12	9/14/2026 1:08:27 PM	57.2	38.9	0.0	3.9			90.1	89.9	1.5
CHIWP013	P-13	9/14/2026 1:02:12 PM	51.6	35.3	0.0	13.1			91.5	91.2	1.5
CHIWP014	P-14	9/14/2026 10:49:55 AM	27.0	27.7	0.4	44.9			87.8	88.0	1.0
CHIWP15R	P-15R	9/11/2026 9:23:55 AM	50.1	34.4	0.0	15.5			93.3	93.6	1.5
CHIWP016	P-16	9/11/2026 9:31:08 AM	52.9	35.6	0.0	11.5			99.1	99.0	1.5
CHIWP017	P-17	9/11/2026 1:40:34 PM	37.7	29.5	0.0	32.8			114.1	114.1	1.3
CHIP18RD	P-18RD	9/11/2026 1:30:44 PM	50.6	32.8	0.0	16.6			100.3	100.7	1.5
CHIP18RS	P-18RS	9/11/2026 1:34:14 PM	39.2	32.8	0.0	28.0			99.8	99.8	1.2
CHIWP019	P-19	9/11/2026 1:55:29 PM	29.6	27.6	0.0	42.8			96.5	96.4	1.1
CHIWP20R	P-20R	9/11/2026 1:23:45 PM	46.0	32.8	0.0	21.2			101.6	101.7	1.4
CHIWP021	P-21	9/11/2026 1:17:27 PM	33.6	29.2	0.0	37.2			98.9	98.5	1.2
CHIP21RD	P-21RD	9/11/2026 1:06:36 PM	41.4	32.0	0.0	26.6			105.3	105.4	1.3
CHIP21RS	P-21RS	9/11/2026 1:09:45 PM	44.4	35.6	0.0	20.0			110.0	110.1	1.2
CHIP22RD	P-22RD	9/11/2026 8:08:10 AM	53.5	40.5	0.0	6.0			120.4	120.4	1.3

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIP22RS	P-22RS	9/11/2026 8:04:52 AM	31.5	29.8	0.0	38.7			121.9	122.0	1.1
CHIWP023	P-23	9/11/2026 1:01:52 PM	4.9	19.7	0.1	75.3			103.2	106.6	0.2
CHIWP024	P-24	9/13/2026 1:20:31 PM	20.0	27.3	0.0	52.7			101.1	101.2	0.7
CHIWP026	P-26	9/13/2026 1:35:13 PM	44.9	31.8	0.0	23.3			90.7	89.4	1.4
CHIWP027	P-27	9/13/2026 1:42:38 PM	11.1	20.9	0.0	68.0			96.8	96.9	0.5
CHIWP028	P-28	9/13/2026 1:49:04 PM	36.7	30.9	0.0	32.4			98.6	98.6	1.2
CHIWP028	P-28	9/25/2026 2:03:37 PM	37.9	25.5	1.8	34.8					1.5
CHIWP29R	P-29R	9/14/2026 8:03:35 AM	28.6	29.6	0.0	41.8			87.8	87.7	1.0
CHIWP30R	P-30R	9/14/2026 8:11:45 AM	24.2	28.5	0.0	47.3			86.7	86.7	0.8
CHIP32R1	P-32R1	9/14/2026 8:36:49 AM	27.5	30.8	0.6	41.1			113.4	113.4	0.9
CHIP32R2	P-32R2	9/14/2026 8:45:03 AM	32.4	32.8	0.1	34.7			110.0	110.0	1.0
CHIWP033	P-33	9/14/2026 8:50:19 AM	46.3	37.1	0.0	16.6			93.2	93.4	1.2
CHIWP036	P-36	9/14/2026 9:06:39 AM	24.9	30.3	0.0	44.8			85.6	99.7	0.8
CHIWP036	P-36	9/14/2026 9:07:30 AM	24.6	30.6	0.0	44.8			100.0	101.6	0.8
CHIWP037	P-37	9/14/2026 9:26:35 AM	11.3	25.4	0.4	62.9			93.5	93.8	0.4
CHIP38RD	P-38RD	9/9/2026 1:02:10 PM	41.9	35.5	0.0	22.6			109.1	109.1	1.2
CHIP38RS	P-38RS	9/9/2026 12:58:14 PM	30.6	30.1	0.0	39.3			107.9	107.9	1.0
CHIWP039	P-39	9/9/2026 1:09:03 PM	4.6	5.0	18.3	72.1			114.9	115.1	0.9
CHIWP039	P-39	9/9/2026 1:12:07 PM	5.0	4.6	18.1	72.3			116.8	116.7	1.1
CHIWP041	P-41	9/9/2026 1:35:32 PM	35.3	29.7	2.8	32.2			118.7	118.8	1.2
CHIWP42R	P-42R	9/9/2026 1:46:37 PM	48.1	35.2	0.0	16.7			117.9	118.0	1.4
CHIWP043	P-43	9/9/2026 1:51:47 PM	22.7	28.4	0.4	48.5			119.1	119.1	0.8
CHIP44RD	P-44RD	9/9/2026 1:59:38 PM	48.3	34.6	0.0	17.1			114.8	115.3	1.4
CHIP44RS	P-44RS	9/9/2026 1:56:43 PM	20.7	25.9	0.0	53.4			123.8	123.8	0.8
CHIP45RD	P-45RD	9/11/2026 7:34:35 AM	45.5	35.5	0.0	19.0			117.2	117.2	1.3
CHIP45RS	P-45RS	9/11/2026 7:38:47 AM	2.6	21.3	0.0	76.1			114.0	114.0	0.1
CHIP46RD	P-46RD	9/11/2026 7:48:05 AM	52.4	36.5	0.0	11.1			107.4	107.6	1.4
CHIP46RS	P-46RS	9/11/2026 7:50:57 AM	17.6	27.6	0.0	54.8			121.9	122.0	0.6
CHIWP047	P-47	9/11/2026 7:57:45 AM	2.4	18.1	1.1	78.4			88.7	89.0	0.1

Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHIWP048	P-48	9/11/2026 8:17:55 AM	15.3	23.0	0.0	61.7			123.4	130.5	0.7
CHIP49RD	P-49RD	9/2/2026 12:40:19 PM	56.9	38.3	0.0	4.8			114.9	114.9	1.5
CHIP49RS	P-49RS	9/2/2026 12:36:19 PM	38.3	32.4	0.2	29.1			115.4	115.4	1.2
CHIWP052	P-52	9/2/2026 12:48:58 PM	32.8	32.3	0.0	34.9			114.9	115.0	1.0
CHIWP053	P-53	9/2/2026 12:54:52 PM	25.7	28.2	0.0	46.1			114.9	114.7	0.9
CHIWP054	P-54	9/2/2026 1:04:15 PM	37.8	31.7	0.0	30.5			101.0	101.9	1.2
CHIWP055	P-55	9/2/2026 1:11:35 PM	36.3	31.8	0.0	31.9			101.6	101.6	1.1
CHIWP056	P-56	9/2/2026 1:26:56 PM	19.9	26.7	0.0	53.4			104.5	104.5	0.7
CHIWP057	P-57	9/2/2026 1:19:29 PM	32.3	28.9	1.3	37.5			89.5	89.5	1.1
CHIWP60R	P-60R	9/2/2026 1:44:59 PM	60.5	38.4	0.0	1.1			96.1	95.7	1.6
CHIWP061	P-61	9/3/2026 10:41:33 AM	42.8	35.8	0.0	21.4			88.6	88.7	1.2
CHIWP065	P-65	9/3/2026 10:49:34 AM	29.7	29.3	0.0	41.0			87.2	87.1	1.0
CHIWP071	P-71	9/11/2026 8:24:58 AM	39.5	32.8	0.0	27.7			82.4	82.7	1.2
CHIWP075	P-75	9/2/2026 1:35:58 PM	55.9	36.6	0.0	7.5			94.5	94.8	1.5
CHIWP076	P-76	9/9/2026 12:51:44 PM	19.2	27.9	0.0	52.9			120.2	120.5	0.7
CHIWP079	P-79	9/11/2026 1:48:37 PM	24.1	27.0	0.0	48.9			100.0	99.6	0.9
CHIWP079	P-79	9/14/2026 7:34:29 AM	19.1	25.5	1.3	54.1			89.2	89.7	0.7
CSC2000E	SC-2000E	9/25/2026 8:57:52 AM	45.9	39.7	0.0	14.4			120.7	120.7	1.2
CSC2501E	SC-2501E	9/8/2026 9:59:28 AM	2.6	71.6	0.4	25.4			189.2	189.3	0.0
CSC2501E	SC-2501E	9/8/2026 10:01:00 AM					1240				
CSC2501E	SC-2501E	9/14/2026 9:17:00 AM					1190				
CSC2501E	SC-2501E	9/14/2026 9:21:21 AM	10.6	69.6	1.3	18.5			188.8	189.1	0.2
CSC2501E	SC-2501E	9/14/2026 9:23:51 AM	14.0	68.9	0.9	16.2			189.2	189.1	0.2
CSC2501E	SC-2501E	9/21/2026 9:24:00 AM					1120				
CSC2501E	SC-2501E	9/21/2026 9:24:06 AM	12.2	72.7	0.9	14.2			189.9	189.9	0.2
CSC2501E	SC-2501E	9/28/2026 8:44:16 AM	9.2	72.4	0.9	17.5			189.9	189.8	0.1
CSC2501E	SC-2501E	9/28/2026 8:50:00 AM					1140				
CSC2501W	SC-2501W	9/14/2026 1:14:36 PM	2.2	73.5	0.5	23.8			190.3	190.3	0.0
CSC2501W	SC-2501W	9/14/2026 1:16:00 PM	2.5	73.3	0.4	23.8			190.3	190.3	0.0



Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CSC2501W	SC-2501W	9/21/2026 9:47:01 AM	13.5	67.7	2.1	16.7			189.2	189.2	0.2
CSC2501W	SC-2501W	9/21/2026 9:50:00 AM					722				
CSC2501W	SC-2501W	9/28/2026 9:27:48 AM	16.8	64.8	1.8	16.6			188.8	188.9	0.3
CSC2501W	SC-2501W	9/28/2026 9:30:00 AM					741.5				
CHISW010	SW-10	9/28/2026 10:08:23 AM	19.5	35.0	2.2	43.3			89.7	89.9	0.6
CHISW115	SW-115	9/17/2026 1:39:25 PM	41.5	34.0	1.0	23.5			90.2	90.2	1.2
CHSW1445	SW-1445	9/29/2026 12:27:40 PM	39.0	31.6	0.1	29.3			92.5	92.2	1.2
CHSW1455	SW-1455	9/30/2026 4:06:16 PM	48.4	39.4	0.0	12.2			113.7	114.9	1.2
CHISW154	SW-154	9/30/2026 2:17:21 PM	0.0	2.9	19.5	77.6			105.2	105.4	0.0
CSW17135	SW-17-135	9/30/2026 4:01:25 PM	38.3	27.5	0.0	34.2			111.1	111.9	1.4
CHISW187	SW-187	9/23/2026 9:03:24 AM	19.3	40.9	1.9	37.9			83.6	83.9	0.5
CHISW020	SW-20	9/14/2026 10:03:19 AM	0.0	4.7	15.9	79.4			93.7	94.2	0.0
CHISW020	SW-20	9/14/2026 10:04:06 AM	0.0	4.8	16.0	79.2			94.7	94.6	0.0
SW2501D_	SW-2501D	9/28/2026 8:51:48 AM	0.5	5.8	19.5	74.2			74.7	74.7	0.1
SW2501M_	SW-2501M	9/28/2026 8:37:05 AM	14.7	24.8	12.2	48.3			67.5	67.5	0.6
SW2501MD	SW-2501MD	9/28/2026 8:48:27 AM	21.0	52.3	3.5	23.2			72.4	72.5	0.4
SW2501S_	SW-2501S	9/28/2026 8:34:18 AM	4.2	11.6	11.1	73.1			65.9	65.9	0.4
SW2502D_	SW-2502D	9/28/2026 1:31:44 PM	7.0	79.2	0.1	13.7			93.8	93.9	0.1
SW2502M_	SW-2502M	9/28/2026 1:35:12 PM	0.0	3.5	19.6	76.9			94.5	94.5	0.0
SW2502MD	SW-2502MD	9/28/2026 9:07:21 AM	6.6	49.6	9.8	34.0			82.3	82.3	0.1
SW2502S_	SW-2502S	9/28/2026 9:04:57 AM	5.2	23.9	10.4	60.5			82.5	82.5	0.2
SW2503D_	SW-2503D	9/28/2026 9:31:14 AM	2.9	11.7	17.2	68.2			81.0	81.1	0.2
SW2503M_	SW-2503M	9/28/2026 9:36:56 AM	0.0	1.5	20.0	78.5			85.9	86.6	0.0
SW2503MD	SW-2503MD	9/28/2026 9:43:35 AM	5.2	21.3	12.5	61.0			86.2	86.2	0.2
SW2503S_	SW-2503S	9/28/2026 9:40:46 AM	12.3	22.7	12.3	52.7			82.0	82.1	0.5
SW2504D_	SW-2504D	9/28/2026 9:56:00 AM	0.2	1.6	19.5	78.7			81.4	81.5	0.1
SW2504M_	SW-2504M	9/28/2026 9:49:08 AM	0.1	2.4	19.6	77.9			85.0	85.2	0.0
SW2504MD	SW-2504MD	9/28/2026 9:59:28 AM	12.5	28.8	7.7	51.0			82.7	82.9	0.4
SW2504S_	SW-2504S	9/28/2026 9:52:36 AM	14.4	14.4	10.9	60.3			85.6	85.7	1.0




Chiquita Canyon Landfill - Well Data - 09/01/2026 to 09/30/2026

Point ID	Point Name	Record Date	CH4 (% by vol)	CO2 (% by vol)	O2 (% by vol)	Bal Gas (% by vol)	CO (ppmv)	H2 (ppmv)	Init Temp (F)	Adj Temp (F)	CH4:CO2 Ratio
CHISW030	SW-30	9/28/2026 8:56:46 AM	5.1	27.6	11.2	56.1			73.2	73.5	0.2
CHISW032	SW-32	9/28/2026 8:26:06 AM	14.0	53.1	7.6	25.3			71.2	71.6	0.3
CHISW064	SW-64	9/28/2026 8:59:49 AM	13.0	76.2	1.2	9.6			77.6	77.4	0.2
CHISW065	SW-65	9/17/2026 10:54:03 AM	36.4	33.5	0.9	29.2			87.8	87.8	1.1
CHISW065	SW-65	9/17/2026 11:10:21 AM	43.3	55.0	0.0	1.7			110.6	110.4	0.8
CHISW066	SW-66	9/30/2026 2:19:22 PM	6.0	6.1	13.9	74.0			91.8	91.8	1.0
CHISW068	SW-68	9/28/2026 8:30:14 AM	13.1	34.5	1.8	50.6			66.4	66.4	0.4
CHISW070	SW-70	9/23/2026 9:06:01 AM	14.5	66.2	0.9	18.4			89.1	89.1	0.2
CHISW071	SW-71	9/13/2026 1:27:50 PM	13.5	17.5	7.2	61.8			95.2	95.1	0.8
CHISW071	SW-71	9/13/2026 1:29:03 PM	13.4	17.6	7.1	61.9			95.1	95.1	0.8
CHISW072	SW-72	9/14/2026 8:57:13 AM	22.8	22.4	5.0	49.8			76.6	76.4	1.0
CHISW080	SW-80	9/3/2026 12:03:20 PM	27.1	28.6	1.8	42.5			92.6	93.3	0.9
CHISW009	SW-9	9/23/2026 9:09:10 AM	0.9	20.8	13.2	65.1			86.4	86.4	0.0
CHH1961C	TC-1961C	9/24/2026 11:07:18 AM	6.0	24.0	0.0	70.0			118.5	118.5	0.3
CHH1961E	TC-1961E	9/1/2026 9:15:54 AM	45.2	48.9	0.0	5.9			125.0	124.8	0.9
CHTC2174	TC-2174	9/8/2026 9:41:41 AM	1.4	78.8	0.0	19.8			185.6	185.6	0.0
CHTC2174	TC-2174	9/8/2026 9:44:00 AM					1880				
CHTC2174	TC-2174	9/14/2026 8:44:26 AM	3.3	78.6	0.0	18.1			185.7	185.7	0.0
CHTC2174	TC-2174	9/14/2026 8:47:00 AM					2370				
CHTC2174	TC-2174	9/21/2026 9:00:00 AM					2080				
CHTC2174	TC-2174	9/21/2026 9:00:43 AM	6.3	77.1	0.0	16.6			185.7	185.6	0.1
CHTC2174	TC-2174	9/28/2026 8:20:43 AM	2.0	77.9	0.0	20.1			185.8	185.9	0.0
CHTC2174	TC-2174	9/28/2026 8:25:00 AM					1710				
CHIWVL02	VL-02	9/30/2026 10:59:45 AM	59.1	34.6	0.2	6.1			99.8	100.2	1.7



Thirty Day Maximum Vertical Temperature Map from Temperature Probes at Chiquita Landfill

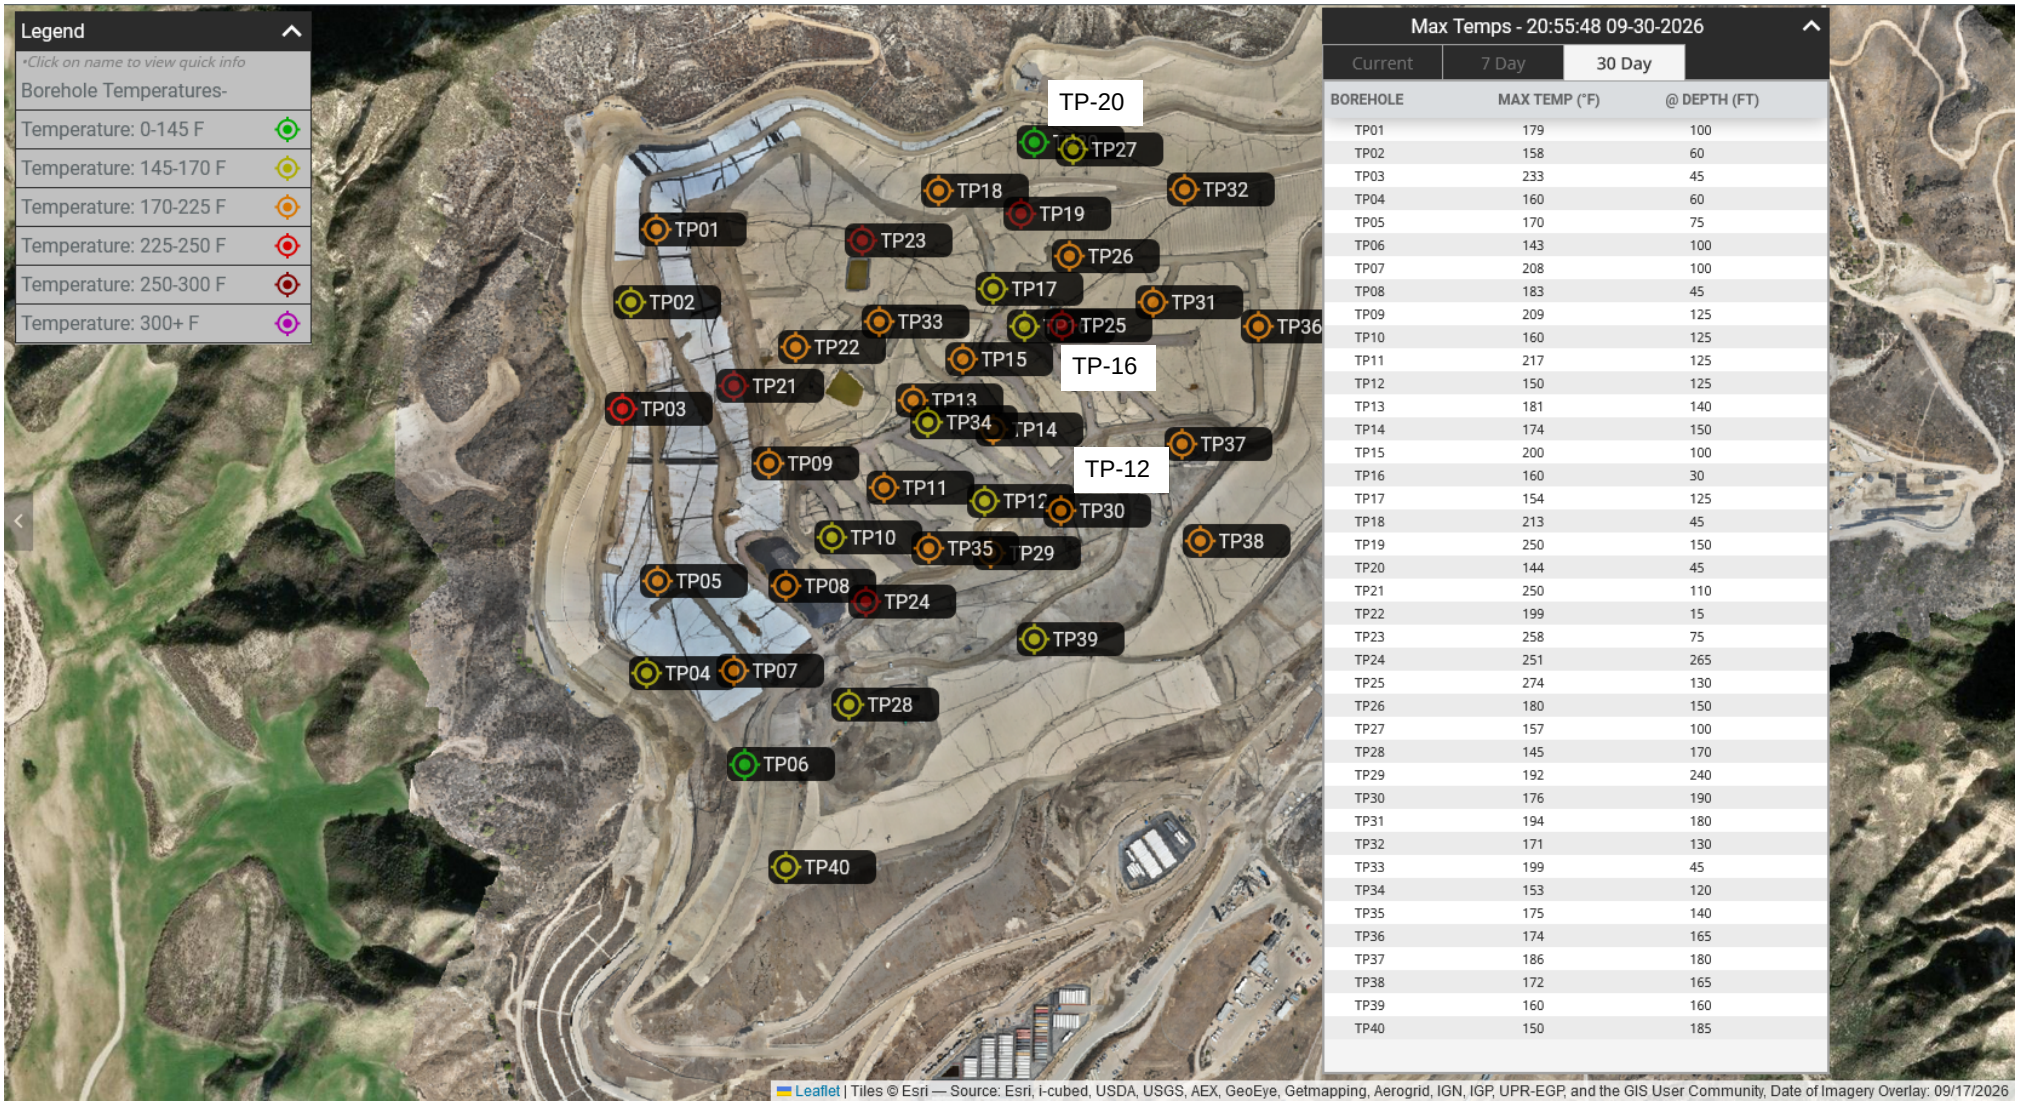

Max Temps - 20:55:48 09-30-2026

Current | 7 Day | 30 Day

BOREHOLE	MAX TEMP (°F)	@ DEPTH (FT)
TP01	179	100
TP02	158	60
TP03	233	45
TP04	160	60
TP05	170	75
TP06	143	100
TP07	208	100
TP08	183	45
TP09	209	125
TP10	160	125
TP11	217	125
TP12	150	125
TP13	181	140
TP14	174	150
TP15	200	100
TP16	160	30
TP17	154	125
TP18	213	45
TP19	250	150
TP20	144	45
TP21	250	110
TP22	199	15
TP23	258	75
TP24	251	265
TP25	274	130
TP26	180	150
TP27	157	100
TP28	145	170
TP29	192	240
TP30	176	190
TP31	194	180
TP32	171	130
TP33	199	45
TP34	153	120
TP35	175	140
TP36	174	165
TP37	186	180
TP38	172	165
TP39	160	160
TP40	150	185

Solid Waste Daily Borehole Temperature Averages

for September 1, 2026 to September 30, 2026

SCS ENGINEERS

07224053.00 | October 7, 2026

274 Granite Run Drive
Lancaster, PA 17601
717-550-6330

Note: Data represents the arithmatic mean of the available temperature readings for the specified date.

Solid Waste Daily Borehole Temperature Averages for Borehole 1

Chiquita LF

	Depth from Surface						
TP-01	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**	**125 ft**
Sep 1	173.6	128.3	138.5	144.3	147.0	166.4	152.0
Sep 2	174.8	128.4	138.4	144.5	147.1	166.8	152.1
Sep 3	174.4	128.4	138.4	144.6	147.1	167.3	152.3
Sep 4	175.8	128.4	138.3	144.7	147.1	167.8	152.4
Sep 5	176.3	128.6	138.3	144.8	147.2	168.2	152.6
Sep 6	174.7	128.2	138.1	144.5	147.0	168.3	152.3
Sep 7	176.3	128.7	138.3	144.9	147.5	169.0	152.8
Sep 8	176.7	128.7	138.2	145.0	147.5	169.6	153.0
Sep 9	176.7	129.2	138.7	145.4	147.9	170.3	153.6
Sep 10	178.2	129.2	138.5	145.4	147.8	170.6	153.6
Sep 11	177.9	129.0	138.4	145.5	147.6	171.0	153.6
Sep 12	177.3	129.0	138.3	145.7	147.5	171.4	153.7
Sep 13	176.6	128.9	138.3	145.7	147.5	171.8	153.7
Sep 14	175.8	129.0	138.5	145.8	147.5	172.3	153.8
Sep 15	175.6	128.9	138.4	145.9	147.4	172.7	153.9
Sep 16	176.0	128.8	138.7	145.9	147.4	173.0	153.9
Sep 17	175.7	128.9	139.3	146.0	147.5	173.4	154.0
Sep 18	175.3	128.9	139.7	146.2	147.5	174.0	154.2
Sep 19	174.9	129.0	140.0	146.3	147.5	174.4	154.4
Sep 20	175.3	129.0	139.9	146.3	147.5	174.7	154.4
Sep 21	175.3	129.0	139.9	146.4	147.5	175.1	154.5
Sep 22	175.4	129.2	140.0	146.6	147.6	175.7	154.8
Sep 23	174.1	129.5	140.2	146.9	148.0	176.2	155.2
Sep 24	173.3	129.4	140.2	146.8	147.8	176.5	155.2
Sep 25	172.4	129.5	140.3	146.9	147.9	177.0	155.4
Sep 26	172.4	129.6	140.3	147.1	147.9	177.5	155.6
Sep 27	173.5	129.5	140.1	147.1	148.0	177.8	155.6
Sep 28	173.7	129.4	140.1	147.2	147.9	178.2	155.7
Sep 29	173.5	129.6	140.1	147.3	148.1	178.7	155.9
Sep 30	173.9	129.7	140.0	147.4	148.0	179.0	156.1
Average	**175.2**	**129.0**	**139.1**	**145.9**	**147.6**	**172.8**	**154.0**

Solid Waste Daily Borehole Temperature Averages for Borehole 2

Chiquita LF

	Depth from Surface			
TP-02	**15 ft**	**30 ft**	**45 ft**	**60 ft**
Sep 1	113.9	138.6	146.6	156.3
Sep 2	113.9	138.5	146.5	156.3
Sep 3	114.0	138.5	146.6	156.4
Sep 4	114.0	138.6	146.6	156.4
Sep 5	114.1	138.7	146.7	156.4
Sep 6	113.6	138.3	146.3	156.0
Sep 7	114.1	138.5	146.5	156.3
Sep 8	114.0	138.4	146.4	156.2
Sep 9	114.5	138.8	146.8	156.4
Sep 10	114.5	138.8	146.8	156.6
Sep 11	114.3	138.7	146.7	156.5
Sep 12	114.3	138.8	146.7	156.5
Sep 13	114.1	138.6	146.6	156.5
Sep 14	114.2	138.6	146.6	156.4
Sep 15	114.1	138.5	146.6	156.4
Sep 16	114.2	138.5	146.5	156.4
Sep 17	114.2	138.4	146.5	156.4
Sep 18	114.3	138.5	146.5	156.5
Sep 19	114.5	138.6	146.7	156.6
Sep 20	114.4	138.4	146.6	156.4
Sep 21	114.4	138.4	146.5	156.3
Sep 22	114.6	138.5	146.7	156.6
Sep 23	114.9	138.6	146.9	156.8
Sep 24	114.9	138.6	147.1	156.9
Sep 25	115.0	138.7	147.3	157.0
Sep 26	115.2	138.7	147.5	157.1
Sep 27	115.1	138.6	147.5	157.0
Sep 28	115.0	138.8	147.5	157.1
Sep 29	115.3	138.9	147.6	157.2
Sep 30	115.3	138.9	147.7	157.2
Average	**114.4**	**138.6**	**146.8**	**156.6**

Solid Waste Daily Borehole Temperature Averages for Borehole 3

Chiquita LF

	Depth from Surface		
TP-03	**15 ft**	**30 ft**	**45 ft**
Sep 1	198.5	211.6	231.5
Sep 2	198.4	211.6	231.5
Sep 3	198.6	211.6	231.5
Sep 4	198.4	211.5	231.5
Sep 5	198.7	211.7	231.7
Sep 6	198.0	211.2	231.2
Sep 7	198.5	211.6	231.5
Sep 8	198.3	211.7	231.5
Sep 9	199.0	212.1	231.9
Sep 10	199.2	212.0	231.9
Sep 11	199.1	211.7	231.8
Sep 12	198.9	211.7	231.8
Sep 13	198.8	211.5	231.6
Sep 14	198.6	211.5	231.6
Sep 15	198.5	211.5	231.5
Sep 16	198.2	211.5	231.3
Sep 17	197.9	211.6	231.4
Sep 18	197.9	211.4	231.4
Sep 19	198.2	211.3	231.5
Sep 20	198.1	211.3	231.5
Sep 21	198.3	211.2	231.4
Sep 22	198.6	211.1	231.4
Sep 23	198.7	211.3	231.6
Sep 24	198.5	211.3	231.5
Sep 25	198.3	211.4	231.6
Sep 26	198.4	211.5	231.6
Sep 27	198.4	211.4	231.4
Sep 28	198.3	211.1	231.4
Sep 29	198.8	211.0	231.4
Sep 30	198.5	211.1	231.5
Average	**198.5**	**211.5**	**231.5**

Solid Waste Daily Borehole Temperature Averages for Borehole 4

Chiquita LF

	Depth from Surface			
TP-04	**15 ft**	**30 ft**	**45 ft**	**60 ft**
Sep 1	152.1	157.3	156.4	157.8
Sep 2	152.2	157.4	156.4	157.8
Sep 3	152.1	157.3	156.5	157.9
Sep 4	152.4	157.4	156.6	157.9
Sep 5	152.5	157.6	156.8	158.1
Sep 6	152.2	157.3	156.5	157.8
Sep 7	152.7	157.6	156.9	158.2
Sep 8	152.6	157.5	156.8	158.1
Sep 9	152.9	157.8	157.0	158.3
Sep 10	153.0	157.8	157.0	158.4
Sep 11	152.6	157.6	156.8	158.3
Sep 12	152.9	157.7	156.9	158.4
Sep 13	152.9	157.7	156.9	158.3
Sep 14	152.8	157.6	156.9	158.3
Sep 15	152.8	157.5	156.8	158.4
Sep 16	153.1	157.6	157.0	158.5
Sep 17	153.0	157.5	156.9	158.4
Sep 18	153.0	157.6	157.0	158.4
Sep 19	153.4	157.7	157.1	158.6
Sep 20	153.5	157.6	157.1	158.5
Sep 21	153.3	157.5	157.0	158.5
Sep 22	153.7	157.6	157.2	158.7
Sep 23	154.0	157.8	157.4	158.8
Sep 24	153.9	157.6	157.3	158.7
Sep 25	154.0	157.8	157.4	158.8
Sep 26	154.1	157.8	157.4	158.8
Sep 27	154.0	157.7	157.4	158.8
Sep 28	154.0	157.7	157.3	158.7
Sep 29	154.1	157.8	157.4	158.8
Sep 30	154.1	157.8	157.5	158.9
Average	**153.1**	**157.6**	**157.0**	**158.4**

Solid Waste Daily Borehole Temperature Averages for Borehole 5

Chiquita LF

	Depth from Surface				
TP-05	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**75 ft**
Sep 1	137.2	155.6	160.1	161.0	167.8
Sep 2	137.2	155.6	160.0	161.0	167.7
Sep 3	137.2	155.6	160.0	161.0	167.8
Sep 4	137.2	155.6	160.0	161.0	167.9
Sep 5	137.2	155.6	160.0	161.1	167.9
Sep 6	136.5	155.2	159.7	161.0	167.7
Sep 7	137.2	155.3	159.6	161.0	167.9
Sep 8	137.1	155.4	159.5	160.9	167.9
Sep 9	137.6	155.7	159.7	161.1	168.1
Sep 10	137.6	155.6	159.7	161.1	168.1
Sep 11	137.4	155.6	159.6	161.2	168.2
Sep 12	137.3	155.5	159.6	161.2	168.2
Sep 13	137.1	155.5	159.5	161.2	168.3
Sep 14	137.1	155.5	159.5	161.2	168.3
Sep 15	137.0	155.4	159.4	161.2	168.4
Sep 16	136.9	155.4	159.4	161.2	168.4
Sep 17	136.9	155.4	159.4	161.3	168.4
Sep 18	136.8	155.4	159.3	161.1	168.5
Sep 19	136.8	155.4	159.3	161.2	168.6
Sep 20	136.8	155.5	159.4	161.2	168.7
Sep 21	136.7	155.4	159.3	161.3	168.7
Sep 22	136.7	155.5	159.3	161.3	168.8
Sep 23	136.9	155.6	159.3	161.3	168.9
Sep 24	136.8	155.5	159.4	161.4	169.0
Sep 25	136.8	155.5	159.4	161.4	169.1
Sep 26	136.8	155.6	159.3	161.4	169.1
Sep 27	136.7	155.5	159.3	161.4	169.2
Sep 28	136.7	155.5	159.3	161.5	169.3
Sep 29	136.7	155.6	159.3	161.6	169.4
Sep 30	136.7	155.6	159.4	161.7	169.5
Average	**137.0**	**155.5**	**159.5**	**161.2**	**168.5**

Solid Waste Daily Borehole Temperature Averages for Borehole 6

Chiquita LF

	Depth from Surface							
TP-06	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**	**120 ft**	**140 ft**
Sep 1	111.5	115.5	117.4	116.2	131.0	139.8	138.5	141.6
Sep 2	111.4	115.5	117.4	116.2	130.9	139.9	138.5	141.6
Sep 3	111.6	115.5	117.5	116.2	131.0	139.9	138.6	141.7
Sep 4	111.6	115.6	117.5	116.2	131.1	139.9	138.6	141.7
Sep 5	111.7	115.6	117.6	116.2	131.1	139.9	138.7	141.7
Sep 6	111.4	115.4	117.6	116.2	130.8	139.9	138.6	141.7
Sep 7	111.8	115.7	117.8	116.3	131.2	140.1	138.8	141.9
Sep 8	111.8	115.6	117.6	116.2	131.1	140.0	138.7	141.7
Sep 9	112.0	115.8	117.7	116.3	131.4	140.1	138.9	141.9
Sep 10	112.1	115.9	118.1	116.7	131.4	140.2	139.2	142.3
Sep 11	112.0	115.9	118.1	116.8	131.2	140.3	139.2	142.5
Sep 12	111.9	115.8	118.1	116.9	131.1	140.3	139.2	142.5
Sep 13	112.0	115.8	118.1	116.9	131.1	140.3	139.2	142.5
Sep 14	111.9	115.8	118.0	116.9	131.0	140.2	139.1	142.4
Sep 15	111.9	115.8	118.2	117.1	131.0	140.4	139.3	142.6
Sep 16	111.8	115.8	118.0	116.9	130.9	140.4	139.2	142.5
Sep 17	111.9	115.8	118.0	117.0	131.1	140.4	139.3	142.6
Sep 18	111.9	115.8	118.1	117.0	131.1	140.4	139.2	142.6
Sep 19	111.9	115.7	118.0	116.9	131.1	140.4	139.1	142.4
Sep 20	111.8	115.8	118.1	116.9	131.0	140.3	139.1	142.4
Sep 21	111.9	115.8	118.3	117.1	131.1	140.5	139.3	142.7
Sep 22	112.0	115.7	117.9	116.5	131.1	140.2	138.8	141.9
Sep 23	112.3	115.9	118.0	116.5	131.4	140.2	138.9	142.0
Sep 24	112.2	115.8	118.0	116.6	131.1	140.2	138.8	141.9
Sep 25	112.3	115.9	118.0	116.6	131.3	140.2	138.8	141.9
Sep 26	112.3	115.9	118.0	116.6	131.2	140.2	138.8	141.9
Sep 27	112.4	115.9	118.1	116.6	131.3	140.2	138.8	141.9
Sep 28	112.4	115.9	118.2	116.6	131.2	140.2	138.7	141.8
Sep 29	112.5	115.9	118.4	116.5	131.2	140.2	138.8	141.9
Sep 30	112.5	115.9	118.5	116.6	131.2	140.2	138.9	141.9
Average	**112.0**	**115.8**	**117.9**	**116.6**	**131.1**	**140.2**	**138.9**	**142.1**

Solid Waste Daily Borehole Temperature Averages for Borehole 7

Chiquita LF

	Depth from Surface					
TP-07	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**75 ft**	**100 ft**
Sep 1	146.2	128.9	136.3	138.3	144.3	190.2
Sep 2	146.3	128.9	136.3	138.4	144.2	193.1
Sep 3	146.5	129.0	136.2	138.4	144.3	196.7
Sep 4	146.5	129.0	136.2	138.4	144.3	199.9
Sep 5	146.6	129.0	136.2	138.5	144.5	201.8
Sep 6	146.7	128.9	136.1	138.3	144.1	203.1
Sep 7	146.7	129.0	136.1	138.4	144.4	205.0
Sep 8	146.7	128.9	135.9	138.2	144.4	205.6
Sep 9	146.9	129.1	136.1	138.5	144.8	206.7
Sep 10	147.0	129.1	136.1	138.5	144.9	207.0
Sep 11	147.0	129.1	136.1	138.5	144.7	207.0
Sep 12	147.2	129.1	136.1	138.5	144.6	207.1
Sep 13	147.3	129.1	136.0	138.5	144.4	206.9
Sep 14	147.5	129.1	136.0	138.5	144.4	207.0
Sep 15	147.7	129.1	136.0	138.5	144.3	207.1
Sep 16	147.9	129.1	136.0	138.6	144.3	207.2
Sep 17	148.1	129.1	136.0	138.6	144.2	207.3
Sep 18	148.3	129.1	135.9	138.5	144.3	207.3
Sep 19	148.5	129.1	135.9	138.5	144.3	207.1
Sep 20	148.6	129.1	135.9	138.5	144.2	207.0
Sep 21	148.8	129.1	136.0	138.7	144.2	207.0
Sep 22	148.9	129.1	135.8	138.5	144.3	206.9
Sep 23	149.3	129.3	136.0	138.7	144.6	207.2
Sep 24	149.5	129.2	135.9	138.6	144.4	207.1
Sep 25	149.9	129.3	135.9	138.7	144.5	207.1
Sep 26	150.0	129.2	135.9	138.6	144.4	207.1
Sep 27	150.3	129.2	135.8	138.6	144.4	207.0
Sep 28	150.5	129.2	135.8	138.6	144.3	206.9
Sep 29	150.8	129.4	135.9	138.7	144.5	207.0
Sep 30	151.1	129.4	135.9	138.7	144.4	207.2
Average	**148.1**	**129.1**	**136.0**	**138.5**	**144.4**	**205.0**

Solid Waste Daily Borehole Temperature Averages for Borehole 8

Chiquita LF

	Depth from Surface		
TP-08	**15 ft**	**30 ft**	**45 ft**
Sep 1	136.8	175.3	181.0
Sep 2	150.3	176.1	180.2
Sep 3	153.0	175.0	179.9
Sep 4	154.4	176.1	181.3
Sep 5	155.3	175.2	181.5
Sep 6	155.6	173.4	180.2
Sep 7	156.6	173.8	181.7
Sep 8	156.8	173.6	181.5
Sep 9	157.4	173.9	182.0
Sep 10	156.1	168.7	172.2
Sep 11	151.4	159.8	162.8
Sep 12	152.5	161.1	158.9
Sep 13	152.4	161.2	157.5
Sep 14	152.8	165.5	166.9
Sep 15	153.9	165.6	163.0
Sep 16	155.5	164.7	156.8
Sep 17	154.9	163.5	154.8
Sep 18	155.1	164.1	156.4
Sep 19	155.1	164.3	155.7
Sep 20	155.3	164.6	156.2
Sep 21	156.0	165.8	163.6
Sep 22	157.0	168.1	170.5
Sep 23	155.5	165.5	160.1
Sep 24	153.5	162.6	155.0
Sep 25	152.9	161.8	154.7
Sep 26	152.8	162.0	155.0
Sep 27	153.2	162.4	155.7
Sep 28	153.1	162.3	155.3
Sep 29	152.8	161.9	155.7
Sep 30	153.1	162.3	156.3
Average	**153.7**	**167.0**	**165.7**

Solid Waste Daily Borehole Temperature Averages for Borehole 9

Chiquita LF

	Depth from Surface						
TP-09	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**	**125 ft**
Sep 1	110.9	122.6	129.8	136.2	141.1	177.5	207.6
Sep 2	110.8	122.6	129.8	136.2	141.1	177.3	207.6
Sep 3	110.9	122.7	129.8	136.2	141.1	178.0	207.5
Sep 4	110.9	122.7	129.9	136.2	141.2	178.2	207.5
Sep 5	110.9	122.8	129.9	136.2	141.2	178.1	207.6
Sep 6	110.8	122.5	129.6	135.9	141.0	177.8	207.2
Sep 7	111.0	122.8	129.8	136.1	141.3	178.1	207.5
Sep 8	110.8	122.7	129.8	136.1	141.3	178.1	207.6
Sep 9	111.1	123.0	130.0	136.4	141.7	178.4	208.1
Sep 10	111.1	122.9	130.0	136.3	141.8	179.0	207.9
Sep 11	111.0	122.9	130.0	136.3	141.6	179.5	207.7
Sep 12	111.1	122.9	130.0	136.3	141.6	179.4	207.7
Sep 13	111.1	122.9	130.0	136.3	141.5	179.7	207.5
Sep 14	111.1	122.9	130.0	136.3	141.5	180.2	207.4
Sep 15	111.1	122.9	130.0	136.3	141.5	179.8	207.4
Sep 16	111.1	122.9	129.9	136.3	141.5	179.2	207.5
Sep 17	111.0	122.9	129.9	136.2	141.5	178.7	207.6
Sep 18	111.1	122.9	130.0	136.4	141.5	178.9	207.6
Sep 19	111.1	123.0	130.0	136.4	141.6	179.7	207.5
Sep 20	111.0	122.9	129.9	136.2	141.5	180.0	207.3
Sep 21	111.1	122.9	130.0	136.3	141.6	179.9	207.3
Sep 22	111.1	123.0	130.1	136.4	141.6	180.3	207.4
Sep 23	111.1	123.1	130.1	136.4	141.9	180.7	207.6
Sep 24	111.2	123.1	130.1	136.5	141.8	180.3	207.5
Sep 25	111.2	123.1	130.2	136.5	141.9	180.3	207.6
Sep 26	111.2	123.1	130.2	136.5	141.9	180.4	207.6
Sep 27	111.2	123.1	130.1	136.4	141.9	180.6	207.5
Sep 28	111.3	123.1	130.2	136.5	141.8	181.3	207.3
Sep 29	111.3	123.2	130.2	136.5	142.0	182.7	207.3
Sep 30	111.4	123.2	130.2	136.6	142.0	182.4	207.5
Average	**111.1**	**122.9**	**130.0**	**136.3**	**141.5**	**179.5**	**207.5**

Solid Waste Daily Borehole Temperature Averages for Borehole 10

Chiquita LF

	Depth from Surface						
TP-10	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**	**125 ft**
Sep 1	124.8	133.6	140.0	142.4	139.7	141.9	155.0
Sep 2	125.1	134.5	140.1	142.3	139.3	141.6	154.9
Sep 3	125.4	134.7	140.0	142.4	139.5	141.8	155.0
Sep 4	125.5	133.7	139.7	142.5	139.0	141.5	155.5
Sep 5	125.5	132.8	139.3	142.8	139.7	142.0	156.1
Sep 6	124.9	131.2	138.3	142.3	139.4	141.6	155.7
Sep 7	125.3	133.7	138.9	142.6	140.1	142.2	156.3
Sep 8	125.0	135.8	140.2	142.2	139.9	142.1	155.7
Sep 9	125.8	137.1	140.9	142.7	140.7	142.8	155.7
Sep 10	125.7	137.8	141.0	142.6	140.4	142.7	155.2
Sep 11	125.7	137.0	140.7	142.7	139.5	142.3	155.5
Sep 12	125.5	135.8	140.4	142.8	140.2	142.7	156.1
Sep 13	125.3	134.7	140.1	142.9	140.6	142.9	156.5
Sep 14	125.2	135.1	140.1	142.8	140.5	142.7	156.7
Sep 15	125.3	136.9	140.5	142.4	139.9	142.1	156.0
Sep 16	125.7	136.8	140.6	142.4	139.4	141.9	155.7
Sep 17	125.8	137.0	140.5	142.4	139.1	141.8	155.4
Sep 18	125.9	134.7	140.4	142.7	140.1	142.6	155.9
Sep 19	125.8	134.5	140.2	142.8	140.7	142.8	156.1
Sep 20	125.8	137.7	140.4	142.6	139.6	142.1	155.6
Sep 21	125.9	136.4	140.5	142.5	138.6	141.7	155.6
Sep 22	126.1	134.6	140.7	142.7	139.7	142.3	156.3
Sep 23	126.0	133.7	140.6	143.0	141.0	143.1	156.7
Sep 24	125.9	133.6	140.7	143.0	140.6	142.9	156.8
Sep 25	125.9	133.3	140.8	143.1	140.9	143.1	157.1
Sep 26	125.8	132.1	140.6	143.2	141.3	143.3	157.2
Sep 27	125.6	131.6	140.3	143.1	141.4	143.3	157.1
Sep 28	125.4	131.1	140.2	143.2	141.5	143.3	157.2
Sep 29	125.3	130.7	140.2	143.2	141.9	143.6	157.4
Sep 30	125.2	130.4	140.2	143.3	142.0	143.6	157.5
Average	**125.5**	**134.4**	**140.2**	**142.7**	**140.2**	**142.5**	**156.1**

Solid Waste Daily Borehole Temperature Averages for Borehole 11

Chiquita LF

	Depth from Surface					
TP-11	**15 ft**	**30 ft**	**45 ft**	**80 ft**	**100 ft**	**125 ft**
Sep 1	171.7	186.3	189.0	199.1	211.3	212.2
Sep 2	171.7	186.1	188.6	199.0	211.4	212.1
Sep 3	171.4	185.3	187.9	198.5	211.1	211.7
Sep 4	171.5	185.7	188.5	199.3	212.0	212.5
Sep 5	171.7	186.0	188.7	199.5	212.1	212.7
Sep 6	171.5	185.7	188.4	199.1	211.8	212.2
Sep 7	171.8	186.2	188.8	199.7	212.3	212.9
Sep 8	172.1	187.4	190.4	201.6	214.1	215.1
Sep 9	172.7	188.0	190.9	202.3	214.5	215.7
Sep 10	172.9	187.8	190.7	202.2	214.4	215.5
Sep 11	172.8	187.4	190.4	201.6	213.8	214.9
Sep 12	172.5	187.2	190.2	201.1	213.5	214.5
Sep 13	172.5	187.2	190.3	201.2	213.6	214.6
Sep 14	172.4	187.2	190.4	201.4	213.9	214.9
Sep 15	172.5	187.5	190.5	201.5	214.2	215.0
Sep 16	172.5	187.3	190.5	201.3	214.0	214.8
Sep 17	172.6	187.2	190.4	201.3	213.9	214.7
Sep 18	172.5	187.2	190.5	201.4	214.1	214.9
Sep 19	172.5	187.0	190.4	201.5	214.2	215.0
Sep 20	172.5	187.4	190.4	201.7	214.5	215.3
Sep 21	172.7	187.3	190.4	201.7	214.5	215.2
Sep 22	172.8	187.6	190.5	202.0	214.6	215.5
Sep 23	172.6	187.7	190.5	202.2	214.7	215.7
Sep 24	172.5	187.6	190.5	202.1	214.8	215.7
Sep 25	172.6	187.7	190.6	202.2	214.7	215.7
Sep 26	172.7	187.5	190.7	202.3	214.8	215.8
Sep 27	172.8	187.3	190.6	202.1	214.5	215.5
Sep 28	172.6	187.0	190.5	202.0	214.5	215.4
Sep 29	172.6	187.2	190.6	202.1	214.6	215.6
Sep 30	172.7	187.3	190.7	202.2	214.6	215.6
Average	**172.4**	**187.0**	**190.1**	**201.2**	**213.7**	**214.6**

Solid Waste Daily Borehole Temperature Averages for Borehole 12

Chiquita LF

	Depth from Surface					
TP-12	**15 ft**	**30 ft**	**45 ft**	**80 ft**	**100 ft**	**125 ft**
Sep 1	100.3	120.4	125.3	134.5	138.6	148.3
Sep 2	100.4	120.4	125.3	134.5	138.6	148.3
Sep 3	100.4	120.4	125.2	134.5	138.7	148.3
Sep 4	100.5	120.5	125.3	134.6	138.7	148.3
Sep 5	100.6	120.6	125.4	134.7	138.8	148.4
Sep 6	100.3	120.1	125.0	134.3	138.4	148.1
Sep 7	100.7	120.5	125.3	134.7	138.9	148.4
Sep 8	100.7	120.6	125.4	134.8	139.0	148.6
Sep 9	101.1	121.0	125.7	135.2	139.4	148.8
Sep 10	101.1	121.0	125.7	135.1	139.4	148.8
Sep 11	101.0	120.8	125.6	135.0	139.2	148.6
Sep 12	101.0	120.8	125.6	134.9	139.1	148.6
Sep 13	100.9	120.6	125.5	134.8	139.0	148.5
Sep 14	101.0	120.6	125.5	134.8	138.9	148.5
Sep 15	100.9	120.5	125.4	134.7	138.8	148.4
Sep 16	100.9	120.4	125.4	134.6	138.7	148.4
Sep 17	100.9	120.5	125.3	134.6	138.7	148.4
Sep 18	101.0	120.5	125.5	134.7	138.8	148.4
Sep 19	101.1	120.5	125.5	134.7	138.8	148.5
Sep 20	101.1	120.5	125.4	134.7	138.7	148.4
Sep 21	101.1	120.4	125.4	134.7	138.7	148.4
Sep 22	101.3	120.6	125.5	134.8	138.9	148.5
Sep 23	101.5	120.8	125.7	135.0	139.2	148.7
Sep 24	101.5	120.8	125.6	134.9	139.0	148.6
Sep 25	101.6	120.8	125.6	135.0	139.1	148.6
Sep 26	101.6	120.9	125.6	135.0	139.1	148.6
Sep 27	101.6	120.8	125.6	135.0	139.1	148.7
Sep 28	101.5	120.7	125.5	134.8	139.0	148.5
Sep 29	101.8	120.9	125.6	135.0	139.1	148.6
Sep 30	101.8	120.8	125.6	134.9	139.1	148.6
Average	**101.0**	**120.6**	**125.5**	**134.8**	**138.9**	**148.5**

Solid Waste Daily Borehole Temperature Averages for Borehole 13

Chiquita LF

	Depth from Surface					
TP-13	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**100 ft**	**140 ft**
Sep 1	145.9	151.3	150.8	159.9	166.2	175.6
Sep 2	145.9	151.4	151.3	160.3	163.5	177.8
Sep 3	146.1	151.5	151.1	159.5	162.3	178.3
Sep 4	146.0	151.4	150.9	159.2	160.6	176.6
Sep 5	145.9	151.4	150.6	159.4	165.5	175.3
Sep 6	145.4	150.8	150.0	158.7	164.1	175.4
Sep 7	145.7	151.1	150.3	158.5	161.2	176.4
Sep 8	145.5	151.0	150.3	158.6	162.9	176.2
Sep 9	145.8	151.2	150.7	157.5	165.9	173.4
Sep 10	145.7	150.8	150.8	157.4	167.9	172.9
Sep 11	145.7	150.8	150.7	157.2	166.6	174.7
Sep 12	145.3	150.7	150.8	157.3	165.5	175.8
Sep 13	145.8	150.9	150.8	156.4	162.7	176.7
Sep 14	145.8	150.9	150.7	155.8	162.3	176.5
Sep 15	145.8	150.9	151.0	155.4	164.1	178.2
Sep 16	145.9	151.0	151.5	156.2	164.6	178.9
Sep 17	145.8	150.9	151.8	154.8	162.6	178.2
Sep 18	145.5	150.6	151.7	154.3	159.1	176.6
Sep 19	145.1	150.2	151.7	153.2	163.7	175.3
Sep 20	144.8	150.0	151.4	152.6	166.4	174.3
Sep 21	144.7	149.9	151.3	151.5	165.9	174.3
Sep 22	144.5	149.9	151.5	150.6	167.6	174.4
Sep 23	144.8	149.6	152.0	151.3	170.2	172.1
Sep 24	144.5	149.2	151.8	150.6	167.8	170.3
Sep 25	144.2	148.8	151.7	150.4	168.4	170.5
Sep 26	144.0	148.6	151.0	150.7	168.3	170.4
Sep 27	143.9	148.4	150.4	151.2	168.4	170.5
Sep 28	143.9	148.4	150.2	151.6	168.8	170.8
Sep 29	143.9	148.3	150.1	152.3	169.2	171.1
Sep 30	144.0	148.4	150.9	152.6	169.8	171.6
Average	**145.2**	**150.3**	**151.0**	**155.2**	**165.4**	**174.6**

Solid Waste Daily Borehole Temperature Averages for Borehole 14

Chiquita LF

	Depth from Surface						
TP-14	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**100 ft**	**125 ft**	**150 ft**
Sep 1	91.5	112.7	129.0	145.2	157.2	167.0	172.6
Sep 2	91.4	112.7	129.0	145.2	157.2	167.0	172.6
Sep 3	91.6	112.7	129.0	145.2	157.2	167.0	172.7
Sep 4	91.6	112.7	129.0	145.2	157.2	167.0	172.7
Sep 5	91.8	112.7	129.1	145.3	157.3	167.2	172.8
Sep 6	91.4	112.4	128.9	144.9	157.1	166.9	172.6
Sep 7	91.9	112.7	129.1	145.2	157.3	167.2	172.9
Sep 8	91.9	112.6	129.2	145.3	157.3	167.3	172.9
Sep 9	92.4	112.8	129.4	145.7	157.5	167.7	173.1
Sep 10	92.4	112.8	129.4	145.7	157.4	167.7	173.1
Sep 11	92.3	112.7	129.3	145.5	157.3	167.5	173.0
Sep 12	92.3	112.6	129.3	145.4	157.3	167.4	173.0
Sep 13	92.2	112.5	129.2	145.4	157.2	167.3	172.9
Sep 14	92.2	112.6	129.2	145.3	157.2	167.3	172.9
Sep 15	92.2	112.5	129.3	145.3	157.3	167.3	172.9
Sep 16	92.1	112.4	129.2	145.2	157.2	167.2	172.9
Sep 17	92.1	112.4	129.2	145.2	157.2	167.3	172.9
Sep 18	92.3	112.4	129.3	145.2	157.2	167.2	172.9
Sep 19	92.3	112.4	129.3	145.1	157.1	167.3	172.9
Sep 20	92.2	112.3	129.2	145.1	157.2	167.3	172.9
Sep 21	92.2	112.3	129.2	145.1	157.2	167.3	173.0
Sep 22	92.4	112.3	129.3	145.1	157.2	167.4	173.0
Sep 23	92.9	112.5	129.3	145.5	157.3	167.7	173.2
Sep 24	92.7	112.3	129.3	145.3	157.2	167.6	173.1
Sep 25	92.7	112.4	129.3	145.4	157.3	167.7	173.1
Sep 26	92.8	112.4	129.4	145.4	157.3	167.6	173.2
Sep 27	92.7	112.3	129.4	145.3	157.2	167.6	173.2
Sep 28	92.6	112.2	129.3	145.2	157.2	167.4	173.0
Sep 29	92.8	112.3	129.3	145.3	157.2	167.7	173.1
Sep 30	92.8	112.3	129.4	145.4	157.3	167.7	173.3
Average	**92.2**	**112.5**	**129.2**	**145.3**	**157.2**	**167.4**	**172.9**

Solid Waste Daily Borehole Temperature Averages for Borehole 15

Chiquita LF

	Depth from Surface				
TP-15	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**100 ft**
Sep 1	178.2	174.3	177.6	182.3	195.9
Sep 2	178.0	174.6	179.1	182.8	196.7
Sep 3	176.6	173.9	183.3	184.5	191.1
Sep 4	176.1	174.9	185.9	186.7	191.6
Sep 5	175.5	177.0	187.5	188.3	192.4
Sep 6	175.4	177.2	188.2	188.9	192.6
Sep 7	175.6	178.5	189.2	189.9	193.1
Sep 8	175.6	178.5	189.4	190.2	193.3
Sep 9	175.9	179.4	190.1	191.0	193.9
Sep 10	176.9	181.3	191.1	192.0	194.8
Sep 11	176.9	181.6	191.2	192.1	194.9
Sep 12	177.3	181.9	191.5	192.4	195.1
Sep 13	176.7	182.4	191.7	192.5	195.3
Sep 14	177.0	182.5	191.9	192.7	195.3
Sep 15	177.4	182.8	192.3	193.0	195.6
Sep 16	177.6	183.3	192.5	193.3	195.9
Sep 17	177.1	183.2	192.6	193.3	195.9
Sep 18	176.9	183.3	192.7	193.5	196.0
Sep 19	176.2	183.5	192.8	193.6	196.0
Sep 20	176.3	183.7	192.9	193.6	196.1
Sep 21	176.4	184.1	193.0	193.6	196.1
Sep 22	176.6	184.4	193.0	193.8	196.2
Sep 23	176.2	184.4	192.8	193.6	196.1
Sep 24	176.4	184.3	192.9	193.8	196.3
Sep 25	176.6	184.5	193.0	193.9	196.5
Sep 26	176.7	184.8	193.0	193.9	196.4
Sep 27	177.0	185.3	193.1	194.0	196.5
Sep 28	176.7	186.3	193.0	193.8	196.3
Sep 29	176.6	187.1	192.8	193.7	196.3
Sep 30	176.7	186.7	193.1	193.9	196.4
Average	**176.6**	**181.7**	**190.4**	**191.5**	**195.2**

Solid Waste Daily Borehole Temperature Averages for Borehole 16

Chiquita LF

	Depth from Surface					
TP-16	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**
Sep 1	132.3	159.4	151.6	144.1	141.7	143.1
Sep 2	132.9	159.3	151.6	144.1	141.6	143.0
Sep 3	132.1	159.2	151.7	144.1	141.5	143.1
Sep 4	134.2	159.2	151.8	144.1	141.6	143.1
Sep 5	133.7	159.2	151.9	144.1	141.7	143.2
Sep 6	131.7	159.1	151.8	144.1	141.4	142.9
Sep 7	134.1	159.6	152.1	144.3	141.8	143.3
Sep 8	133.1	159.4	152.0	144.2	141.8	143.2
Sep 9	133.4	159.5	152.4	144.4	142.2	143.6
Sep 10	134.2	159.6	152.4	144.4	142.2	143.6
Sep 11	132.0	159.3	152.3	144.3	142.1	143.4
Sep 12	131.8	159.3	152.3	144.4	142.1	143.3
Sep 13	131.0	159.4	152.3	144.4	142.1	143.3
Sep 14	129.6	159.5	152.3	144.4	142.0	143.2
Sep 15	128.8	159.6	152.4	144.6	142.0	143.2
Sep 16	128.4	159.6	152.4	144.6	141.9	143.2
Sep 17	126.3	159.4	152.4	144.6	142.0	143.2
Sep 18	128.0	159.0	152.4	144.5	142.0	143.2
Sep 19	127.0	158.7	152.5	144.6	142.1	143.3
Sep 20	127.2	158.6	152.6	144.7	142.1	143.3
Sep 21	126.5	158.4	152.6	144.8	142.1	143.3
Sep 22	127.3	158.2	152.6	144.7	142.2	143.3
Sep 23	126.7	158.0	152.9	144.7	142.4	143.5
Sep 24	126.6	157.8	152.8	144.7	142.4	143.4
Sep 25	126.8	157.6	152.9	144.8	142.4	143.5
Sep 26	127.6	157.5	153.0	144.8	142.5	143.5
Sep 27	129.0	157.3	153.0	144.8	142.5	143.5
Sep 28	127.4	157.1	152.9	144.8	142.4	143.4
Sep 29	126.7	157.0	153.1	144.9	142.7	143.6
Sep 30	127.1	156.9	153.2	145.0	142.7	143.7
Average	**129.8**	**158.7**	**152.4**	**144.5**	**142.1**	**143.3**

Solid Waste Daily Borehole Temperature Averages for Borehole 17

Chiquita LF

	Depth from Surface						
TP-17	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**	**125 ft**
Sep 1	142.2	149.0	138.7	136.9	142.0	143.7	152.2
Sep 2	142.4	148.6	138.5	136.7	141.9	143.6	152.2
Sep 3	142.3	148.8	138.8	136.7	141.9	143.8	152.2
Sep 4	142.7	148.6	138.5	136.6	141.9	143.8	152.3
Sep 5	142.8	148.6	138.6	136.7	142.1	144.0	152.4
Sep 6	141.9	148.6	138.5	136.3	141.7	143.4	152.0
Sep 7	142.9	149.7	138.8	136.7	142.0	144.0	152.7
Sep 8	143.2	150.6	138.5	136.5	141.7	143.9	152.8
Sep 9	144.3	150.9	138.7	136.7	142.2	144.2	153.4
Sep 10	145.8	150.8	138.3	136.5	141.9	144.2	153.0
Sep 11	145.4	149.1	138.6	136.3	141.8	144.0	152.9
Sep 12	144.7	148.0	138.7	136.4	142.1	144.0	153.0
Sep 13	144.0	147.2	138.6	136.4	142.2	143.9	152.9
Sep 14	143.4	145.8	139.1	136.6	142.3	144.0	152.9
Sep 15	142.6	147.5	139.3	136.7	142.1	143.9	152.8
Sep 16	140.1	149.9	139.3	136.8	142.3	143.8	152.8
Sep 17	142.3	149.9	139.4	137.0	142.3	143.8	153.0
Sep 18	144.0	147.9	139.2	137.0	142.5	143.9	152.9
Sep 19	143.7	147.7	139.5	136.7	142.5	143.8	152.9
Sep 20	143.4	147.4	139.3	136.5	142.4	143.7	152.9
Sep 21	143.2	147.5	139.8	136.4	142.3	143.7	153.0
Sep 22	143.5	147.6	140.9	136.4	142.3	143.9	153.2
Sep 23	143.4	147.8	141.3	136.7	142.6	144.0	153.4
Sep 24	143.0	147.5	141.2	137.1	142.5	143.9	153.3
Sep 25	143.0	147.4	141.4	137.2	142.7	143.9	153.4
Sep 26	142.8	147.1	141.4	137.1	142.7	144.0	153.5
Sep 27	142.3	146.4	140.7	137.1	142.7	143.9	153.4
Sep 28	141.8	146.2	140.9	137.1	142.6	143.8	153.3
Sep 29	141.6	146.3	141.4	137.1	142.7	144.0	153.5
Sep 30	141.7	146.3	141.4	137.2	142.6	144.0	153.5
Average	**143.0**	**148.2**	**139.6**	**136.7**	**142.2**	**143.9**	**152.9**

Solid Waste Daily Borehole Temperature Averages for Borehole 18

Chiquita LF

	Depth from Surface		
TP-18	**15 ft**	**30 ft**	**45 ft**
Sep 1	137.7	173.1	210.0
Sep 2	137.6	173.1	209.8
Sep 3	137.6	173.3	209.8
Sep 4	137.6	173.4	209.8
Sep 5	137.7	173.6	209.9
Sep 6	137.2	173.2	209.5
Sep 7	137.7	174.8	209.7
Sep 8	137.7	177.3	208.4
Sep 9	138.1	178.4	208.8
Sep 10	138.1	178.8	208.3
Sep 11	138.1	178.8	208.3
Sep 12	138.1	178.2	209.1
Sep 13	138.1	178.2	209.0
Sep 14	138.2	177.6	209.2
Sep 15	138.1	176.6	210.1
Sep 16	138.1	176.9	210.1
Sep 17	138.3	177.5	209.7
Sep 18	138.3	177.8	209.7
Sep 19	138.5	177.9	209.7
Sep 20	138.6	177.9	209.7
Sep 21	138.7	177.9	209.8
Sep 22	139.0	177.8	210.1
Sep 23	139.3	178.0	210.2
Sep 24	139.3	177.8	210.2
Sep 25	139.5	177.7	210.5
Sep 26	139.7	177.7	210.7
Sep 27	139.7	177.4	210.7
Sep 28	139.8	177.0	211.0
Sep 29	139.7	176.1	211.4
Sep 30	139.7	177.0	211.6
Average	**138.5**	**176.7**	**209.8**

Solid Waste Daily Borehole Temperature Averages for Borehole 19

Chiquita LF

	Depth from Surface						
TP-19	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**100 ft**	**125 ft**	**150 ft**
Sep 1	144.6	148.0	156.3	152.9	158.5	164.5	236.8
Sep 2	144.5	147.9	155.9	152.1	158.2	164.3	236.8
Sep 3	144.5	147.8	155.6	151.5	158.3	164.3	236.5
Sep 4	144.4	147.8	155.4	151.2	158.2	164.3	237.2
Sep 5	144.5	147.8	155.2	150.9	158.3	164.3	237.0
Sep 6	144.2	147.4	154.8	150.3	158.0	163.9	237.3
Sep 7	144.3	147.5	154.8	150.8	158.2	164.2	237.8
Sep 8	144.2	147.4	154.6	150.6	158.2	163.8	237.4
Sep 9	144.3	147.5	154.6	151.1	159.7	164.2	239.9
Sep 10	144.3	147.7	154.8	151.1	158.9	164.0	237.3
Sep 11	144.4	147.8	154.7	150.8	158.3	163.8	237.0
Sep 12	144.4	147.8	154.6	150.4	158.1	163.8	236.8
Sep 13	144.4	147.7	154.4	150.3	157.8	163.7	235.9
Sep 14	144.4	147.6	154.3	150.0	157.6	163.4	235.6
Sep 15	144.2	147.5	154.2	149.8	157.6	163.3	235.7
Sep 16	144.2	147.4	154.1	149.7	157.7	163.0	236.5
Sep 17	144.1	147.4	154.1	150.0	157.9	163.2	237.0
Sep 18	144.1	147.3	154.1	150.0	157.8	162.9	237.4
Sep 19	144.1	147.4	154.0	150.2	157.8	162.9	237.5
Sep 20	144.1	147.4	154.0	150.2	157.7	163.0	237.2
Sep 21	144.1	147.4	154.0	150.1	157.6	162.8	236.6
Sep 22	144.0	147.3	153.9	149.9	157.6	162.7	236.4
Sep 23	144.0	147.3	153.8	150.0	157.6	162.7	236.5
Sep 24	144.0	147.4	153.8	150.0	157.5	162.6	236.3
Sep 25	144.0	147.4	153.9	150.0	157.6	162.6	236.2
Sep 26	144.0	147.4	153.9	150.2	157.5	162.4	235.7
Sep 27	144.1	147.5	153.9	150.0	157.6	162.4	235.5
Sep 28	144.1	147.4	153.9	149.9	157.6	162.3	236.2
Sep 29	144.1	147.5	153.8	149.8	157.6	162.4	236.4
Sep 30	144.1	147.5	153.9	149.9	157.4	162.4	236.6
Average	**144.2**	**147.5**	**154.4**	**150.5**	**157.9**	**163.3**	**236.8**

*120-ft thermocouple malfunctioned. As an interim measure, a 120-ft thermocouple that was available onsite has been installed. A replacement 125-ft thermocouple has been ordered and is anticipated to be installed in October 2026.

Solid Waste Daily Borehole Temperature Averages for Borehole 20

Chiquita LF

	Depth from Surface		
TP-20	**15 ft**	**30 ft**	**45 ft**
Sep 1	129.6	136.2	142.4
Sep 2	129.6	136.3	142.5
Sep 3	129.8	136.3	142.9
Sep 4	129.9	136.4	143.2
Sep 5	130.1	136.6	143.1
Sep 6	129.7	136.3	142.8
Sep 7	129.9	136.6	143.3
Sep 8	130.0	136.4	143.3
Sep 9	130.2	136.8	143.6
Sep 10	130.3	136.8	143.6
Sep 11	130.4	136.8	143.6
Sep 12	130.4	136.8	143.3
Sep 13	130.3	136.7	143.3
Sep 14	130.4	136.7	143.1
Sep 15	130.3	136.8	143.4
Sep 16	130.5	136.9	143.6
Sep 17	130.5	136.9	143.5
Sep 18	130.4	137.0	143.7
Sep 19	130.5	137.0	143.3
Sep 20	130.6	136.9	143.4
Sep 21	130.7	137.0	143.6
Sep 22	130.5	136.9	143.5
Sep 23	130.8	137.1	143.6
Sep 24	130.8	137.1	143.5
Sep 25	130.9	137.3	143.7
Sep 26	130.8	137.2	142.9
Sep 27	130.6	136.9	142.3
Sep 28	130.3	136.6	141.9
Sep 29	130.2	136.6	141.9
Sep 30	130.1	136.7	142.2
Average	**130.3**	**136.8**	**143.1**

Solid Waste Daily Borehole Temperature Averages for Borehole 21

Chiquita LF

	Depth from Surface							
TP-21	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**70 ft**	**85 ft**	**95 ft**	**110 ft**
Sep 1	105.4	147.8	155.3	159.3	161.9	178.3	198.2	245.6
Sep 2	106.3	147.7	155.3	159.4	161.9	178.0	198.2	245.4
Sep 3	106.5	147.8	155.4	159.4	161.9	177.9	198.0	245.3
Sep 4	106.9	147.8	155.4	159.5	161.9	177.9	198.2	245.2
Sep 5	106.8	147.9	155.5	159.6	162.0	177.8	198.1	245.2
Sep 6	106.0	147.6	155.3	159.4	161.8	177.7	198.1	245.1
Sep 7	106.5	148.0	155.7	159.8	162.1	178.0	198.4	245.2
Sep 8	106.6	148.0	155.7	159.9	162.1	178.0	198.3	245.1
Sep 9	106.8	148.4	156.1	160.4	162.9	178.4	198.0	245.5
Sep 10	107.5	148.3	156.1	160.3	162.6	178.4	198.3	245.2
Sep 11	107.3	148.2	156.0	160.1	162.4	178.1	198.2	245.0
Sep 12	107.0	148.1	155.9	160.0	162.3	178.0	198.3	244.8
Sep 13	106.9	148.1	155.8	159.8	162.2	177.7	198.0	244.6
Sep 14	106.7	148.0	155.8	159.8	162.1	177.7	198.0	244.5
Sep 15	106.7	147.9	155.8	159.8	162.2	177.8	197.9	244.5
Sep 16	106.5	148.0	155.8	159.8	162.2	177.7	197.8	244.5
Sep 17	106.0	147.9	155.8	159.8	162.2	177.5	197.9	244.6
Sep 18	106.4	148.0	155.7	160.3	163.1	177.9	197.3	244.9
Sep 19	107.6	148.4	155.6	161.4	165.0	180.3	196.7	246.8
Sep 20	108.5	148.4	155.5	161.6	165.7	181.1	197.0	247.7
Sep 21	109.2	148.4	155.9	161.7	166.0	181.6	197.3	248.2
Sep 22	109.8	148.4	156.2	161.7	166.2	181.7	197.3	248.2
Sep 23	109.6	148.6	156.7	162.0	166.6	182.1	197.6	248.6
Sep 24	109.4	148.5	156.8	161.9	166.6	182.2	197.7	248.7
Sep 25	109.3	148.5	157.1	161.8	166.4	182.1	198.2	247.8
Sep 26	108.5	148.3	157.4	161.6	165.4	180.8	199.0	246.0
Sep 27	107.7	148.3	156.6	161.0	164.0	179.5	199.1	245.7
Sep 28	106.8	148.2	156.2	160.7	163.3	178.6	199.2	245.2
Sep 29	106.2	148.4	156.3	160.8	163.2	178.2	199.2	245.2
Sep 30	105.7	148.3	156.4	160.7	163.1	178.0	199.2	245.2
Average	**107.2**	**148.1**	**156.0**	**160.4**	**163.4**	**179.0**	**198.1**	**245.8**

Solid Waste Daily Borehole Temperature Averages for Borehole 22

Chiquita LF

	Depth from Surface
TP-22	**15 ft**
Sep 1	101.2
Sep 2	101.2
Sep 3	101.2
Sep 4	101.2
Sep 5	101.3
Sep 6	100.9
Sep 7	101.2
Sep 8	101.1
Sep 9	101.3
Sep 10	101.3
Sep 11	101.2
Sep 12	101.2
Sep 13	101.1
Sep 14	101.0
Sep 15	100.9
Sep 16	100.9
Sep 17	100.9
Sep 18	100.8
Sep 19	101.0
Sep 20	100.9
Sep 21	100.8
Sep 22	100.9
Sep 23	101.0
Sep 24	100.9
Sep 25	101.2
Sep 26	101.0
Sep 27	100.9
Sep 28	100.7
Sep 29	100.9
Sep 30	100.4
Average	**101.0**

Solid Waste Daily Borehole Temperature Averages for Borehole 23

Chiquita LF

	Depth from Surface			
TP-23	**15 ft**	**30 ft**	**45 ft**	**75 ft**
Sep 1	105.0	120.7	136.7	144.1
Sep 2	105.0	120.8	136.8	144.1
Sep 3	105.1	120.7	136.8	144.2
Sep 4	105.2	120.7	136.9	144.2
Sep 5	105.3	120.6	136.9	144.2
Sep 6	105.3	120.1	136.7	144.0
Sep 7	105.6	120.5	136.9	144.3
Sep 8	105.8	120.3	136.8	144.1
Sep 9	106.3	120.4	137.1	144.5
Sep 10	106.3	120.8	137.4	144.4
Sep 11	106.6	120.6	137.3	144.4
Sep 12	106.9	120.5	137.3	144.4
Sep 13	107.1	120.4	137.3	144.3
Sep 14	107.5	120.3	137.2	144.3
Sep 15	107.8	120.2	137.1	144.4
Sep 16	108.1	120.2	137.1	144.4
Sep 17	108.4	120.2	137.1	144.4
Sep 18	108.5	120.5	137.4	144.4
Sep 19	108.7	120.5	137.6	144.4
Sep 20	108.8	120.7	137.7	144.4
Sep 21	108.9	120.7	137.6	144.4
Sep 22	109.2	120.7	137.7	144.4
Sep 23	109.5	120.7	137.6	144.5
Sep 24	109.7	120.7	137.5	144.5
Sep 25	109.9	120.8	137.5	144.5
Sep 26	110.1	120.8	137.6	144.6
Sep 27	110.2	121.0	137.7	144.5
Sep 28	110.0	121.1	137.7	144.5
Sep 29	109.4	121.3	137.8	144.6
Sep 30	109.5	121.3	137.6	144.6
Average	**107.7**	**120.6**	**137.3**	**144.4**

Solid Waste Daily Borehole Temperature Averages for Borehole 24

Chiquita LF

	Depth from Surface							
TP-24	**15 ft**	**30 ft**	**45 ft**	**100 ft**	**155 ft**	**210 ft**	**265 ft**	**320 ft**
Sep 1	116.1	121.0	132.1	148.5	173.8	199.1	215.2	152.4
Sep 2	116.1	120.5	132.1	148.4	172.2	197.4	215.4	152.3
Sep 3	116.1	120.2	131.6	148.3	170.7	195.3	215.6	152.4
Sep 4	116.0	120.0	131.2	148.4	170.2	195.9	215.8	152.4
Sep 5	116.0	119.9	130.7	148.2	169.8	195.6	216.0	152.6
Sep 6	115.5	119.4	130.2	147.2	170.1	197.6	211.7	152.4
Sep 7	115.6	119.6	131.0	147.3	169.7	197.1	210.2	152.9
Sep 8	115.4	119.5	131.0	147.6	169.5	196.1	216.4	152.7
Sep 9	115.8	119.9	130.8	148.6	169.6	196.3	217.0	153.0
Sep 10	115.6	119.6	129.9	147.9	169.6	196.7	217.0	153.0
Sep 11	115.4	119.5	129.9	147.7	169.6	197.1	217.0	152.9
Sep 12	115.2	119.3	129.9	147.6	169.5	196.8	217.1	152.9
Sep 13	115.5	120.0	130.1	150.5	180.2	204.2	216.3	152.9
Sep 14	115.3	119.4	128.9	153.7	177.0	198.1	216.4	152.8
Sep 15	115.2	119.0	128.4	148.3	170.5	194.9	216.9	152.8
Sep 16	115.5	118.7	128.3	147.0	168.9	193.2	217.1	152.8
Sep 17	115.6	118.8	128.0	146.6	168.3	193.0	217.3	152.8
Sep 18	116.1	119.3	128.6	148.9	167.6	192.4	217.4	152.8
Sep 19	117.9	119.6	128.7	150.3	167.4	192.8	217.6	152.8
Sep 20	118.9	119.5	128.7	151.1	167.2	192.4	217.7	152.8
Sep 21	119.7	119.1	128.2	149.6	170.5	197.2	217.7	152.8
Sep 22	120.4	119.6	128.4	151.3	168.0	192.6	217.8	152.8
Sep 23	121.7	119.2	128.4	147.9	168.1	195.6	218.1	152.9
Sep 24	121.2	118.8	127.9	146.2	168.5	196.6	218.0	152.8
Sep 25	121.9	118.9	127.7	145.6	169.1	197.4	218.2	152.9
Sep 26	122.4	118.7	127.6	145.5	169.7	198.2	218.4	152.9
Sep 27	122.5	118.7	127.4	145.2	170.3	198.9	218.4	152.9
Sep 28	122.5	118.6	127.3	144.9	169.9	197.6	218.3	152.8
Sep 29	122.4	118.6	127.3	145.1	169.8	197.7	218.6	152.9
Sep 30	122.2	118.7	127.6	145.1	173.2	202.7	218.5	152.9
Average	**117.9**	**119.4**	**129.3**	**147.9**	**170.3**	**196.6**	**216.8**	**152.8**

Solid Waste Daily Borehole Temperature Averages for Borehole 25

Chiquita LF

	Depth from Surface							
TP-25	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**75 ft**	**90 ft**	**110 ft**	**130 ft**
Sep 1	208.9	208.5	208.9	208.5	208.5	209.2	237.2	258.3
Sep 2	208.9	208.6	208.9	208.6	208.6	209.3	227.7	258.5
Sep 3	208.8	208.6	208.8	208.5	208.6	209.3	240.2	257.8
Sep 4	208.7	208.4	208.8	208.4	208.4	209.0	232.3	257.9
Sep 5	208.8	208.5	208.9	208.4	208.5	209.2	244.6	258.1
Sep 6	209.0	208.9	209.1	209.0	208.9	209.7	246.7	258.4
Sep 7	209.3	209.0	209.5	209.3	209.2	210.2	247.2	258.8
Sep 8	208.8	208.6	208.9	208.6	208.5	209.3	226.1	259.1
Sep 9	208.9	208.7	209.1	208.7	208.5	209.4	242.3	259.7
Sep 10	208.8	208.5	208.9	208.6	208.5	209.3	246.0	258.1
Sep 11	208.6	208.1	208.7	208.2	208.1	209.0	247.2	252.7
Sep 12	208.7	208.3	208.8	208.3	208.3	209.1	247.6	255.0
Sep 13	208.7	208.5	208.8	208.5	208.5	209.3	246.9	262.3
Sep 14	208.7	208.2	208.8	208.2	208.3	209.4	247.8	262.9
Sep 15	208.8	208.2	208.9	208.2	208.2	209.3	245.5	263.7
Sep 16	208.8	208.4	208.9	208.5	208.5	209.3	241.6	266.7
Sep 17	209.3	208.9	209.4	209.0	209.1	210.0	237.8	268.0
Sep 18	209.4	209.1	209.6	209.1	209.2	210.5	236.6	268.5
Sep 19	209.0	208.6	209.2	208.6	208.7	210.8	237.3	267.3
Sep 20	208.8	208.8	208.9	208.9	208.9	210.5	243.0	268.6
Sep 21	209.0	208.6	209.2	208.7	208.8	210.5	234.3	268.7
Sep 22	209.1	208.7	209.3	208.7	208.7	210.4	239.7	269.3
Sep 23	209.9	209.6	210.1	209.6	209.6	211.1	242.8	270.5
Sep 24	209.8	209.4	210.0	209.4	209.5	210.9	244.7	270.7
Sep 25	209.8	209.4	210.0	209.4	209.5	211.9	243.6	270.5
Sep 26	209.6	209.2	209.7	209.1	209.3	211.4	245.8	270.9
Sep 27	209.2	208.8	209.3	208.8	208.9	212.1	246.8	271.8
Sep 28	209.5	209.1	209.7	209.1	209.3	210.8	244.0	272.1
Sep 29	209.3	209.0	209.4	208.9	209.1	210.1	240.6	272.7
Sep 30	209.1	208.5	209.3	208.4	208.7	208.9	242.7	273.0
Average	**209.1**	**208.7**	**209.2**	**208.7**	**208.8**	**210.0**	**241.5**	**264.4**

*TP-25 malfunctioned at 90 ft on June 23, all depths malfunctioned on July 10.

Solid Waste Daily Borehole Temperature Averages for Borehole 26

Chiquita LF

	Depth from Surface							
TP-26	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**	**125 ft**	**150 ft**
Sep 1	117.8	136.6	142.1	148.1	150.1	167.4	170.4	177.9
Sep 2	117.9	136.6	142.0	148.0	150.1	167.4	170.4	177.9
Sep 3	118.0	136.6	142.1	148.1	150.2	167.4	170.4	178.0
Sep 4	118.1	136.6	142.0	148.1	150.3	167.5	170.6	178.2
Sep 5	118.1	136.6	142.0	148.0	150.3	167.6	170.5	178.1
Sep 6	117.6	136.4	141.8	147.8	150.1	167.3	170.2	177.7
Sep 7	117.9	136.6	141.9	148.0	150.3	167.4	170.4	178.0
Sep 8	117.7	136.4	141.8	147.9	150.2	167.3	170.3	177.9
Sep 9	117.9	136.7	142.0	148.1	150.4	167.7	170.6	178.3
Sep 10	118.2	136.6	141.9	148.1	150.3	167.8	170.5	178.2
Sep 11	118.2	136.5	141.9	148.0	150.3	167.7	170.5	178.1
Sep 12	118.3	136.6	141.9	148.1	150.4	167.8	170.5	178.2
Sep 13	118.2	136.5	141.9	148.0	150.3	167.6	170.5	178.1
Sep 14	118.1	136.5	141.9	148.1	150.4	167.6	170.5	178.2
Sep 15	118.0	136.5	141.9	148.1	150.3	167.6	170.5	178.1
Sep 16	118.0	136.5	141.9	148.1	150.4	167.6	170.5	178.2
Sep 17	117.9	136.5	141.9	148.1	150.3	167.5	170.4	178.1
Sep 18	118.2	136.5	141.9	148.2	150.4	167.7	170.6	178.2
Sep 19	118.2	136.5	141.9	148.1	150.4	167.7	170.5	178.2
Sep 20	118.1	136.4	141.9	148.1	150.4	167.7	170.5	178.2
Sep 21	118.1	136.5	141.9	148.1	150.4	167.6	170.5	178.2
Sep 22	118.1	136.5	141.9	148.2	150.5	167.6	170.6	178.3
Sep 23	118.2	136.6	142.0	148.3	150.6	167.8	170.7	178.6
Sep 24	118.1	136.5	141.9	148.2	150.5	167.6	170.6	178.3
Sep 25	118.1	136.5	141.9	148.3	150.5	167.7	170.6	178.4
Sep 26	118.2	136.5	142.0	148.3	150.6	167.7	170.6	178.4
Sep 27	118.3	136.4	141.9	148.2	150.5	167.5	170.5	178.4
Sep 28	118.3	136.5	141.9	148.3	150.6	167.6	170.6	178.4
Sep 29	118.2	136.4	141.9	148.2	150.5	167.5	170.5	178.4
Sep 30	118.2	136.5	141.9	148.3	150.6	167.6	170.6	178.5
Average	**118.1**	**136.5**	**141.9**	**148.1**	**150.4**	**167.6**	**170.5**	**178.2**

Solid Waste Daily Borehole Temperature Averages for Borehole 27

Chiquita LF

	Depth from Surface							
TP-27	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**80 ft**	**100 ft**	**125 ft**	**150 ft**
Sep 1	122.3	135.2	139.2	148.6	154.6	155.5	153.0	128.4
Sep 2	122.3	135.2	139.2	148.6	154.6	155.6	153.0	128.4
Sep 3	122.3	135.3	139.2	148.6	154.6	155.6	153.0	128.4
Sep 4	122.3	135.3	139.2	148.7	154.7	155.6	153.1	128.5
Sep 5	122.3	135.3	139.2	148.7	154.6	155.6	153.0	128.4
Sep 6	121.8	135.0	139.0	148.4	154.5	155.4	152.9	128.2
Sep 7	122.1	135.2	139.2	148.6	154.7	155.6	153.0	128.4
Sep 8	122.0	135.2	139.2	148.5	154.7	155.6	153.1	128.5
Sep 9	122.3	135.4	139.5	148.6	154.9	155.7	153.2	128.6
Sep 10	122.4	135.4	139.5	148.6	154.8	155.7	153.2	128.5
Sep 11	122.4	135.4	139.4	148.5	154.8	155.7	153.1	128.5
Sep 12	122.3	135.3	139.4	148.5	154.8	155.6	153.1	128.5
Sep 13	122.3	135.3	139.4	148.5	154.7	155.6	153.1	128.4
Sep 14	122.3	135.3	139.4	148.5	154.7	155.6	153.1	128.4
Sep 15	122.1	135.2	139.4	148.4	154.7	155.6	153.1	128.4
Sep 16	121.9	135.2	139.3	148.4	154.7	155.6	153.0	128.3
Sep 17	121.8	135.1	139.3	148.4	154.6	155.6	153.0	128.3
Sep 18	122.1	135.3	139.4	148.4	154.7	155.6	153.0	128.4
Sep 19	122.7	135.4	139.4	148.4	154.6	155.6	153.0	128.4
Sep 20	122.8	135.3	139.3	148.4	154.7	155.6	153.1	128.3
Sep 21	122.9	135.2	139.3	148.3	154.6	155.6	153.0	128.3
Sep 22	123.2	135.4	139.4	148.4	154.7	155.6	153.0	128.4
Sep 23	123.3	135.4	139.5	148.5	154.8	155.7	153.1	128.4
Sep 24	123.2	135.4	139.5	148.5	154.7	155.6	153.1	128.4
Sep 25	122.8	135.4	139.5	148.5	154.8	155.7	153.1	128.4
Sep 26	122.7	135.4	139.6	148.5	154.7	155.6	153.0	128.4
Sep 27	122.7	135.4	139.6	148.5	154.8	155.6	153.1	128.4
Sep 28	122.7	135.4	139.5	148.4	154.7	155.6	153.0	128.3
Sep 29	122.7	135.3	139.4	148.4	154.7	155.6	153.0	128.3
Sep 30	122.6	135.4	139.6	148.5	154.8	155.6	153.1	128.4
Average	**122.5**	**135.3**	**139.4**	**148.5**	**154.7**	**155.6**	**153.1**	**128.4**

Solid Waste Daily Borehole Temperature Averages for Borehole 28

Chiquita LF

	Depth from Surface							
TP-28	**15 ft**	**30 ft**	**45 ft**	**70 ft**	**95 ft**	**120 ft**	**145 ft**	**170 ft**
Sep 1	84.6	91.7	113.7	125.7	132.2	131.6	140.7	143.5
Sep 2	84.6	91.8	113.6	125.6	132.2	131.6	140.7	143.5
Sep 3	84.7	91.8	113.7	125.7	132.3	131.6	140.8	143.6
Sep 4	84.8	91.7	113.7	125.7	132.3	131.7	140.8	143.6
Sep 5	84.9	91.7	113.7	125.8	132.3	131.8	140.9	143.7
Sep 6	84.8	91.4	113.5	125.6	132.4	131.5	140.8	143.5
Sep 7	85.1	91.8	113.8	126.0	132.8	131.9	141.1	143.9
Sep 8	85.1	91.6	113.7	125.9	132.6	131.6	140.9	143.7
Sep 9	85.4	91.8	114.0	126.2	132.7	131.9	141.2	144.0
Sep 10	85.5	91.9	114.0	126.2	132.7	131.9	141.2	144.0
Sep 11	85.4	91.6	113.8	126.0	132.7	131.9	141.0	143.8
Sep 12	85.4	91.5	113.8	126.0	132.7	131.9	141.1	143.8
Sep 13	85.4	91.5	113.7	126.0	132.6	131.8	140.9	143.8
Sep 14	85.5	91.4	113.7	126.0	132.6	131.9	141.0	143.8
Sep 15	85.5	91.4	113.7	126.0	132.7	132.0	141.1	143.9
Sep 16	85.5	91.3	113.7	126.0	132.7	132.0	141.2	143.9
Sep 17	85.6	91.3	113.6	126.0	132.7	132.0	141.2	143.9
Sep 18	85.6	91.4	113.6	126.0	132.7	131.9	141.0	143.8
Sep 19	85.6	91.4	113.7	126.0	132.7	131.9	140.9	143.9
Sep 20	85.6	91.4	113.7	126.0	132.8	132.0	141.0	143.9
Sep 21	85.7	91.5	113.8	126.2	133.0	132.1	141.1	144.0
Sep 22	85.7	91.5	113.7	126.1	132.9	132.0	141.1	143.8
Sep 23	85.8	91.6	113.8	126.2	133.0	132.1	141.3	143.9
Sep 24	85.8	91.5	113.7	126.2	133.0	132.0	141.3	143.8
Sep 25	85.9	91.6	113.8	126.2	133.1	132.1	141.2	144.0
Sep 26	85.9	91.6	113.7	126.2	133.0	132.1	141.2	143.9
Sep 27	85.8	91.6	113.7	126.2	133.0	132.0	141.2	143.9
Sep 28	85.8	91.7	113.6	126.2	133.0	132.0	141.2	143.8
Sep 29	85.9	91.8	113.7	126.2	133.0	132.0	141.4	143.9
Sep 30	85.9	91.8	113.8	126.3	133.1	132.1	141.4	144.0
Average	**85.4**	**91.6**	**113.7**	**126.0**	**132.7**	**131.9**	**141.1**	**143.8**

Solid Waste Daily Borehole Temperature Averages for Borehole 29

Chiquita LF

	Depth from Surface							
TP-29	**15 ft**	**30 ft**	**45 ft**	**80 ft**	**120 ft**	**160 ft**	**200 ft**	**240 ft**
Sep 1	110.7	128.6	129.9	133.9	147.7	154.4	165.9	186.9
Sep 2	110.0	128.6	130.0	134.0	147.8	154.4	166.0	186.9
Sep 3	109.3	128.6	130.0	134.0	147.8	154.5	166.0	187.0
Sep 4	109.1	128.6	130.0	134.1	147.9	154.5	166.0	187.0
Sep 5	108.8	128.5	130.0	134.1	147.9	154.5	166.0	187.0
Sep 6	109.0	128.4	129.9	134.0	147.9	154.1	166.0	188.5
Sep 7	107.5	128.6	130.0	134.1	148.1	154.4	166.1	188.0
Sep 8	107.1	128.5	130.1	134.0	148.0	154.7	166.1	187.2
Sep 9	111.9	128.7	130.1	134.1	148.1	154.7	166.0	187.1
Sep 10	108.7	128.6	130.1	134.2	148.0	154.6	166.0	187.1
Sep 11	108.0	128.6	130.1	134.1	148.0	154.6	166.0	187.1
Sep 12	111.1	128.6	130.1	134.3	148.0	154.5	166.0	187.3
Sep 13	112.7	128.6	130.1	134.2	148.0	154.4	166.0	187.2
Sep 14	113.6	128.7	130.1	134.2	148.0	154.5	166.0	187.2
Sep 15	113.0	128.6	130.2	134.2	148.0	154.5	166.1	187.4
Sep 16	112.8	128.6	130.2	134.2	148.0	154.5	166.1	187.3
Sep 17	112.0	128.6	130.2	134.2	148.0	154.5	166.1	187.3
Sep 18	115.5	128.7	130.3	134.3	148.0	154.6	166.1	187.3
Sep 19	115.9	128.7	130.2	134.2	148.0	154.5	166.0	187.4
Sep 20	116.4	128.7	130.3	134.3	148.0	154.6	166.2	187.6
Sep 21	114.2	128.7	130.2	134.3	148.0	154.6	166.2	187.5
Sep 22	114.8	128.7	130.3	134.4	148.0	154.5	166.1	187.4
Sep 23	113.5	128.8	130.3	134.5	147.9	154.6	166.1	187.3
Sep 24	112.7	128.8	130.3	134.3	147.9	154.5	166.1	187.5
Sep 25	112.4	128.8	130.3	134.5	147.9	154.6	166.1	187.4
Sep 26	113.1	128.8	130.3	134.5	147.9	154.6	166.1	187.3
Sep 27	115.0	128.7	130.4	134.6	147.9	154.7	166.2	187.4
Sep 28	115.2	128.8	130.4	134.6	147.9	154.6	166.1	187.3
Sep 29	112.7	128.8	130.4	134.6	147.9	154.6	166.1	187.3
Sep 30	110.3	128.9	130.4	134.7	147.9	154.6	166.1	187.3
Average	**111.9**	**128.7**	**130.2**	**134.2**	**147.9**	**154.5**	**166.1**	**187.3**

Solid Waste Daily Borehole Temperature Averages for Borehole 30

Chiquita LF

	Depth from Surface							
TP-30	**15 ft**	**30 ft**	**45 ft**	**70 ft**	**100 ft**	**130 ft**	**160 ft**	**190 ft**
Sep 1	107.2	114.5	115.8	145.5	171.0	167.5	167.4	173.9
Sep 2	107.2	114.5	115.7	145.4	171.2	167.6	167.3	174.1
Sep 3	107.3	114.5	115.6	145.5	171.3	167.6	167.3	174.2
Sep 4	107.4	114.5	115.7	145.6	171.4	167.6	167.4	174.3
Sep 5	107.3	114.5	115.7	145.6	171.5	167.6	167.4	174.2
Sep 6	107.1	114.4	115.4	145.4	171.4	167.6	167.9	173.4
Sep 7	107.3	114.5	115.6	145.6	171.5	167.8	167.9	173.8
Sep 8	107.4	114.6	115.7	145.6	171.5	167.8	167.4	174.3
Sep 9	107.7	114.8	115.9	145.7	171.7	167.9	167.6	174.6
Sep 10	107.7	114.8	115.9	145.7	171.7	167.9	167.5	174.6
Sep 11	107.7	114.7	115.9	145.7	171.7	167.9	167.5	174.5
Sep 12	107.6	114.8	115.9	145.8	171.7	167.9	167.6	174.5
Sep 13	107.6	114.7	115.9	145.7	171.6	167.8	167.5	174.4
Sep 14	107.7	114.7	115.9	145.7	171.7	167.8	167.5	174.4
Sep 15	107.7	114.8	115.9	145.7	171.8	167.9	167.6	174.5
Sep 16	107.7	114.8	116.0	145.6	171.8	167.9	167.6	174.6
Sep 17	107.7	114.8	116.0	145.6	171.9	167.9	167.6	174.6
Sep 18	107.8	114.8	115.9	145.6	171.8	167.9	167.5	174.5
Sep 19	107.8	114.8	116.0	145.7	171.8	167.9	167.5	174.4
Sep 20	107.8	114.8	116.0	145.8	171.8	167.9	167.7	174.5
Sep 21	107.9	114.8	116.0	145.9	171.9	168.0	167.7	174.6
Sep 22	108.0	114.9	116.0	145.9	171.9	167.9	167.6	174.6
Sep 23	108.1	115.0	116.2	146.3	172.0	168.1	167.6	174.7
Sep 24	108.0	114.9	116.1	146.2	172.0	168.0	167.7	174.5
Sep 25	108.1	115.1	116.2	146.4	172.0	168.1	167.7	174.7
Sep 26	108.2	115.0	116.2	146.1	172.0	168.1	167.6	174.7
Sep 27	108.1	115.0	116.2	146.1	172.0	168.1	167.6	174.8
Sep 28	108.1	114.9	116.1	146.0	171.9	168.0	167.5	174.6
Sep 29	108.2	115.0	116.1	146.1	172.0	168.0	167.5	174.7
Sep 30	108.3	115.0	116.1	146.1	172.0	168.0	167.6	174.6
Average	**107.7**	**114.8**	**115.9**	**145.8**	**171.7**	**167.9**	**167.6**	**174.4**

Solid Waste Daily Borehole Temperature Averages for Borehole 31

Chiquita LF

	Depth from Surface							
TP-31	**15 ft**	**30 ft**	**45 ft**	**80 ft**	**130 ft**	**180 ft**	**230 ft**	**280 ft**
Sep 1	110.5	126.5	129.8	138.7	159.4	192.4	187.5	140.7
Sep 2	110.5	126.5	129.9	138.7	159.1	192.4	187.6	140.7
Sep 3	110.6	126.5	129.9	138.7	158.9	192.5	187.7	140.8
Sep 4	110.7	126.4	130.1	138.7	158.7	192.5	187.7	140.8
Sep 5	110.7	126.4	130.2	138.7	159.4	192.6	187.8	140.9
Sep 6	110.5	126.3	129.9	138.5	158.8	192.2	187.8	140.5
Sep 7	110.6	126.4	130.2	138.7	159.0	192.4	187.9	140.8
Sep 8	110.6	126.3	130.0	138.5	158.6	192.3	187.6	140.6
Sep 9	110.6	126.4	130.2	138.7	158.6	192.5	187.8	141.0
Sep 10	110.7	126.4	130.3	138.6	158.5	192.4	187.8	140.9
Sep 11	110.6	126.3	130.2	138.6	158.7	192.3	187.8	140.8
Sep 12	110.7	126.3	130.3	138.6	159.1	192.2	187.8	140.9
Sep 13	110.6	126.3	130.3	138.5	159.1	192.2	187.8	140.8
Sep 14	110.6	126.3	130.2	138.5	158.8	192.3	187.9	140.8
Sep 15	110.6	126.3	130.2	138.6	158.8	192.4	188.0	141.0
Sep 16	110.5	126.3	130.1	138.5	158.7	192.3	187.9	140.9
Sep 17	110.6	126.3	130.1	138.5	158.7	192.4	187.9	140.9
Sep 18	110.5	126.2	130.2	138.5	158.3	192.4	187.9	140.9
Sep 19	110.6	126.2	130.2	138.5	158.5	192.4	187.9	140.9
Sep 20	110.5	126.2	130.2	138.4	158.5	192.5	188.0	140.9
Sep 21	110.5	126.2	130.2	138.4	158.6	192.6	188.0	140.9
Sep 22	110.5	126.2	130.2	138.4	158.5	192.7	188.0	140.9
Sep 23	110.5	126.3	130.3	138.5	158.4	192.8	188.0	141.0
Sep 24	110.5	126.2	130.2	138.4	158.3	192.7	188.0	140.9
Sep 25	110.5	126.2	130.3	138.4	158.2	192.8	188.0	140.9
Sep 26	110.5	126.2	130.2	138.4	158.2	192.9	188.0	140.9
Sep 27	110.5	126.1	130.3	138.3	158.3	192.8	187.9	140.8
Sep 28	110.5	126.2	130.3	138.4	158.5	192.9	188.0	140.9
Sep 29	110.4	126.2	130.2	138.3	158.5	192.9	188.0	140.9
Sep 30	110.4	126.2	130.2	138.4	158.4	192.9	188.1	141.0
Average	**110.6**	**126.3**	**130.2**	**138.5**	**158.7**	**192.5**	**187.9**	**140.8**

Solid Waste Daily Borehole Temperature Averages for Borehole 32

Chiquita LF

	Depth from Surface							
TP-32	**15 ft**	**30 ft**	**45 ft**	**70 ft**	**100 ft**	**130 ft**	**160 ft**	**190 ft**
Sep 1	126.8	139.4	143.4	154.5	164.0	169.5	164.8	147.7
Sep 2	126.8	139.4	143.4	154.5	164.0	169.5	164.9	147.7
Sep 3	126.8	139.4	143.4	154.3	164.0	169.5	164.9	147.7
Sep 4	126.8	139.4	143.4	154.3	164.0	169.6	164.9	147.7
Sep 5	126.9	139.4	143.4	154.3	164.0	169.6	164.9	147.7
Sep 6	126.5	139.2	143.2	154.2	163.8	169.5	164.8	147.6
Sep 7	126.8	139.3	143.4	154.3	163.9	169.5	164.8	147.7
Sep 8	126.7	139.3	143.4	154.4	164.0	169.6	164.9	147.8
Sep 9	127.0	139.6	143.6	154.6	164.2	169.7	165.0	147.9
Sep 10	126.9	139.5	143.5	154.5	164.1	169.7	164.9	147.8
Sep 11	126.6	139.5	143.5	154.3	164.1	169.7	165.0	147.8
Sep 12	126.5	139.5	143.5	154.5	164.1	169.7	164.9	147.8
Sep 13	126.3	139.5	143.5	154.6	164.1	169.6	164.8	147.7
Sep 14	126.3	139.5	143.5	154.4	164.0	169.6	164.8	147.7
Sep 15	126.0	139.3	143.3	154.5	164.0	169.5	164.7	147.5
Sep 16	126.0	139.3	143.4	154.7	164.0	169.6	164.9	147.7
Sep 17	125.9	139.3	143.4	154.7	164.0	169.6	164.8	147.7
Sep 18	126.1	139.4	143.4	154.7	164.1	169.6	164.8	147.6
Sep 19	126.0	139.4	143.4	154.3	164.1	169.6	164.8	147.7
Sep 20	125.8	139.3	143.3	154.2	164.1	169.6	164.8	147.7
Sep 21	125.7	139.3	143.3	154.1	164.1	169.6	164.8	147.6
Sep 22	125.8	139.4	143.3	154.2	164.1	169.6	164.8	147.6
Sep 23	125.8	139.5	143.4	154.2	164.1	169.7	164.9	147.7
Sep 24	125.8	139.4	143.4	154.4	164.1	169.7	164.9	147.7
Sep 25	125.8	139.5	143.4	154.4	164.1	169.7	164.9	147.7
Sep 26	125.8	139.4	143.4	154.5	164.1	169.7	164.8	147.7
Sep 27	125.8	139.4	143.4	154.6	164.2	169.8	164.9	147.7
Sep 28	125.8	139.4	143.4	154.5	164.1	169.7	164.8	147.6
Sep 29	125.8	139.4	143.4	154.3	164.2	169.7	164.8	147.6
Sep 30	125.8	139.4	143.4	154.6	164.2	169.7	164.8	147.6
Average	**126.2**	**139.4**	**143.4**	**154.4**	**164.1**	**169.6**	**164.8**	**147.7**

Solid Waste Daily Borehole Temperature Averages for Borehole 33

Chiquita LF

	Depth from Surface		
TP-33	**15 ft**	**30 ft**	**45 ft**
Sep 1	165.2	173.9	197.4
Sep 2	165.1	173.9	197.5
Sep 3	165.1	173.6	197.6
Sep 4	165.1	173.7	197.7
Sep 5	165.2	173.5	197.8
Sep 6	139.9	151.0	197.3
Sep 7	136.4	140.1	195.7
Sep 8	160.2	163.1	197.0
Sep 9	162.6	168.1	197.7
Sep 10	163.3	169.8	197.9
Sep 11	163.7	170.8	198.0
Sep 12	164.0	171.2	198.1
Sep 13	164.1	171.9	198.1
Sep 14	164.3	172.7	198.2
Sep 15	164.5	173.0	198.3
Sep 16	164.5	173.2	198.3
Sep 17	164.5	173.1	198.4
Sep 18	164.7	173.9	198.3
Sep 19	164.8	173.9	198.1
Sep 20	164.8	173.9	198.1
Sep 21	164.9	174.3	198.2
Sep 22	165.0	174.6	198.3
Sep 23	165.2	175.5	198.4
Sep 24	165.2	175.5	198.4
Sep 25	165.3	175.7	198.5
Sep 26	165.3	175.9	198.6
Sep 27	165.3	175.7	198.6
Sep 28	165.4	176.0	198.8
Sep 29	165.5	176.5	199.0
Sep 30	165.5	176.3	199.1
Average	**162.8**	**171.5**	**198.0**

Solid Waste Daily Borehole Temperature Averages for Borehole 34

Chiquita LF

	Depth from Surface							
TP-34	**15 ft**	**30 ft**	**45 ft**	**60 ft**	**75 ft**	**90 ft**	**110 ft**	**120 ft**
Sep 1	124.7	132.6	138.4	134.7	135.3	136.3	144.0	150.6
Sep 2	124.8	132.7	138.4	134.7	135.3	136.4	144.1	150.7
Sep 3	124.9	132.8	138.5	134.8	135.3	136.4	144.1	150.7
Sep 4	125.8	132.8	138.5	134.8	135.3	136.4	144.1	150.7
Sep 5	125.4	132.9	138.5	134.8	135.3	136.4	144.2	150.8
Sep 6	124.3	132.6	138.3	134.5	135.0	136.1	143.7	150.3
Sep 7	125.3	132.9	138.4	134.7	135.2	136.3	144.0	150.5
Sep 8	125.1	132.9	138.4	134.7	135.2	136.3	144.0	150.5
Sep 9	125.0	133.1	138.7	134.9	135.4	136.5	144.3	150.9
Sep 10	125.5	133.1	138.7	134.8	135.4	136.5	144.2	150.8
Sep 11	125.5	133.1	138.6	134.8	135.4	136.4	144.1	150.7
Sep 12	125.1	133.2	138.7	134.9	135.4	136.5	144.2	150.9
Sep 13	124.8	133.2	138.6	134.9	135.4	136.5	144.2	150.8
Sep 14	124.6	133.2	138.7	134.8	135.4	136.5	144.1	150.8
Sep 15	124.6	133.3	138.7	134.8	135.4	136.5	144.1	150.8
Sep 16	124.5	133.3	138.6	134.7	135.4	136.4	144.0	150.7
Sep 17	123.9	133.3	138.6	134.7	135.3	136.4	144.0	150.6
Sep 18	123.9	133.4	138.7	134.8	135.5	136.6	144.2	150.9
Sep 19	123.7	133.4	138.7	134.8	135.5	136.5	144.2	150.9
Sep 20	124.0	133.4	138.6	134.8	135.4	136.5	144.1	150.8
Sep 21	123.8	133.4	138.6	134.7	135.3	136.4	144.0	150.7
Sep 22	123.9	133.5	138.7	134.8	135.5	136.6	144.2	151.0
Sep 23	123.3	133.6	138.8	134.9	135.6	136.7	144.3	151.0
Sep 24	123.2	133.6	138.8	134.8	135.6	136.6	144.3	151.0
Sep 25	123.2	133.7	138.9	134.9	135.7	136.7	144.3	151.2
Sep 26	123.4	133.7	138.9	134.9	135.7	136.7	144.4	151.2
Sep 27	124.0	133.7	138.8	134.8	135.6	136.6	144.2	151.1
Sep 28	123.6	133.7	138.9	134.9	135.6	136.7	144.4	151.3
Sep 29	123.7	133.8	139.0	134.9	135.7	136.7	144.4	151.3
Sep 30	124.0	133.9	138.9	134.9	135.7	136.7	144.4	151.4
Average	**124.4**	**133.3**	**138.7**	**134.8**	**135.4**	**136.5**	**144.2**	**150.9**

Solid Waste Daily Borehole Temperature Averages for Borehole 35

Chiquita LF

	Depth from Surface							
TP-35	**15 ft**	**30 ft**	**45 ft**	**65 ft**	**85 ft**	**105 ft**	**125 ft**	**140 ft**
Sep 1	99.5	123.2	135.4	137.0	148.5	160.8	170.3	172.8
Sep 2	100.1	123.1	135.4	136.6	148.5	160.8	170.3	172.9
Sep 3	100.3	123.1	135.5	136.6	148.6	160.9	170.4	172.9
Sep 4	100.0	123.1	135.5	136.7	148.5	160.8	170.4	172.9
Sep 5	99.7	123.1	135.5	136.8	148.5	160.8	170.3	172.9
Sep 6	99.9	122.9	135.4	136.7	148.4	160.6	170.2	172.8
Sep 7	99.7	123.0	135.5	137.0	148.5	160.8	170.2	172.8
Sep 8	99.7	123.0	135.5	137.1	148.6	160.9	170.4	173.0
Sep 9	100.1	123.2	135.7	137.3	148.7	161.0	170.4	173.2
Sep 10	99.6	123.2	135.7	137.2	148.6	160.9	170.3	173.0
Sep 11	99.6	123.1	135.6	137.3	148.6	160.9	170.3	173.0
Sep 12	99.8	123.2	135.6	137.2	148.6	160.9	170.4	173.0
Sep 13	99.8	123.2	135.6	137.2	148.6	160.8	170.4	173.0
Sep 14	100.0	123.2	135.6	137.1	148.5	160.8	170.3	172.9
Sep 15	100.0	123.3	135.6	137.0	148.5	160.7	170.3	172.9
Sep 16	100.0	123.3	135.6	137.1	148.5	160.7	170.3	172.9
Sep 17	100.5	123.3	135.6	137.1	148.6	160.7	170.3	172.8
Sep 18	100.7	123.5	135.7	137.1	148.7	160.9	170.5	173.1
Sep 19	100.7	123.4	135.7	137.1	148.7	160.7	170.4	173.0
Sep 20	100.5	123.4	135.6	137.0	148.6	160.7	170.3	172.9
Sep 21	100.7	123.3	135.6	137.0	148.6	160.6	170.3	172.8
Sep 22	100.9	123.4	135.7	137.0	148.7	160.8	170.4	173.0
Sep 23	101.3	123.5	135.8	137.0	148.7	160.7	170.4	173.0
Sep 24	101.5	123.4	135.7	137.0	148.7	160.7	170.3	172.9
Sep 25	101.7	123.5	135.8	137.0	148.8	160.8	170.4	173.0
Sep 26	101.6	123.5	135.8	137.0	148.8	160.8	170.4	173.0
Sep 27	101.3	123.4	135.7	137.0	148.7	160.7	170.3	173.0
Sep 28	101.7	123.4	135.8	137.0	148.7	160.7	170.4	172.9
Sep 29	102.1	123.4	135.8	137.0	148.8	160.8	170.3	173.0
Sep 30	102.3	123.4	135.8	137.1	148.9	160.8	170.4	173.0
Average	**100.5**	**123.3**	**135.6**	**137.0**	**148.6**	**160.8**	**170.3**	**172.9**

Solid Waste Daily Borehole Temperature Averages for Borehole 36

Chiquita LF

	Depth from Surface							
TP-36	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**120 ft**	**165 ft**	**210 ft**	**250 ft**
Sep 1	103.3	125.2	134.6	136.5	154.1	172.0	160.2	134.3
Sep 2	103.3	125.2	134.6	136.5	154.2	171.9	160.2	134.4
Sep 3	103.3	125.2	134.6	136.5	154.2	172.0	160.2	134.4
Sep 4	103.4	125.3	134.7	136.5	154.2	172.0	160.2	134.4
Sep 5	103.4	125.3	134.7	136.5	154.2	172.0	160.3	134.4
Sep 6	103.4	125.1	134.6	136.4	154.0	171.8	160.0	134.1
Sep 7	103.5	125.2	134.6	136.5	154.1	171.9	160.2	134.3
Sep 8	103.5	125.2	134.5	136.3	154.0	171.8	160.0	134.1
Sep 9	103.6	125.3	134.8	136.6	154.3	172.1	160.3	134.5
Sep 10	103.6	125.4	134.8	136.6	154.2	172.1	160.3	134.5
Sep 11	103.6	125.3	134.7	136.5	154.3	172.1	160.3	134.4
Sep 12	103.7	125.4	134.8	136.6	154.3	172.1	160.3	134.5
Sep 13	103.7	125.3	134.8	136.5	154.2	172.1	160.3	134.4
Sep 14	103.8	125.3	134.8	136.6	154.2	172.1	160.3	134.4
Sep 15	103.8	125.2	134.7	136.5	154.2	172.0	160.2	134.3
Sep 16	103.9	125.2	134.8	136.5	154.2	172.1	160.2	134.3
Sep 17	103.9	125.1	134.7	136.5	154.1	172.0	160.1	134.2
Sep 18	103.9	125.3	134.8	136.6	154.2	172.1	160.2	134.4
Sep 19	104.0	125.3	134.9	136.6	154.2	172.1	160.3	134.4
Sep 20	104.0	125.2	134.8	136.5	154.1	172.0	160.1	134.3
Sep 21	104.0	125.2	134.8	136.5	154.1	172.0	160.1	134.2
Sep 22	104.0	125.2	134.8	136.6	154.3	172.2	160.3	134.5
Sep 23	104.2	125.3	135.0	136.8	154.4	172.3	160.5	134.7
Sep 24	104.2	125.3	135.0	136.7	154.4	172.3	160.5	134.6
Sep 25	104.2	125.4	135.0	136.8	154.4	172.3	160.5	134.7
Sep 26	104.2	125.4	135.1	136.8	154.4	172.4	160.5	134.7
Sep 27	104.2	125.4	135.0	136.7	154.3	172.2	160.3	134.4
Sep 28	104.3	125.5	135.0	136.8	154.4	172.3	160.4	134.6
Sep 29	104.3	125.4	135.0	136.8	154.4	172.3	160.4	134.6
Sep 30	104.4	125.4	135.1	136.9	154.5	172.4	160.5	134.7
Average	**103.8**	**125.3**	**134.8**	**136.6**	**154.2**	**172.1**	**160.3**	**134.4**

Solid Waste Daily Borehole Temperature Averages for Borehole 37

Chiquita LF

	Depth from Surface							
TP-37	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**100 ft**	**130 ft**	**155 ft**	**180 ft**
Sep 1	104.0	115.7	134.8	135.6	141.4	161.0	176.1	182.7
Sep 2	104.0	115.7	134.8	135.6	141.5	161.1	176.2	182.7
Sep 3	104.1	115.7	134.8	135.6	141.4	161.1	176.2	182.7
Sep 4	104.1	115.7	134.9	135.6	141.5	161.1	176.2	182.7
Sep 5	104.2	115.8	135.0	135.7	141.5	161.1	176.3	182.8
Sep 6	103.8	115.4	134.6	135.3	141.1	160.6	175.9	182.1
Sep 7	104.3	115.8	134.9	135.6	141.4	160.9	176.2	182.6
Sep 8	104.1	115.7	135.0	135.6	141.5	160.9	176.3	182.7
Sep 9	104.6	116.1	135.4	136.0	141.9	161.3	176.7	183.2
Sep 10	104.6	116.2	135.4	136.0	141.9	161.3	176.7	183.2
Sep 11	104.5	116.0	135.2	135.9	141.8	161.1	176.6	183.1
Sep 12	104.5	116.0	135.2	135.8	141.7	161.0	176.6	183.1
Sep 13	104.4	115.9	135.1	135.8	141.6	160.9	176.4	183.0
Sep 14	104.4	115.9	135.0	135.7	141.6	160.8	176.4	183.0
Sep 15	104.4	115.8	135.0	135.6	141.5	160.6	176.3	182.8
Sep 16	104.3	115.8	134.9	135.6	141.5	160.6	176.2	182.7
Sep 17	104.4	115.8	134.9	135.6	141.4	160.4	176.1	182.6
Sep 18	104.4	115.8	135.0	135.8	141.7	160.6	176.4	182.9
Sep 19	104.5	115.9	135.0	135.8	141.8	160.7	176.5	182.9
Sep 20	104.4	115.8	134.9	135.6	141.6	160.5	176.2	182.7
Sep 21	104.5	115.8	134.9	135.6	141.6	160.3	176.2	182.6
Sep 22	104.5	115.9	135.1	135.8	141.9	160.5	176.5	183.0
Sep 23	104.7	116.1	135.3	135.9	142.1	160.7	176.7	183.2
Sep 24	104.6	115.9	135.2	135.8	142.0	160.6	176.6	183.0
Sep 25	104.7	116.0	135.2	135.9	142.1	160.7	176.6	183.1
Sep 26	104.8	116.1	135.3	136.1	142.3	160.8	176.7	183.2
Sep 27	104.6	115.9	135.2	135.9	142.1	160.5	176.5	183.0
Sep 28	104.6	115.9	135.2	135.8	142.2	160.5	176.6	183.1
Sep 29	104.7	116.0	135.2	135.9	142.2	160.5	176.7	183.2
Sep 30	104.8	116.1	135.2	135.9	142.3	160.5	176.7	183.2
Average	**104.4**	**115.9**	**135.1**	**135.7**	**141.7**	**160.8**	**176.4**	**182.9**

Solid Waste Daily Borehole Temperature Averages for Borehole 38

Chiquita LF

	Depth from Surface							
TP-38	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**120 ft**	**165 ft**	**210 ft**	**250 ft**
Sep 1	115.5	136.3	143.1	151.1	161.5	171.6	161.2	135.0
Sep 2	115.6	136.6	143.2	151.0	161.4	171.6	161.2	135.0
Sep 3	115.7	136.5	143.2	151.0	161.4	171.7	161.2	135.1
Sep 4	115.6	136.6	143.2	151.0	161.5	171.7	161.3	135.1
Sep 5	115.7	136.4	143.1	151.2	161.6	171.7	161.3	135.1
Sep 6	115.4	135.3	142.8	151.1	161.3	171.4	161.0	134.9
Sep 7	115.5	135.6	143.1	151.2	161.5	171.9	161.5	135.4
Sep 8	115.5	135.3	142.9	151.1	161.7	171.9	161.4	135.3
Sep 9	115.7	135.3	143.0	151.5	162.1	172.2	161.7	135.6
Sep 10	115.9	136.1	143.2	151.4	161.8	172.0	161.6	135.4
Sep 11	116.0	135.9	143.2	151.6	161.6	171.7	161.5	135.3
Sep 12	115.9	135.9	143.1	151.8	161.7	171.5	161.5	135.3
Sep 13	115.7	135.8	143.1	152.0	162.0	171.4	161.5	135.2
Sep 14	115.8	135.4	143.0	151.9	162.0	171.4	161.5	135.1
Sep 15	115.7	135.0	142.9	151.8	161.8	171.4	161.5	135.2
Sep 16	115.7	134.9	142.9	151.4	161.6	171.7	161.5	135.2
Sep 17	115.7	134.6	143.0	151.5	161.6	171.5	161.5	135.2
Sep 18	115.9	135.6	143.1	151.9	161.6	171.5	161.4	135.1
Sep 19	115.9	135.8	143.1	151.7	161.5	171.5	161.4	135.1
Sep 20	115.9	135.7	143.1	151.6	161.7	171.6	161.4	135.1
Sep 21	115.8	135.4	143.1	151.6	161.8	171.9	161.4	135.2
Sep 22	115.7	134.4	143.0	151.9	162.0	171.6	161.4	135.1
Sep 23	115.8	133.6	143.0	151.8	162.4	171.8	161.5	135.3
Sep 24	115.9	133.3	142.9	151.7	162.4	171.8	161.4	135.2
Sep 25	115.9	133.2	143.0	151.6	162.1	171.7	161.5	135.3
Sep 26	116.0	133.2	143.1	151.7	162.3	171.7	161.5	135.3
Sep 27	115.9	133.4	143.1	151.3	162.0	171.6	161.5	135.2
Sep 28	115.8	133.2	143.2	151.5	162.2	171.6	161.5	135.2
Sep 29	116.0	132.8	143.3	151.5	162.0	171.6	161.7	135.3
Sep 30	116.0	132.8	143.5	151.6	162.1	171.4	161.8	135.3
Average	**115.8**	**135.0**	**143.1**	**151.5**	**161.8**	**171.6**	**161.4**	**135.2**

Solid Waste Daily Borehole Temperature Averages for Borehole 39

Chiquita LF

	Depth from Surface						
TP-39	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**105 ft**	**135 ft**	**160 ft**
Sep 1	105.0	120.7	136.7	144.1	150.4	156.8	159.0
Sep 2	105.0	120.8	136.8	144.1	150.4	156.8	159.0
Sep 3	105.1	120.7	136.8	144.2	150.4	156.8	159.1
Sep 4	105.2	120.7	136.9	144.2	150.3	156.9	159.1
Sep 5	105.3	120.6	136.9	144.2	150.4	156.9	159.2
Sep 6	105.3	120.1	136.7	144.0	150.1	156.6	158.9
Sep 7	105.6	120.5	136.9	144.3	150.3	156.9	159.1
Sep 8	105.8	120.3	136.8	144.1	150.2	156.8	159.0
Sep 9	106.3	120.4	137.1	144.5	150.5	157.1	159.4
Sep 10	106.3	120.8	137.4	144.4	150.4	157.1	159.3
Sep 11	106.6	120.6	137.3	144.4	150.3	157.0	159.3
Sep 12	106.9	120.5	137.3	144.4	150.3	157.0	159.3
Sep 13	107.1	120.4	137.3	144.3	150.3	156.9	159.2
Sep 14	107.5	120.3	137.2	144.3	150.3	157.0	159.2
Sep 15	107.8	120.2	137.1	144.4	150.3	156.9	159.1
Sep 16	108.1	120.2	137.1	144.4	150.2	156.9	159.2
Sep 17	108.4	120.2	137.1	144.4	150.2	156.9	159.2
Sep 18	108.5	120.5	137.4	144.4	150.2	156.9	159.1
Sep 19	108.7	120.5	137.6	144.4	150.2	156.9	159.2
Sep 20	108.8	120.7	137.7	144.4	150.2	156.9	159.2
Sep 21	108.9	120.7	137.6	144.4	150.2	156.9	159.2
Sep 22	109.2	120.7	137.7	144.4	150.2	156.9	159.2
Sep 23	109.5	120.7	137.6	144.5	150.3	157.1	159.4
Sep 24	109.7	120.7	137.5	144.5	150.2	157.0	159.3
Sep 25	109.9	120.8	137.5	144.5	150.3	157.0	159.4
Sep 26	110.1	120.8	137.6	144.6	150.3	157.0	159.3
Sep 27	110.2	121.0	137.7	144.5	150.2	156.9	159.3
Sep 28	110.0	121.1	137.7	144.5	150.2	157.0	159.3
Sep 29	109.4	121.3	137.8	144.6	150.3	157.0	159.4
Sep 30	109.5	121.3	137.6	144.6	150.3	157.0	159.4
Average	**107.7**	**120.6**	**137.3**	**144.4**	**150.3**	**156.9**	**159.2**

Solid Waste Daily Borehole Temperature Averages for Borehole 40

Chiquita LF

	Depth from Surface							
TP-40	**15 ft**	**30 ft**	**45 ft**	**75 ft**	**110 ft**	**155 ft**	**185 ft**	**220 ft**
Sep 1	101.2	120.7	128.5	129.0	125.6	142.9	148.1	132.0
Sep 2	101.2	120.7	128.5	129.0	125.5	142.9	148.1	132.0
Sep 3	101.2	120.7	128.5	129.1	125.6	143.0	148.2	132.1
Sep 4	101.2	120.7	128.5	129.2	125.7	143.0	148.1	132.1
Sep 5	101.3	120.7	128.6	129.3	125.7	143.1	148.2	132.2
Sep 6	100.9	120.5	128.5	129.1	125.6	142.9	148.0	131.9
Sep 7	101.2	120.7	128.7	129.5	125.9	143.0	148.3	132.0
Sep 8	101.1	120.6	128.6	129.3	125.8	143.0	148.1	131.6
Sep 9	101.3	120.8	128.8	129.7	126.2	143.4	148.5	132.1
Sep 10	101.3	120.9	128.9	129.6	126.1	143.3	148.5	132.0
Sep 11	101.2	120.7	128.8	129.5	126.0	143.2	148.3	131.8
Sep 12	101.2	120.6	128.7	129.5	126.0	143.2	148.3	131.9
Sep 13	101.1	120.7	128.6	129.5	125.9	143.1	148.2	131.7
Sep 14	101.0	120.6	128.7	129.5	126.0	143.1	148.2	131.8
Sep 15	100.9	120.6	128.7	129.5	126.1	143.2	148.3	131.9
Sep 16	100.9	120.6	128.6	129.6	126.0	143.1	148.3	131.9
Sep 17	100.9	120.5	128.6	129.6	126.0	143.2	148.3	132.0
Sep 18	100.8	120.5	128.6	129.5	125.9	143.1	148.2	131.9
Sep 19	101.0	120.5	128.6	129.5	126.0	143.1	148.2	131.9
Sep 20	100.9	120.5	128.6	129.5	126.1	143.1	148.2	131.9
Sep 21	100.8	120.6	128.7	129.6	126.2	143.2	148.3	132.1
Sep 22	100.9	120.6	128.7	129.5	126.1	143.1	148.2	131.9
Sep 23	101.0	120.7	128.8	129.8	126.3	143.3	148.4	132.1
Sep 24	100.9	120.5	128.7	129.7	126.2	143.1	148.3	131.7
Sep 25	101.2	120.5	128.7	129.8	126.2	143.2	148.3	131.7
Sep 26	101.0	120.5	128.7	129.8	126.2	143.2	148.3	131.7
Sep 27	100.9	120.6	128.7	129.7	126.3	143.2	148.3	131.8
Sep 28	100.7	120.5	128.7	129.7	126.2	143.1	148.2	131.8
Sep 29	100.9	120.5	128.8	129.7	126.4	143.2	148.4	132.0
Sep 30	100.4	120.6	128.5	129.9	125.7	142.6	148.3	132.0
Average	**101.0**	**120.6**	**128.7**	**129.5**	**126.0**	**143.1**	**148.3**	**131.9**

Attachment F

Draeger Tube Readings


Attachment F - Lab Analysis
September 2026

Date Sampled	Permanent Flare Station				Zeeco Inlet TOx (Reaction Area)			Zeeco South Station TOx (Reaction Area)			Parnel TOx (Reaction Area)			Hero TOx (Reaction Area)		
	Lab Analysis (ppmv)				Lab Analysis (ppmv)			Lab Analysis (ppmv)			Lab Analysis (ppmv)			Lab Analysis (ppmv)		
	Flare	H2S	DMS	TRS	H2S	DMS	TRS	H2S	DMS	TRS	H2S	DMS	TRS	H2S	DMS	TRS
09/01/26	FL-2009	187	305	631.9	133	744	1224.9	155	249	529.4	291	1155	2106.8	239	1291	2134.3
09/02/26	FL-1995	177	313	630.5	145	731	1234.2	144	238	496.8	299	1261	2290.2	241	1342	2207.9
09/03/26	FL-2009	183	325	650.5	130	694	1139.5	145	165	395.1	275	1050	1920.1	220	1226	2013.4
09/04/26	FL-2009	245	280	644.2	149	916	1482.9	155	235	509.4	265	1195	2122.0	212	1238	2038.9
09/05/26	FL-1995	36	51	108.4	139	883	1389.9	181	285	583.9	291	1206	2163.7	249	1442	2370.6
09/06/26	FL-1995	187	357	699.0				210	373	741.1	164	940	1564.6	159	960	1542.1
09/07/26	FL-1995	127	290	520.8				213	480	926.5	156	855	1420.2	132	848	1326.7
09/08/26	FL-1995	192	269	570.7	126	826	1305.3	161	299	587.5	245	1065	1886.5	181	1149	1838.2
09/09/26	FL-2009	217	449	858.4	143	731	1220.2	145	292	575.3	182	987	1668.0	161	1011	1613.3
09/10/26	FL-2009	214	484	917.3				188	284	605.1	219	907	1595.0	166	1169	1844.8
09/11/26	FL-1995	200	420	801.0	121	811	1260.9	160	248	528.7	258	1083	1911.4	151	1105	1738.7
09/12/26	FL-2009	206	274	600.3	102	705	1089.8	143	170	381.1	271	1105	1958.3	175	1216	1945.0
09/13/26	FL-2009	191	278	587.5	125	784	1240.2	134	202	417.5	273	1130	2008.6	146	1036	1646.6
09/14/26	FL-2009	188	260	556.4	90	691	1071.3	146	148	354.5	234	919	1637.6	163	1119	1789.3
09/15/26	FL-2009	207	328	677.7	127	701	1138.9	146	170	388.2				172	1285	2046.2
09/16/26	FL-2009	190	282	597.8	124	941	1485.7	149	333	626.5				186	1218	1961.6
09/17/26	FL-2009	194	251	559.4	122	683	1113.2	155	167	394.7	249	1009	1780.8	160	1171	1855.4
09/18/26	FL-2009	177	376	710.4	160	688	1177.6	218	121	402.5	182	1141	1861.9	166	1044	1644.4
09/19/26	FL-2009	168	285	569.6	120	644	1056.3	132	156	352.9	94	1111	1541.4	165	956	1536.7
09/20/26	FL-2009	142	364	658.2	130	628	1061.0	144	169	388.4	186	1087	1814.6	177	1023	1648.6
09/21/26	FL-2009	202	351	712.8	135	674	1115.6	137	152	358.0	171	914	1533.1	209	1105	1813.3
09/22/26	FL-2009	194	278	599.9	151	667	1143.8	139	137	343.6	172	958	1617.1	166	931	1504.0
09/23/26	FL-2009	192	298	609.2	157	656	1114.9	111	176	353.7	168	924	1556.6	145	815	1308.9
09/24/26	FL-2009	185	276	582.0	164	712	1221.0	122	202	405.8	149	958	1581.5	145	889	1421.3
09/25/26	FL-2009	203	296	639.7	158	721	1236.1	104	228	429.3				198	1024	1680.0
09/26/26	FL-2009	194	280	592.5	161	716	1190.0	119	312	537.3				195	960	1569.7
09/27/26	FL-2009	182	237	527.2	165	663	1139.7	136	223	430.4	168	790	1365.6	220	1012	1676.4
09/28/26	FL-2009	175	320	636.2	165	777	1298.2	159	226	472.1				186	959	1569.9
09/29/26	FL-1995	128	385	662.5	118	793	1258.0	172	224	475.3				212	1122	1879.5
09/30/26	FL-1995	142	379	674.1	153	831	1374.4	171	211	463.5				223	1218	2035.2

Draeger Tube readings no longer required as of June 4, 2026 SOFA revision.
Zeeco 7 offline on 9/6/26 to 9/7/26 due to restart failure after routine meter cleaning and on 9/10/26 to remove and regrade surface for TOx stack due to settlement
Parnel TOx ran intermittently between 9/15/26 and 9/30/26

Attachment G

Graphic Maps

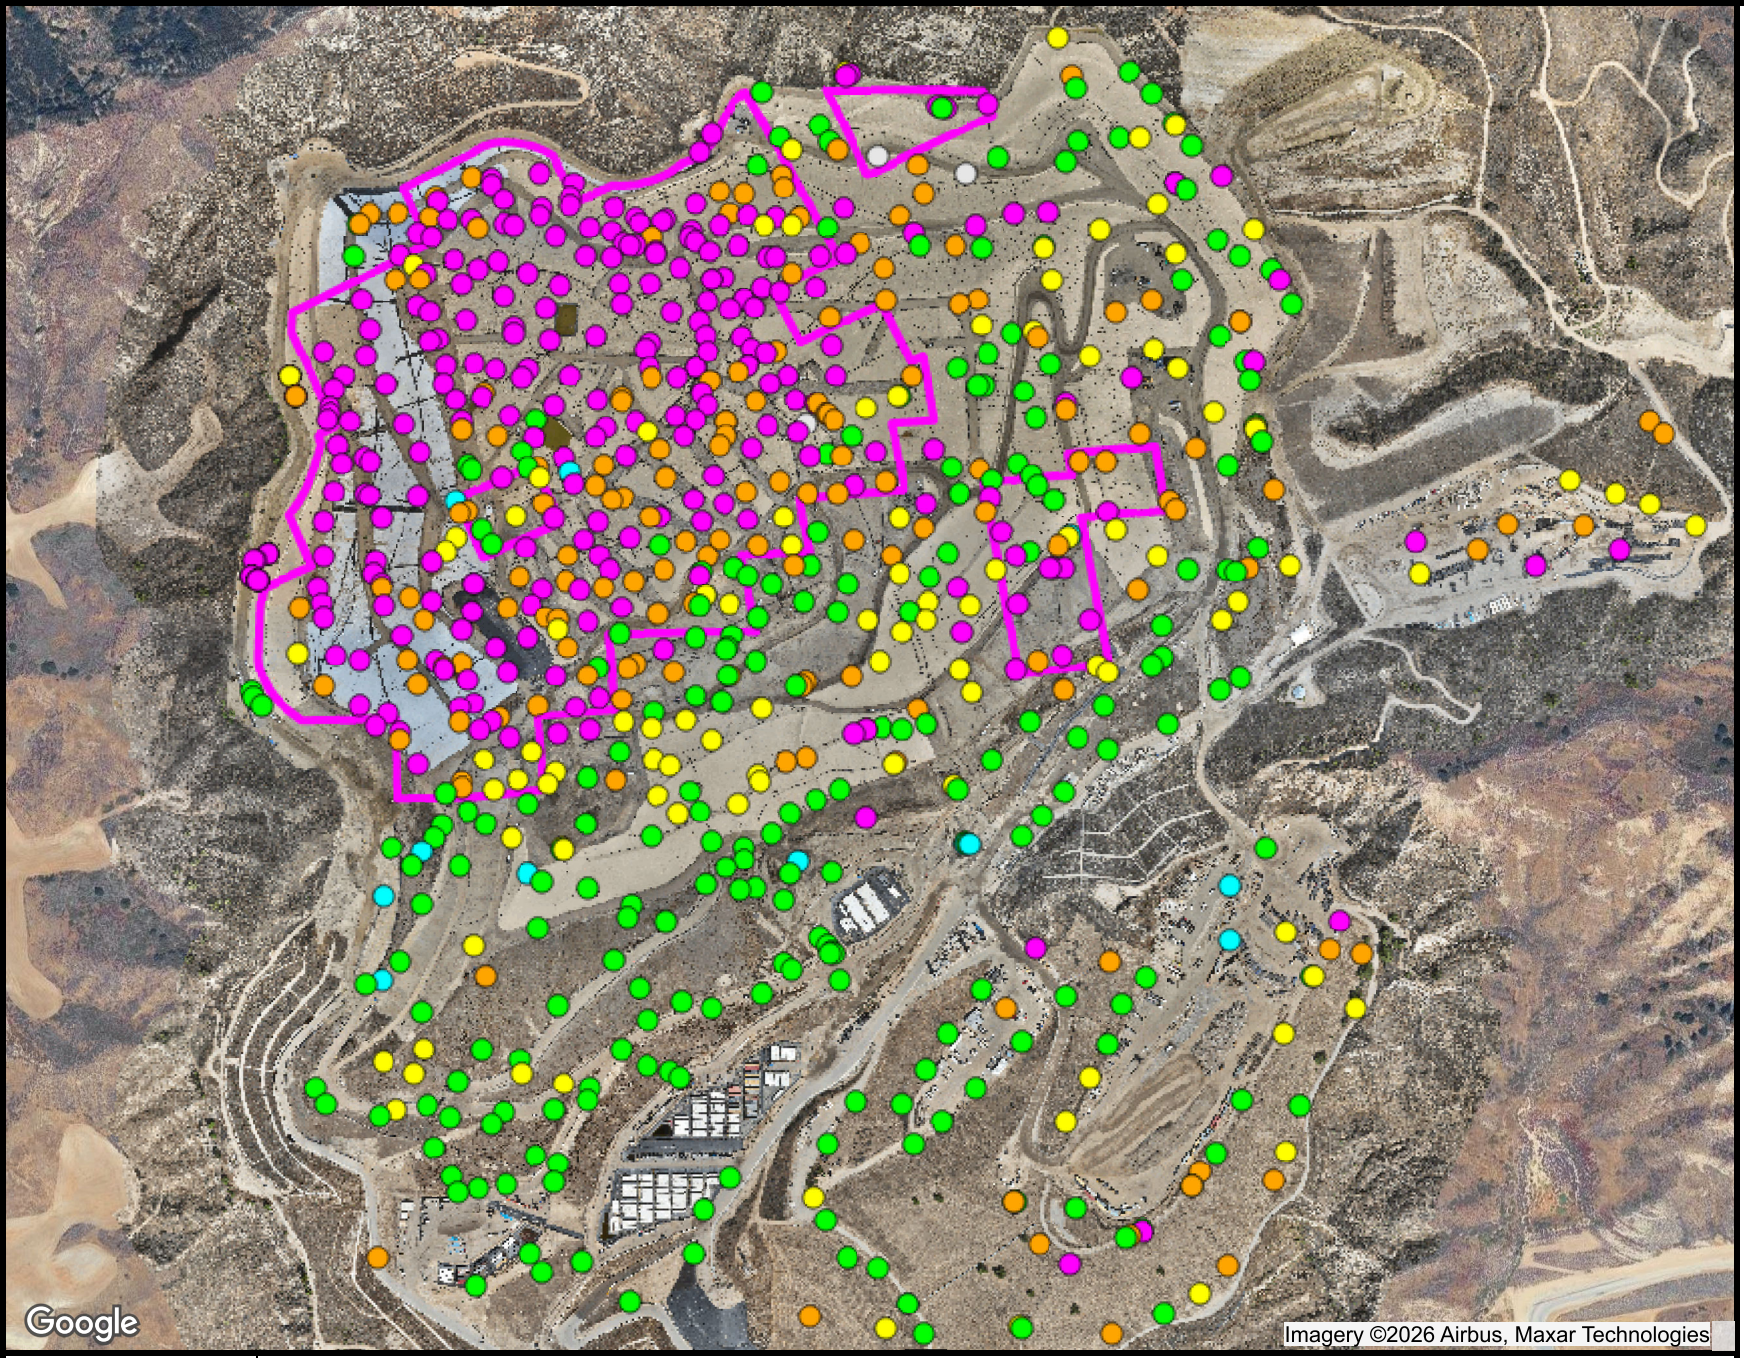

Ranges Mapped

						# Points
	>=	0	and	<	0.5	274
	>=	0.5	and	<	0.9	158
	>=	0.9	and	<	1.1	102
	>=	1.1	and	<	1.5	240
	>=	1.5	and	<	101	13
		N/A			N/A	3

Point Type Legend

well

N

SCSeTools

Chiquita Canyon Landfill

Range Map

Parameter: CH4/CO2 Ratio (high range)

Analysis Method: Average

Date Range: 09/01/2026 - 09/30/2026

Map generation date : 10/12/2026



Ranges Mapped

						# Points
	>=	0	and	<	500	31
	>=	500	and	<	1000	25
	>=	1000	and	<	1500	36
	>=	1500	and	<	2000	25
	>=	2000	and	<	1000000	37

Point Type Legend

well

N

SCSeTools

Chiquita Canyon Landfill

Range Map

Parameter: CO (mid range)

Analysis Method: Average

Date Range: 09/01/2026 - 09/30/2026

Map generation date : 10/12/2026



Ranges Mapped

						# Points
	>=	0	and	<	20000	16
	>=	20000	and	<	50000	20
	>=	50000	and	<	100000	24
	>=	100000	and	<	10000000	53

Point Type Legend

well

N

SCSeTools

Chiquita Canyon Landfill


Range Map

Parameter: H2 (mid range)

Analysis Method: Average

Date Range: 09/01/2026 - 09/30/2026

Map generation date : 10/12/2026

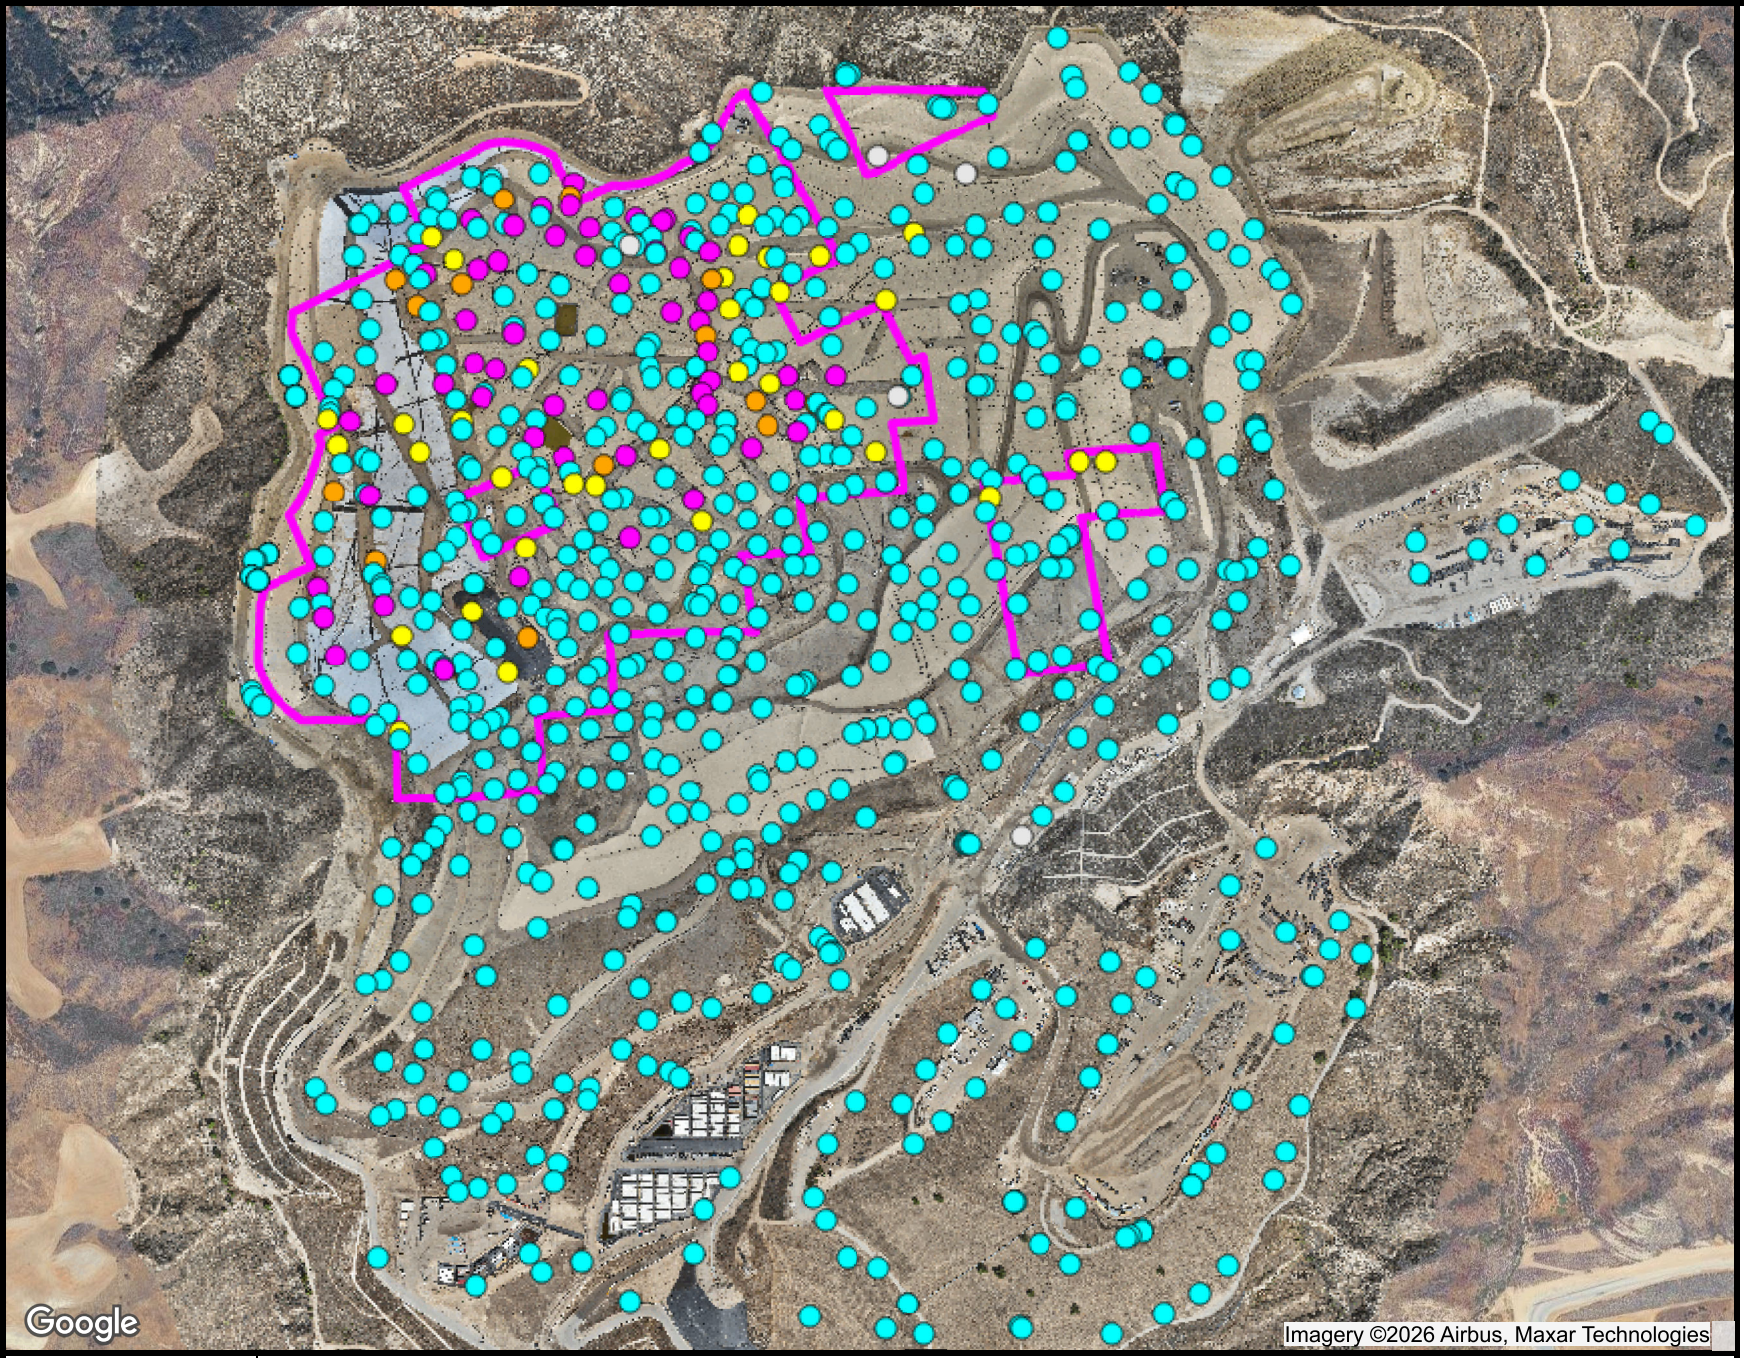

Ranges Mapped

						# Points
	>	-50	and	<=	145	682
	>	145	and	<=	160	36
	>	160	and	<=	169.99	14
	>	169.99	and	<=	999	53
		N/A			N/A	5

Point Type Legend

well

N

SCSeTools

Chiquita Canyon Landfill


Range Map

Parameter: Adj Temp (mid range)

Analysis Method: MostRecent

Date Range: 09/01/2026 - 09/30/2026

Map generation date : 10/12/2026

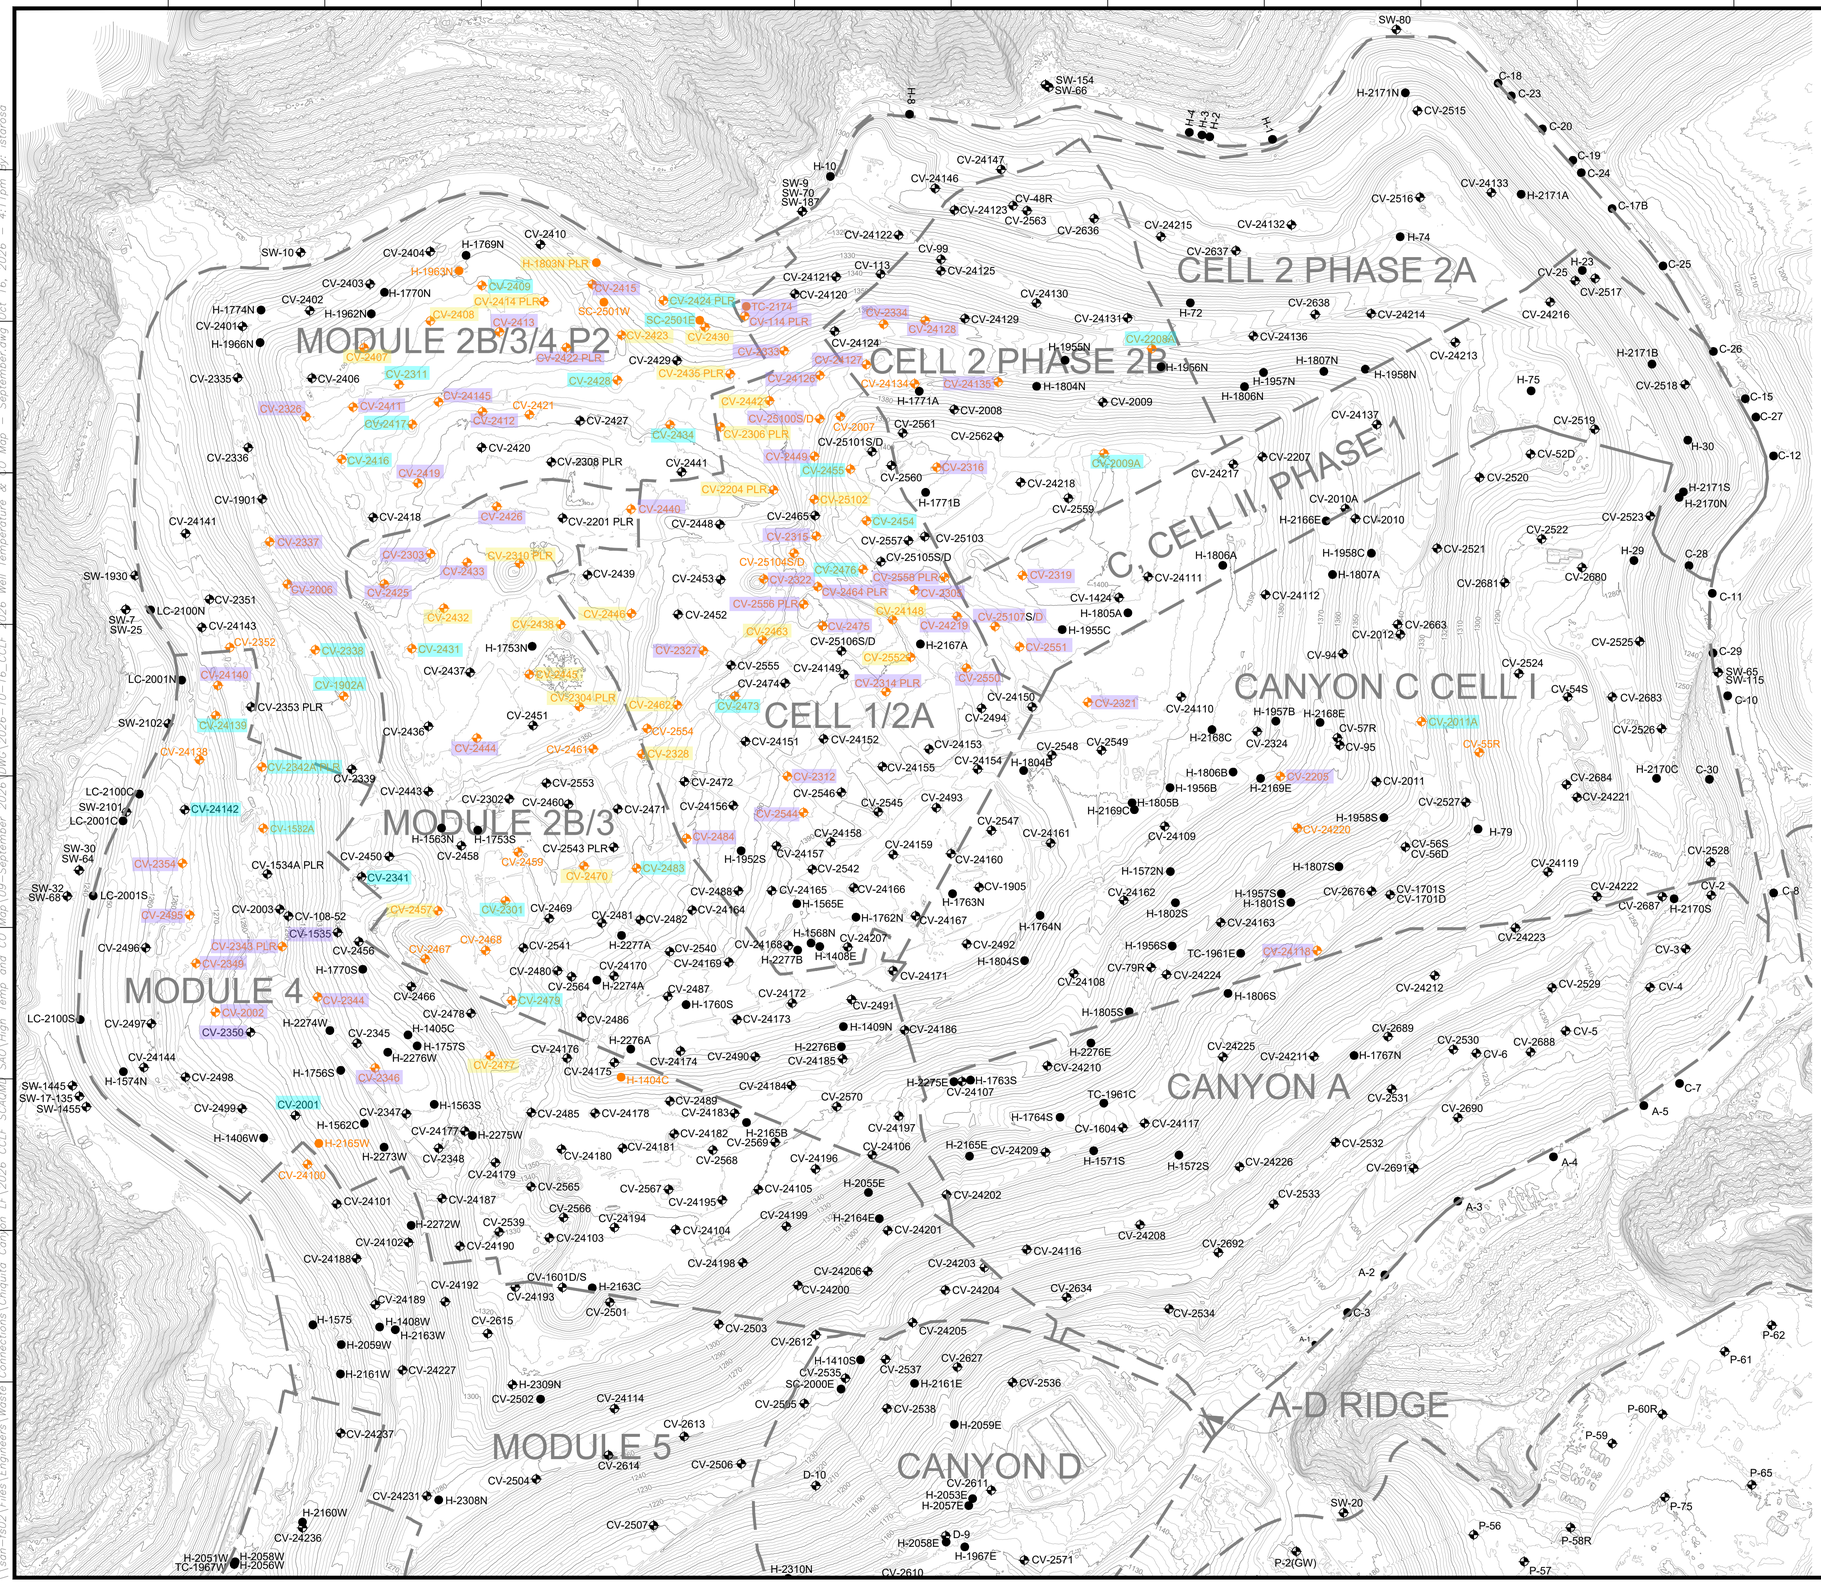

GENERAL DRAWING NOTES:

1. EXISTING AS-BUILT GCCS INFORMATION DATED SEPTEMBER 28, 2026
2. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER DATED SEPTEMBER 30, 2026.
3. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: WELL TEMPERATURE & CARBON MONOXIDE MAP SEPTEMBER 2026

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO.	DWN. BY:	CHK. BY:	ACAD FILE:	APP. BY:
01204123.45	ISR	SRM	ENGINEERS	SRM
DSN. BY: -				

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 1

J:\sdr-fs02\Files\Engineers\Waste Connections\Chiquita Canyon LF\2026 CCLF SCAQMD SAO\High Temp and CO Map\09-September 2026\DWG\2026-10-16_CCLF_2026 Well Temperature & CO Map - September.dwg Oct 16, 2026 - 4:11pm by: istarosa

Attachment H

Inspection Logs

CHIQUITA CANYON
A Waste Connections Company

September 8, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of August 31, 2026 through September 6, 2026. During this time, there was no ongoing leachate seepage or pooling at the Chiquita Canyon Landfill (the "Landfill") that occurred at a location more than once within the calendar week.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 1, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of August 31 through September 6, 2026, leachate seepage was observed on August 31, 2026, in Grid 94 at the Landfill, at approximately 7:53 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 9:30 a.m. on August 31, 2026. The seepage is estimated to have been present for approximately eight hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 12 square feet. The saturation of the soil was characterized as "Saturated." The odor intensity was characterized as "Very Light." This seepage was not observed again during the twice daily inspections during the week. Chiquita is planning to install a collection sump in the area to further minimize the potential for recurrence.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior "west slope toe drain project," in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita completed the installation of a sump pump in the area on August 11, 2026, and is currently compacting and placing fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Sarah Phillips

Sarah Phillips
Corporate Compliance Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from August 31 – September 6, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection

31 Aug 2026 / Tom Roe

Complete

Conducted on	31 Aug 2026 6:34 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

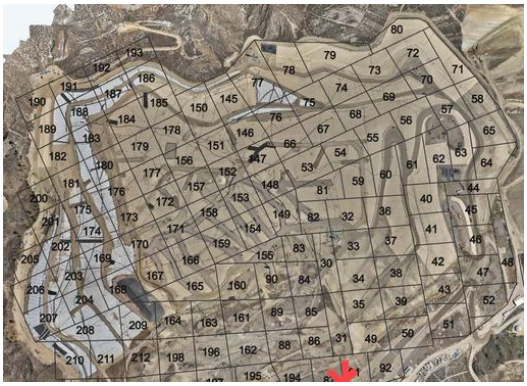




Photo 1

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43103202156213, -118.64536455843471)
Time seep/pooling was discovered	31 Aug 2026 7:53 AM PDT
Estimated duration of presence of leachate at such location	8 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	12 sq ft
Odor type	Leachate

Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling

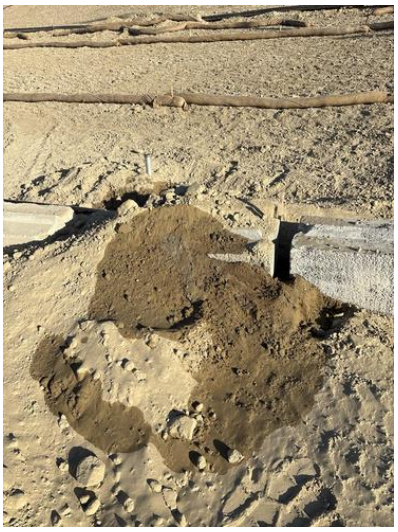


Photo 2

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Fresh soil added to contain seep.



Photo 3

4050 - Chiquita Leachate Seep/Pooling Inspection

31 Aug 2026 / Tom Roe

Complete

Conducted on	31 Aug 2026 3:11 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seep observed in grid 94 was not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Sep 2026 / Tom Roe

Complete

Conducted on	1 Sep 2026 6:43 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

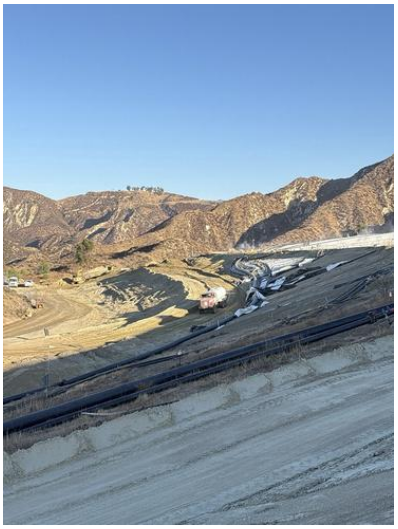


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Sep 2026 / Tom Roe

Complete

Conducted on	1 Sep 2026 1:43 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Grid 94. None of the seepage observed in this area or on the Westside was observed at the time of this inspection. Permanent repairs to the westside are currently underway.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Sep 2026 / Tom Roe

Complete

Conducted on	2 Sep 2026 7:22 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Sep 2026 / Tom Roe

Complete

Conducted on	2 Sep 2026 2:33 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Sep 2026 / John Boucher

Complete

Conducted on	3 Sep 2026 6:53 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Sep 2026 / John Boucher

Complete

Conducted on	3 Sep 2026 2:33 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Sep 2026 / John Boucher

Complete

Conducted on	4 Sep 2026 8:27 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

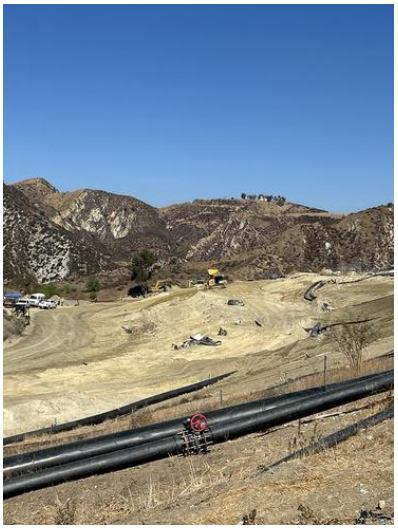


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Sep 2026 / John Boucher

Complete

Conducted on	4 Sep 2026 1:44 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

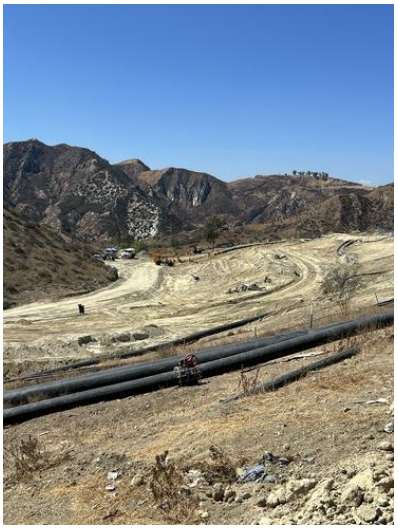


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

5 Sep 2026 / John Boucher

Complete

Conducted on	5 Sep 2026 7:30 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

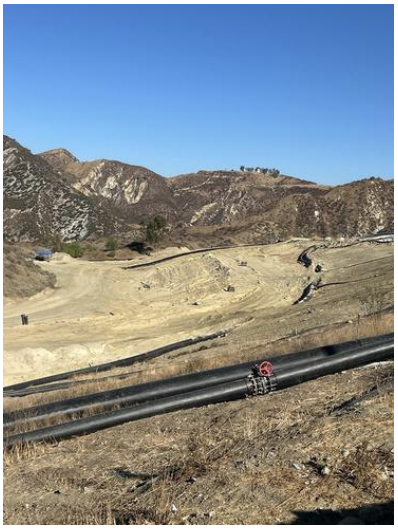


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

5 Sep 2026 / John Boucher

Complete

Conducted on	5 Sep 2026 1:08 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

6 Sep 2026 / John Boucher

Complete

Conducted on	6 Sep 2026 9:05 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

6 Sep 2026 / John Boucher

Complete

Conducted on	6 Sep 2026 1:07 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

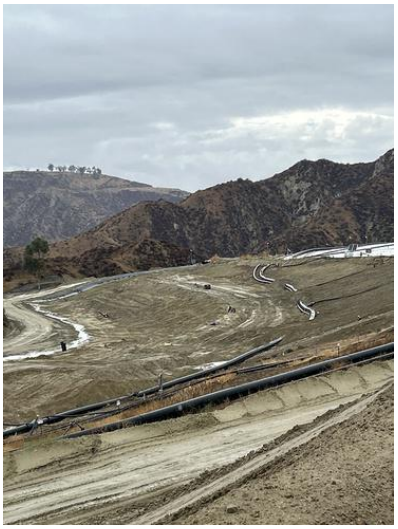


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

CHIQUITA CANYON
A Waste Connections Company

September 15, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 7, 2026 through September 13, 2026.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the morning of September 10, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that morning. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 7 through September 13, 2026, leachate seepage was observed on September 8, 2026, in Grid 94 at the Chiquita Canyon Landfill (the "Landfill"), at approximately 8:05 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 9:30 a.m. on September 8, 2026. The seepage is estimated to have been present for approximately five hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 16 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Very Light." This seepage was not observed again during the twice daily inspections during the week. Chiquita is planning to install a collection sump in the area to further minimize the potential for recurrence.

On September 9, 2026, at approximately 1:06 p.m., different seepage was initially observed in Grid 194. The specific location of this seep is shown on the maps included in the attachment. Upon

discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 3:00 p.m. on September 9, 2026. The seepage is estimated to have been present for approximately five hours. The total volume of leachate associated with this seepage is estimated to have been between 11 and 20 gallons. The observed area impacted by the seepage was approximately 35 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Light."

Seepage was again observed in Grid 194 on September 13, at approximately 7:27 a.m. Chiquita continued to implement response measures, including adding fresh soil to the affected area. The seepage was estimated to have been present for approximately four hours. The total volume of leachate associated with this seepage is estimated to have been between six and ten gallons. The observed area impacted by the seepage was approximately 16 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor was characterized as "Light." The seepage was not observed during the afternoon inspection conducted that same day.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior "west slope toe drain project," in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita completed the installation of a sump pump in the area on August 11, 2026, and is currently compacting and placing fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Sarah Phillips

Sarah Phillips
Corporate Compliance Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 7 – September 13, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection

7 Sep 2026 / Tom Roe

Complete

Conducted on	7 Sep 2026 6:47 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

7 Sep 2026 / Tom Roe

Complete

Conducted on	7 Sep 2026 1:07 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


8 Sep 2026 / Tom Roe

Complete

Conducted on	8 Sep 2026 6:48 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

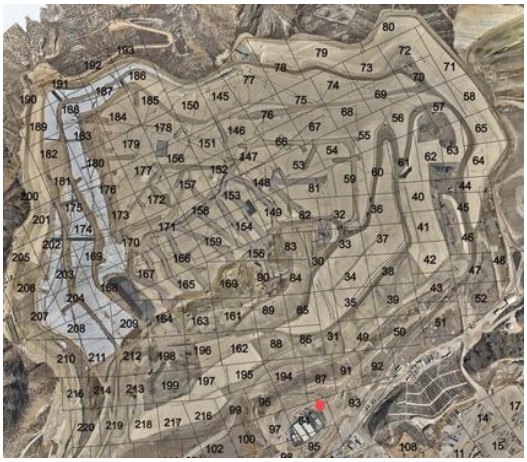

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43109548536677, -118.64515220812355)
Time seep/pooling was discovered	8 Sep 2026 8:05 AM PDT
Estimated duration of presence of leachate at such location	5 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	16 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Fresh soil added. Seep collector planned to be installed later this month.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

8 Sep 2026 / Tom Roe

Complete

Conducted on	8 Sep 2026 1:45 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seep observed in grid 94 was not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

9 Sep 2026 / Tom Roe

Complete

Conducted on	9 Sep 2026 7:25 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


9 Sep 2026 / Tom Roe

Complete

Conducted on	9 Sep 2026 1:06 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

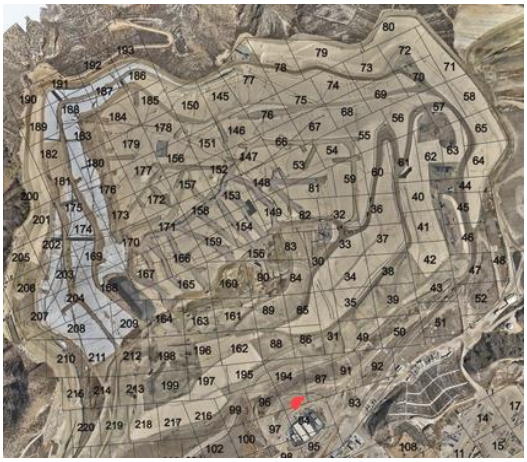

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.429721642482185, -118.64545066355299)
Time seep/pooling was discovered	9 Sep 2026 1:06 PM PDT
Estimated duration of presence of leachate at such location	5 hours
Estimated quantity of leachate	11-20 gallons
Extent of area impacted (approximate sq ft impacted)	35 sq ft
Odor type	Leachate
Odor intensity	2 - Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1



Photo 2



Photo 3

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added and compacted



Photo 4

4050 - Chiquita Leachate Seep/Pooling Inspection

10 Sep 2026 / John Boucher

Complete

Conducted on	10 Sep 2026 7:27 AM PDT

Entire main canyon inspected for 27(b)(ii)

Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

10 Sep 2026 / John Boucher

Complete

Conducted on	10 Sep 2026 1:21 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

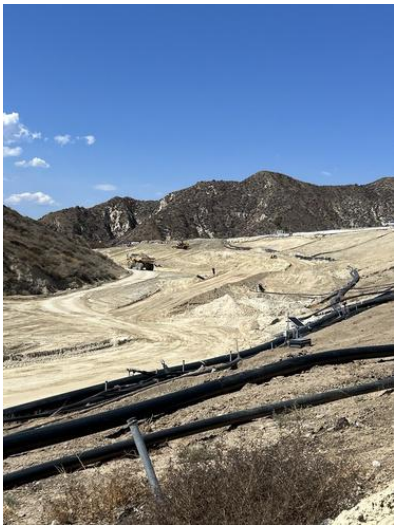


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

11 Sep 2026 / John Boucher

Complete

Conducted on	11 Sep 2026 7:15 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

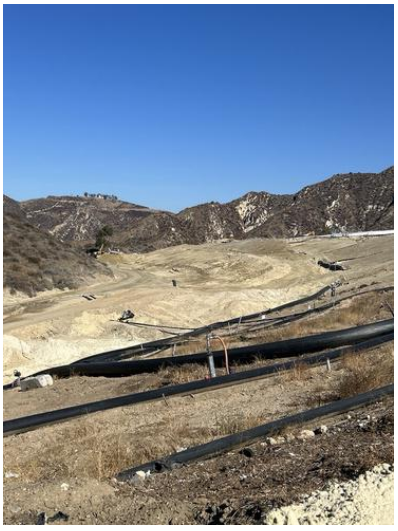


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

11 Sep 2026 / John Boucher

Complete

Conducted on	11 Sep 2026 2:12 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

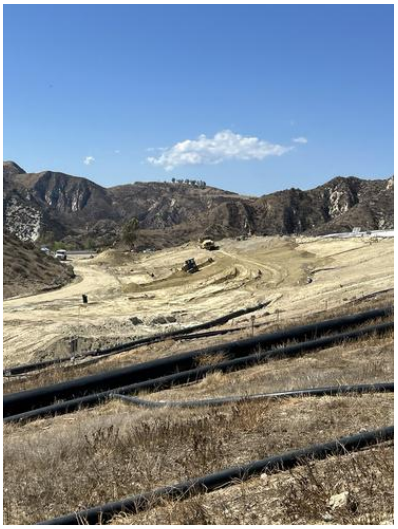


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

12 Sep 2026 / John Boucher

Complete

Conducted on	12 Sep 2026 8:04 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

12 Sep 2026 / John Boucher

Complete

Conducted on	12 Sep 2026 1:07 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


13 Sep 2026 / Tom Roe

Complete

Conducted on	13 Sep 2026 6:48 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

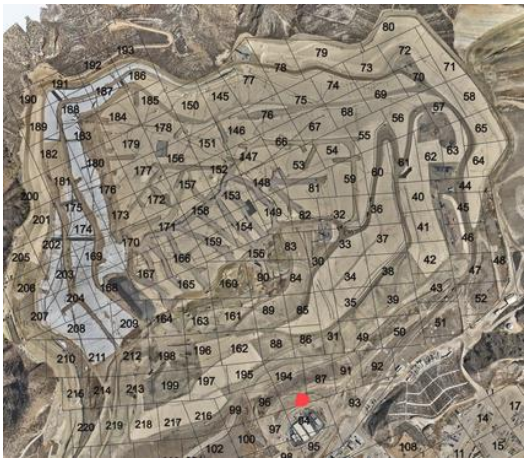

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43099405154067, -118.6455685739579)
Time seep/pooling was discovered	13 Sep 2026 7:27 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	6-10 gallons
Extent of area impacted (approximate sq ft impacted)	16 sqft
Odor type	Leachate
Odor intensity	2 - Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

13 Sep 2026 / Tom Roe

Complete

Conducted on	13 Sep 2026 1:05 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

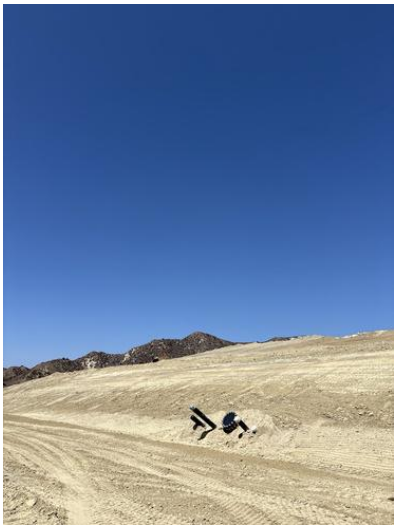


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well. The seep observed this morning in grid 194 was not observed during this inspection.

CHIQUITA CANYON
A Waste Connections Company

September 22, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 14, 2026 through September 20, 2026.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 16, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 14 through September 20, 2026, leachate seepage was initially observed on September 14, 2026, in Grid 194 at the Chiquita Canyon Landfill (the "Landfill"), at approximately 7:11 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 8:45 a.m. on September 14, 2026. The seepage is estimated to have been present for approximately three hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 16 square feet. The saturation of the soil was characterized as "Saturated." The odor intensity was characterized as "Very Light."

Seepage was again observed at the same location during the morning inspections conducted on September 15 and September 16. Chiquita continued to implement response measures, including adding fresh soil to the affected area. During September 15 and September 16, seepage observed

in Grid 194 was estimated to have been present for a cumulative total of approximately eight hours: approximately four hours on September 15, and four hours on September 16. The estimated quantity of leachate was between one and five gallons on each date. The observed area impacted by the seepage varied during the reporting period, ranging from approximately four to eight square feet. The saturation of the soil was characterized as "Standing Free Liquid." The odor was characterized as "Very Light." The seepage was not observed during subsequent inspections conducted that week.

On September 15, 2026, seepage was also observed in Grid 94, at approximately 9:24 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 11:00 a.m. on September 15, 2026. The seepage is estimated to have been present for approximately six hours total. The total volume of leachate associated with this seepage during that period is estimated to have been between 11 and 20 gallons. The observed area impacted by the seepage was approximately 100 square feet. The saturation of the soil was characterized as "Standing Free Liquid." No odor associated with this seepage was detected. This seepage was not observed again during the twice daily inspections conducted that week. This seepage is related to the previously reported seepage that occurred in Grid 94. Chiquita is planning to begin work on the installation of a seep collector, similar to a leachate toe drain, in the area this week to minimize the potential for future recurrence.

Additional seepage was observed in Grid 87 and Grid 206 on September 15 and September 16, respectively, as further described in the enclosed logs.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior west slope toe drain project, in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita is continuing to compact and place fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Sarah Phillips

Sarah Phillips
Corporate Compliance Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 14 – September 20, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection


14 Sep 2026 / Tom Roe

Complete

Conducted on	14 Sep 2026 7:11 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

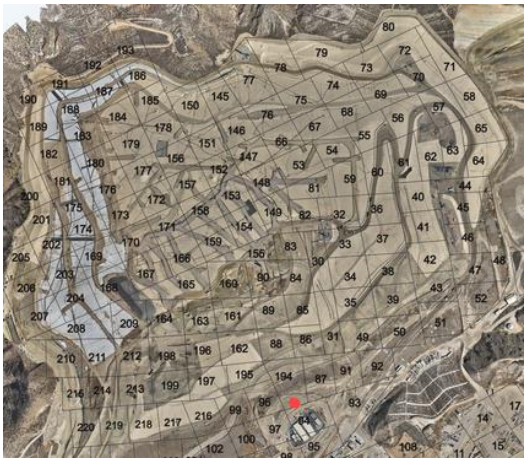

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43042935465008, -118.64554660034025)
Time seep/pooling was discovered	14 Sep 2026 7:11 AM PDT
Estimated duration of presence of leachate at such location	3 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	16 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep.

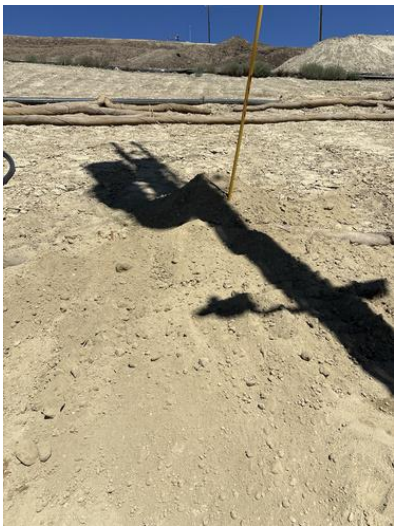


Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

14 Sep 2026 / Tom Roe

Complete

Conducted on	14 Sep 2026 1:39 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well. The seep observed in grid 194 was not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection


15 Sep 2026 / Tom Roe

Complete

Conducted on	15 Sep 2026 8:08 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

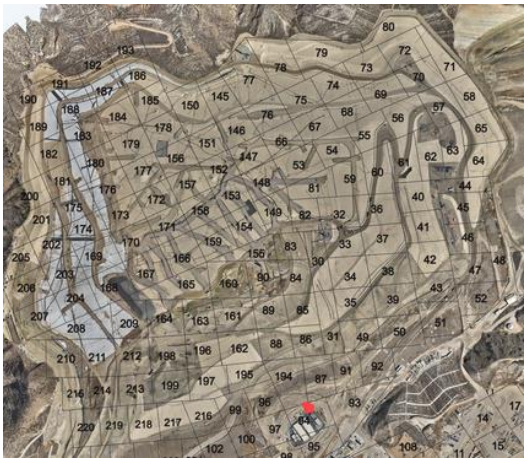

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.430730928586094, -118.64528325173862)
Time seep/pooling was discovered	15 Sep 2026 9:24 AM PDT
Estimated duration of presence of leachate at such location	6 hours
Estimated quantity of leachate	11-20 gallons
Extent of area impacted (approximate sq ft impacted)	100 sq ft
Odor type	Leachate
Odor intensity	0 - No Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep



Photo 2

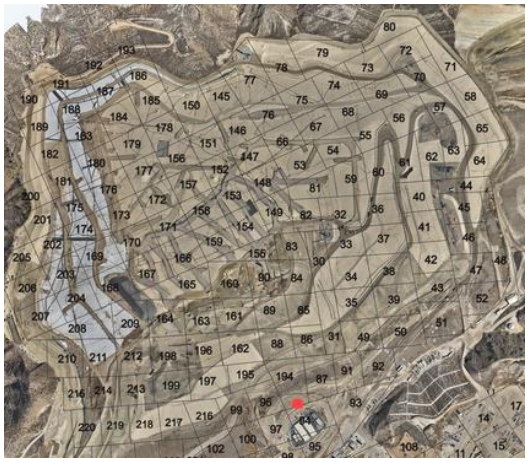


Photo 3

Leachate seep/pooling Inspection 2

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location



Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.431010844133375, -118.6455883406354)
Time seep/pooling was discovered	15 Sep 2026 9:38 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	4 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 4

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep

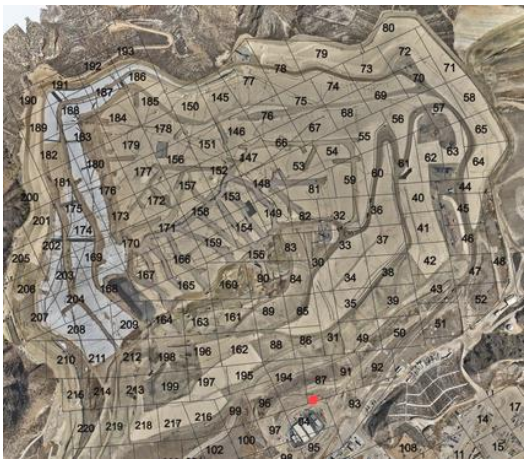


Photo 5

Leachate seep/pooling Inspection 3

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	87

Indicate on the map the location



Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43101135334356, -118.64552800241071)
Time seep/pooling was discovered	15 Sep 2026 9:42 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	1-5 gallons

Extent of area impacted (approximate sq ft impacted)	10sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling



Photo 6

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep



Photo 7

4050 - Chiquita Leachate Seep/Pooling Inspection

15 Sep 2026 / Tom Roe

Complete

Conducted on	15 Sep 2026 1:51 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seep observed in grids 94, 194, and 87 were not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection


16 Sep 2026 / Tom Roe

Complete

Conducted on	16 Sep 2026 6:45 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

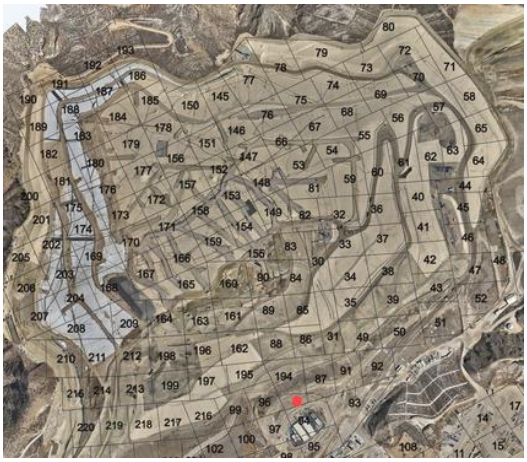

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.42984709505895, -118.64531673763602)
Time seep/pooling was discovered	16 Sep 2026 7:49 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	8sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Dirt added and a piece of liner put in place to contain seep.

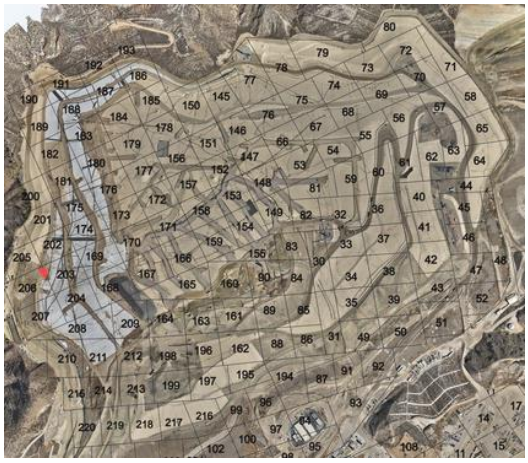


Photo 2

Leachate seep/pooling Inspection 2

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	206

Indicate on the map the location



Drop Pin to record lat/long of seep/pooling location.	(34.43748033111619, -118.65205339077002)
Time seep/pooling was discovered	16 Sep 2026 9:36 AM PDT
Estimated duration of presence of leachate at such location	3 hours
Estimated quantity of leachate	11-20 gallons
Extent of area impacted (approximate sq ft impacted)	150 sq ft
Odor type	Leachate
Odor intensity	4 - Strong Odor
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 3

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Liquid vacuumed out. The previously buried drainage pipe, which had been temporarily plugged during the West Toe Project, was uncovered and the plug was removed. The pipe is now open and properly draining into the West Toe Project area as intended.



Photo 4

4050 - Chiquita Leachate Seep/Pooling Inspection

16 Sep 2026 / Tom Roe

Complete

Conducted on	16 Sep 2026 2:25 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seeps observed in grid 194 and 206 were not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 8:13 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 2:09 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

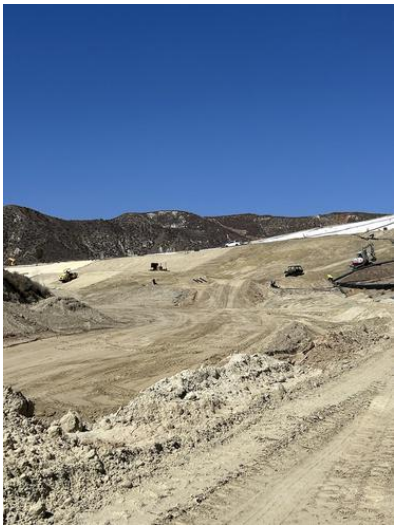


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 8:13 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 2:09 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

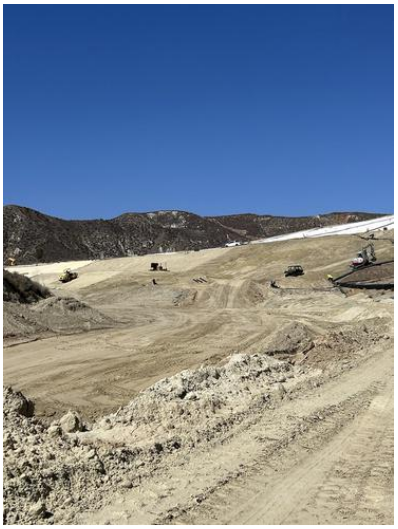


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

18 Sep 2026 / John Boucher

Complete

Conducted on	18 Sep 2026 7:22 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

18 Sep 2026 / John Boucher

Complete

Conducted on	18 Sep 2026 2:20 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

19 Sep 2026 / John Boucher

Complete

Conducted on	19 Sep 2026 8:07 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

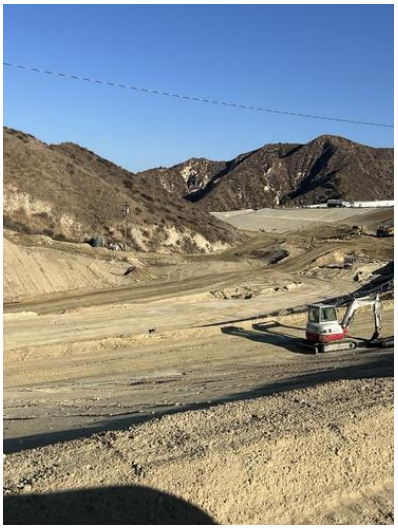


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

19 Sep 2026 / John Boucher

Complete

Conducted on	19 Sep 2026 1:02 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

20 Sep 2026 / Edwin DeLeon/Mike Alvarez

Complete

Conducted on	20 Sep 2026 6:21 AM PDT
Prepared by	Edwin DeLeon/Mike Alvarez

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No

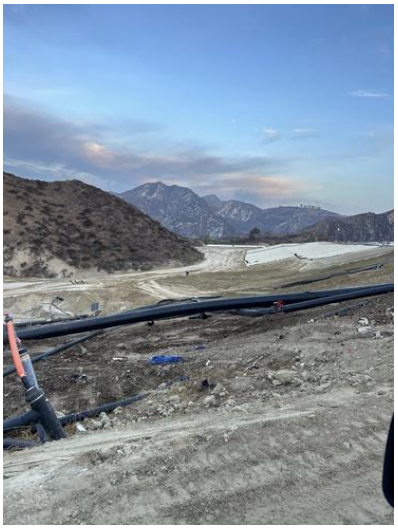


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

20 Sep 2026 / Edwin DeLeon/Mike Alvarez

Complete

Conducted on	20 Sep 2026 1:10 PM PDT
Prepared by	Edwin DeLeon/Mike Alvarez

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

CHIQUITA CANYON
A Waste Connections Company

September 29, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 21, 2026 through September 27, 2026.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 23, 2026, in accordance with the new Condition 27(b)(ii) of the Order. Leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 21 through September 27, 2026, leachate seepage was initially observed on September 21, 2026, in Grid 94 at the Chiquita Canyon Landfill (the "Landfill"), at approximately 9:27 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 11:00 a.m. on September 21, 2026. The seepage is estimated to have been present for approximately six hours. The total volume of leachate associated with this seepage is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 12 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Very Light." This seepage is related to the previously reported seepage that occurred in Grid 94 and Grid 194. Chiquita is currently installing a seep collector, similar to a leachate toe drain, in the area to minimize the potential for future recurrence.

Seepage was again observed at the same location during the afternoon inspection conducted on September 23, 2026. Chiquita continued to implement response measures, including adding fresh soil to the affected area. Seepage observed in Grid 94 was estimated to have been present for approximately two hours on September 23. The estimated quantity of leachate was between one and five gallons during that period. The observed area impacted was approximately seven square feet. The saturation of the soil was characterized as "Standing free liquid." No odor associated with this seepage was detected. The seepage was not observed during subsequent inspections conducted that week.

On September 22, 2026, seepage was also observed in Grid 194, at approximately 3:03 p.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 3:30 p.m. on September 22, 2026. The seepage is estimated to have been present for approximately three hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately six square feet. The saturation of the soil was characterized as "Saturated." The odor intensity was characterized as "Very Light." This seepage was not observed again during the twice daily inspections conducted that week.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior west slope toe drain project, in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita is continuing to compact and place fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Matt Breuer
Environmental Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 21 – September 27, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection


21 Sep 2026 / Tom Roe

Complete

Conducted on	21 Sep 2026 6:54 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

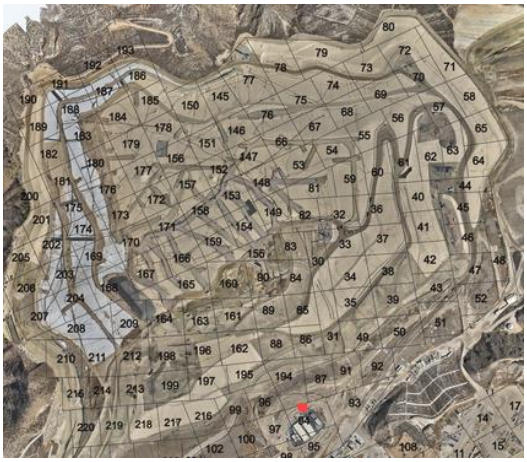

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.429568314455985, -118.64553770982519)
Time seep/pooling was discovered	21 Sep 2026 9:27 AM PDT
Estimated duration of presence of leachate at such location	6 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	12 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep. Construction of leachate interceptor trench to prevent future seepage scheduled to begin this week.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

21 Sep 2026 / Tom Roe

Complete

Conducted on	21 Sep 2026 2:45 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Grid 94. None of the seepage observed in this area or on the Westside was observed at the time of this inspection. Permanent repairs to the westside are currently underway.

4050 - Chiquita Leachate Seep/Pooling Inspection

22 Sep 2026 / Tom Roe

Complete

Conducted on	22 Sep 2026 6:59 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No

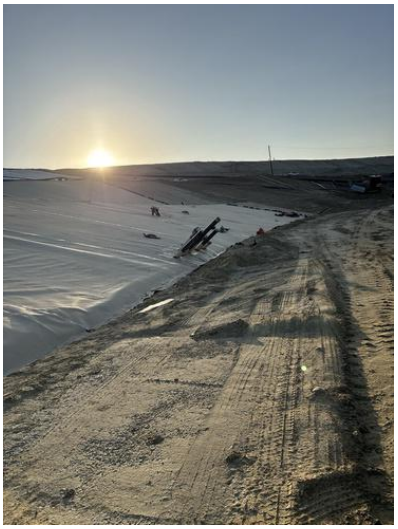


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


22 Sep 2026 / Tom Roe

Complete

Conducted on	22 Sep 2026 2:01 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

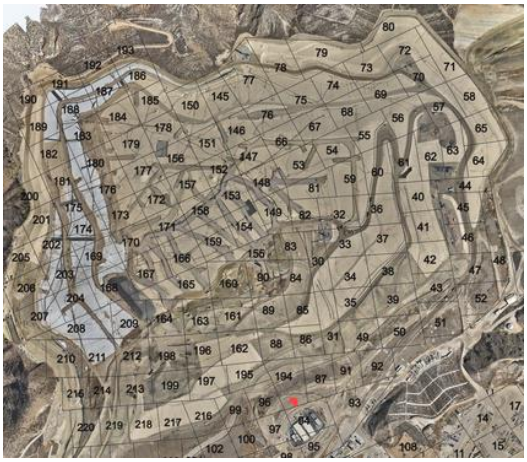

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.42927249578992, -118.64584659211286)
Time seep/pooling was discovered	22 Sep 2026 3:03 PM PDT
Estimated duration of presence of leachate at such location	3 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	6 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep. Construction of interceptor trench scheduled to begin this week.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

23 Sep 2026 / Tom Roe

Complete

Conducted on	23 Sep 2026 7:17 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No

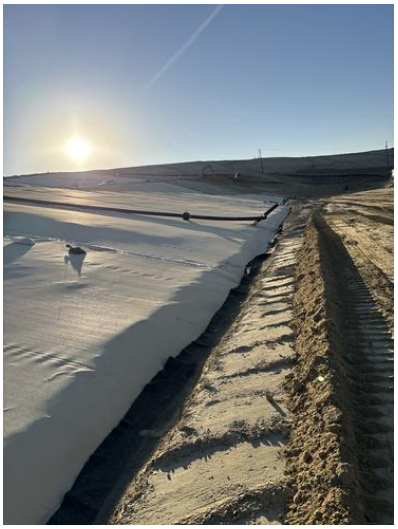


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

23 Sep 2026 / Tom Roe

Complete


Conducted on	23 Sep 2026 2:03 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

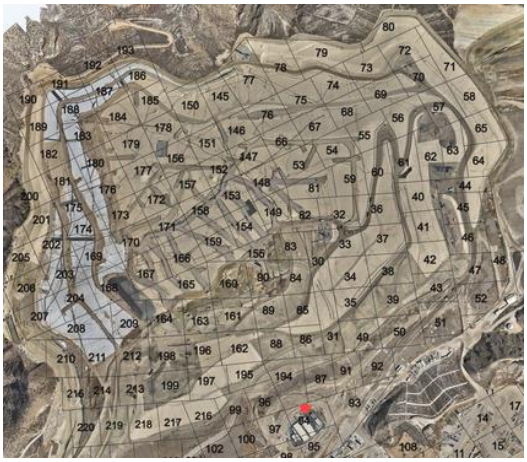

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.42969961471349, -118.64579633425224)
Time seep/pooling was discovered	23 Sep 2026 2:44 PM PDT
Estimated duration of presence of leachate at such location	2 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	7sq ft
Odor type	Leachate
Odor intensity	0 - No Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep. Interceptor trench scheduled to begin soon.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

24 Sep 2026 / John Boucher

Complete

Conducted on	24 Sep 2026 7:05 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

24 Sep 2026 / John Boucher

Complete

Conducted on	24 Sep 2026 1:02 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

25 Sep 2026 / Nancy Bahena Hernandez

Complete

Conducted on	25 Sep 2026 7:34 AM PDT
Prepared by	Nancy Bahena Hernandez

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

25 Sep 2026 / Nancy Bahena Hernandez

Complete

Conducted on	25 Sep 2026 1:04 PM PDT
Prepared by	Nancy Bahena Hernandez

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

26 Sep 2026 / John Boucher

Complete

Conducted on	26 Sep 2026 8:05 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

26 Sep 2026 / John Boucher

Complete

Conducted on	26 Sep 2026 1:00 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

27 Sep 2026 / Edwin DeLeon

Complete

Conducted on	27 Sep 2026 7:06 AM PDT
Prepared by	Edwin DeLeon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

27 Sep 2026 / Edwin DeLeon

Complete

Conducted on	27 Sep 2026 1:08 PM PDT
Prepared by	Edwin DeLeon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

CHIQUITA CANYON
A Waste Connections Company

October 6, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 28, 2026 through October 4, 2026. During this time, there was no ongoing leachate seepage or pooling at the Chiquita Canyon Landfill (the "Landfill") that occurred at a location more than once within the calendar week.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 30, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 28, 2026 through October 4, 2026, multiple related seeps were observed on September 30, 2026, in Grid 87 and Grid 194 at the Landfill, at approximately 6:30 a.m. The specific location of the seepage is shown on the maps included in the attachment. Upon discovery of the seepage, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected areas. This initial response work was completed by approximately 8:15 a.m. on September 30, 2026. The seepage is estimated to have been present for approximately four hours. The total volume of leachate from the seepage is estimated to have been between six and ten gallons. The combined area impacted by the seepage was approximately 25 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Light." This seepage was not observed again during the twice daily inspections during the week. This seepage is related to the previously reported seepage that occurred in Grid 94 and Grid 194. On October 2, 2026, Chiquita completed the installation of a seep collector, similar to a leachate toe drain, in the area to further minimize the potential for recurrence.

Chiquita is also continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior "west slope toe drain project," in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita recently completed the construction of the lower and upper buttresses and is continuing work on the remainder of the west toe project, including the installation of stormwater infrastructure and completion of roadway improvements.

Please contact me if you have any questions regarding this matter.

Regards,

Tessa Lenz

Tessa Lenz
Environmental Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 28 – October 4, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection

28 Sep 2026 / Tom Roe

Complete

Conducted on	28 Sep 2026 6:45 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

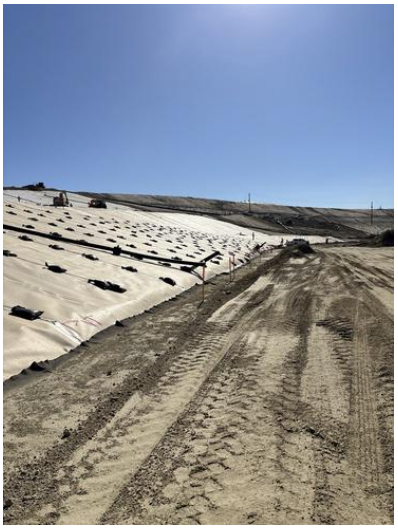


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

28 Sep 2026 / Tom Roe

Complete

Conducted on	28 Sep 2026 2:50 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

29 Sep 2026 / Tom Roe

Complete

Conducted on	29 Sep 2026 7:17 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

29 Sep 2026 / Tom Roe

Complete

Conducted on	29 Sep 2026 2:10 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

30 Sep 2026 / Tom Roe

Complete

Conducted on	30 Sep 2026 6:28 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection


Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194,87

Seeping from multiple locations, all related.

Indicate on the map the location

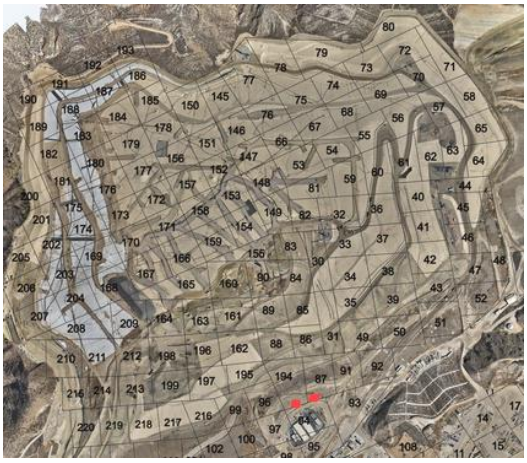

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43111202925636, -118.64528987991329)
Time seep/pooling was discovered	30 Sep 2026 6:30 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	6-10 gallons

Volume combined between areas

Extent of area impacted (approximate sq ft impacted)	25 sq ft (combined between locations)
Odor type	Leachate
Odor intensity	2 - Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1



Photo 2



Photo 3

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seeps. Seep collector construction is in progress.



Photo 4

4050 - Chiquita Leachate Seep/Pooling Inspection

30 Sep 2026 / Tom Roe

Complete

Conducted on	30 Sep 2026 2:09 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seeps observed in grid 194 and 87 were also not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Oct 2026 / John Boucher

Complete

Conducted on	1 Oct 2026 8:09 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Oct 2026 / John Boucher

Complete

Conducted on	1 Oct 2026 1:47 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Oct 2026 / John Boucher

Complete

Conducted on	2 Oct 2026 7:10 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Oct 2026 / John Boucher

Complete

Conducted on	2 Oct 2026 2:11 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

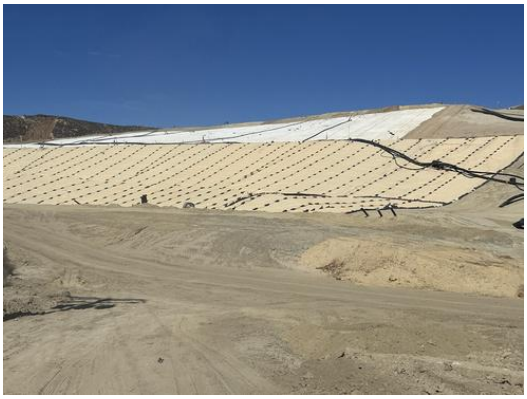


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Oct 2026 / Edwin De Leon

Complete

Conducted on	3 Oct 2026 6:34 AM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

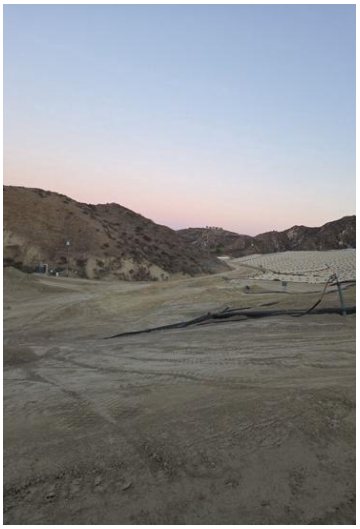


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Oct 2026 / Edwin De Leon

Complete

Conducted on	3 Oct 2026 1:40 PM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Oct 2026 / Edwin De Leon

Complete

Conducted on	4 Oct 2026 6:40 AM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

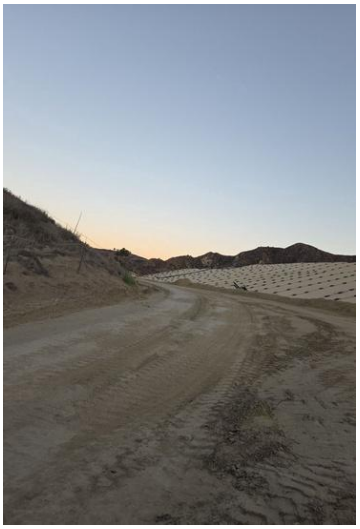


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Oct 2026 / Edwin De Leon

Complete

Conducted on	4 Oct 2026 1:05 PM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No

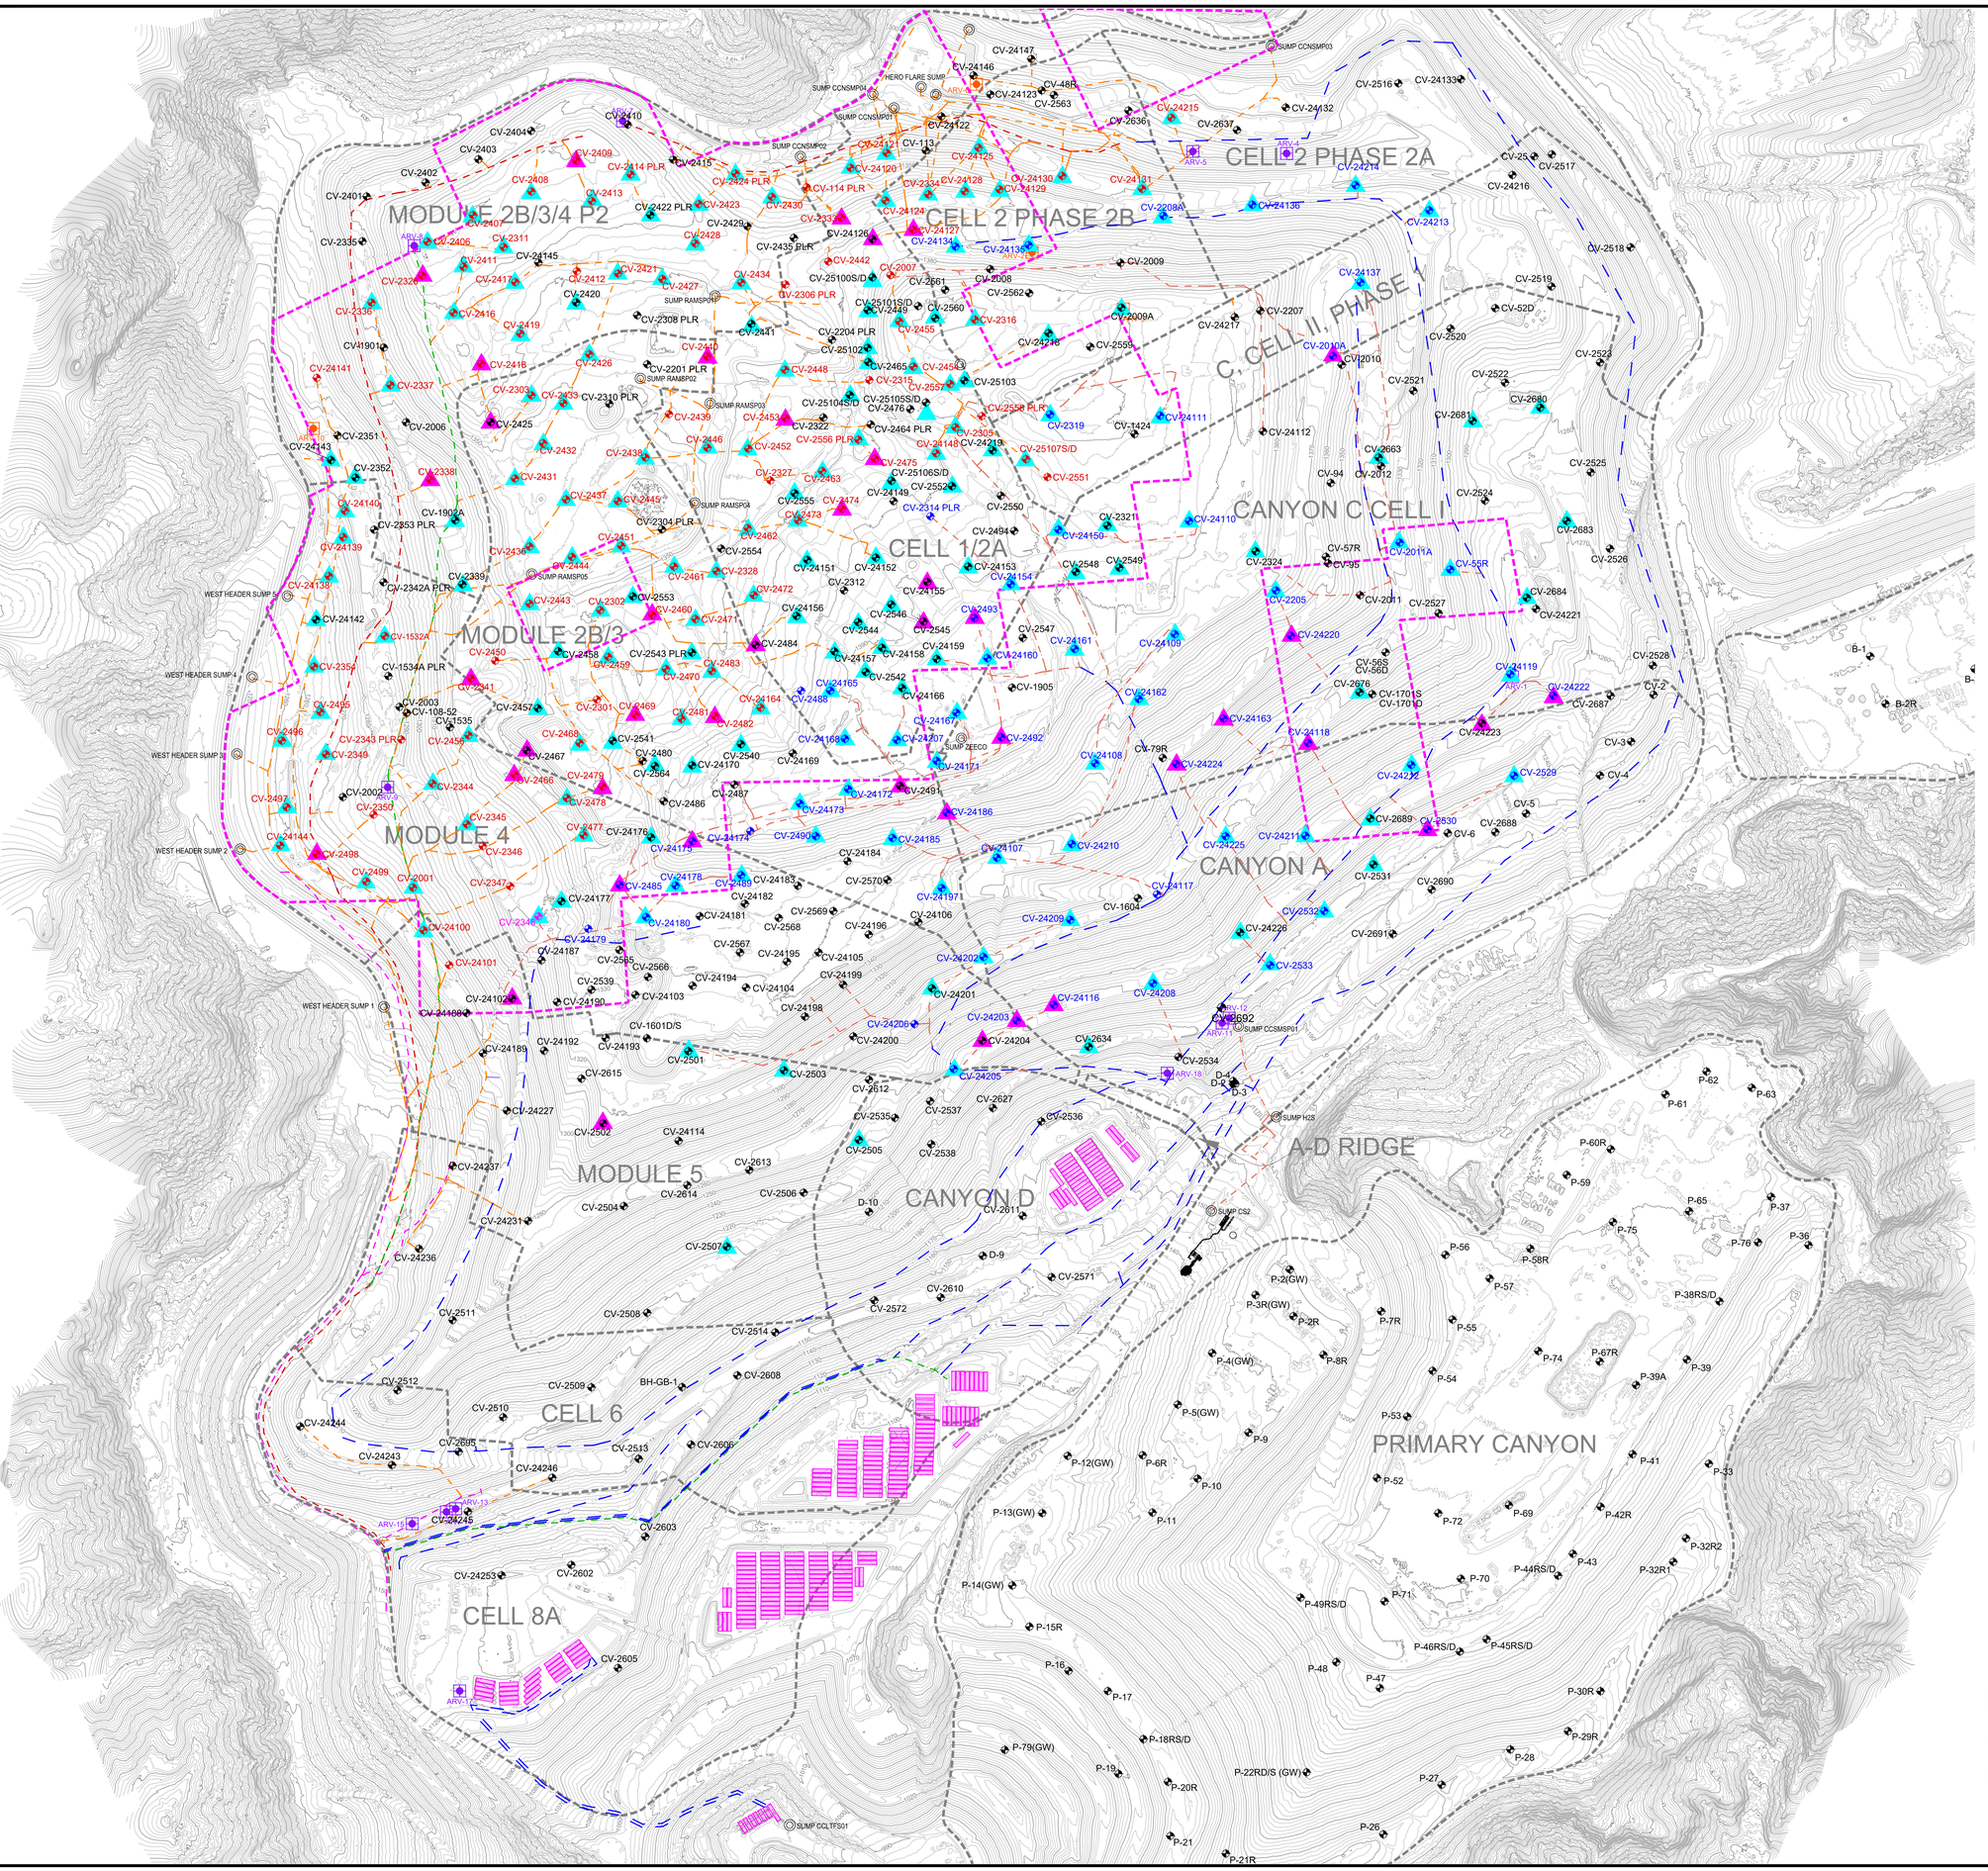



Photo 1


Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

Attachment I

Drilling and Waste Characterization Map, Surface Emissions Monitoring Grid Map, GCCS As-Built Map, and Condition 8(m) Maps


MODULE 2B/3/4 P2
CELL 2 PHASE 2B
CELL 2 PHASE 2A
C, CELL II, PHASE
CANYON C CELL I
CELL 1/2A
MODULE 2B/3
MODULE 4
CANYON A
MODULE 5
CANYON D
A-D RIDGE
CELL 6
PRIMARY CANYON
CELL 8A
WEST HEADER SUMP 1
WEST HEADER SUMP 2
WEST HEADER SUMP 3
WEST HEADER SUMP 4
WEST HEADER SUMP 5
SUMP CCSMSP01
SUMP CCSMSP02
SUMP CCSMSP03
SUMP CCSMSP04
SUMP CCSMSP05
SUMP RAMSP01
SUMP RAMSP02
SUMP RAMSP03
SUMP RAMSP04
SUMP RAMSP05
SUMP ZEECO
SUMP H2S
SUMP CS2
SUMP CCLTFS01
HERO FLARE SUMP
ARV-1
ARV-2
ARV-3
ARV-4
ARV-5
ARV-11
ARV-12
ARV-13
ARV-15
ARV-18
ARV-19
CV-2147
CV-24146
CV-24123
CV-2563
CV-2636
CV-2637
CV-2516
CV-24133
CV-24215
CV-24132
CV-24122
CV-24121
CV-113
CV-24125
CV-24128
CV-24130
CV-24129
CV-24131
CV-2208A
CV-24136
CV-24214
CV-25
CV-2517
CV-24216
CV-24213
CV-2518
CV-2519
CV-52D
CV-2520
CV-2523
CV-2522
CV-2680
CV-2681
CV-24137
CV-2207
CV-24217
CV-2009A
CV-2009
CV-2008
CV-2561
CV-25101S/D
CV-2562
CV-2560
CV-2316
CV-24218
CV-2559
CV-2010A
CV2010
CV-2521
CV-24111
CV-24112
CV-2663
CV-2012
CV-94
CV-2525
CV-2524
CV-2683
CV-2526
CV-57R
CV-95
CV-2011A
CV-55R
CV-2324
CV-2205
CV-2011
CV-2527
CV-24220
CV-2684
CV-24221
CV-56S
CV-56D
CV-2676
CV-1701S
CV-1701D
CV-24119
CV-24222
CV-2687
CV-2528
CV-2
CV-24223
CV-3
CV-24118
CV-24108
CV-79R
CV-24224
CV-24212
CV-2529
CV-4
CV-5
CV-2689
CV-2530
CV-6
CV-2688
CV-24225
CV-24211
CV-2531
CV-2690
CV-24117
CV-1604
CV-24209
CV-2532
CV-24226
CV-2691
CV-2533
CV-24208
CV-24116
CV-2692
CV-2634
CV-2534
CV-24205
CV-24203
CV-24204
CV-24206
CV-24200
CV-24201
CV-24202
CV-24197
CV-24106
CV-24196
CV-24105
CV-24195
CV-24104
CV-24194
CV-24199
CV-24198
CV-24103
CV-24102
CV-24190
CV-1601D/S
CV-24192
CV-24193
CV-24189
CV-2501
CV-2503
CV-2615
CV-24227
CV-2502
CV-24114
CV-24237
CV-24231
CV-24236
CV-2504
CV-2614
CV-2613
CV-2506
CV-2507
CV-2505
CV-2538
CV-2535
CV-2537
CV-2627
CV-2536
CV-2612
CV-24184
CV-2570
CV-24183
CV-24182
CV-24181
CV-2569
CV-2568
CV-2567
CV-24187
CV-2565
CV-2566
CV-2539
CV-24177
CV-24176
CV-24175
CV-24174
CV-24173
CV-24172
CV-24171
CV-24170
CV-24169
CV-24168
CV-24167
CV-24166
CV-24165
CV-24164
CV-24163
CV-24162
CV-24161
CV-24160
CV-1905
CV-24159
CV-24158
CV-24157
CV-24156
CV-2546
CV-2544
CV-2545
CV-24493
CV-2547
CV-24154
CV-24153
CV-2548
CV-2549
CV-24150
CV-2321
CV-24110
CV-24148
CV-24149
CV-2552
CV-2551
CV-2550
CV-2494
CV-2312
CV-24155
CV-24152
CV-24151
CV-2554
CV-2462
CV-2555
CV-2474
CV-2473
CV-2314 PLR
CV-2304 PLR
CV-2463
CV-2556 PLR
CV-2452
CV-2453
CV-2322
CV-2464 PLR
CV-2305
CV-2475
CV-25106S/D
CV-2476
CV-25105S/D
CV-25104S/D
CV-2558 PLR
CV-2315
CV-2557
CV-25103
CV-25102
CV-2465
CV-2454
CV-2448
CV-2201 PLR
CV-2446
CV-2439
CV-2438
CV-2327
CV-2328
CV-2461
CV-2472
CV-2484
CV-2483
CV-2481
CV-2482
CV-2488
CV-2541
CV-2540
CV-2564
CV-24170
CV-2487
CV-2486
CV-24173
CV-24186
CV-24185
CV-24107
CV-24210
CV-2491
CV-2492
CV-24207
CV-24197
CV-24178
CV-2485
CV-24179
CV-24180
CV-24189
CV-24183
CV-2490
CV-24474
CV-24475
CV-2469
CV-2470
CV-2471
CV-2460
CV-2302
CV-2553
CV-2543 PLR
CV-2458
CV-2459
CV-2450
CV-2457
CV-2301
CV-2468
CV-2467
CV-2466
CV-2479
CV-2478
CV-24477
CV-24476
CV-2345
CV-2346
CV-2347
CV-2344
CV-24100
CV-24101
CV-2349
CV-2350
CV-2498
CV-2499
CV-2001
CV-2002
CV-2003
CV-108-52
CV-1535
CV-2343 PLR
CV-2496
CV-2495
CV-2341
CV-1534A PLR
CV-2354
CV-1532A
CV-2342A PLR
CV-24142
CV-24138
CV-2339
CV-24139
CV-24140
CV-1902A
CV-2853 PLR
CV-2352
CV-24143
CV-2351
CV-2006
CV-2425
CV-2432
CV-2431
CV-2457
CV-2445
CV-2444
CV-2436
CV-2554
CV-2328
CV-2472
CV-2312

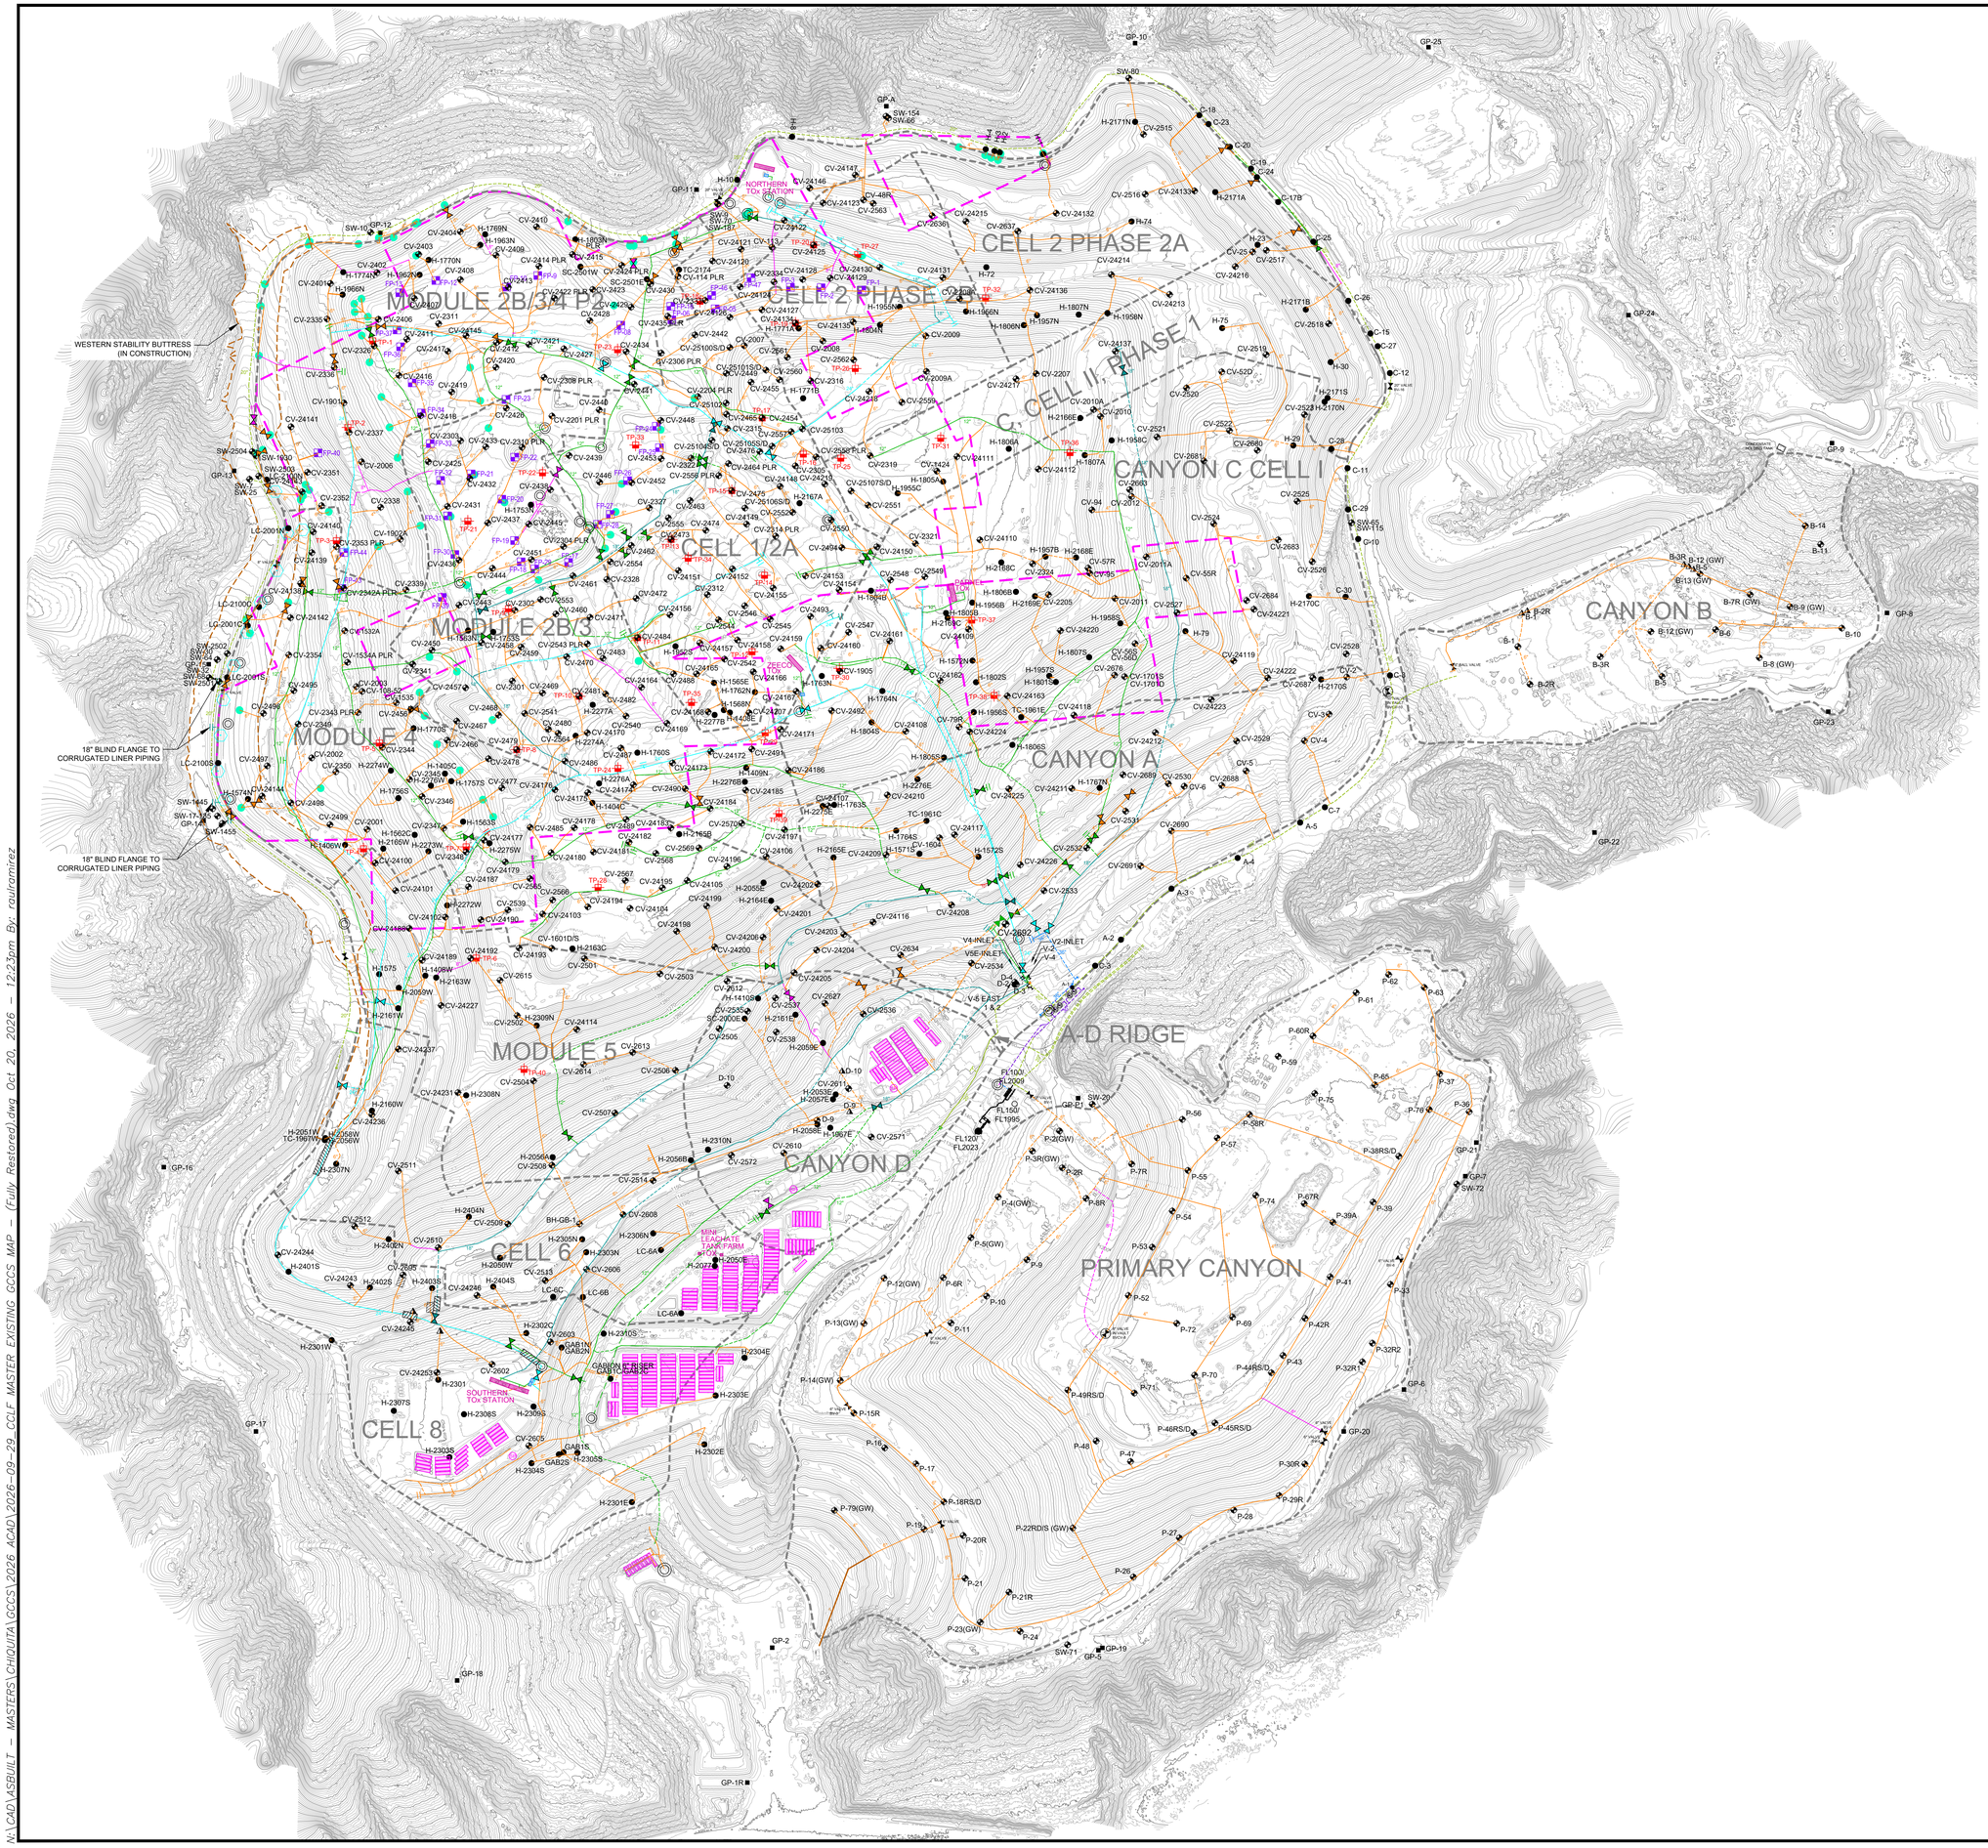
CELL 2 PHASE 2A
CELL 2 PHASE 2B
CELL II PHASE 1
CANYON C CELL I
CELL 1/2A
MODULE 2B/3
MODULE 2B/3/4 P2
MODULE 4
MODULE 5
CELL 6
CELL 8
CANYON A
CANYON B
CANYON D
PRIMARY CANYON
A-D RIDGE
WESTERN STABILITY BUTTRESS (IN CONSTRUCTION)
18" BLIND FLANGE TO CORRUGATED LINER PIPING
18" BLIND FLANGE TO CORRUGATED LINER PIPING
NORTHERN TOx STATION
SOUTHERN TOx STATION
MSW LEACHATE TANK FARM
GABION RISER
GABION RISER
GABION RISER

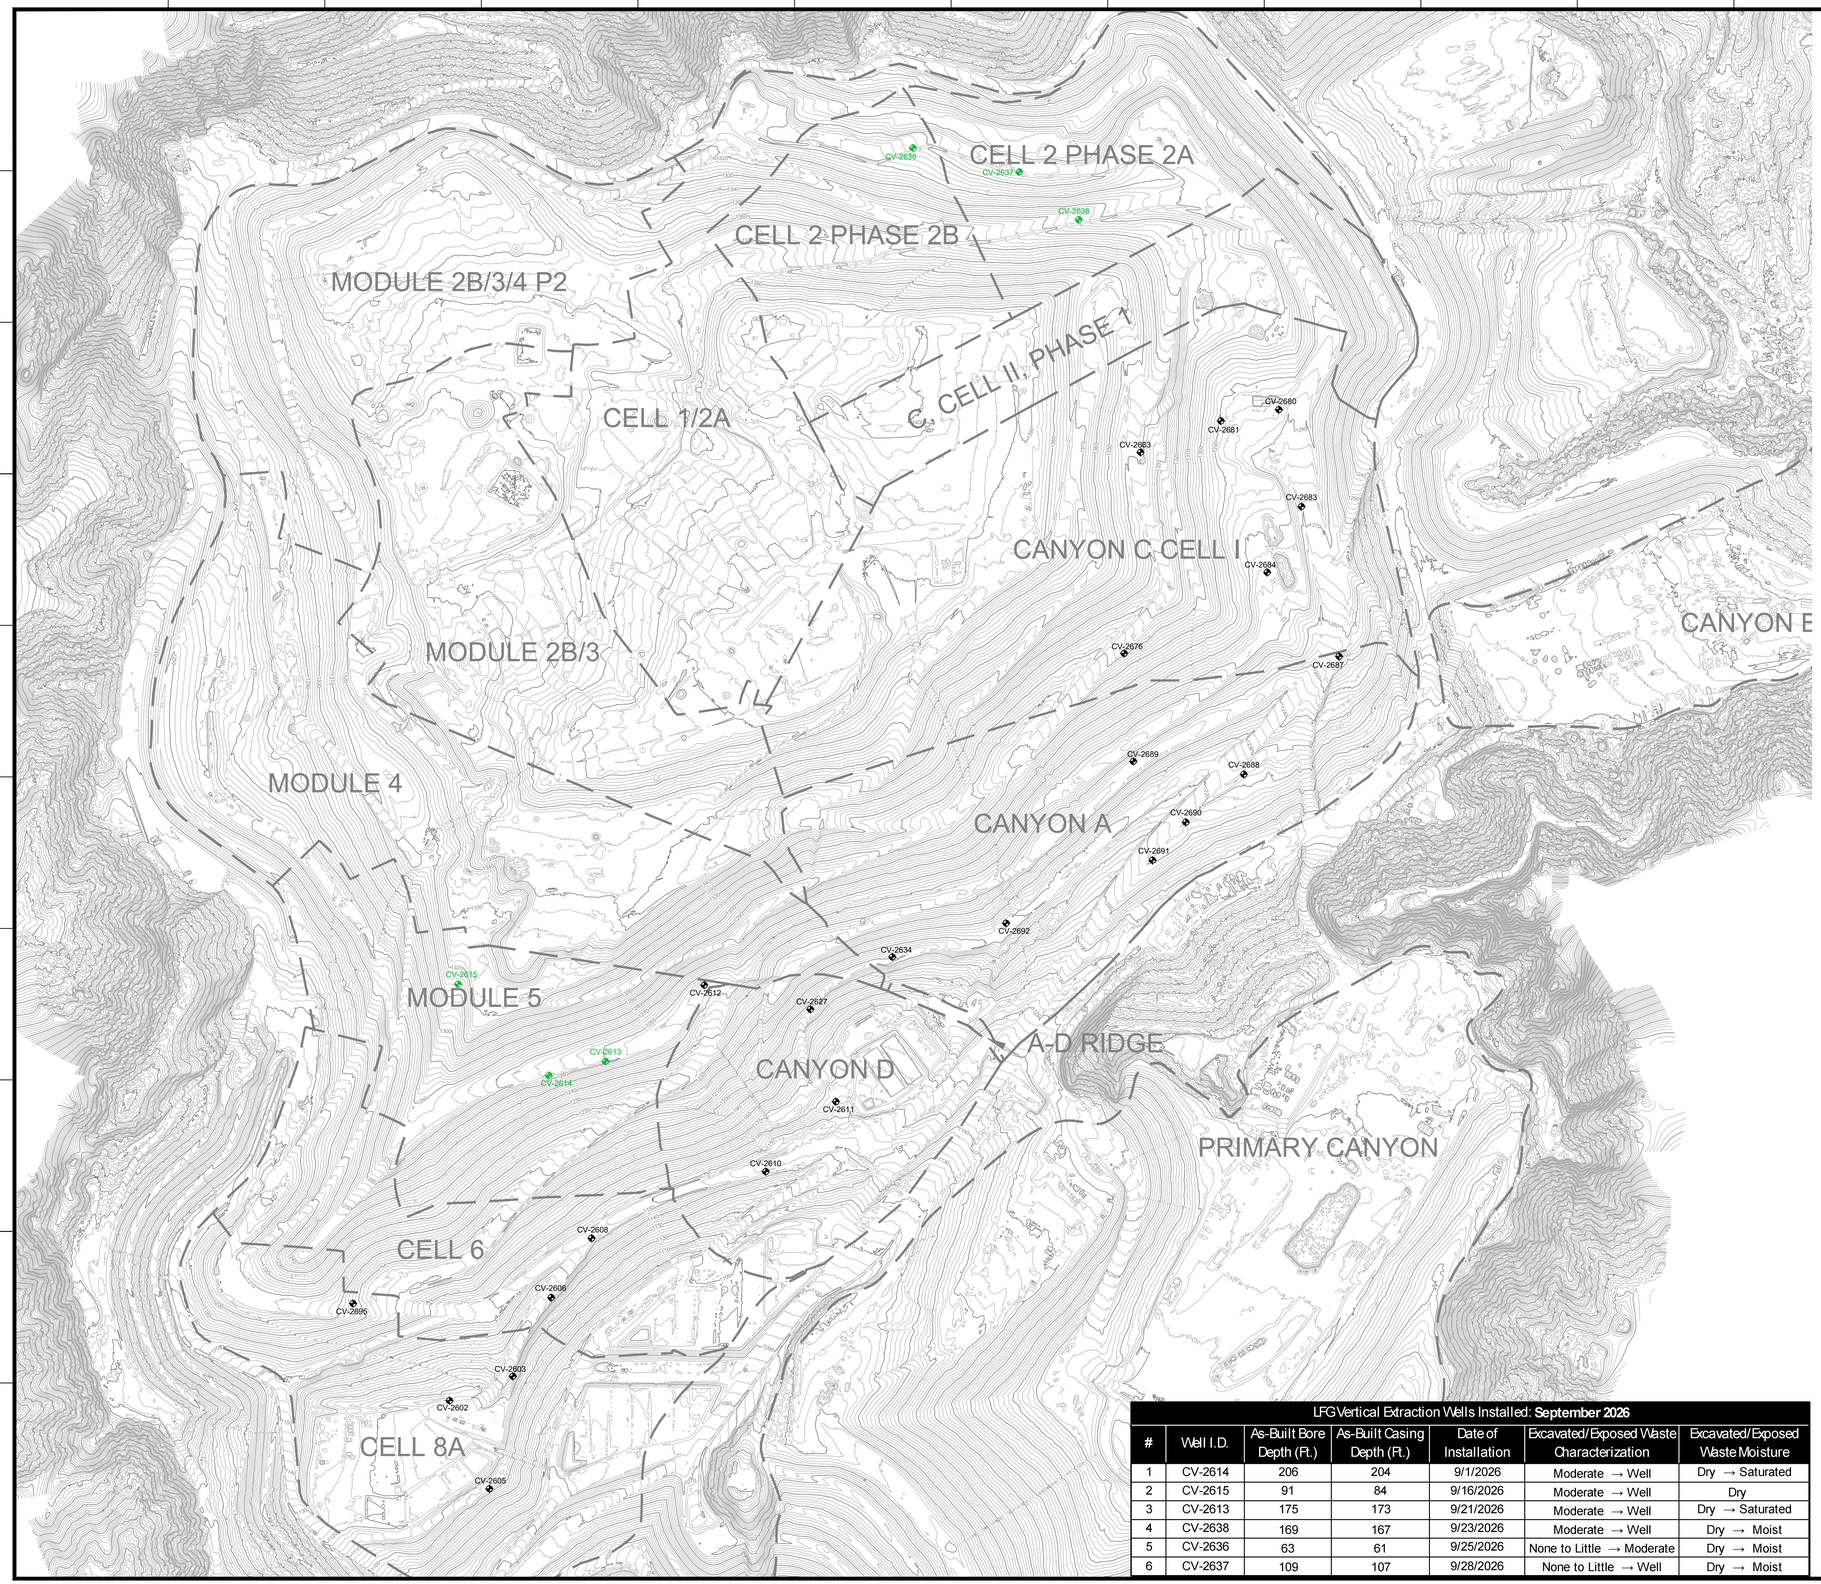

N

GRAPHIC SCALE

200 100 0 200 400 600

SCALE: 1"=200'

LEGEND

1150	EXISTING TOPOGRAPHIC CONTOUR
	EXISTING CELL LIMITS (APPROXIMATE)
CV-XX	PROPOSED LFG EXTRACTION WELL - INSTALLED 2026
CV-XX	PROPOSED LFG EXTRACTION WELL - INSTALLED SEPTEMBER 2026

LFG Vertical Extraction Wells Installed: **September 2026**

#	Well I.D.	As-Built Bore Depth (Ft.)	As-Built Casing Depth (Ft.)	Date of Installation	Excavated/Exposed Waste Characterization	Excavated/Exposed Waste Moisture
1	CV-2614	206	204	9/1/2026	Moderate → Well	Dry → Saturated
2	CV-2615	91	84	9/16/2026	Moderate → Well	Dry
3	CV-2613	175	173	9/21/2026	Moderate → Well	Dry → Saturated
4	CV-2638	169	167	9/23/2026	Moderate → Well	Dry → Moist
5	CV-2636	63	61	9/25/2026	None to Little → Moderate	Dry → Moist
6	CV-2637	109	107	9/28/2026	None to Little → Well	Dry → Moist

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER AERIAL PHOTOGRAPHY DATED SEPTEMBER 30, 2026.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: LFG EXTRACTION WELL INSTALLATION WASTE CHARACTERIZATION MAP- SEPTEMBER 2026

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO: 01204123.45 | DWN. BY: ISR | CHK. BY: SRM | ACAD FILE: - | APP. BY: SRM | DSN. BY: -

DATE: 10/05/2026

SCALE: AS SHOWN

SHEET: 1

DRILLING LOG

Record Prepared By:	Tyler Davidson	**Well ID:**	**CV-2613**
Site:	Chiquita Canyon Landfill	**Driller Name:**	Continuum Environmental Services
Date:	9/18/2026 & 9/21/2026	**Bench (Y/N)**	Y
Northing:	1979716.823	**Weather:**	SUNNY
Easting:	6366275.479	**Start Drill Time:**	8:20:00 AM (9/18) / 07:42:00 AM (9/21)
Surface Elevation:	1262	**End Drill Time:**	1:00:00 PM (9/18) / 3:47:00 PM (9/21)
Liner Elevation:	1030		
Well Pipe Size: (In.)	8	**Well Seal Type:**	Bentonite Plug and Foam Plug
Well Material:	CPVC		
Solid Pipe: (Ft.)	30 (reference from top of ground surface)	**Latitude:**	34.4306038° N
Perforated Pipe: (Ft.)	143	**Longitude:**	118.6479771° W
Boring depth: (Ft.)	175		

Starting Depth	Ending Depth	Composition	Temp (F)	Degree of Decomposition	Amount of Moisture	Comments
0	**10**	PLASTIC/WOOD/RUBBER PIECES/MSW	98	moderate	dry	
10	**20**	PLASTIC/WOOD/RUBBER PIECES/MSW	104	moderate	dry	
20	**30**	PLASTIC/WOOD/RUBBER PIECES/MSW	136	moderate	dry	
30	**40**	PLASTIC/WOOD/RUBBER PIECES/MSW	120	moderate	dry	
40	**50**	PLASTIC/WOOD/RUBBER PIECES/MSW	124	moderate	dry	
50	**60**	PLASTIC/WOOD/RUBBER PIECES/MSW	128	moderate	dry	
60	**70**	PLASTIC/WOOD/RUBBER PIECES/MSW	116	moderate	dry	
70	**80**	PLASTIC/WOOD/RUBBER PIECES/MSW	120	moderate	dry	
80	**90**	PLASTIC/WOOD/RUBBER PIECES/MSW	124	moderate	dry	
90	**98**	PLASTIC/WOOD/RUBBER PIECES/MSW	130	moderate	dry	
100	**110**	PLASTIC/WOOD/RUBBER PIECES/MSW	124	moderate	dry	
110	**120**	PLASTIC/WOOD/RUBBER PIECES/MSW	122	moderate	moist	
120	**130**	PLASTIC/WOOD/RUBBER PIECES/MSW	118	moderate	moist	
130	**140**	PLASTIC/WOOD/RUBBER PIECES/MSW	128	well	moist	
140	**150**	PLASTIC/WOOD/RUBBER PIECES/MSW	136	well	moist	
150	**160**	PLASTIC/WOOD/RUBBER PIECES/MSW	146	well	moist	
160	**170**	PLASTIC/WOOD/RUBBER PIECES/MSW	165	well	moist	
170	**175**	SLUDGE	100	well	free liquids	Depth to Water: 170-feet

Comments:
(9/18) Drilling ceased at 116' due to drill rig repairs. Per WC's discretion, the borehole was sealed with a steel plate, EVOH liner, and soil for the weekend
(9/21) Drilling was completed at 175 feet bgs due to reaching the maximum cable depth of the drilling rig.
During gravel backfilling, bridging occurred within the borehole, resulting in the top of gravel being near surface grade. The borehole was subsequently excavated to 10 feet bgs, and excess gravel was removed. Borehole completion was then performed as follows: geocomposite ring installed at 10 feet bgs, followed by 1 foot of soil, 1 foot of bentonite, 1 foot of soil, 1 foot of bentonite, 1 foot of soil, 2 feet of foam plug, and soil to grade.

ETOOLS ID	Alias
CHCV2613	CV-2613

Site Name: **Chiquita Canyon Landfill**


Date Installed: **9/21/2026**

City: **Castaic** State: **CA**

Installation Contractor:
Continuum Environmental Services

Pipe Material: CPVC

General Comments:
Coordinates :
Northing: 1979716.823
Easting: 6366275.479
Ground Elevation (MSL): 1262
Notes: Please refer to the drilling log.

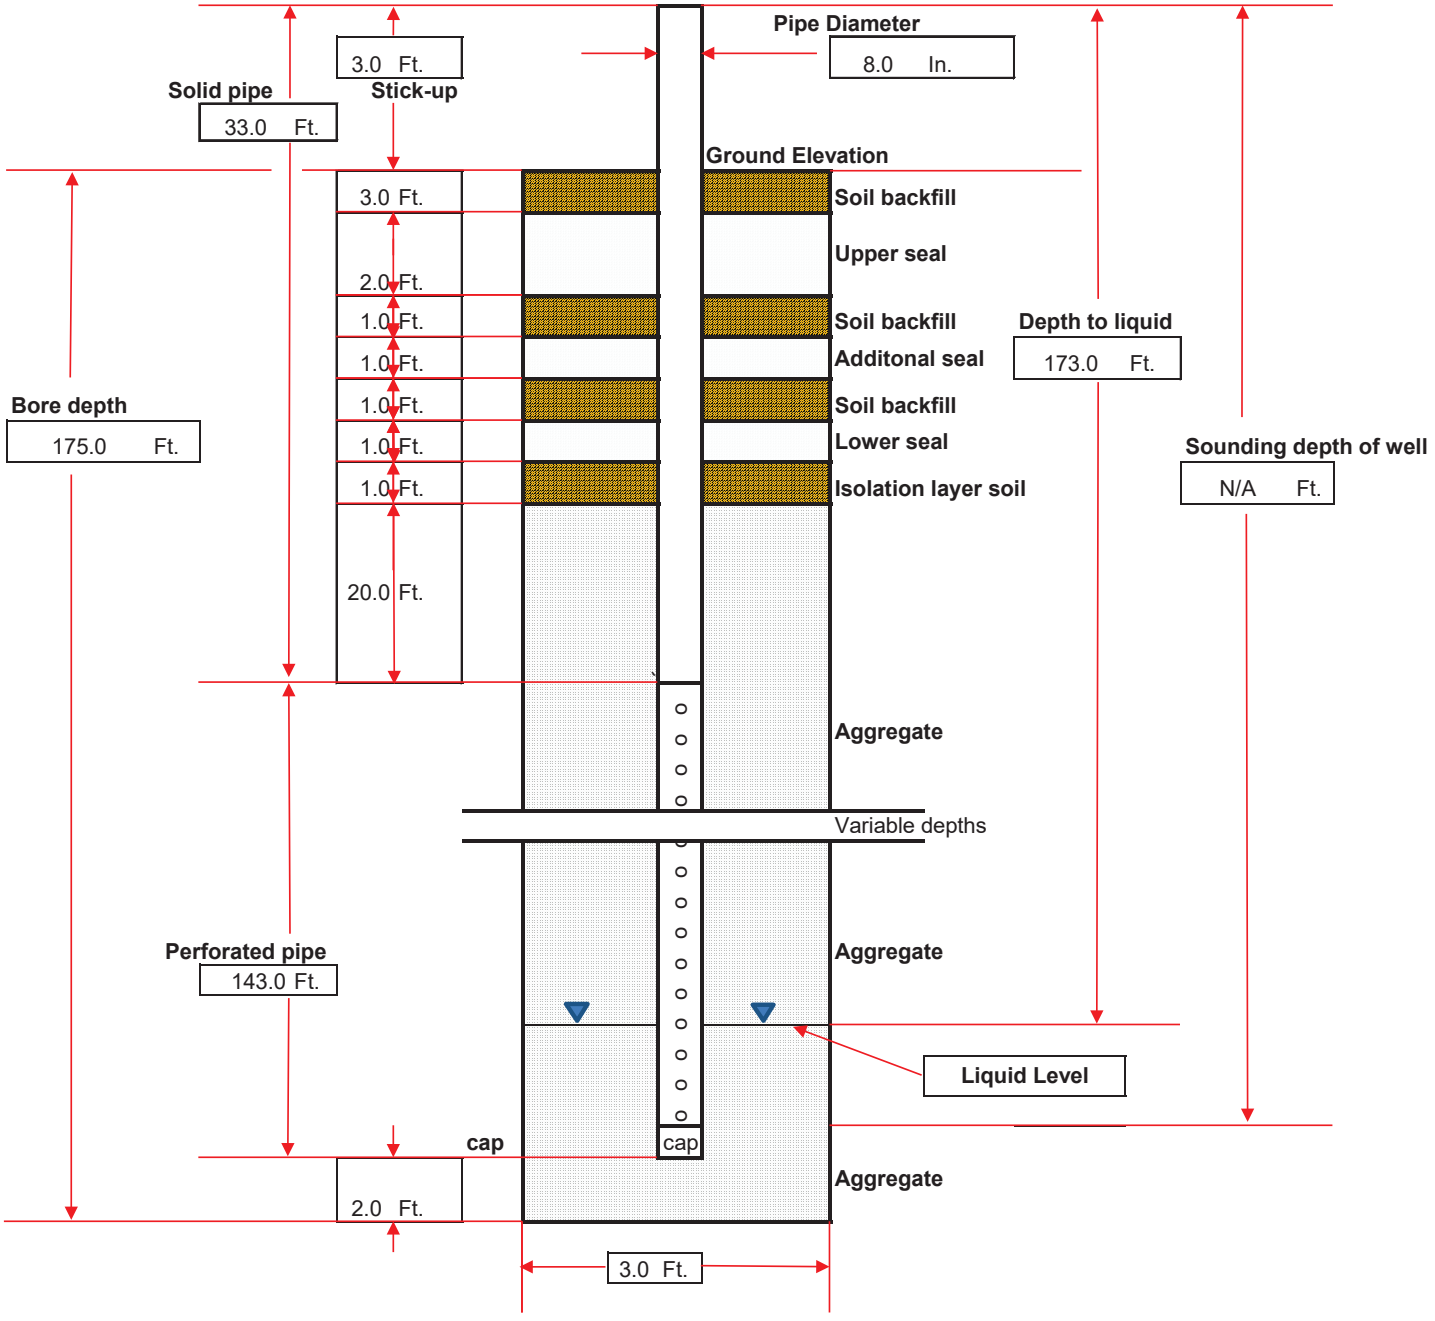

DRILLING LOG

Record Prepared By:	Tyler Davidson	**Well ID:**	**CV-2614**
Site:	Chiquita Canyon Landfill	**Driller Name:**	Continuum Environmental Services
Date:	9/1/2026	**Bench (Y/N)**	Y
Northing:	1979683.724	**Weather:**	SUNNY
Easting:	6366135.189	**Start Drill Time:**	6:40:00 AM
Surface Elevation:	1266	**End Drill Time:**	1:54:00 PM
Liner Elevation:	1030		
Well Pipe Size: (In.)	8	**Well Seal Type:**	Bentonite Plug & Foam Plug
Well Material:	CPVC		
Solid Pipe: (Ft.)	30 (reference from top of ground surface)	**Latitude:**	34.4305104° N
Perforated Pipe: (Ft.)	174	**Longitude:**	118.6484417° W
Boring depth: (Ft.)	206		

Starting Depth	Ending Depth	Composition	Temp (F)	Degree of Decomposition	Amount of Moisture	Comments
0	**10**	PLASTIC/WOOD/MSW	95	moderate	dry	
10	**20**	PLASTIC/WOOD/RUBBER PIECES/MSW	106	moderate	dry	
20	**30**	PLASTIC/WOOD/MSW	108	moderate	dry	
30	**40**	PLASTIC/WOOD/FABRIC/MSW	112	moderate	dry	
40	**50**	PLASTIC/WOOD/FABRIC/HOSE/MSW	116	moderate	dry	
50	**60**	PLASTIC/WOOD/FABRIC/MSW	122	moderate	dry	
60	**70**	PLASTIC/WOOD/FABRIC/MSW	110	moderate	dry	
70	**80**	PLASTIC/WOOD/FABRIC/MSW	125	moderate	dry	
80	**90**	PLASTIC/WOOD/FABRIC/MSW	116	moderate	dry	
90	**100**	PLASTIC/WOOD/FABRIC/MSW	122	moderate	dry	
100	**110**	PLASTIC/WOOD/FABRIC/MSW	126	moderate	moist	
110	**120**	PLASTIC/WOOD/FABRIC/MSW	124	moderate	moist	
120	**130**	PLASTIC/WOOD/FABRIC/MSW	132	moderate	moist	
130	**140**	PLASTIC/WOOD/FABRIC/MSW	124	moderate	moist	
140	**150**	PLASTIC/WOOD/FABRIC/MSW	150	well	dry	
150	**160**	PLASTIC/WOOD/FABRIC/MSW	144	well	dry	
160	**170**	PLASTIC/WOOD/FABRIC/MSW	138	well	dry	
170	**180**	PLASTIC/WOOD/FABRIC/MSW	140	well	dry	
180	**190**	PLASTIC/WOOD/FABRIC/MSW	132	well	moist	
190	**200**	PLASTIC/WOOD/FABRIC/MSW	128	well	moist	
200	**206**	PLASTIC/SLUDGE/MSW	124	well	free liquids	Depth to Water

Comments:

ETOOLS ID	Alias
CHCV2614	CV-2614

Site Name: **Chiquita Canyon Landfill**


Date Installed: **9/1/2026**

City: **Castaic** State: **CA**

Installation Contractor:
Continuum Environmental Services

Pipe Material: CPVC

General Comments:
Coordinates :
Northing: 1979683.724
Easting: 6366135.189
Ground Elevation (MSL): 1266
Notes:

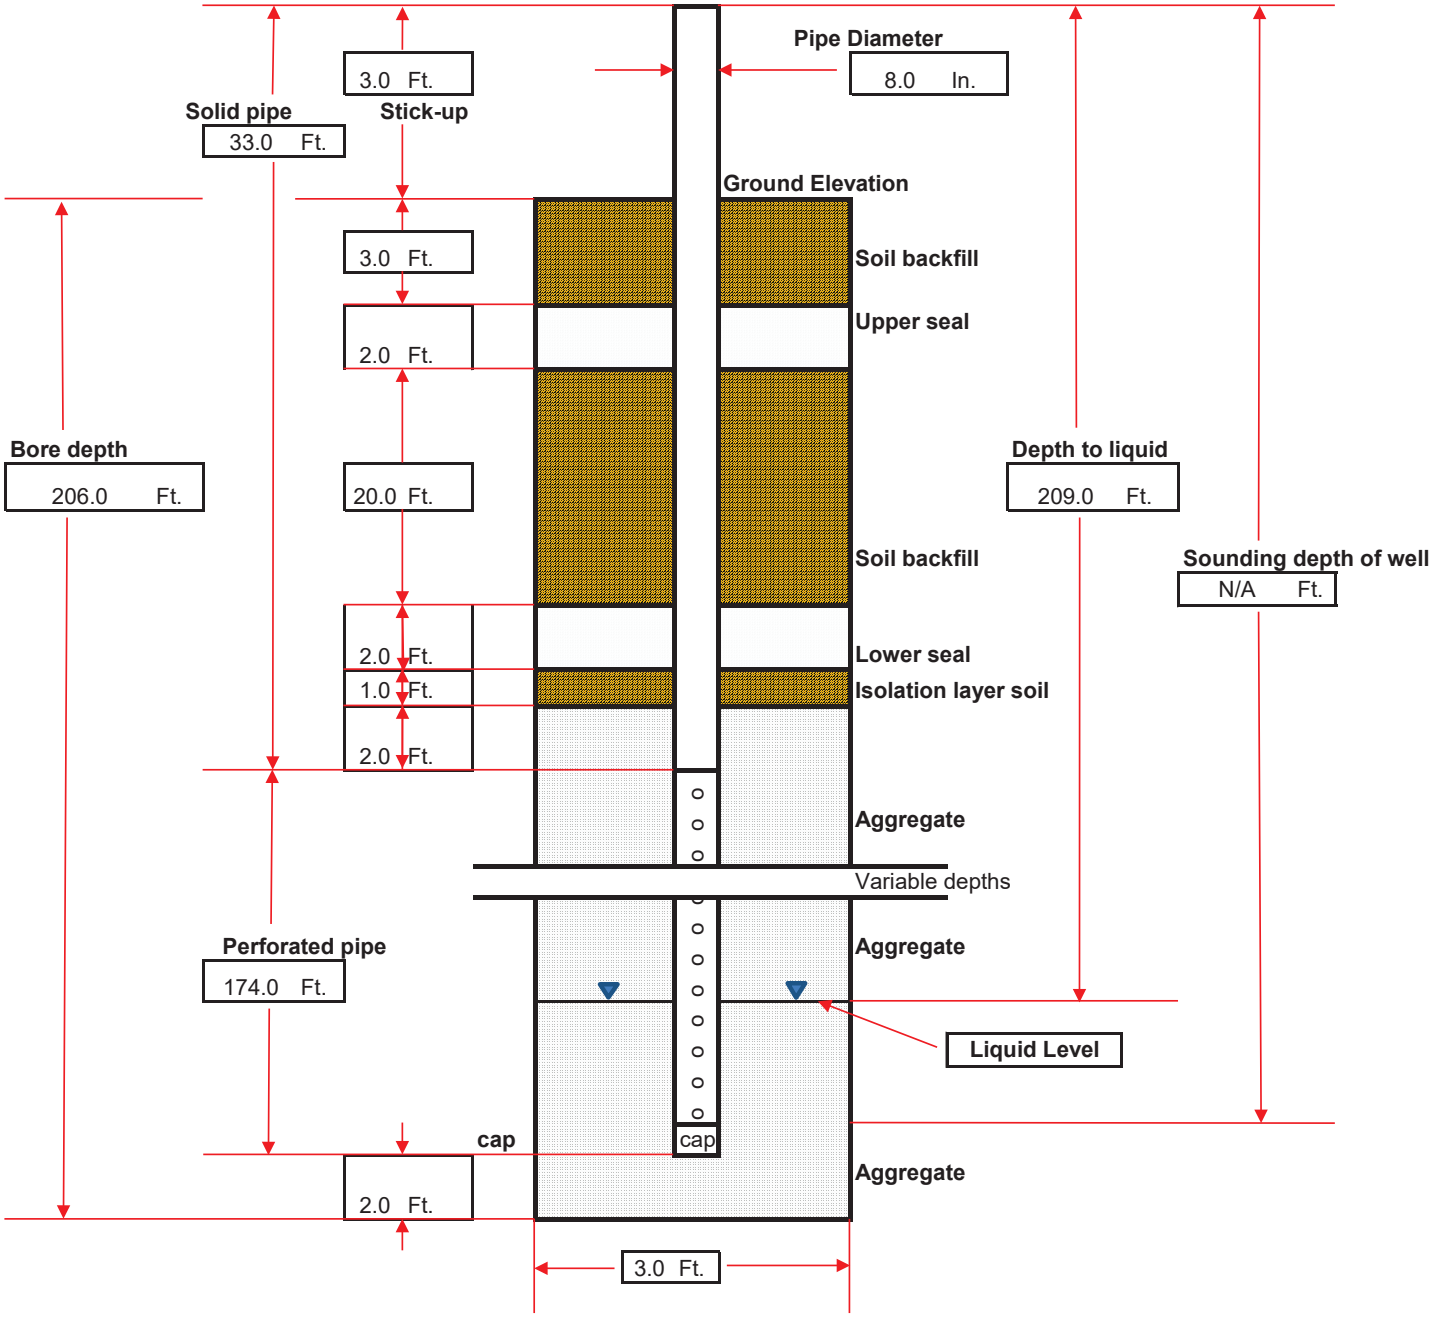

DRILLING LOG

Record Prepared By:	Tyler Davidson	**Well ID:**	**CV-2615**
Site:	Chiquita Canyon Landfill	**Driller Name:**	Continuum Environmental Services
Date:	9/16/2026	**Bench (Y/N)**	Y
Northing:	1979942.001	**Weather:**	SUNNY
Easting:	6365896.263	**Start Drill Time:**	6:43:00 AM
Surface Elevation:	1318	**End Drill Time:**	1:00:00 PM
Liner Elevation:	1056		
Well Pipe Size: (In.)	8	**Well Seal Type:**	Bentonite Plug & Foam Plug
Well Material:	CPVC		
Solid Pipe: (Ft.)	30 (reference from top of ground surface)	**Latitude:**	34.4312158° N
Perforated Pipe: (Ft.)	54	**Longitude:**	118.6492395° W
Boring depth: (Ft.)	91		

Starting Depth	Ending Depth	Composition	Temp (F)	Degree of Decomposition	Amount of Moisture	Comments
0	**10**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	80	moderate	dry	
10	**20**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	104	moderate	dry	
20	**30**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	106	moderate	dry	
30	**40**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	110	moderate	dry	
40	**50**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	112	moderate	dry	
50	**60**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	112	moderate	dry	
60	**70**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	116	moderate	dry	
70	**80**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	128	well	dry	
80	**90**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	120	well	dry	
90	**91**	PLASTIC/WOOD/FABRIC/METAL/RUBBER	120	well	dry	

Comments:
Drilling ceased due to an obstruction encountered at 91’ bgs. The well casing was set per WC’s discretion. Before the well casing installation, a cave-in of 5’ occurred to a depth of 86' bgs. As a result, the well casing was adjusted accordingly.

ETOOLS ID: CHCV2615

Alias: CV-2615

Site Name: **Chiquita Canyon Landfill**

Date Installed: **9/16/2026**

City: **Castaic**


State: **CA**

Installation Contractor:
Continuum Environmental Services

Pipe Material: CPVC

General Comments:

Coordinates :
Northing: 1979942.001
Easting: 6365896.263
Ground Elevation (MSL): 1318
Notes: Drilling ceased due to an obstruction encountered at 91' bgs. The well casing was set per WC's discretion. Before the well casing installation, a cave-in of 5' occurred to a depth of 86' bgs. As a result, the well casing was adjusted accordingly.

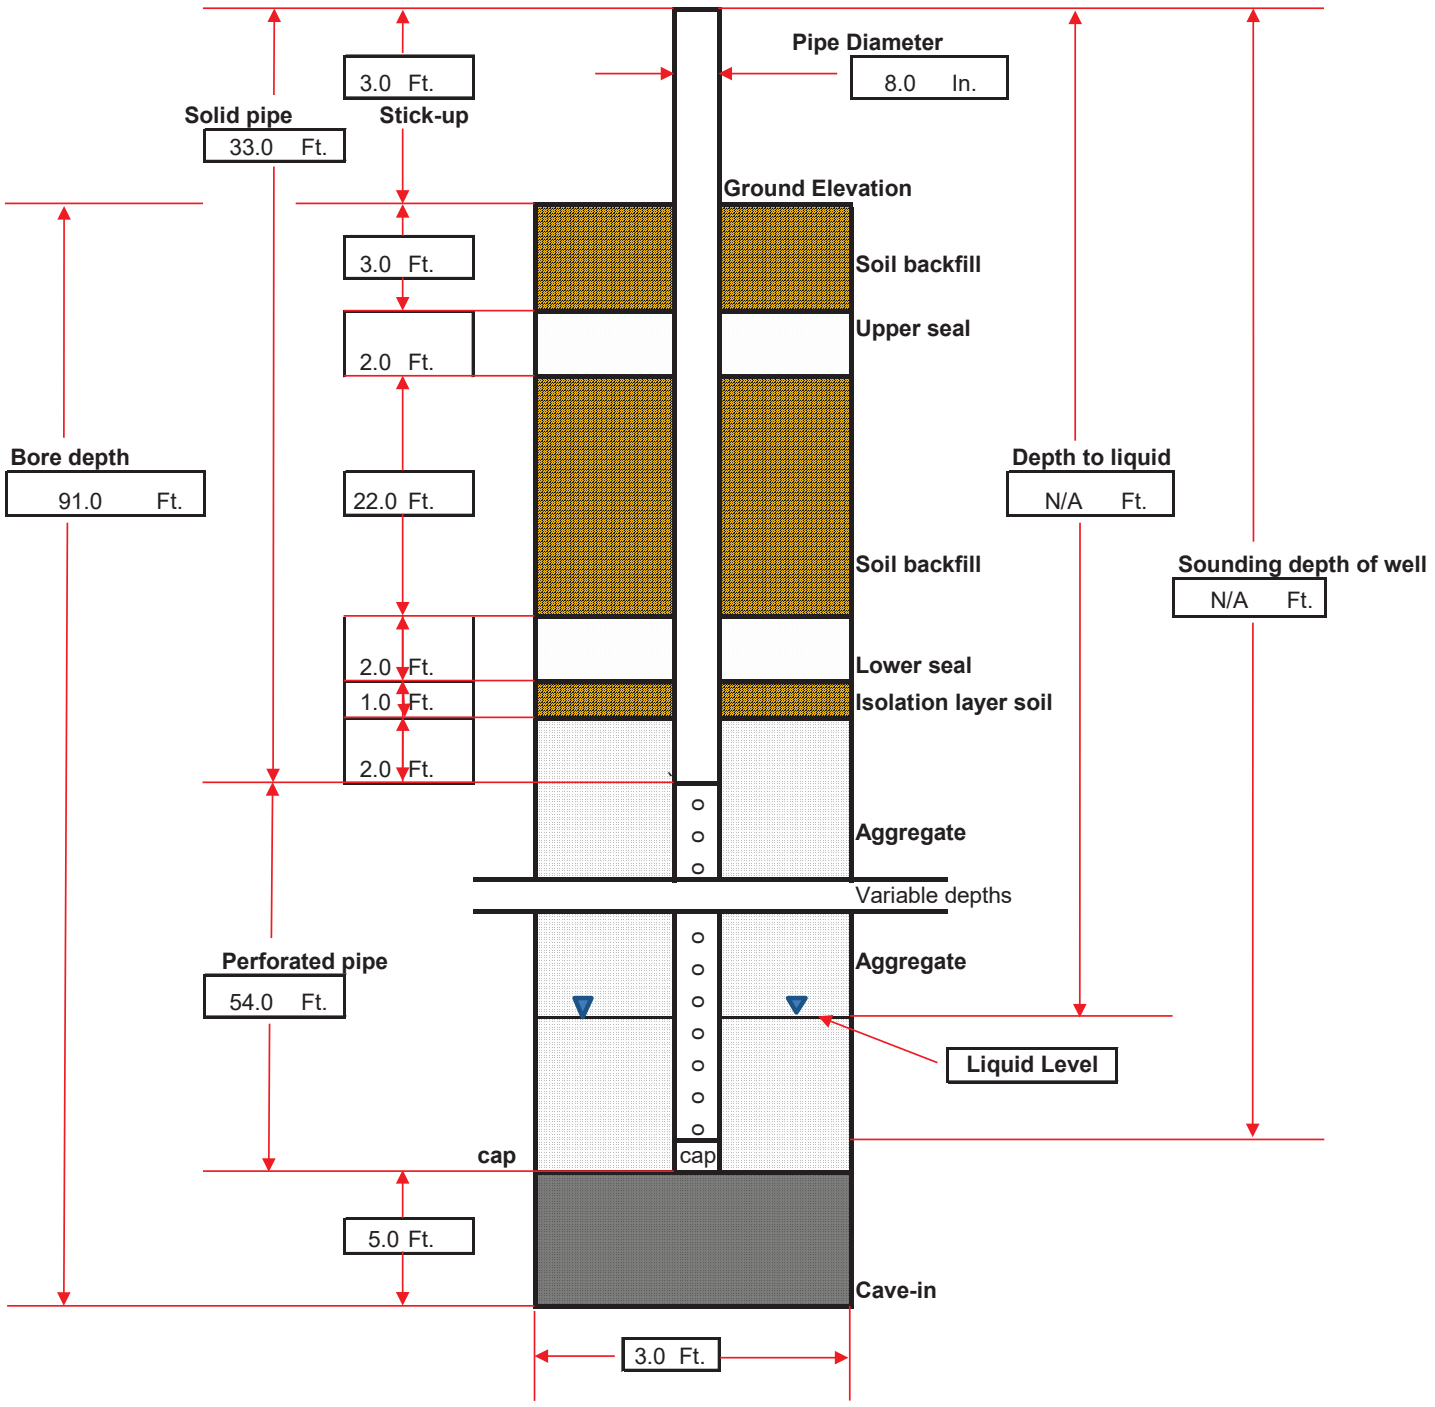

DRILLING LOG

Record Prepared By:	**Tyler Davidson**	**Well ID:**	**CV-2636**
Site:	Chiquita Canyon Landfill	**Driller Name:**	Continuum Environmental Services
Date:	9/25/2026	**Bench (Y/N)**	Y
Northing:	1982131.732	**Weather:**	SUNNY
Easting:	6367096.759	**Start Drill Time:**	10:56:00 AM
Surface Elevation:	1302	**End Drill Time:**	1:00:00 PM
Liner Elevation:	1175		
Well Pipe Size: (In.)	8	**Well Seal Type:**	Bentonite Plug & Foam Plug
Well Material:	CPVC		
Solid Pipe: (Ft.)	30 (reference from **top of ground surface**)	**Latitude:**	34.4372540° N
Perforated Pipe: (Ft.)	31	**Longitude:**	118.6453050° W
Boring depth: (Ft.)	63		

Starting Depth	Ending Depth	Composition	Temp (F)	Degree of Decomposition	Amount of Moisture	Comments
0	**10**	SOIL/PLASTIC/WOOD/FABRIC/METAL	82	moderate	dry	
10	**20**	PLASTIC/WOOD/FABRIC/MSW	92	moderate	dry	
20	**30**	PLASTIC/WOOD/FABRIC/MSW	102	moderate	moist	
30	**40**	PLASTIC/WOOD/FABRIC/MSW	120	moderate	moist	
40	**50**	PLASTIC/WOOD/FABRIC/MSW	122	moderate	moist	
50	**60**	PLASTIC/WOOD/FABRIC/MSW	124	moderate	moist	
60	**63**	PLASTIC/WOOD/FABRIC/MSW	124	moderate	moist	

Comments:
Stopped drilling at 63' bgs due to an obstruction.

ETOOLS ID CHCV2636

Alias CV-2636

Site Name: **Chiquita Canyon Landfill**

Date Installed: **9/25/2026**


City: **Castaic** State: **CA**

Installation Contractor: **Continuum Environmental Services**

Pipe Material: CPVC

General Comments:

Coordinates :
Northing: 1982131.732
Easting:6367096.759
Ground Elevation (MSL): 1302
Notes:

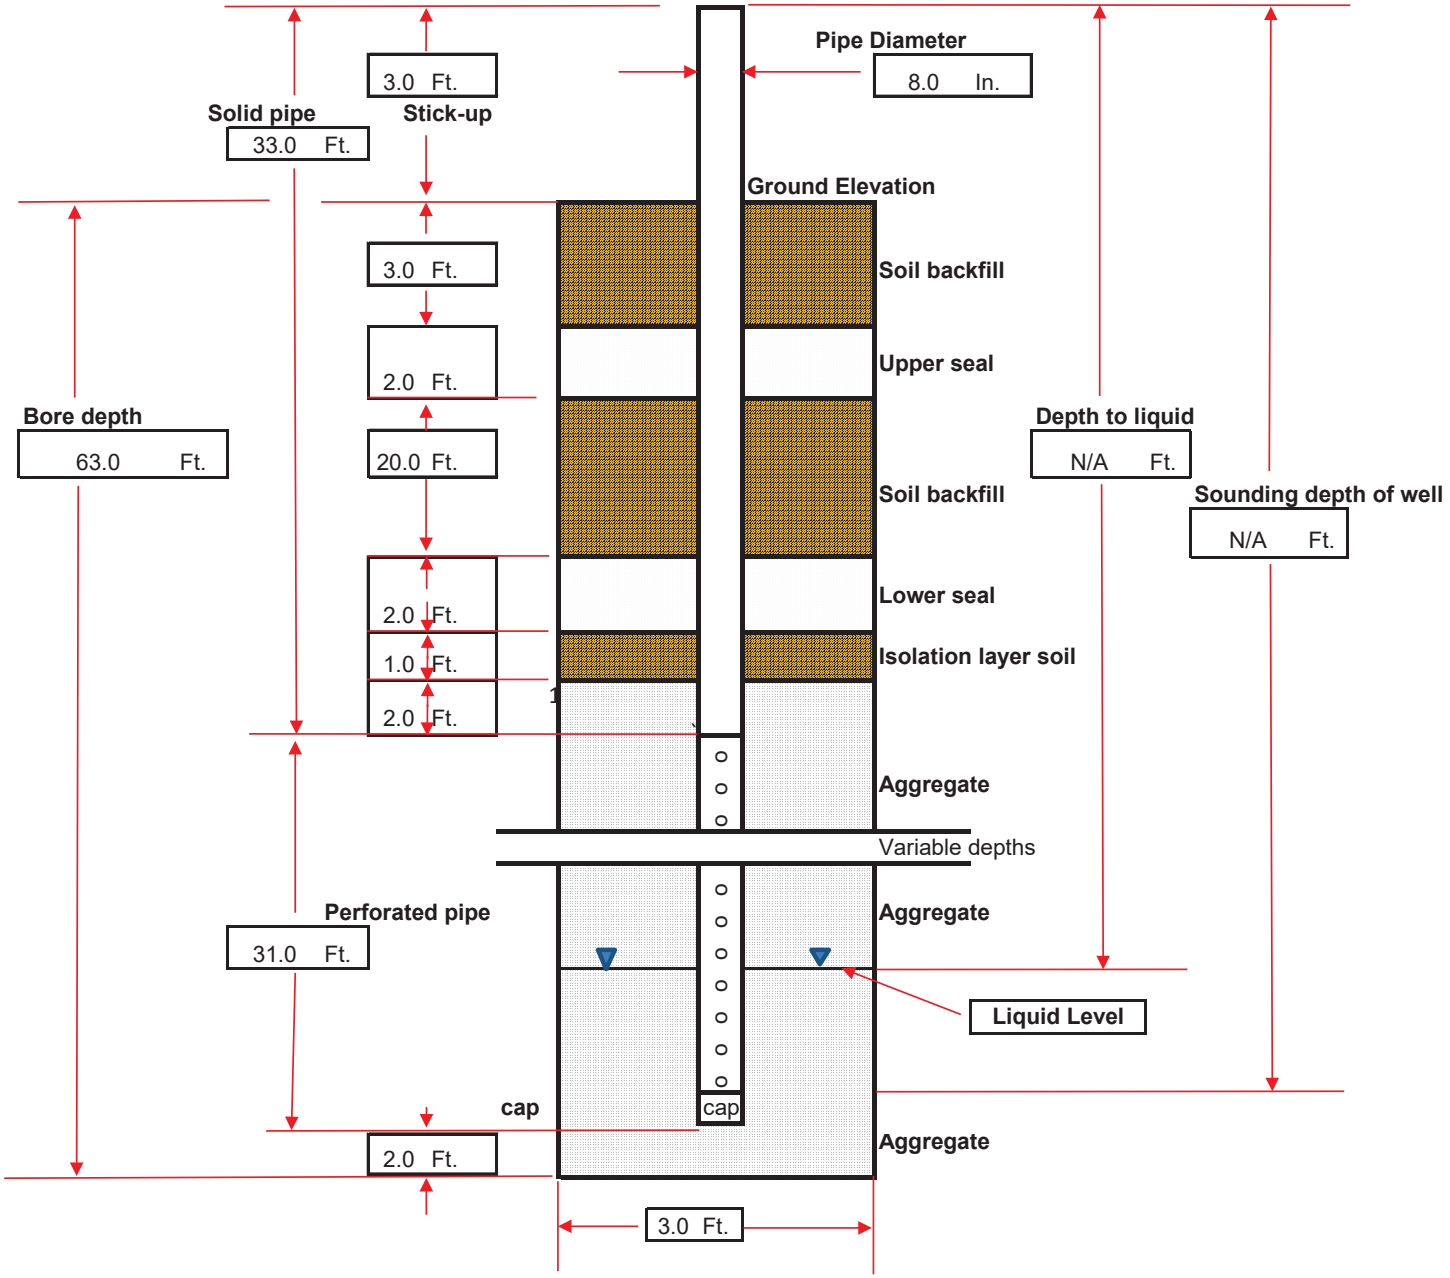

DRILLING LOG

Record Prepared By:	**Tyler Davidson**	**Well ID:**	**CV-2637**
Site:	Chiquita Canyon Landfill	**Driller Name:**	Continuum Environmental Services
Date:	9/28/2026	**Bench (Y/N)**	Y
Northing:	1982068.263	**Weather:**	SUNNY
Easting:	6367377.445	**Start Drill Time:**	7:44:00 AM
Surface Elevation:	1293	**End Drill Time:**	11:51:00 AM
Liner Elevation:	1154		
Well Pipe Size: (In.)	8	**Well Seal Type:**	Bentonite Plug & Foam Plug
Well Material:	CPVC		
Solid Pipe: (Ft.)	33 (reference from **top of ground surface**)	**Latitude:**	34.4370845° N
Perforated Pipe: (Ft.)	77	**Longitude:**	118.6443728° W
Boring depth: (Ft.)	109		

Starting Depth	Ending Depth	Composition	Temp (F)	Degree of Decomposition	Amount of Moisture	Comments
0	**10**	SOIL/PLASTIC/WOOD/FABRIC/METAL	86	moderate	dry	
10	**20**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	108	moderate	moist	
20	**30**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	112	well	moist	
30	**40**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	126	well	moist	
40	**50**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	130	well	dry	
50	**60**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	150	well	dry	
60	**70**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	140	well	moist	
70	**80**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	144	well	moist	
80	**90**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	140	well	moist	
90	**100**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	138	well	moist	
100	**109**	PLASTIC/WOOD/METAL/FABRIC/RUBBER/MSW	132	well	moist	

Comments:

ETOOLS ID CHCV2637

Alias CV-2637

Site Name: **Chiquita Canyon Landfill**

Date Installed: **9/28/2026**

City: **Castaic**


State: **CA**

Installation Contractor: **Continuum Environmental Services**

Pipe Material: CPVC

General Comments:

Coordinates :
Northing:1982068.263
Easting:6367377.445
Ground Elevation (MSL): 1293
Notes:

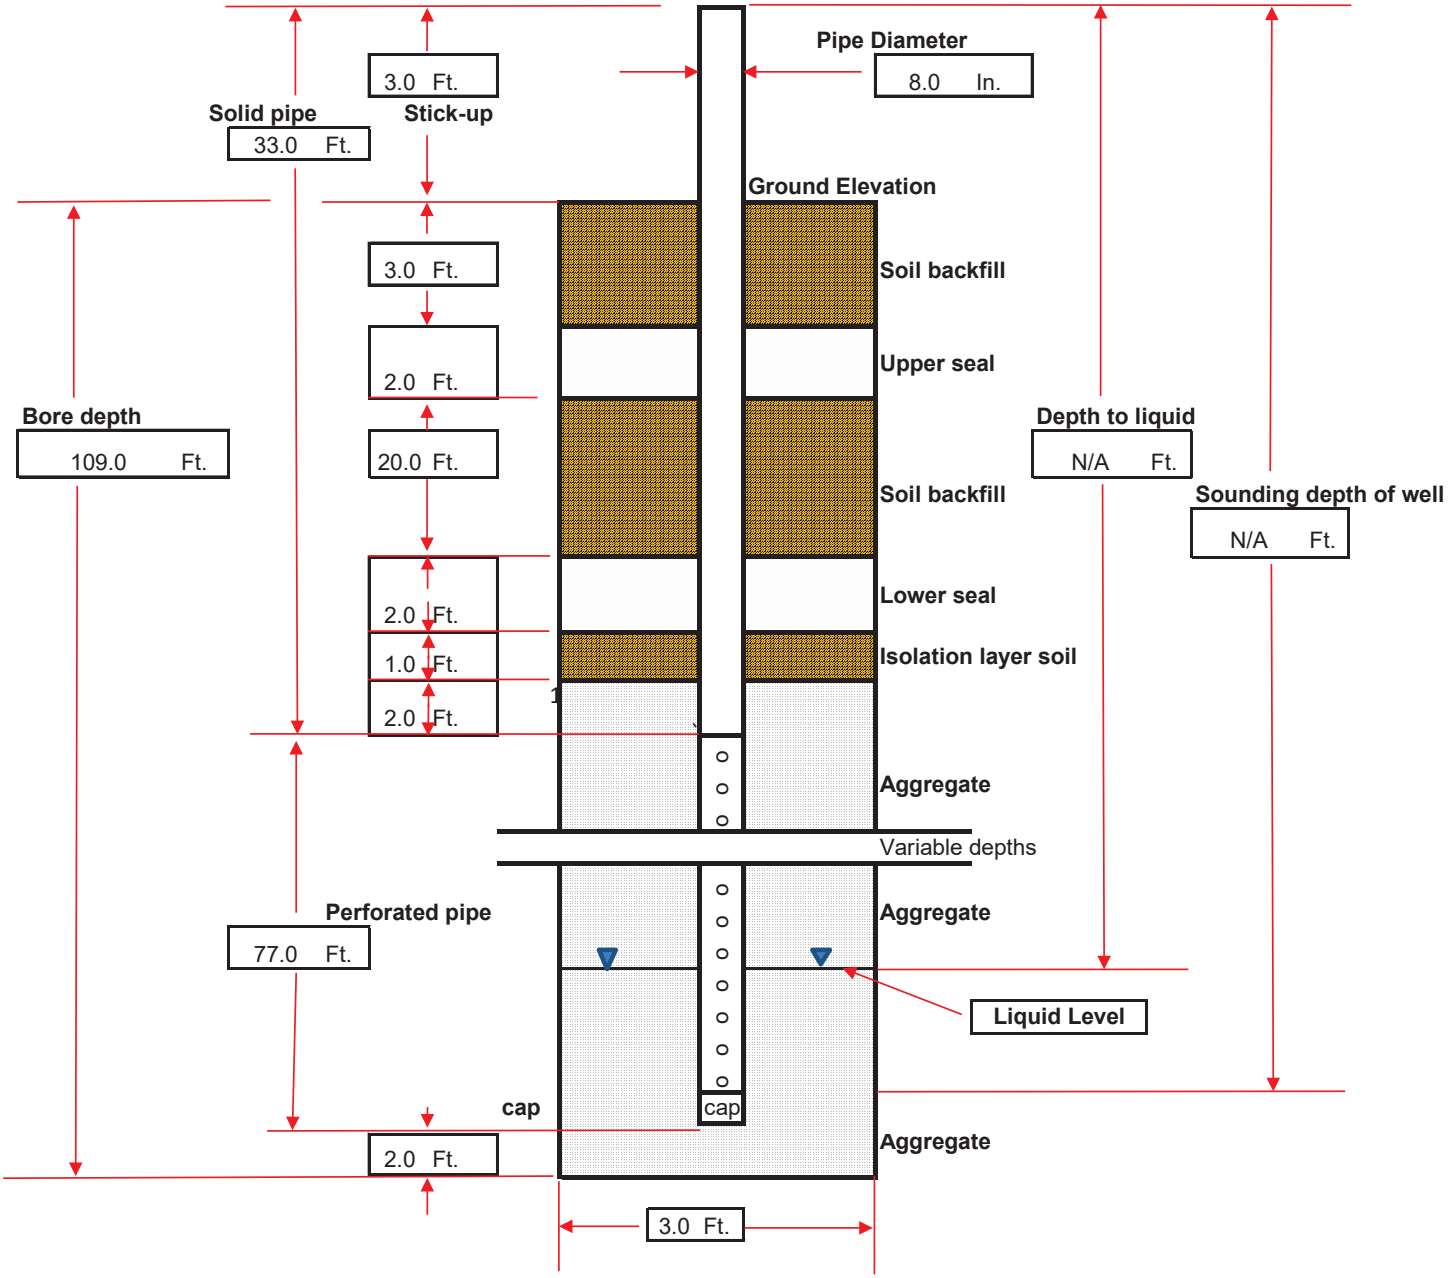

DRILLING LOG

Record Prepared By:	Tyler Davidson	**Well ID:**	**CV-2638**
Site:	Chiquita Canyon Landfill	**Driller Name:**	Continuum Environmental Services
Date:	9/23/2026	**Bench (Y/N)**	Y
Northing:	1981942.124	**Weather:**	SUNNY
Easting:	6367534.502	**Start Drill Time:**	6:39:00 AM
Surface Elevation:	1324	**End Drill Time:**	1:17:00 PM
Liner Elevation:	1125		
Well Pipe Size: (In.)	8	**Well Seal Type:**	Bentonite Plug & Foam Plug
Well Material:	CPVC		
Solid Pipe: (Ft.)	30 (reference from top of ground surface)	**Latitude:**	34.4367407° N
Perforated Pipe: (Ft.)	137	**Longitude:**	118.6438492° W
Boring depth: (Ft.)	169		

Starting Depth	Ending Depth	Composition	Temp (F)	Degree of Decomposition	Amount of Moisture	Comments
0	**10**	SOIL/PLASTIC/WOOD/FABRIC/METAL	86	moderate	dry	
10	**20**	PLASTIC/WOOD/FABRIC/MSW	96	moderate	dry	
20	**30**	PLASTIC/WOOD/FABRIC/MSW	114	moderate	moist	
30	**40**	PLASTIC/WOOD/FABRIC/MSW	128	well	moist	
40	**50**	PLASTIC/WOOD/FABRIC/MSW	132	well	moist	
50	**60**	PLASTIC/WOOD/FABRIC/MSW	142	well	moist	
60	**70**	PLASTIC/WOOD/FABRIC/MSW	154	well	moist	
70	**80**	PLASTIC/WOOD/FABRIC/MSW	154	well	moist	
80	**90**	PLASTIC/WOOD/FABRIC/MSW	160	well	moist	
90	**100**	PLASTIC/WOOD/FABRIC/MSW	155	well	moist	
100	**110**	PLASTIC/WOOD/FABRIC/MSW	158	well	moist	
110	**120**	PLASTIC/WOOD/FABRIC/MSW	154	well	moist	
120	**130**	PLASTIC/WOOD/FABRIC/MSW	152	well	moist	
130	**140**	PLASTIC/WOOD/FABRIC/MSW	154	well	moist	
140	**150**	PLASTIC/WOOD/FABRIC/MSW	150	well	moist	
150	**160**	PLASTIC/WOOD/FABRIC/MSW	144	well	moist	
160	**169**	PLASTIC/WOOD/FABRIC/MSW	136	well	moist	

Comments:
During backfilling, the borehole was overfilled by 3 additional feet of gravel. As a result, 17 feet of soil backfill was installed between the bentonite and foam plugs, instead of 20 feet. Borehole completion was then performed according to design.

ETOOLS ID	Alias
CHCV2638	CV-2638

Site Name: **Chiquita Canyon Landfill**

Date Installed: **9/23/2026**


City: **Castaic** State: **CA**


Installation Contractor:
Continuum Environmental Services

Pipe Material: CPVC

General Comments:

Coordinates :
Northing: 1981942.124
Easting: 6367534.502
Ground Elevation (MSL): 1324
Notes: During backfilling, the borehole was overfilled by 3 additional feet of gravel. As a result, 17 feet of soil backfill was installed between the bentonite and foam plugs, instead of 20 feet. Borehole completion was then performed according to design.

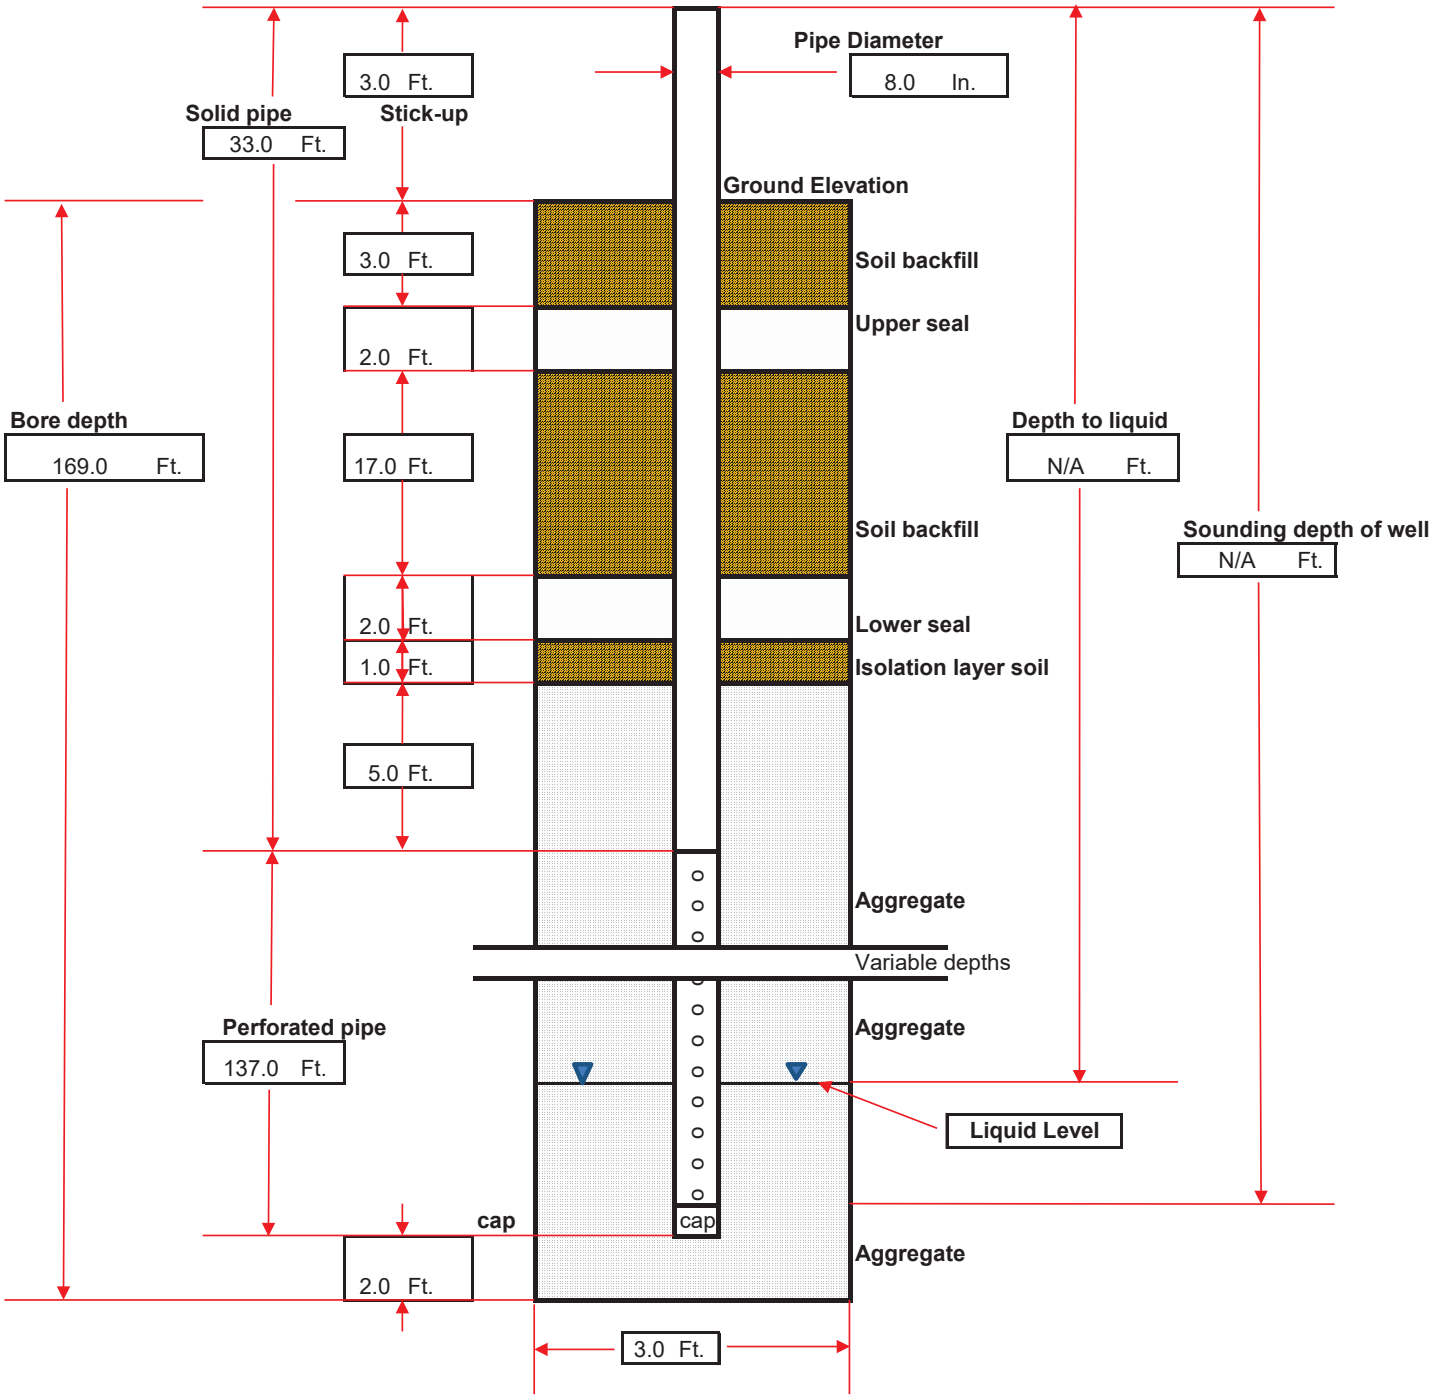

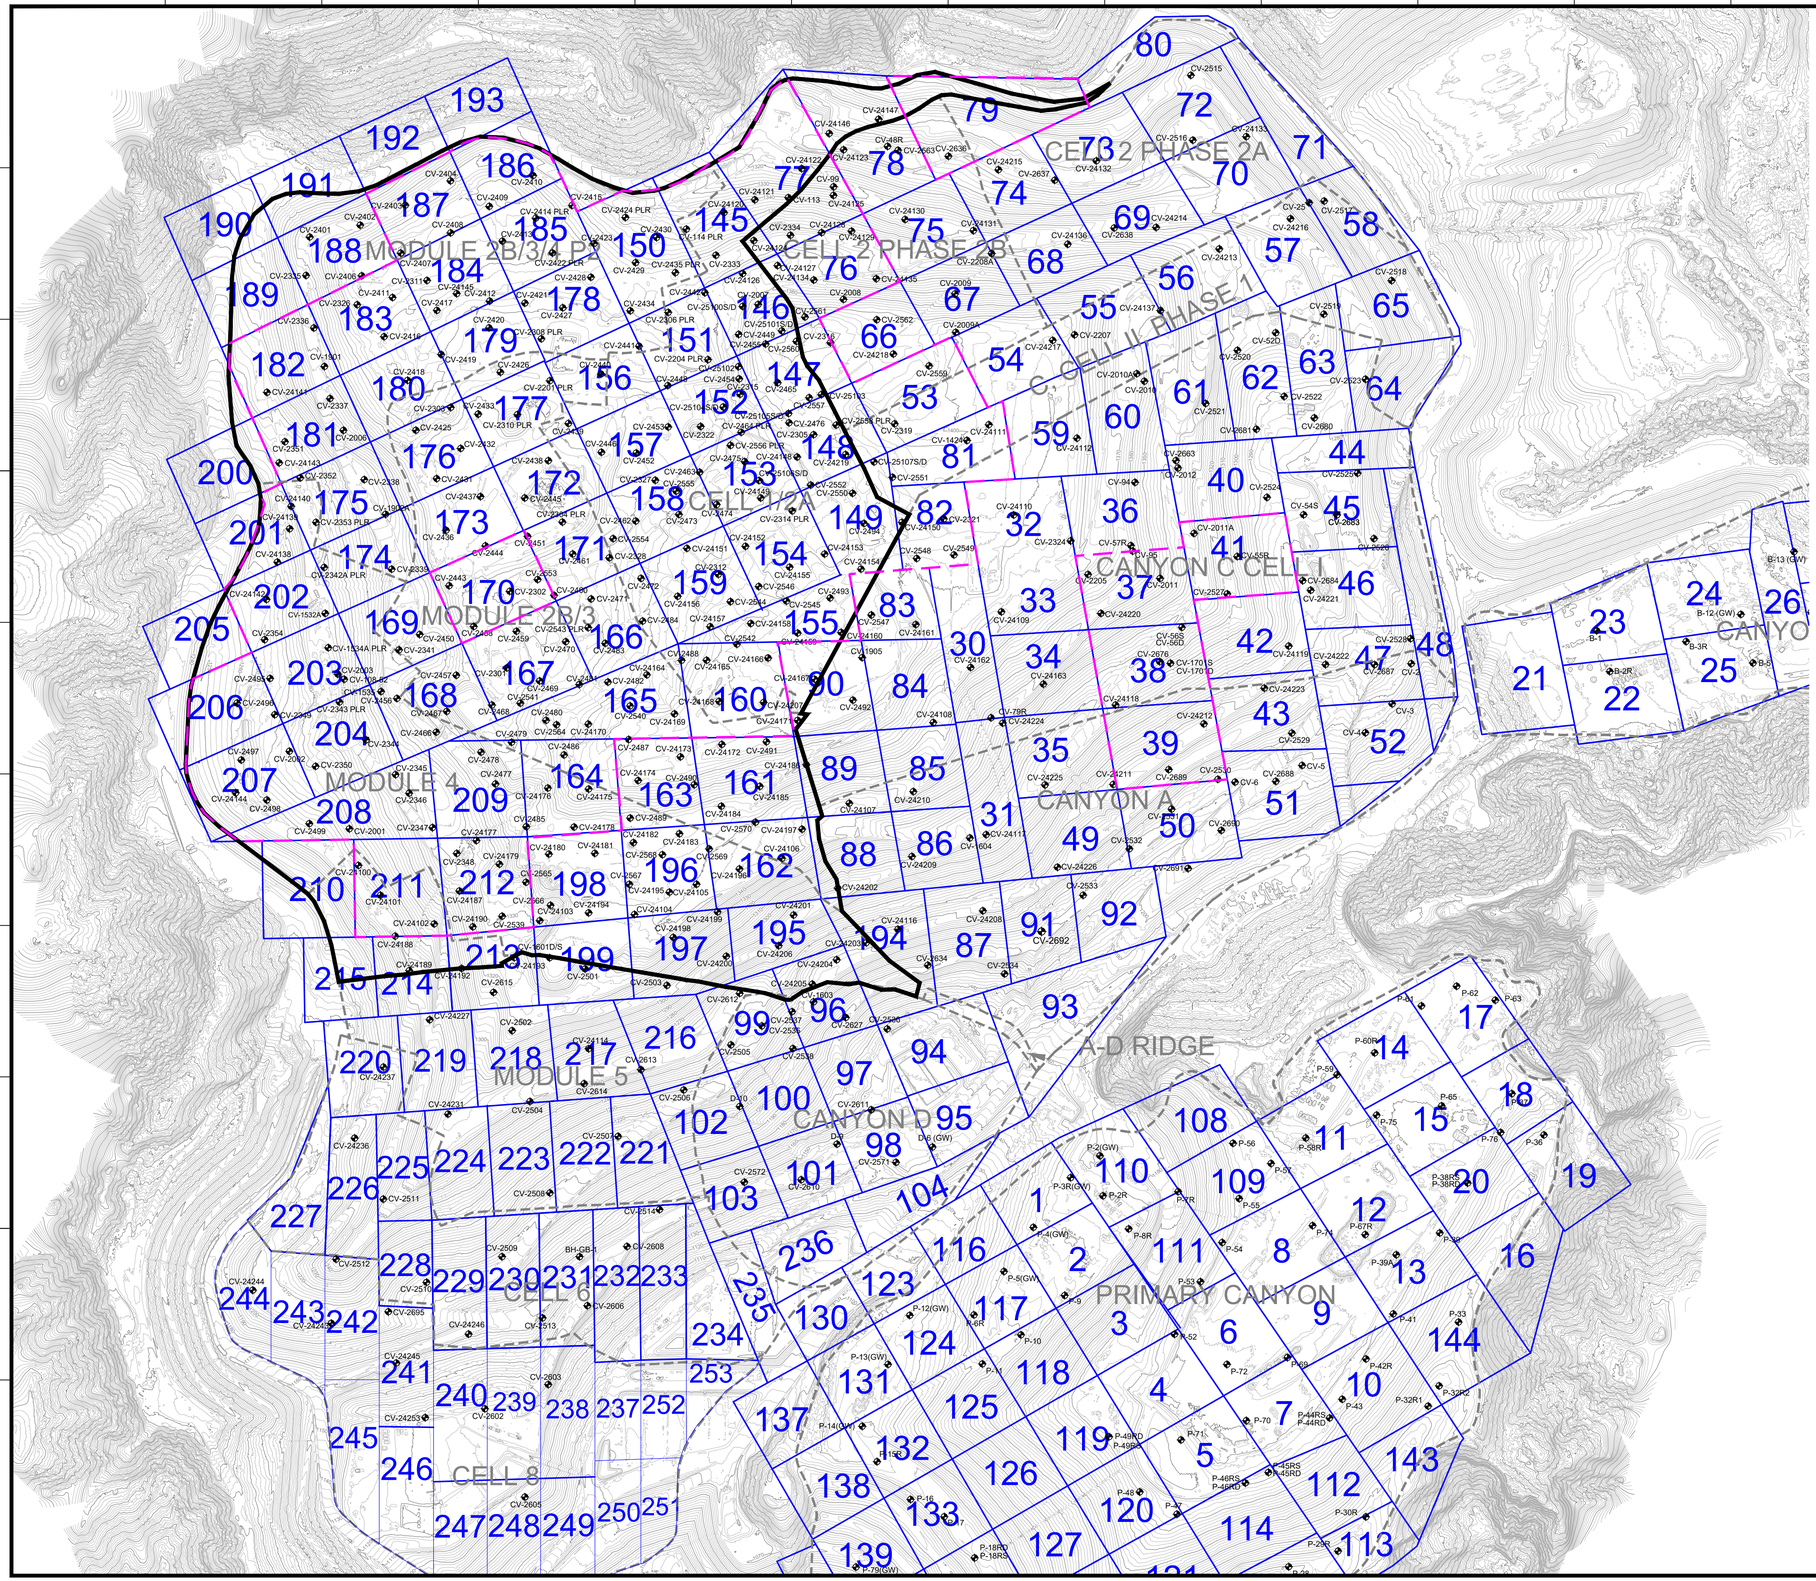

GENERAL DRAWING NOTES:

1. EXISTING GCCS AS-BUILT DATED SEPTEMBER 30, 2026.
3. APPROXIMATE REACTION MITIGATION AREA BOUNDARY ADJUSTMENTS DATED OCTOBER 9, 2026, BASED ON SEPTEMBER 2026 WELLFIELD DATA, PER SOFA CONDITION 8(m) AS DEFINED IN 9A.
4. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER DATED SEPTEMBER 30, 2026.
5. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.
6. THE LOCATION OF ANY EXISTING GCCS AND OTHER FEATURES ARE APPROXIMATE AND SHOULD BE USED FOR INFORMATIONAL PURPOSES ONLY.

DATE

REVISION

NO.

SHEET TITLE: SURFACE EMISSION MONITORING GRIDS AND VERTICAL LFG EXTRACTION WELLS

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544


ACAD FILE: WELLFIELD SERVICES
APP. BY: SRM
DWN. BY: ISR
CHK. BY: SRM
PROJ. NO. 01204123.45
DSN. BY: -

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 1

\\san-fs02\Files\Engineers\Waste Connections\Chiquita Canyon LF\2026 CCLF SCAQMD SAO\STIPULATED ORDER (GRID) MAPS\DWG\09-September 2026\2026-10-16_CCLF-Revised SOFA Map-SEM Grids and Installed Master Wells.dwg Oct 16, 2026 - 4:27pm By: istarosa

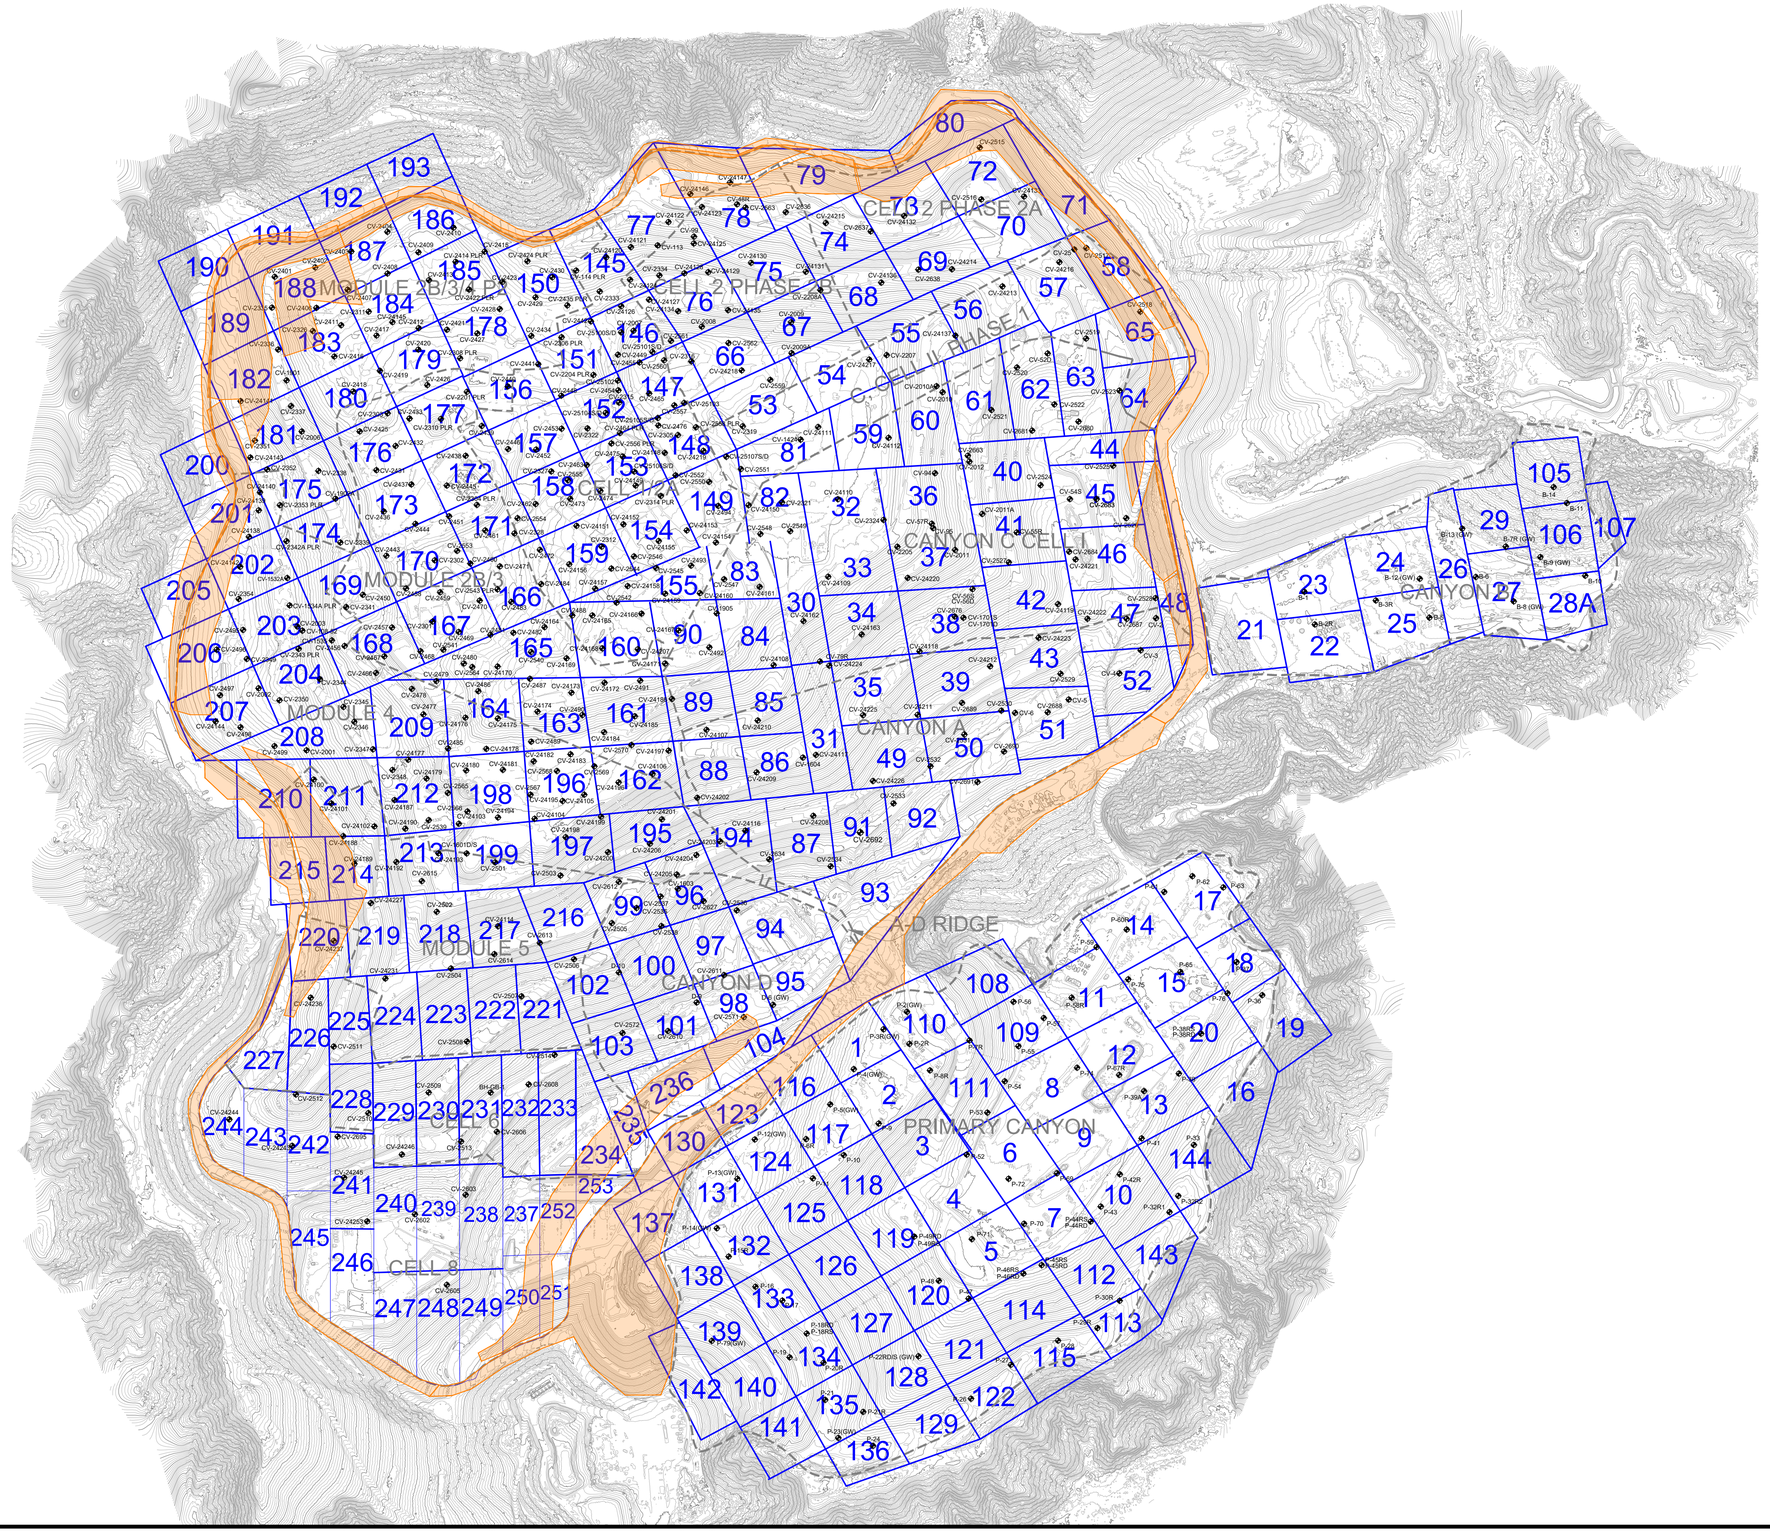

N

GRAPHIC SCALE

250 125 0 250 500 750

SCALE: 1"=250'

LEGEND

- 1150 — TOPOGRAPHIC CONTOUR
- EXISTING CELL LIMITS (APPROXIMATE)
- 23 — SURFACE EMISSION MONITORING GRID
- AREAS EXCLUDED FROM CONDITION 15(b)
- CV-XX — EXISTING VERTICAL LFG EXTRACTION WELL
- CV-XX PLR — EXISTING LFG VERTICAL EXTRACTION WELL - PRESSURIZED LEACHATE RELEASE

GENERAL DRAWING NOTES:

1. EXISTING GCCS AS-BUILT DATED SEPTEMBER 30, 2026.
2. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER DATED SEPTEMBER 30, 2026.
3. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.
4. THE LOCATION OF ANY EXISTING GCCS AND OTHER FEATURES ARE APPROXIMATE AND SHOULD BE USED FOR INFORMATIONAL PURPOSES ONLY.

NO.	REVISION	DATE

SHEET TITLE: SURFACE EMISSION MONITORING GRIDS AND VERTICAL LFG EXTRACTION WELLS

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO. 01204123.45 | DWN. BY: ISR | CHK. BY: SRM | ACAD FILE: FIELD SERVICES | APP. BY: SRM | DSN. BY: -

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 1

Attachment J

Leachate Temperature Data

Chiquita Canyon Landfill
Leachate Tank Temperatures

Date: 9/29/2026

Technician: Erick Estrada

Time	Location	Temperature (F)
1:00PM	LCRS Settling Frac Tank (20K Brown)	98
1:15PM	Tank Farm #10	72
1:30PM	Tank Farm #13	80
1:45PM	Tank Farm #7	91

Comments

North Perimeter Receiving Tanks (Tank Farm #6) no longer in service.

East Perimeter Receiving Tanks (Tank Farm #2) no longer in service.

Canyon D Receiving Tanks no longer in service.



N

GRAPHIC SCALE

200 100 0 200 400 600

SCALE: 1"=200'

LEGEND

EXISTING CELL LIMITS (APPROXIMATE)

EXISTING FRAK TANK

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLOR. AERIAL PHOTOGRAPHY DATED NOVEMBER 12, 2025.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM LOCATION MAP

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO: 01204123.41 | DWN. BY: SRM | ACAD FILE: | APP. BY: -

DSN. BY: - | CHK. BY: - | PE ENGINEERS

DATE: 11/20/2025

SCALE: AS SHOWN

SHEET: 1

N:\CAD\ASBUILT - MASTERS\CHIQUITA\GCCS\2025 ACAD\2025 CCLF Tank Farm Site Maps_2025-11-20.dwg Nov 20, 2025 - 8:23am By: bmedina



N

GRAPHIC SCALE

30 15 0 30 60 90

SCALE: 1"= 30'

LEGEND

EXISTING FRAC TANK

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLOR. AERIAL PHOTOGRAPHY DATED NOVEMBER 12, 2025.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM 7

PROJECT TITLE: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO. 01204123.41 | DWN. BY: SRM | CHK. BY: - | ACAD FILE: - | APP. BY: -

DSN. BY: -

DATE: 11/20/2025

SCALE: AS SHOWN

SHEET: 2

N:\CAD\ASBUILT - MASTERS\CHIQUITA\GCCS\2025 ACAD\2025 CCLF Tank Farm Site Maps_2025-11-20.dwg Nov 20, 2025 - 8:24am By: smedina



N

GRAPHIC SCALE

18 9 0 18 36 54

SCALE: 1"=18'

LEGEND

EXISTING FRAC TANK

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLOR. AERIAL PHOTOGRAPHY DATED NOVEMBER 12, 2025.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM 10

PROJECT TITLE: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544


PROJ. NO. 01204123.41 | DSN. BY: - | DWN. BY: SRM | CHK. BY: - | ACAD FILE ENGINEERS | APP. BY: -

DATE: 11/20/2025

SCALE: AS SHOWN

SHEET: 3

N:\CAD\ASBUILT - MASTERS\CHQ\TA\CCCS\2025 ACAD\2025 CCLF Tank Farm Site Maps_2025-11-20.dwg Nov 20, 2025 - 8:24am By: smedina

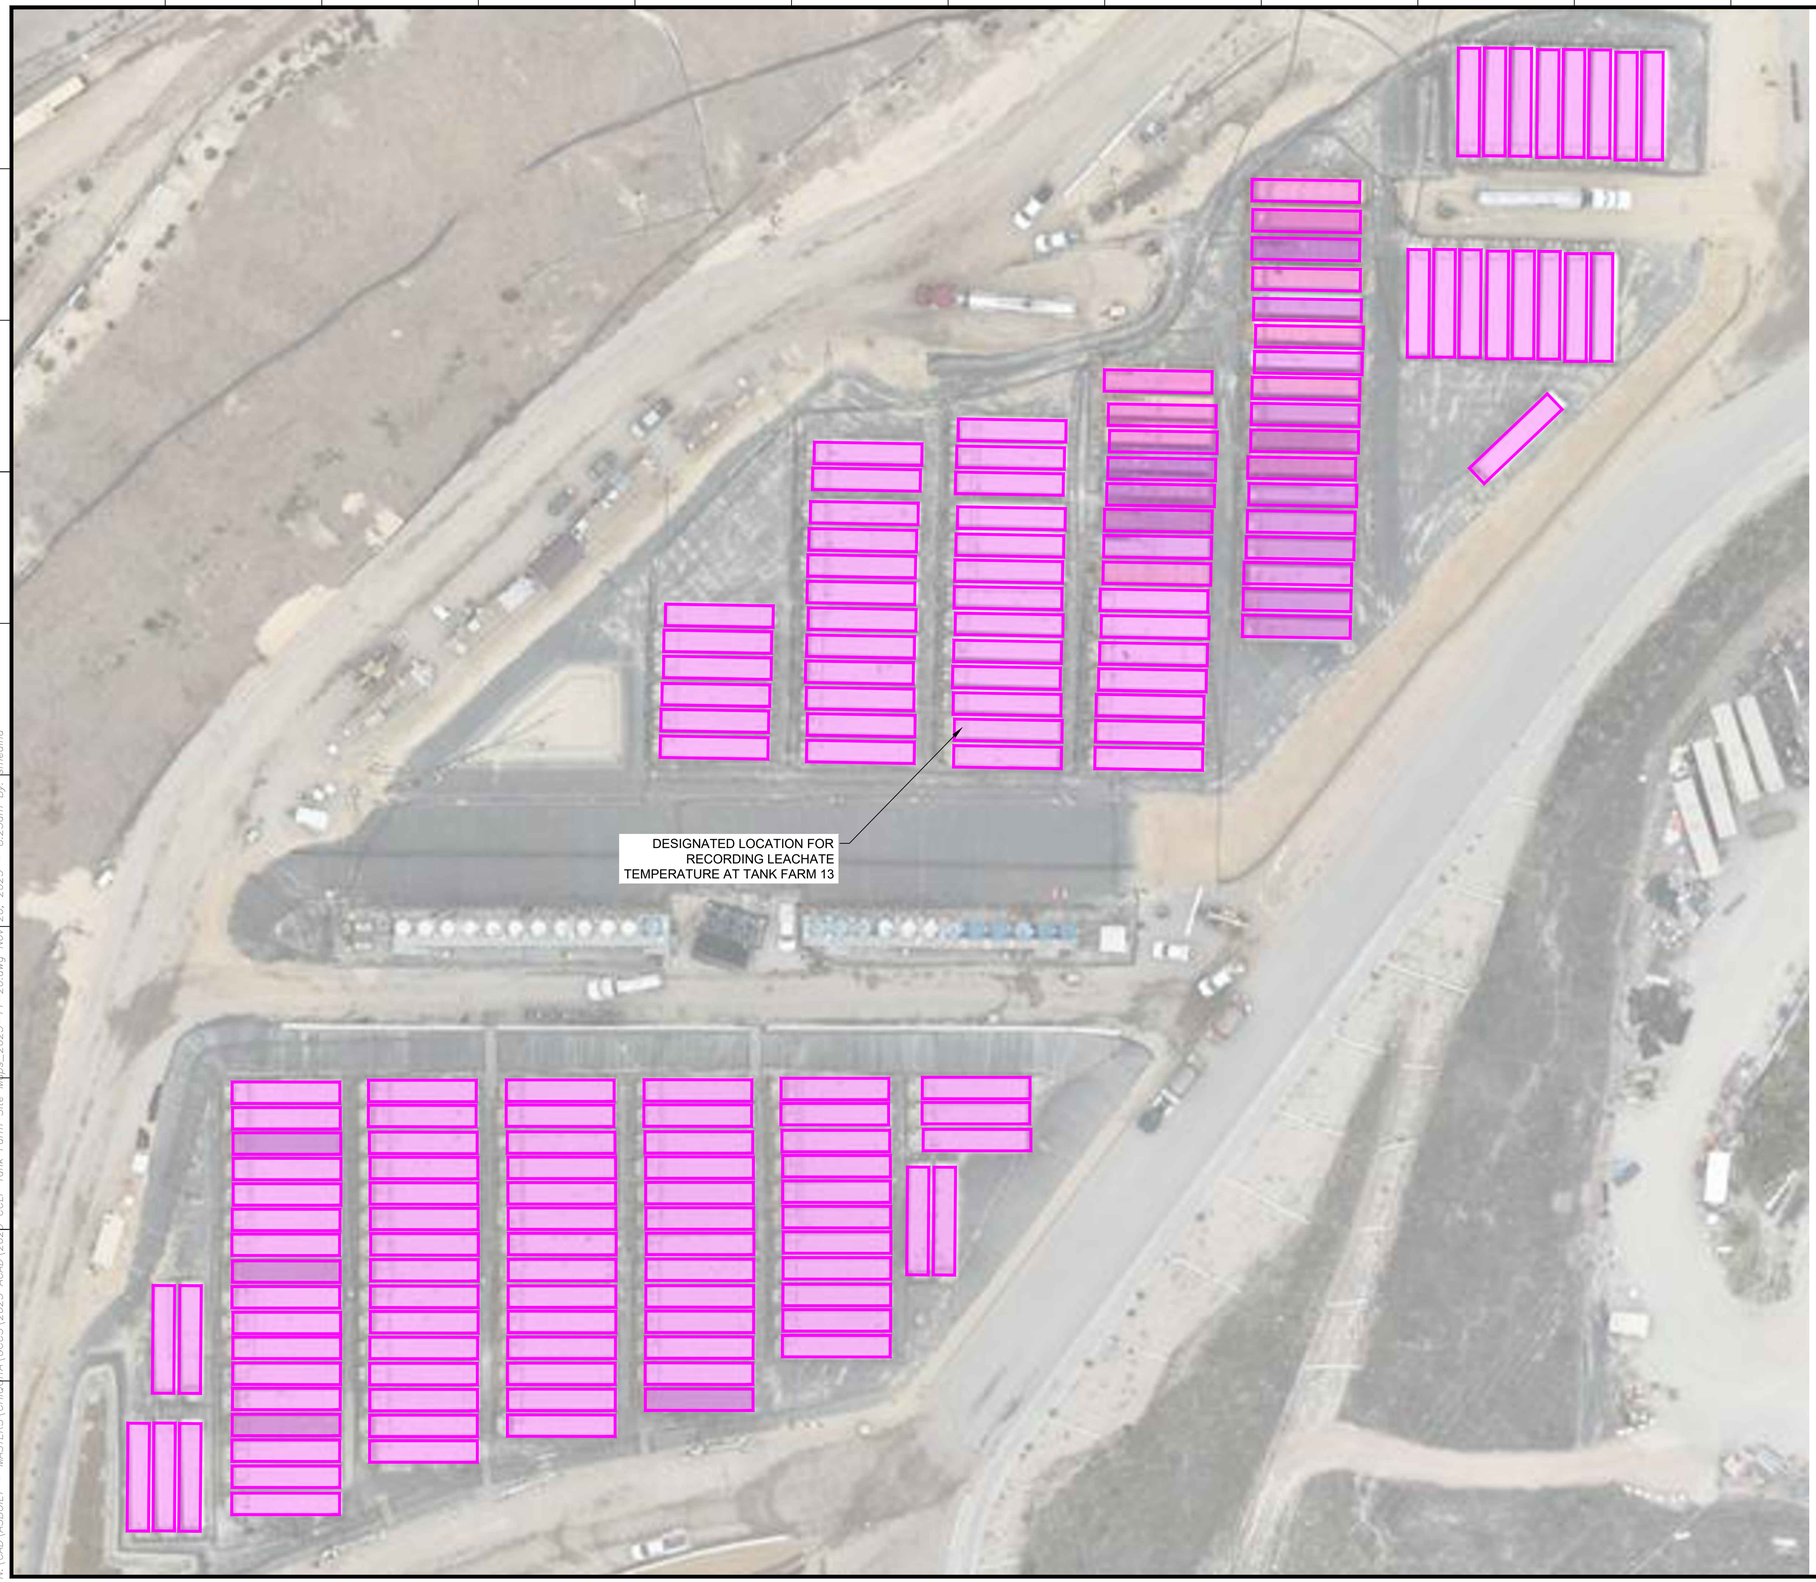

N

GRAPHIC SCALE

30 15 0 30 60 90

SCALE: 1"= 30'

LEGEND

EXISTING FRAC TANK

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLOR. AERIAL PHOTOGRAPHY DATED NOVEMBER 12, 2025.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM 13

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO. 01204123.41 | DWN. BY: SRM | ACAD FILE: | CHK. BY: - | APP. BY: -

DSN. BY: -

DATE: 11/20/2025

SCALE: AS SHOWN

SHEET: 4

N:\CAD\ASBUILT - MASTERS\CHIQUITA\CCCS\2025 ACAD\2025 CCLF Tank Farm Site Maps_2025-11-20.dwg Nov 20, 2025 - 8:25am By: smedina



N

GRAPHIC SCALE

20 10 0 20 40 60

SCALE: 1"= 20'

LEGEND

EXISTING FRAC TANK

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLOR. AERIAL PHOTOGRAPHY DATED NOVEMBER 12, 2025.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO. | REVISION | DATE

SHEET TITLE: LCRS FRAC TANKS

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO. 01204123.41 | DWN. BY: SRM | ACAD FILE: | APP. BY: -
DSN. BY: - | CHK. BY: - | PE/ENGINEERS

DATE: 11/20/2025

SCALE: AS SHOWN

SHEET: 5

N:\CAD\ASBUILT - MASTERS\CHIQUITA\CCCS\2025 ACAD\2025 CCLF Tank Farm Site Maps_2025-11-20.dwg Nov 20, 2025 - 8:26am By: smedina

Attachment K

Leachate Seep Report

CHIQUITA CANYON
A Waste Connections Company

September 8, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of August 31, 2026 through September 6, 2026. During this time, there was no ongoing leachate seepage or pooling at the Chiquita Canyon Landfill (the "Landfill") that occurred at a location more than once within the calendar week.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 1, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of August 31 through September 6, 2026, leachate seepage was observed on August 31, 2026, in Grid 94 at the Landfill, at approximately 7:53 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 9:30 a.m. on August 31, 2026. The seepage is estimated to have been present for approximately eight hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 12 square feet. The saturation of the soil was characterized as "Saturated." The odor intensity was characterized as "Very Light." This seepage was not observed again during the twice daily inspections during the week. Chiquita is planning to install a collection sump in the area to further minimize the potential for recurrence.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior "west slope toe drain project," in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita completed the installation of a sump pump in the area on August 11, 2026, and is currently compacting and placing fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Sarah Phillips

Sarah Phillips
Corporate Compliance Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from August 31 – September 6, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection

31 Aug 2026 / Tom Roe

Complete

Conducted on	31 Aug 2026 6:34 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

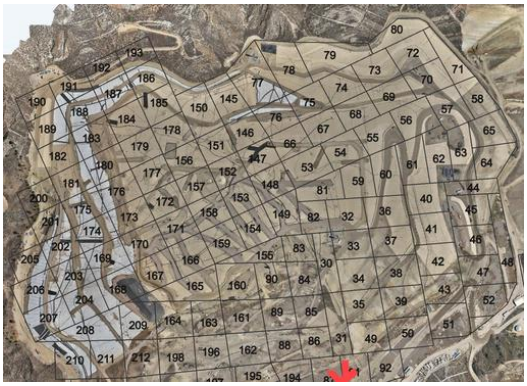




Photo 1

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43103202156213, -118.64536455843471)
Time seep/pooling was discovered	31 Aug 2026 7:53 AM PDT
Estimated duration of presence of leachate at such location	8 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	12 sq ft
Odor type	Leachate

Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling

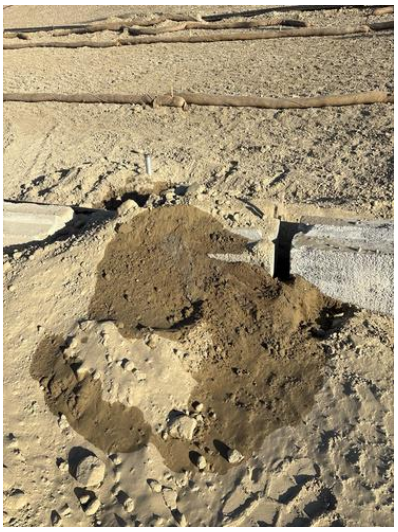


Photo 2

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Fresh soil added to contain seep.



Photo 3

4050 - Chiquita Leachate Seep/Pooling Inspection

31 Aug 2026 / Tom Roe

Complete

Conducted on	31 Aug 2026 3:11 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seep observed in grid 94 was not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Sep 2026 / Tom Roe

Complete

Conducted on	1 Sep 2026 6:43 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

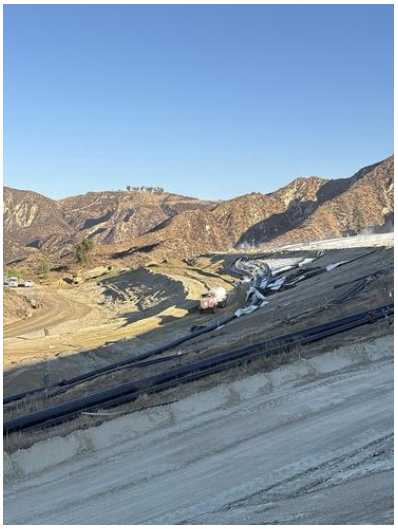


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Sep 2026 / Tom Roe

Complete

Conducted on	1 Sep 2026 1:43 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Grid 94. None of the seepage observed in this area or on the Westside was observed at the time of this inspection. Permanent repairs to the westside are currently underway.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Sep 2026 / Tom Roe

Complete

Conducted on	2 Sep 2026 7:22 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Sep 2026 / Tom Roe

Complete

Conducted on	2 Sep 2026 2:33 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Sep 2026 / John Boucher

Complete

Conducted on	3 Sep 2026 6:53 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Sep 2026 / John Boucher

Complete

Conducted on	3 Sep 2026 2:33 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Sep 2026 / John Boucher

Complete

Conducted on	4 Sep 2026 8:27 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

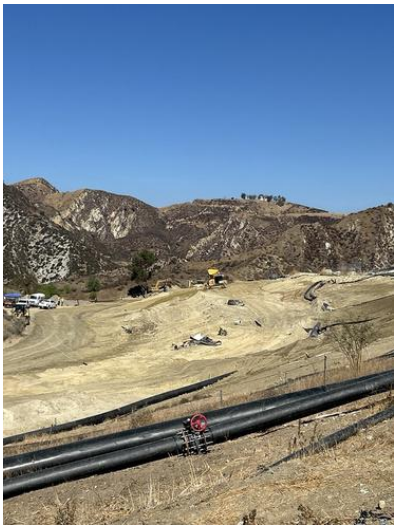


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Sep 2026 / John Boucher

Complete

Conducted on	4 Sep 2026 1:44 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

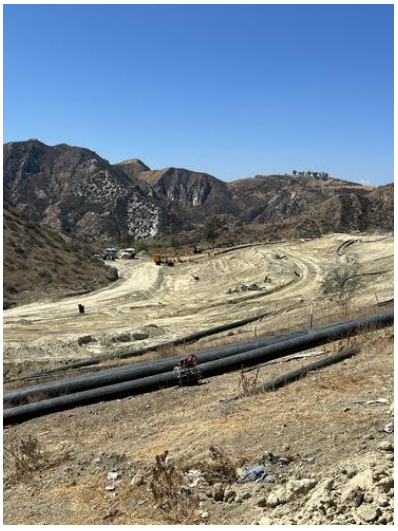


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

5 Sep 2026 / John Boucher

Complete

Conducted on	5 Sep 2026 7:30 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

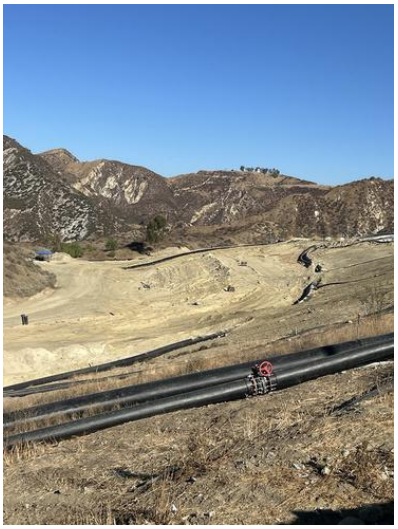


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

5 Sep 2026 / John Boucher

Complete

Conducted on	5 Sep 2026 1:08 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

6 Sep 2026 / John Boucher

Complete

Conducted on	6 Sep 2026 9:05 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

6 Sep 2026 / John Boucher

Complete

Conducted on	6 Sep 2026 1:07 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

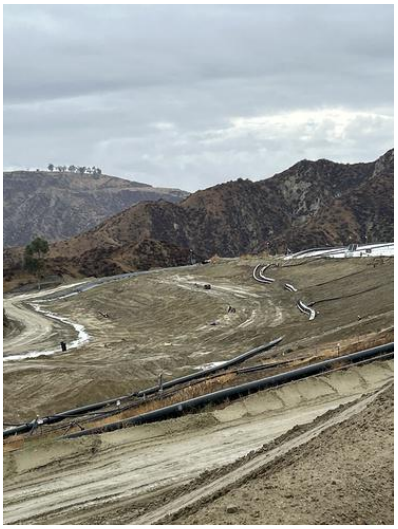


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

CHIQUITA CANYON
A Waste Connections Company

September 15, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 7, 2026 through September 13, 2026.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the morning of September 10, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that morning. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 7 through September 13, 2026, leachate seepage was observed on September 8, 2026, in Grid 94 at the Chiquita Canyon Landfill (the "Landfill"), at approximately 8:05 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 9:30 a.m. on September 8, 2026. The seepage is estimated to have been present for approximately five hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 16 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Very Light." This seepage was not observed again during the twice daily inspections during the week. Chiquita is planning to install a collection sump in the area to further minimize the potential for recurrence.

On September 9, 2026, at approximately 1:06 p.m., different seepage was initially observed in Grid 194. The specific location of this seep is shown on the maps included in the attachment. Upon

discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 3:00 p.m. on September 9, 2026. The seepage is estimated to have been present for approximately five hours. The total volume of leachate associated with this seepage is estimated to have been between 11 and 20 gallons. The observed area impacted by the seepage was approximately 35 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Light."

Seepage was again observed in Grid 194 on September 13, at approximately 7:27 a.m. Chiquita continued to implement response measures, including adding fresh soil to the affected area. The seepage was estimated to have been present for approximately four hours. The total volume of leachate associated with this seepage is estimated to have been between six and ten gallons. The observed area impacted by the seepage was approximately 16 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor was characterized as "Light." The seepage was not observed during the afternoon inspection conducted that same day.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior "west slope toe drain project," in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita completed the installation of a sump pump in the area on August 11, 2026, and is currently compacting and placing fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Sarah Phillips

Sarah Phillips
Corporate Compliance Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 7 – September 13, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection

7 Sep 2026 / Tom Roe

Complete

Conducted on	7 Sep 2026 6:47 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

7 Sep 2026 / Tom Roe

Complete

Conducted on	7 Sep 2026 1:07 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


8 Sep 2026 / Tom Roe

Complete

Conducted on	8 Sep 2026 6:48 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

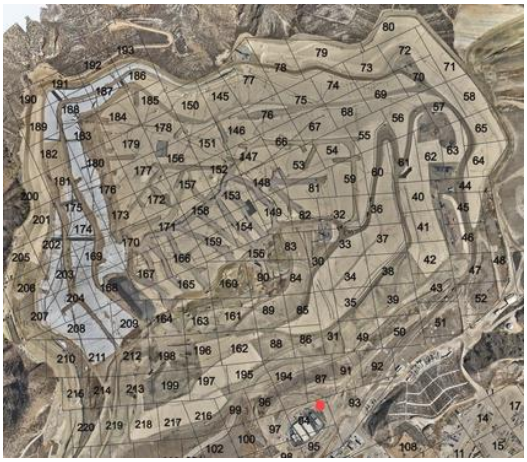

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43109548536677, -118.64515220812355)
Time seep/pooling was discovered	8 Sep 2026 8:05 AM PDT
Estimated duration of presence of leachate at such location	5 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	16 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Fresh soil added. Seep collector planned to be installed later this month.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

8 Sep 2026 / Tom Roe

Complete

Conducted on	8 Sep 2026 1:45 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seep observed in grid 94 was not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

9 Sep 2026 / Tom Roe

Complete

Conducted on	9 Sep 2026 7:25 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


9 Sep 2026 / Tom Roe

Complete

Conducted on	9 Sep 2026 1:06 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

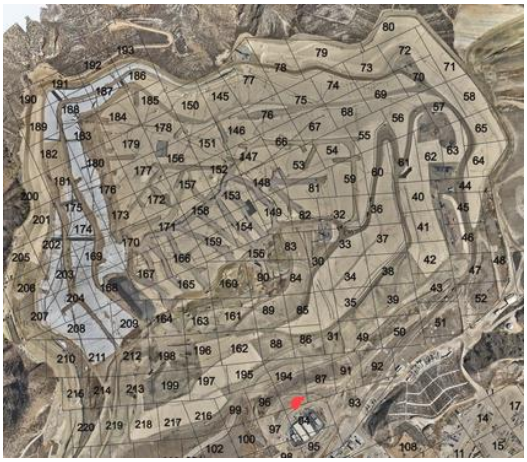

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.429721642482185, -118.64545066355299)
Time seep/pooling was discovered	9 Sep 2026 1:06 PM PDT
Estimated duration of presence of leachate at such location	5 hours
Estimated quantity of leachate	11-20 gallons
Extent of area impacted (approximate sq ft impacted)	35 sq ft
Odor type	Leachate
Odor intensity	2 - Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1



Photo 2



Photo 3

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added and compacted



Photo 4

4050 - Chiquita Leachate Seep/Pooling Inspection

10 Sep 2026 / John Boucher

Complete

Conducted on	10 Sep 2026 7:27 AM PDT

Entire main canyon inspected for 27(b)(ii)

Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

10 Sep 2026 / John Boucher

Complete

Conducted on	10 Sep 2026 1:21 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

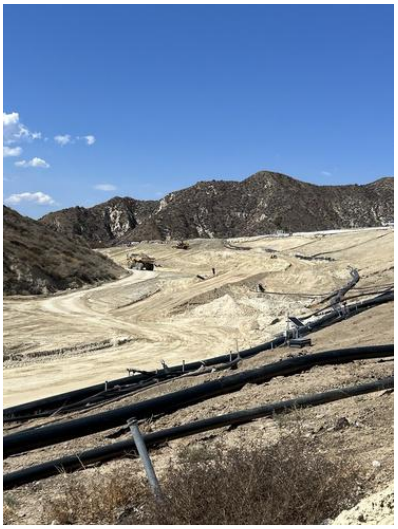


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

11 Sep 2026 / John Boucher

Complete

Conducted on	11 Sep 2026 7:15 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

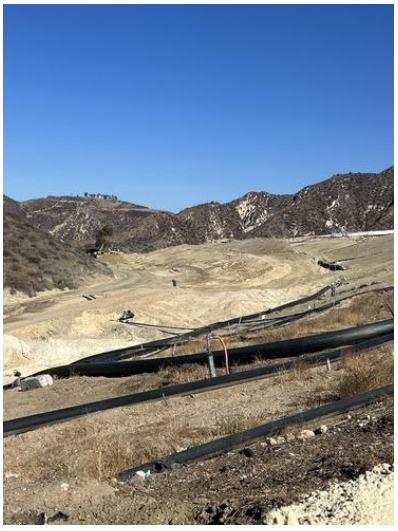


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

11 Sep 2026 / John Boucher

Complete

Conducted on	11 Sep 2026 2:12 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

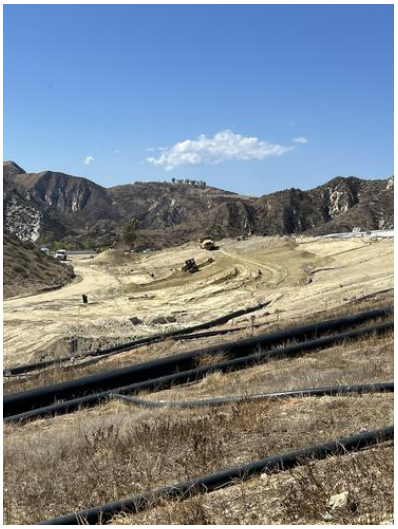


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

12 Sep 2026 / John Boucher

Complete

Conducted on	12 Sep 2026 8:04 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

12 Sep 2026 / John Boucher

Complete

Conducted on	12 Sep 2026 1:07 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


13 Sep 2026 / Tom Roe

Complete

Conducted on	13 Sep 2026 6:48 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

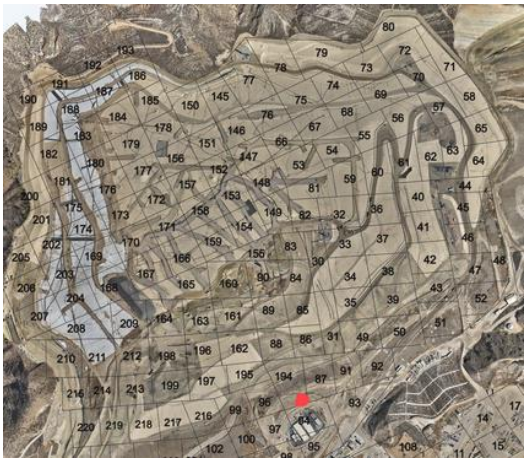

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43099405154067, -118.6455685739579)
Time seep/pooling was discovered	13 Sep 2026 7:27 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	6-10 gallons
Extent of area impacted (approximate sq ft impacted)	16 sqft
Odor type	Leachate
Odor intensity	2 - Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

13 Sep 2026 / Tom Roe

Complete

Conducted on	13 Sep 2026 1:05 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

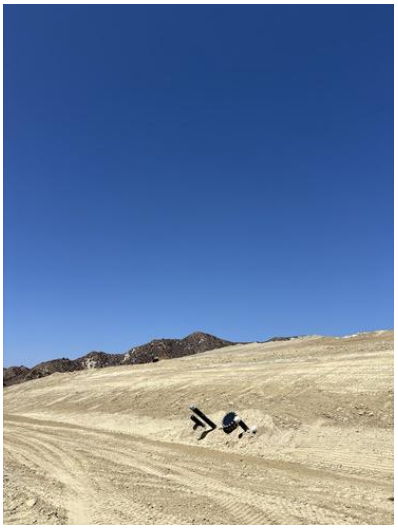


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well. The seep observed this morning in grid 194 was not observed during this inspection.

CHIQUITA CANYON
A Waste Connections Company

September 22, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 14, 2026 through September 20, 2026.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 16, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 14 through September 20, 2026, leachate seepage was initially observed on September 14, 2026, in Grid 194 at the Chiquita Canyon Landfill (the "Landfill"), at approximately 7:11 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 8:45 a.m. on September 14, 2026. The seepage is estimated to have been present for approximately three hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 16 square feet. The saturation of the soil was characterized as "Saturated." The odor intensity was characterized as "Very Light."

Seepage was again observed at the same location during the morning inspections conducted on September 15 and September 16. Chiquita continued to implement response measures, including adding fresh soil to the affected area. During September 15 and September 16, seepage observed

in Grid 194 was estimated to have been present for a cumulative total of approximately eight hours: approximately four hours on September 15, and four hours on September 16. The estimated quantity of leachate was between one and five gallons on each date. The observed area impacted by the seepage varied during the reporting period, ranging from approximately four to eight square feet. The saturation of the soil was characterized as "Standing Free Liquid." The odor was characterized as "Very Light." The seepage was not observed during subsequent inspections conducted that week.

On September 15, 2026, seepage was also observed in Grid 94, at approximately 9:24 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 11:00 a.m. on September 15, 2026. The seepage is estimated to have been present for approximately six hours total. The total volume of leachate associated with this seepage during that period is estimated to have been between 11 and 20 gallons. The observed area impacted by the seepage was approximately 100 square feet. The saturation of the soil was characterized as "Standing Free Liquid." No odor associated with this seepage was detected. This seepage was not observed again during the twice daily inspections conducted that week. This seepage is related to the previously reported seepage that occurred in Grid 94. Chiquita is planning to begin work on the installation of a seep collector, similar to a leachate toe drain, in the area this week to minimize the potential for future recurrence.

Additional seepage was observed in Grid 87 and Grid 206 on September 15 and September 16, respectively, as further described in the enclosed logs.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior west slope toe drain project, in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita is continuing to compact and place fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Sarah Phillips

Sarah Phillips
Corporate Compliance Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 14 – September 20, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection


14 Sep 2026 / Tom Roe

Complete

Conducted on	14 Sep 2026 7:11 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

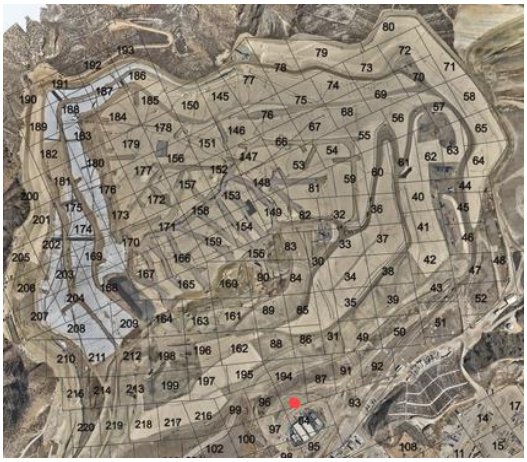

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43042935465008, -118.64554660034025)
Time seep/pooling was discovered	14 Sep 2026 7:11 AM PDT
Estimated duration of presence of leachate at such location	3 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	16 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep.

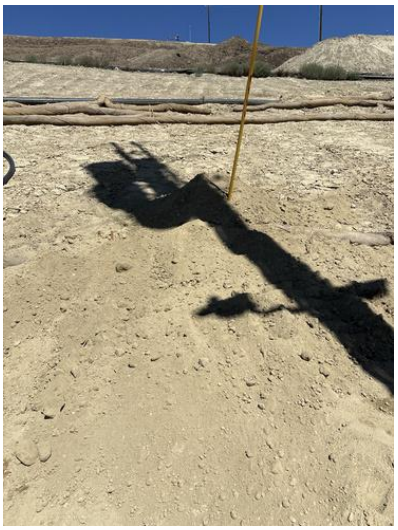


Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

14 Sep 2026 / Tom Roe

Complete

Conducted on	14 Sep 2026 1:39 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well. The seep observed in grid 194 was not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection


15 Sep 2026 / Tom Roe

Complete

Conducted on	15 Sep 2026 8:08 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

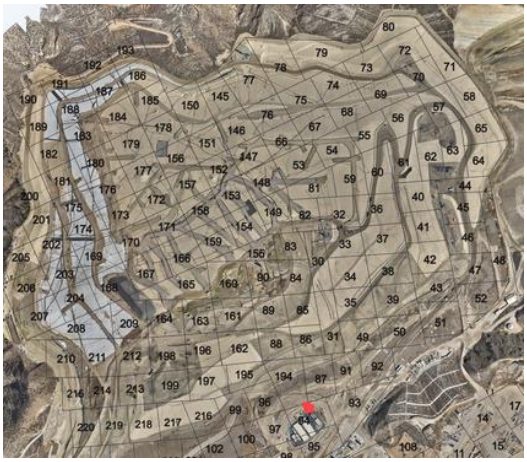

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.430730928586094, -118.64528325173862)
Time seep/pooling was discovered	15 Sep 2026 9:24 AM PDT
Estimated duration of presence of leachate at such location	6 hours
Estimated quantity of leachate	11-20 gallons
Extent of area impacted (approximate sq ft impacted)	100 sq ft
Odor type	Leachate
Odor intensity	0 - No Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep



Photo 2

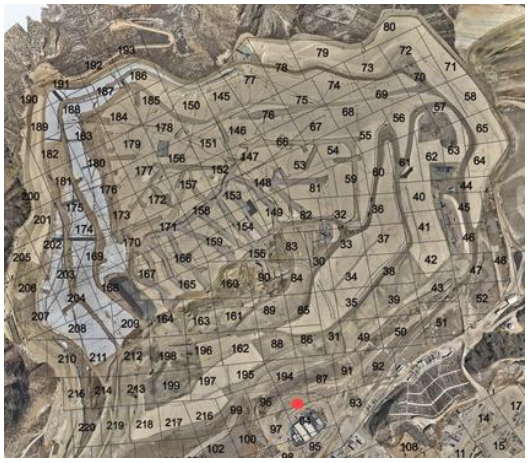


Photo 3

Leachate seep/pooling Inspection 2

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location



Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.431010844133375, -118.6455883406354)
Time seep/pooling was discovered	15 Sep 2026 9:38 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	4 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 4

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep

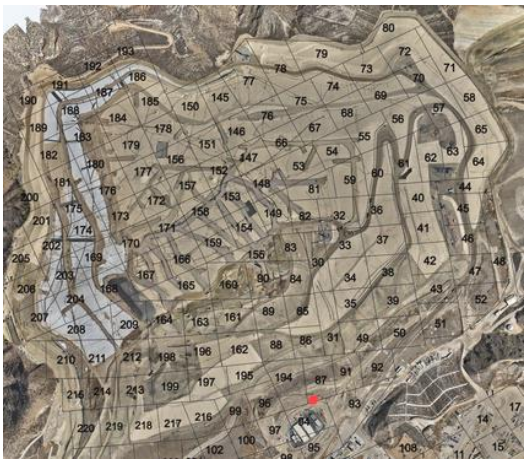


Photo 5

Leachate seep/pooling Inspection 3

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	87

Indicate on the map the location



Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43101135334356, -118.64552800241071)
Time seep/pooling was discovered	15 Sep 2026 9:42 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	1-5 gallons

Extent of area impacted (approximate sq ft impacted)	10sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling



Photo 6

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep



Photo 7

4050 - Chiquita Leachate Seep/Pooling Inspection

15 Sep 2026 / Tom Roe

Complete

Conducted on	15 Sep 2026 1:51 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seep observed in grids 94, 194, and 87 were not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection


16 Sep 2026 / Tom Roe

Complete

Conducted on	16 Sep 2026 6:45 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

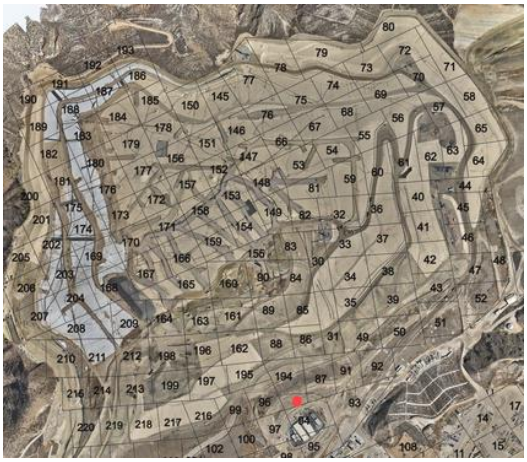

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.42984709505895, -118.64531673763602)
Time seep/pooling was discovered	16 Sep 2026 7:49 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	8sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Dirt added and a piece of liner put in place to contain seep.

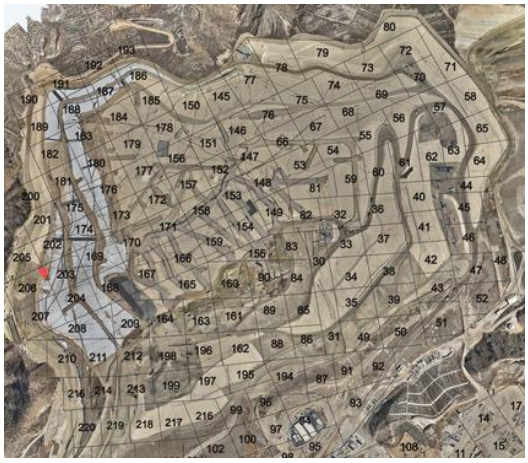


Photo 2

Leachate seep/pooling Inspection 2

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	206

Indicate on the map the location



Drop Pin to record lat/long of seep/pooling location.	(34.43748033111619, -118.65205339077002)
Time seep/pooling was discovered	16 Sep 2026 9:36 AM PDT
Estimated duration of presence of leachate at such location	3 hours
Estimated quantity of leachate	11-20 gallons
Extent of area impacted (approximate sq ft impacted)	150 sq ft
Odor type	Leachate
Odor intensity	4 - Strong Odor
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 3

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Liquid vacuumed out. The previously buried drainage pipe, which had been temporarily plugged during the West Toe Project, was uncovered and the plug was removed. The pipe is now open and properly draining into the West Toe Project area as intended.



Photo 4

4050 - Chiquita Leachate Seep/Pooling Inspection

16 Sep 2026 / Tom Roe

Complete

Conducted on	16 Sep 2026 2:25 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seeps observed in grid 194 and 206 were not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 8:13 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 2:09 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

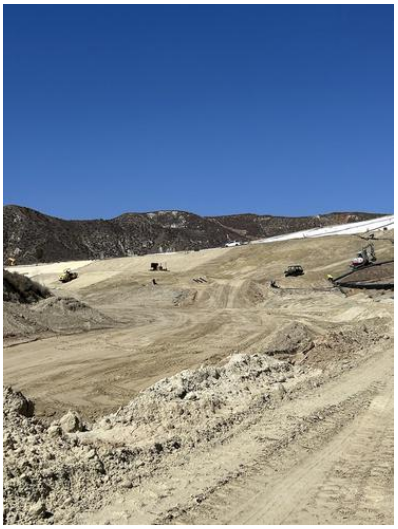


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 8:13 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

17 Sep 2026 / John Boucher

Complete

Conducted on	17 Sep 2026 2:09 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

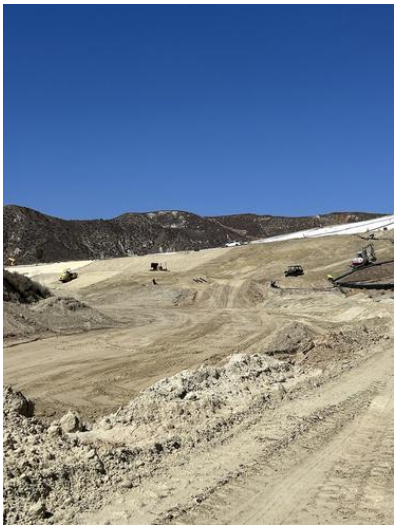


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

18 Sep 2026 / John Boucher

Complete

Conducted on	18 Sep 2026 7:22 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

18 Sep 2026 / John Boucher

Complete

Conducted on	18 Sep 2026 2:20 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

19 Sep 2026 / John Boucher

Complete

Conducted on	19 Sep 2026 8:07 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

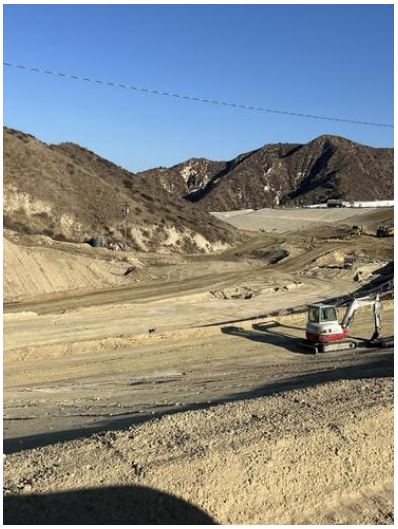


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

19 Sep 2026 / John Boucher

Complete

Conducted on	19 Sep 2026 1:02 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

20 Sep 2026 / Edwin DeLeon/Mike Alvarez

Complete

Conducted on	20 Sep 2026 6:21 AM PDT
Prepared by	Edwin DeLeon/Mike Alvarez

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No

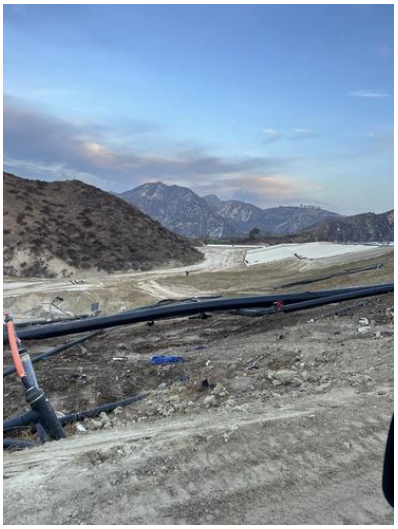


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

20 Sep 2026 / Edwin DeLeon/Mike Alvarez

Complete

Conducted on	20 Sep 2026 1:10 PM PDT
Prepared by	Edwin DeLeon/Mike Alvarez

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

CHIQUITA CANYON
A Waste Connections Company

September 29, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 21, 2026 through September 27, 2026.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 23, 2026, in accordance with the new Condition 27(b)(ii) of the Order. Leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 21 through September 27, 2026, leachate seepage was initially observed on September 21, 2026, in Grid 94 at the Chiquita Canyon Landfill (the "Landfill"), at approximately 9:27 a.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 11:00 a.m. on September 21, 2026. The seepage is estimated to have been present for approximately six hours. The total volume of leachate associated with this seepage is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately 12 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Very Light." This seepage is related to the previously reported seepage that occurred in Grid 94 and Grid 194. Chiquita is currently installing a seep collector, similar to a leachate toe drain, in the area to minimize the potential for future recurrence.

Seepage was again observed at the same location during the afternoon inspection conducted on September 23, 2026. Chiquita continued to implement response measures, including adding fresh soil to the affected area. Seepage observed in Grid 94 was estimated to have been present for approximately two hours on September 23. The estimated quantity of leachate was between one and five gallons during that period. The observed area impacted was approximately seven square feet. The saturation of the soil was characterized as "Standing free liquid." No odor associated with this seepage was detected. The seepage was not observed during subsequent inspections conducted that week.

On September 22, 2026, seepage was also observed in Grid 194, at approximately 3:03 p.m. The specific location of this seep is shown on the maps included in the attachment. Upon discovery of the seep, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected area. This initial response work was completed by approximately 3:30 p.m. on September 22, 2026. The seepage is estimated to have been present for approximately three hours. The total volume of leachate associated with this seepage during that period is estimated to have been between one and five gallons. The observed area impacted by the seepage was approximately six square feet. The saturation of the soil was characterized as "Saturated." The odor intensity was characterized as "Very Light." This seepage was not observed again during the twice daily inspections conducted that week.

Chiquita is continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior west slope toe drain project, in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita is continuing to compact and place fill material.

Please contact me if you have any questions regarding this matter.

Regards,

Matt Breuer
Environmental Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 21 – September 27, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection


21 Sep 2026 / Tom Roe

Complete

Conducted on	21 Sep 2026 6:54 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

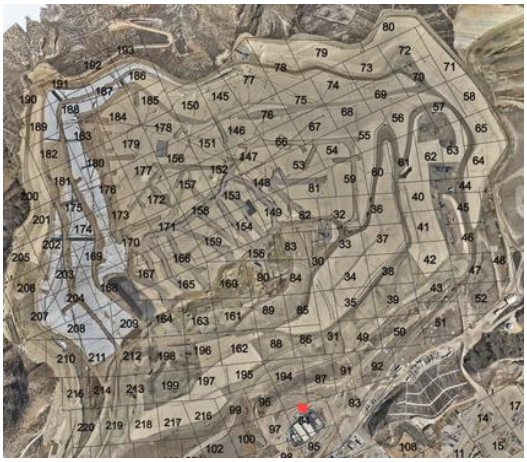

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.429568314455985, -118.64553770982519)
Time seep/pooling was discovered	21 Sep 2026 9:27 AM PDT
Estimated duration of presence of leachate at such location	6 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	12 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep. Construction of leachate interceptor trench to prevent future seepage scheduled to begin this week.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

21 Sep 2026 / Tom Roe

Complete

Conducted on	21 Sep 2026 2:45 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Grid 94. None of the seepage observed in this area or on the Westside was observed at the time of this inspection. Permanent repairs to the westside are currently underway.

4050 - Chiquita Leachate Seep/Pooling Inspection

22 Sep 2026 / Tom Roe

Complete

Conducted on	22 Sep 2026 6:59 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No

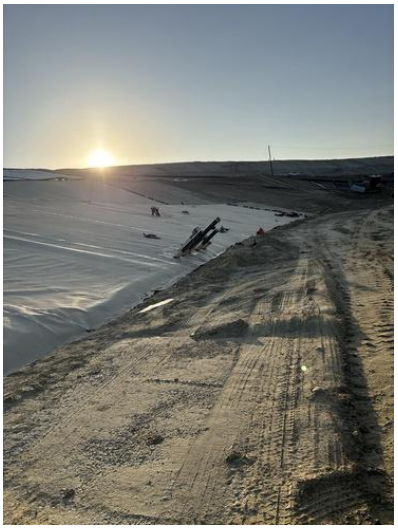


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection


22 Sep 2026 / Tom Roe

Complete

Conducted on	22 Sep 2026 2:01 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194

Indicate on the map the location

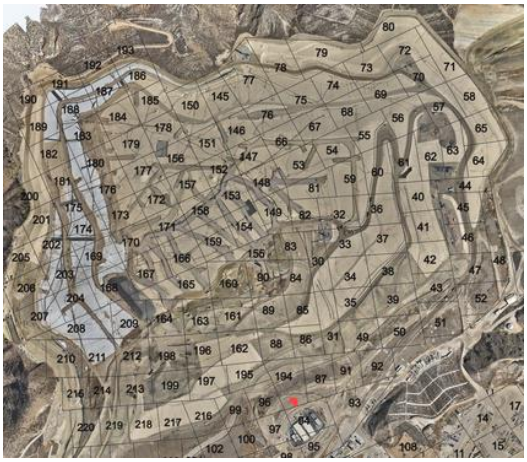

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.42927249578992, -118.64584659211286)
Time seep/pooling was discovered	22 Sep 2026 3:03 PM PDT
Estimated duration of presence of leachate at such location	3 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	6 sq ft
Odor type	Leachate
Odor intensity	1 - Very Light Odor Detected
Surrounding soil saturation level	Saturated

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep. Construction of interceptor trench scheduled to begin this week.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

23 Sep 2026 / Tom Roe

Complete

Conducted on	23 Sep 2026 7:17 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No

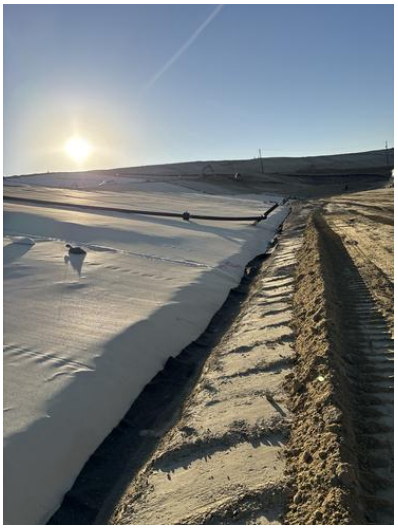


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

23 Sep 2026 / Tom Roe

Complete


Conducted on	23 Sep 2026 2:03 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	94

Indicate on the map the location

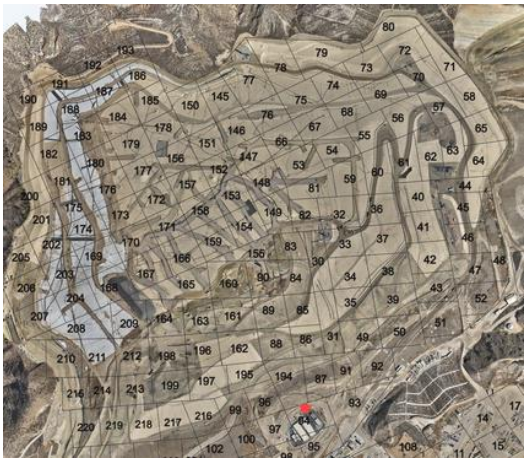

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.42969961471349, -118.64579633425224)
Time seep/pooling was discovered	23 Sep 2026 2:44 PM PDT
Estimated duration of presence of leachate at such location	2 hours
Estimated quantity of leachate	1-5 gallons
Extent of area impacted (approximate sq ft impacted)	7sq ft
Odor type	Leachate
Odor intensity	0 - No Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seep. Interceptor trench scheduled to begin soon.



Photo 2

4050 - Chiquita Leachate Seep/Pooling Inspection

24 Sep 2026 / John Boucher

Complete

Conducted on	24 Sep 2026 7:05 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

24 Sep 2026 / John Boucher

Complete

Conducted on	24 Sep 2026 1:02 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

25 Sep 2026 / Nancy Bahena Hernandez

Complete

Conducted on	25 Sep 2026 7:34 AM PDT
Prepared by	Nancy Bahena Hernandez

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

25 Sep 2026 / Nancy Bahena Hernandez

Complete

Conducted on	25 Sep 2026 1:04 PM PDT
Prepared by	Nancy Bahena Hernandez

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

26 Sep 2026 / John Boucher

Complete

Conducted on	26 Sep 2026 8:05 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

26 Sep 2026 / John Boucher

Complete

Conducted on	26 Sep 2026 1:00 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

27 Sep 2026 / Edwin DeLeon

Complete

Conducted on	27 Sep 2026 7:06 AM PDT
Prepared by	Edwin DeLeon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

27 Sep 2026 / Edwin DeLeon

Complete

Conducted on	27 Sep 2026 1:08 PM PDT
Prepared by	Edwin DeLeon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

CHIQUITA CANYON
A Waste Connections Company

October 6, 2026

Via E-Mail
Baitong Chen, Air Quality Engineer, bchen@aqmd.gov
Nathaniel Dickel, Senior Air Quality Engineer, ndickel@aqmd.gov
Christina Ojeda, Air Quality Inspector, cojeda@aqmd.gov
South Coast Air Quality Management District
21865 East Copley Drive
Diamond Bar, California 91765-4182

Re: Chiquita Canyon, LLC's Weekly Leachate Inspection Report for Stipulated Order for Abatement (Case No. 6177-4), Condition 27(c)

All:

Pursuant to Condition 27(c) of the Stipulated Order for Abatement with the South Coast Air Quality Management District in Case No. 6177-4, as modified on June 3, 2026 (the "Order"), Chiquita Canyon, LLC ("Chiquita") hereby submits the enclosed compilation of the twice daily leachate seep inspection logs for the period of September 28, 2026 through October 4, 2026. During this time, there was no ongoing leachate seepage or pooling at the Chiquita Canyon Landfill (the "Landfill") that occurred at a location more than once within the calendar week.

During this reporting period, Chiquita also conducted and documented an expanded leachate seep inspection of the entire Main Canyon area on the afternoon of September 30, 2026, in accordance with the new Condition 27(b)(ii) of the Order. No leachate seepage was observed during that inspection, as reflected in the enclosed inspection log for that afternoon. Consistent with modified Condition 27(c), this report also identifies any leachate seepage or pooling observed outside of the Condition 27(b) inspections during the reporting period.

For the week of September 28, 2026 through October 4, 2026, multiple related seeps were observed on September 30, 2026, in Grid 87 and Grid 194 at the Landfill, at approximately 6:30 a.m. The specific location of the seepage is shown on the maps included in the attachment. Upon discovery of the seepage, Chiquita promptly initiated response and mitigation measures, including adding fresh soil to the affected areas. This initial response work was completed by approximately 8:15 a.m. on September 30, 2026. The seepage is estimated to have been present for approximately four hours. The total volume of leachate from the seepage is estimated to have been between six and ten gallons. The combined area impacted by the seepage was approximately 25 square feet. The saturation of the soil was characterized as "Standing free liquid." The odor intensity was characterized as "Light." This seepage was not observed again during the twice daily inspections during the week. This seepage is related to the previously reported seepage that occurred in Grid 94 and Grid 194. On October 2, 2026, Chiquita completed the installation of a seep collector, similar to a leachate toe drain, in the area to further minimize the potential for recurrence.

Chiquita is also continuing to construct a soil buttress on the west side of the Landfill, adjacent to the prior "west slope toe drain project," in response to the continued extrusion of reacted material at certain preferential pathways that daylight on the west slope. Chiquita recently completed the construction of the lower and upper buttresses and is continuing work on the remainder of the west toe project, including the installation of stormwater infrastructure and completion of roadway improvements.

Please contact me if you have any questions regarding this matter.

Regards,

Tessa Lenz

Tessa Lenz
Environmental Manager
Chiquita Canyon

Attachment: Leachate Seep/Pooling Inspection Logs from September 28 – October 4, 2026

4050 - Chiquita Leachate Seep/Pooling Inspection

28 Sep 2026 / Tom Roe

Complete

Conducted on	28 Sep 2026 6:45 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

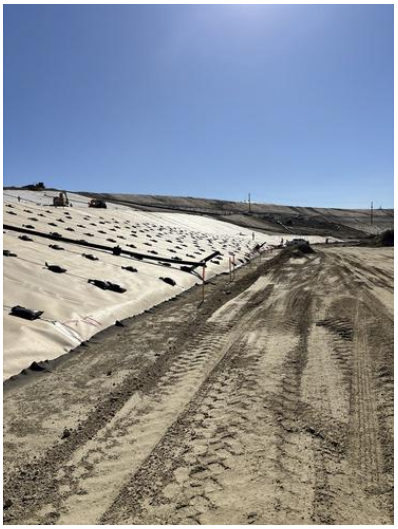


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

28 Sep 2026 / Tom Roe

Complete

Conducted on	28 Sep 2026 2:50 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

29 Sep 2026 / Tom Roe

Complete

Conducted on	29 Sep 2026 7:17 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

29 Sep 2026 / Tom Roe

Complete

Conducted on	29 Sep 2026 2:10 PM PDT
Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area.

4050 - Chiquita Leachate Seep/Pooling Inspection

30 Sep 2026 / Tom Roe

Complete

Conducted on	30 Sep 2026 6:28 AM PDT
Prepared by	Tom Roe

Leachate Seep Inspection


Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	Yes
Which grid is the leachate seep/pooling located?	194,87

Seeping from multiple locations, all related.

Indicate on the map the location

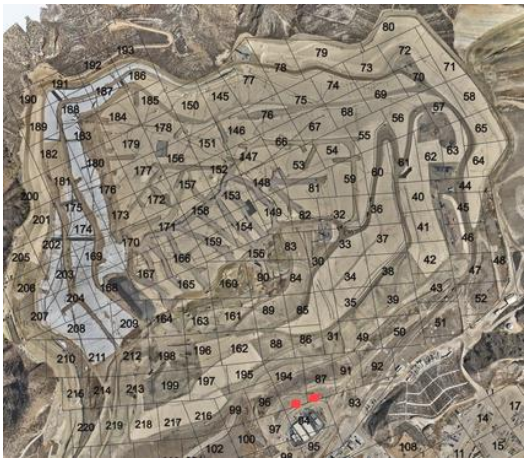

Drop Pin to record lat/long of seep/pooling location.	Castaic CA 91384 United States (34.43111202925636, -118.64528987991329)
Time seep/pooling was discovered	30 Sep 2026 6:30 AM PDT
Estimated duration of presence of leachate at such location	4 hours
Estimated quantity of leachate	6-10 gallons

Volume combined between areas

Extent of area impacted (approximate sq ft impacted)	25 sq ft (combined between locations)
Odor type	Leachate
Odor intensity	2 - Light Odor Detected
Surrounding soil saturation level	Standing free liquid

Image of seep/pooling



Photo 1



Photo 2



Photo 3

Did the seep/pooling travel into the stormwater channel?	No

Actions taken to contain seep/pooling?

Soil added to contain seeps. Seep collector construction is in progress.



Photo 4

4050 - Chiquita Leachate Seep/Pooling Inspection

30 Sep 2026 / Tom Roe

Complete

Conducted on	30 Sep 2026 2:09 PM PDT

Entire Main Canyon inspected for 27(b)(ii)

Prepared by	Tom Roe

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection, permanent repairs are being conducted to contain the seepage in this area. The seeps observed in grid 194 and 87 were also not observed at the time of this inspection.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Oct 2026 / John Boucher

Complete

Conducted on	1 Oct 2026 8:09 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

1 Oct 2026 / John Boucher

Complete

Conducted on	1 Oct 2026 1:47 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Oct 2026 / John Boucher

Complete

Conducted on	2 Oct 2026 7:10 AM PDT
Prepared by	John Boucher

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

2 Oct 2026 / John Boucher

Complete

Conducted on	2 Oct 2026 2:11 PM PDT
Prepared by	John Boucher

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

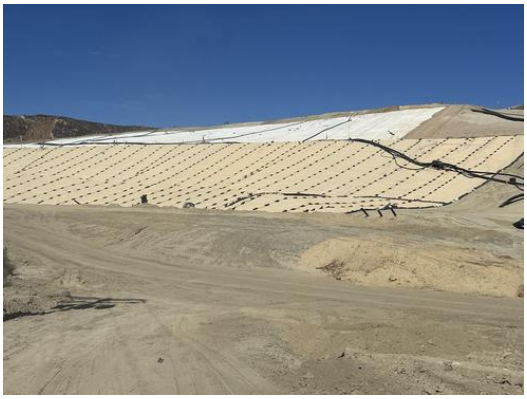


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Oct 2026 / Edwin De Leon

Complete

Conducted on	3 Oct 2026 6:34 AM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

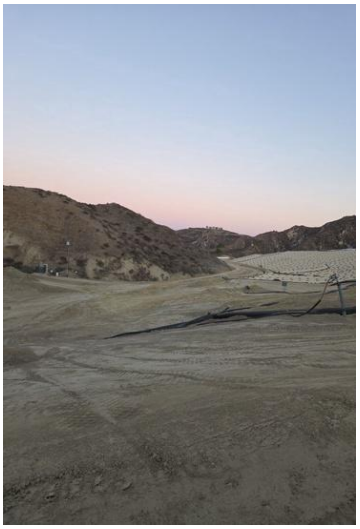


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

3 Oct 2026 / Edwin De Leon

Complete

Conducted on	3 Oct 2026 1:40 PM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Oct 2026 / Edwin De Leon

Complete

Conducted on	4 Oct 2026 6:40 AM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection

Leachate seep/pooling Inspection

Leachate seep/pooling Inspection 1

Has a leachate seep/pooling been located?	No

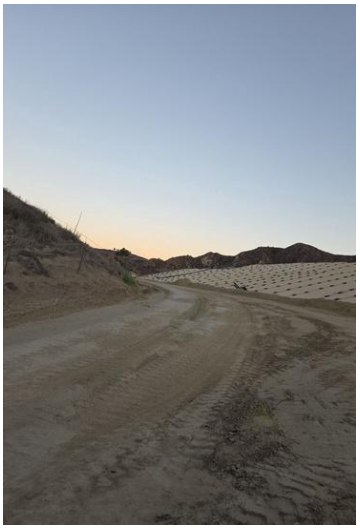


Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

4050 - Chiquita Leachate Seep/Pooling Inspection

4 Oct 2026 / Edwin De Leon

Complete

Conducted on	4 Oct 2026 1:05 PM PDT
Prepared by	Edwin De Leon

Leachate Seep Inspection	
Leachate seep/pooling Inspection	
Leachate seep/pooling Inspection 1	
Has a leachate seep/pooling been located?	No



Photo 1

Description of area in photo where there is no leachate seepage or pooling.	Westside perimeter road. None of the seepage previously observed in this area were observed at the time of this inspection. Permanent repairs are being conducted to contain seepage in this area as well.

Attachment L

Leachate Gallon Data

Leachate Gallons for the Month of September 2026

Off-site Disposal

Week	Date	Facility	Address	Estimated Gallons
1	9/1-9/6	Avalon	14700 S. Avalon Blvd. Gardena, CA 90248	375,061
1	9/1-9/6	East Valley Remediation	62150 Gene Welmas Way Mecca, CA 92254	234,644
1	9/1-9/6	Durham Regional Landfill	22316 South Harmon Rd. Florence, AZ 85132	248,101
1	9/1-9/6	Clean Harbors Nebraska	Clean Harbors, Kimball 2247 South Highway 71 Kimball, NE 69145	15,473
1	9/1-9/6	ReWorld Advanced Processing, Inc.	10020 Bayport Blvd. Pasadena, TX 77507	119,068
1	9/1-9/6	Industrial Recycling, Baja	Industrial Recycling Monte Alban, 126 Benito Juarez, Cuidad de Mexico, C.P. 03020	247,611
1	9/1-9/6	Crystal Clean, Bakersfield	1620 E Brundage Ln, Bakersfield, CA 93307	337,704
1	9/1-9/6	Crystal Clean, Wyoming	2275 Burlingame Ave Wyoming, MI 49509	105,433
2	9/7-9/13	East Valley Remediation	62150 Gene Welmas Way Mecca, CA 92254	278,549
2	9/7-9/13	Durham Regional Landfill	22316 South Harmon Rd. Florence, AZ 85132	300,342
2	9/7-9/13	ReWorld Advanced Processing, Inc.	10020 Bayport Blvd. Pasadena, TX 77507	235,745
2	9/7-9/13	Industrial Recycling, Baja	Industrial Recycling Monte Alban, 126 Benito Juarez, Cuidad de Mexico, C.P. 03020	86,656
2	9/7-9/13	Crystal Clean, Bakersfield	1620 E Brundage Ln, Bakersfield, CA 93307	412,810
2	9/7-9/13	Crystal Clean, Wyoming	2275 Burlingame Ave Wyoming, MI 49509	117,636
3	9/14-9/20	East Valley Remediation	62150 Gene Welmas Way Mecca, CA 92254	279,315
3	9/14-9/20	Durham Regional Landfill	22316 South Harmon Rd. Florence, AZ 85132	378,725
3	9/14-9/20	Midway Environmental Services, Inc.	900536 South 3490 Rd. Chandler, OK 74834	258,382
3	9/14-9/20	Industrial Recycling, Baja	Industrial Recycling Monte Alban, 126 Benito Juarez, Cuidad de Mexico, C.P. 03020	64,267
3	9/14-9/20	Crystal Clean, Bakersfield	1620 E Brundage Ln, Bakersfield, CA 93307	456,615
3	9/14-9/20	Crystal Clean, Wyoming	2275 Burlingame Ave Wyoming, MI 49509	147,034

4	9/21-9/27	East Valley Remediation	62150 Gene Welmas Way Mecca, CA 92254	399,897
4	9/21-9/27	Durham Regional Landfill	22316 South Harmon Rd. Florence, AZ 85132	390,777
4	9/21-9/27	Midway Environmental Services, Inc.	900536 South 3490 Rd. Chandler, OK 74834	617,430
4	9/21-9/27	Crystal Clean, Bakersfield	1620 E Brundage Ln, Bakersfield, CA 93307	411,266
4	9/21-9/27	Crystal Clean, Wyoming	2275 Burlingame Ave Wyoming, MI 49509	108,130
5	9/28-9/30	East Valley Remediation	62150 Gene Welmas Way Mecca, CA 92254	207,587
5	9/28-9/30	Durham Regional Landfill	22316 South Harmon Rd. Florence, AZ 85132	152,416
5	9/28-9/30	Midway Environmental Services, Inc.	900536 South 3490 Rd. Chandler, OK 74834	314,429
5	9/28-9/30	Crystal Clean, Bakersfield	1620 E Brundage Ln, Bakersfield, CA 93307	186,686

On-site Extraction and Treatment

Week	Date	Estimated Gallons Extracted*	Estimated Gallons Treated On-Site
1	9/1/26-9/6/26	1,536,877	1,184,818
2	9/7/26-9/13/26	1,814,023	1,378,398
3	9/14/26-9/20/26	1,793,599	1,396,761
4	9/21/26-9/27/26	1,835,012	1,362,784
5	9/28/26-9/30/26	1,207,384	647,232

Attachment M

Leachate Pressure Gauge Readings

4050 - Daily Pressure Gauge Readings

Tom Roe

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	1 Sep 2026 8:22 AM PDT
Prepared by	Tom Roe

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	Tank Not In Use/In Staging Area
SW 07	Tank Not In Use/In Staging Area
SW 06	Tank Not In Use/In Staging Area
SW 05	0.04
SW 04	-0.02
SW 03	-0.05
SW 02	0
SW 01	-0.02
44	0
111	0
LCM 11	-0.12
LCM 12	-0.06
LCM 13	-0.03
LCM 14	-0.16
LCM 15	-0.01
LCM 6	0.05
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.16
LCM 10	-0.12
LCM 1	0.12
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0.10
D2	0.05
CD3	Tank Not In Use/In Staging Area
CD4	Tank Not In Use/In Staging Area
D17	-0.04
D16	0.10
D15	Maintenance Needed
D14	-0.02
D13	0.08
D12	0.25
D11	0.03
D10	0.11
D9	0.09
D8	0.20
D7	0.03
D6	-0.02
D5	0.20
D4	0.25
D3	0.25
D18	Maintenance Needed

D19	-0.01
D20	-0.10
D21	Maintenance Needed
D22	Maintenance Needed
D23	0.07
D24	-0.03
D25	0.13
D26	0.25
D27	-0.02
D28	0.13
D29	Maintenance Needed
D30	0.10
D31	0.12
D32	0.12
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.07
C13-07	-0.05
C13-06	0.03
C13-05	0

C13-04	0.03
C13-03	0
C13-02	0
C13-01	-0.02
C13-09	Tank Not In Use/In Staging Area
C13-10	Tank Not In Use/In Staging Area
C13-11	Tank Not In Use/In Staging Area
C13-12	Tank Not In Use/In Staging Area
C13-13	Tank Not In Use/In Staging Area
C13-14	Tank Not In Use/In Staging Area
C13-15	Tank Not In Use/In Staging Area
C13-16	Tank Not In Use/In Staging Area
T1/T2 190	-0.03
U13-63	-0.02
U13-62	-0.02
U13-61	-0.01
U13-60	Tank Not In Use/In Staging Area
U13-59	Tank Not In Use/In Staging Area
U13-58	0
U13-57	Tank Not In Use/In Staging Area
U13-56	Tank Not In Use/In Staging Area
U13-55	Tank Not In Use/In Staging Area
U13-54	0.21
U13-53	-0.01

U13-52	-0.15
U13-51	-0.02
U13-50	-0.02
U13-49	Tank Not In Use/In Staging Area
U13-48	Tank Not In Use/In Staging Area
U13-47	Tank Not In Use/In Staging Area
U13-46	0
U13-45	0
U13-44	0.03
U13-43	0.01
U13-42	-0.03
U13-41	-0.02
U13-40	0.03
U13-39	0
U13-38	-0.03
U13-37	-0.02
U13-36	-0.02
U13-35	-0.25
U13-34	-0.02
U13-33	-0.04
U13-32	-0.02
U13-31	Tank Not In Use/In Staging Area
U13-30	Tank Not In Use/In Staging Area
U13-29	Tank Not In Use/In Staging Area

U13-28	Tank Not In Use/In Staging Area
U13-27	Tank Not In Use/In Staging Area
U13-26	Tank Not In Use/In Staging Area
U13-25	Tank Not In Use/In Staging Area
U13-24	Tank Not In Use/In Staging Area
U13-23	Tank Not In Use/In Staging Area
U13-22	Tank Not In Use/In Staging Area
U13-21	Tank Not In Use/In Staging Area
U13-20	Tank Not In Use/In Staging Area
U13-19	Tank Not In Use/In Staging Area
U13-18	Maintenance Needed
U13-17	-0.02
U13-16	-0.08
U13-15	-0.13
U13-14	-0.11
U13-13	-0.10
U13-12	-0.08
U13-11	-0.06
U13-10	-0.08
U13-09	-0.05
U13-08	-0.03
U13-07	-0.05
U13-06	-0.02
U13-05	-0.10

U13-04	Maintenance Needed
U13-03	-0.04
U13-02	-0.04
U13-01	-0.09
L13-01	-0.01
L13-02	-0.15
L13-03	-0.02
L13-04	-0.25
L13-05	-0.25
L13-06	-0.16
L13-07	0
L13-08	-0.15
L13-09	-0.16
L13-10	0
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.01
L13-15	-0.25
L13-16	-0.03
L13-17	-0.03
L13-18	-0.03
L13-19	-0.02
L13-20	0

L13-21	-0.03
L13-22	-0.01
L13-23	-0.01
L13-24	-0.02
L13-25	-0.11
L13-26	0
L13-27	-0.10
L13-28	-0.07
L13-29	-0.02
L13-30	-0.06
L13-31	-0.02
L13-32	-0.02
L13-33	0
L13-34	-0.02
L13-35	-0.02
L13-36	-0.02
L13-37	-0.05
L13-38	0
L13-39	0
L13-40	0.02
L13-41	-0.01
L13-42	0.25
L13-43	0.15
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.02
L13-47	-0.02
L13-48	-0.01
L13-49	0
L13-50	-0.01
L13-51	-0.01
L13-52	0
L13-53	-0.02
L13-54	-0.05
L13-55	-0.15
L13-56	-0.25
L13-57	-0.02
L13-58	0
L13-59	-0.01
L13-60	-0.07
L13-61	-0.02
L13-62	0.01
L13-63	0.04
L13-64	0
L13-65	-0.07
L13-66	-0.03
L13-67	-0.01
L13-68	-0.02

L13-69	-0.02
L13-70	-0.01
L13-71	Maintenance Needed
L13-72	-0.05
L13-73	0.05
L13-74	-0.09
L13-75	-0.04
L13-76	0
L13-77	-0.04
L13-78	-0.05
L13-79	-0.03
L13-80	-0.02

Certification



Tom Roe
1 Sep 2026 3:12 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	2 Sep 2026 1:42 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.02
SW 07	-0.02
SW 06	-0.01
SW 05	0.02
SW 04	0
SW 03	-0.06
SW 02	-0.01
SW 01	-0.01
44	0
111	0
LCM 11	-0.10
LCM 12	-0.03
LCM 13	-0.02
LCM 14	-0.10
LCM 15	0
LCM 6	0.02
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.06
LCM 10	-0.05
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	0
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.02
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.05
D12	-0.03
D11	-0.10
D10	-0.02
D9	-0.02
D8	-0.02
D7	0
D6	-0.03
D5	0
D4	-0.01
D3	-0.05
D18	Maintenance Needed

D19	0
D20	-0.12
D21	Maintenance Needed
D22	0
D23	-0.01
D24	0
D25	-0.05
D26	-0.01
D27	0
D28	0.02
D29	Maintenance Needed
D30	-0.01
D31	-0.01
D32	-0.01
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.02
C13-06	-0.01
C13-05	-0.02

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.03
C13-09	-0.25
C13-10	0
C13-11	0
C13-12	-0.07
C13-13	-0.01
C13-14	-0.07
C13-15	-0.05
C13-16	-0.06
T1/T2 190	-0.05
U13-63	-0.03
U13-62	-0.02
U13-61	0
U13-60	-0.01
U13-59	0
U13-58	0
U13-57	-0.01
U13-56	0
U13-55	-0.05
U13-54	0
U13-53	-0.05

U13-52	-0.15
U13-51	-0.01
U13-50	-0.01
U13-49	-0.02
U13-48	-0.07
U13-47	-0.05
U13-46	0
U13-45	-0.02
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.02
U13-40	-0.01
U13-39	0
U13-38	0
U13-37	-0.01
U13-36	-0.02
U13-35	-0.02
U13-34	-0.05
U13-33	-0.07
U13-32	-0.04
U13-31	-0.12
U13-30	-0.01
U13-29	-0.04

U13-28	0.01
U13-27	0.25
U13-26	Maintenance Needed
U13-25	-0.10
U13-24	-0.06
U13-23	-0.07
U13-22	-0.11
U13-21	-0.10
U13-20	-0.05
U13-19	-0.07
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	0
U13-05	-0.06

U13-04	Maintenance Needed
U13-03	-0.02
U13-02	-0.01
U13-01	-0.10
L13-01	-0.05
L13-02	-0.10
L13-03	-0.01
L13-04	-0.25
L13-05	-0.25
L13-06	-0.25
L13-07	-0.05
L13-08	-0.25
L13-09	-0.25
L13-10	0.05
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.03
L13-14	-0.01
L13-15	-0.25
L13-16	-0.03
L13-17	-0.03
L13-18	-0.01
L13-19	-0.01
L13-20	-0.01

L13-21	-0.02
L13-22	0
L13-23	0
L13-24	-0.02
L13-25	-0.20
L13-26	-0.01
L13-27	-0.20
L13-28	-0.19
L13-29	-0.02
L13-30	-0.06
L13-31	-0.04
L13-32	-0.02
L13-33	-0.02
L13-34	-0.01
L13-35	-0.01
L13-36	-0.02
L13-37	-0.06
L13-38	-0.02
L13-39	-0.02
L13-40	0
L13-41	-0.01
L13-42	-0.01
L13-43	-0.01
L13-44	Maintenance Needed

L13-45	0.01
L13-46	-0.01
L13-47	-0.01
L13-48	0
L13-49	0
L13-50	0
L13-51	-0.01
L13-52	0
L13-53	-0.01
L13-54	-0.20
L13-55	-0.20
L13-56	-0.25
L13-57	-0.02
L13-58	-0.10
L13-59	-0.12
L13-60	-0.19
L13-61	-0.12
L13-62	0
L13-63	-0.11
L13-64	0
L13-65	-0.06
L13-66	-0.02
L13-67	-0.01
L13-68	-0.01

L13-69	0
L13-70	0
L13-71	Maintenance Needed
L13-72	-0.02
L13-73	-0.06
L13-74	-0.12
L13-75	-0.05
L13-76	0
L13-77	-0.01
L13-78	-0.05
L13-79	-0.01
L13-80	-0.05

Certification



Nancy Bahena Hernandez
2 Sep 2026 3:38 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	3 Sep 2026 2:01 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.02
SW 07	-0.02
SW 06	-0.01
SW 05	0.05
SW 04	0
SW 03	-0.05
SW 02	0
SW 01	-0.01
44	0
111	0
LCM 11	-0.10
LCM 12	-0.03
LCM 13	-0.01
LCM 14	-0.06
LCM 15	0
LCM 6	0.02
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	0
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	-0.25
D7	-0.25
D6	-0.25
D5	-0.25
D4	-0.04
D3	-0.25
D18	Maintenance Needed

D19	0.07
D20	-0.10
D21	Maintenance Needed
D22	-0.10
D23	-0.25
D24	-0.01
D25	-0.25
D26	-0.25
D27	0
D28	-0.10
D29	Maintenance Needed
D30	-0.15
D31	-0.25
D32	0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.02
C13-06	-0.02
C13-05	-0.02

C13-04	0
C13-03	-0.02
C13-02	0
C13-01	0
C13-09	-0.22
C13-10	0
C13-11	0
C13-12	-0.07
C13-13	-0.01
C13-14	-0.07
C13-15	-0.05
C13-16	-0.05
T1/T2 190	-0.05
U13-63	-0.05
U13-62	-0.05
U13-61	0
U13-60	0
U13-59	-0.01
U13-58	0
U13-57	-0.02
U13-56	-0.01
U13-55	-0.04
U13-54	-0.02
U13-53	0

U13-52	-0.15
U13-51	-0.02
U13-50	-0.01
U13-49	-0.02
U13-48	-0.05
U13-47	-0.04
U13-46	-0.02
U13-45	-0.02
U13-44	-0.05
U13-43	0
U13-42	0
U13-41	0
U13-40	-0.01
U13-39	0
U13-38	-0.01
U13-37	0
U13-36	-0.07
U13-35	-0.07
U13-34	-0.07
U13-33	-0.07
U13-32	-0.02
U13-31	-0.07
U13-30	-0.02
U13-29	-0.05

U13-28	-0.02
U13-27	-0.02
U13-26	Maintenance Needed
U13-25	-0.04
U13-24	-0.01
U13-23	-0.05
U13-22	-0.06
U13-21	-0.10
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.02
U13-05	-0.10

U13-04	Maintenance Needed
U13-03	-0.05
U13-02	-0.05
U13-01	-0.10
L13-01	-0.02
L13-02	-0.07
L13-03	0
L13-04	-0.25
L13-05	-0.25
L13-06	-0.25
L13-07	-0.05
L13-08	-0.16
L13-09	-0.23
L13-10	0.01
L13-11	Maintenance Needed
L13-12	-0.12
L13-13	-0.02
L13-14	-0.02
L13-15	-0.25
L13-16	-0.04
L13-17	-0.05
L13-18	-0.03
L13-19	-0.01
L13-20	-0.01

L13-21	-0.02
L13-22	0
L13-23	-0.01
L13-24	-0.01
L13-25	-0.17
L13-26	0
L13-27	-0.15
L13-28	-0.16
L13-29	-0.02
L13-30	-0.05
L13-31	-0.05
L13-32	-0.02
L13-33	-0.02
L13-34	-0.02
L13-35	-0.05
L13-36	-0.05
L13-37	-0.10
L13-38	-0.02
L13-39	-0.02
L13-40	0
L13-41	-0.02
L13-42	-0.01
L13-43	-0.02
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.02
L13-47	-0.01
L13-48	0
L13-49	0.01
L13-50	0.05
L13-51	-0.01
L13-52	0
L13-53	-0.05
L13-54	-0.15
L13-55	-0.16
L13-56	-0.25
L13-57	-0.03
L13-58	-0.15
L13-59	-0.15
L13-60	-0.20
L13-61	-0.15
L13-62	0
L13-63	-0.11
L13-64	0
L13-65	-0.06
L13-66	-0.01
L13-67	-0.01
L13-68	-0.02

L13-69	0.01
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.05
L13-73	-0.07
L13-74	-0.11
L13-75	-0.02
L13-76	0
L13-77	-0.02
L13-78	-0.05
L13-79	-0.04
L13-80	-0.03

Certification



Nancy Bahena Hernandez
3 Sep 2026 3:25 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	4 Sep 2026 1:48 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.03
SW 06	0
SW 05	0.02
SW 04	0
SW 03	-0.05
SW 02	-0.01
SW 01	-0.01
44	0
111	-0.05
LCM 11	-0.10
LCM 12	-0.03
LCM 13	-0.01
LCM 14	-0.10
LCM 15	0
LCM 6	0.05
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.01
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.15
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.04
D16	-0.20
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.22
D12	0
D11	-0.25
D10	-0.20
D9	-0.15
D8	Maintenance Needed
D7	-0.02
D6	-0.14
D5	-0.15
D4	-0.02
D3	-0.15
D18	Maintenance Needed

D19	0
D20	-0.10
D21	Maintenance Needed
D22	-0.01
D23	-0.12
D24	-0.02
D25	-0.25
D26	-0.23
D27	0
D28	-0.15
D29	Maintenance Needed
D30	-0.10
D31	-0.20
D32	-0.10
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.06
C13-07	-0.01
C13-06	-0.01
C13-05	-0.01

C13-04	-0.01
C13-03	0
C13-02	-0.01
C13-01	-0.04
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.15
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.01
U13-62	-0.01
U13-61	0
U13-60	0
U13-59	0
U13-58	0
U13-57	-0.02
U13-56	-0.01
U13-55	-0.04
U13-54	-0.10
U13-53	-0.02

U13-52	-0.15
U13-51	-0.01
U13-50	0
U13-49	-0.02
U13-48	-0.07
U13-47	-0.02
U13-46	0
U13-45	-0.01
U13-44	0
U13-43	0
U13-42	-0.01
U13-41	-0.01
U13-40	0
U13-39	0
U13-38	-0.01
U13-37	0
U13-36	-0.16
U13-35	-0.15
U13-34	-0.17
U13-33	-0.05
U13-32	-0.03
U13-31	-0.01
U13-30	-0.03
U13-29	-0.02

U13-28	0.25
U13-27	Maintenance Needed
U13-26	0.25
U13-25	0.25
U13-24	0.25
U13-23	-0.01
U13-22	-0.10
U13-21	-0.07
U13-20	-0.05
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	0
U13-05	-0.12

U13-04	Maintenance Needed
U13-03	-0.12
U13-02	-0.12
U13-01	-0.25
L13-01	-0.02
L13-02	-0.12
L13-03	-0.02
L13-04	-0.25
L13-05	-0.25
L13-06	-0.20
L13-07	-0.06
L13-08	-0.20
L13-09	-0.23
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.01
L13-14	-0.02
L13-15	-0.25
L13-16	-0.07
L13-17	-0.10
L13-18	-0.10
L13-19	-0.08
L13-20	-0.07

L13-21	-0.10
L13-22	-0.05
L13-23	-0.06
L13-24	-0.10
L13-25	-0.20
L13-26	-0.06
L13-27	-0.20
L13-28	-0.20
L13-29	-0.10
L13-30	-0.25
L13-31	-0.22
L13-32	-0.05
L13-33	-0.07
L13-34	-0.05
L13-35	-0.02
L13-36	0.25
L13-37	-0.07
L13-38	-0.04
L13-39	-0.01
L13-40	-0.02
L13-41	-0.01
L13-42	-0.05
L13-43	-0.03
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.02
L13-47	-0.02
L13-48	-0.02
L13-49	-0.02
L13-50	-0.03
L13-51	0
L13-52	0
L13-53	-0.02
L13-54	-0.17
L13-55	-0.17
L13-56	-0.25
L13-57	-0.02
L13-58	-0.16
L13-59	-0.15
L13-60	-0.22
L13-61	-0.17
L13-62	0
L13-63	-0.10
L13-64	-0.02
L13-65	-0.06
L13-66	-0.01
L13-67	0
L13-68	-0.05

L13-69	-0.05
L13-70	-0.02
L13-71	Maintenance Needed
L13-72	-0.07
L13-73	-0.11
L13-74	-0.15
L13-75	-0.07
L13-76	-0.07
L13-77	-0.02
L13-78	-0.07
L13-79	-0.05
L13-80	-0.10

Certification



Nancy Bahena Hernandez
4 Sep 2026 3:18 PM PDT

4050 - Daily Pressure Gauge Readings

John Boucher

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	Marked as ‘my site is not listed here’
Conducted on	5 Sep 2026 7:31 AM PDT
Prepared by	John Boucher

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.02
SW 06	0
SW 05	0.01
SW 04	0
SW 03	-0.05
SW 02	0
SW 01	0
44	0
111	-0.05
LCM 11	-0.10
LCM 12	-0.04
LCM 13	-0.01
LCM 14	-0.10
LCM 15	0
LCM 6	0.05
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	0
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.14
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.19
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.20
D12	0
D11	-0.25
D10	-0.19
D9	-0.13
D8	Maintenance Needed
D7	-0.01
D6	-0.15
D5	-0.15
D4	0
D3	-0.13
D18	Maintenance Needed

D19	-0.01
D20	-0.09
D21	Maintenance Needed
D22	0
D23	-0.10
D24	-0.01
D25	-0.25
D26	-0.25
D27	0
D28	-0.14
D29	Maintenance Needed
D30	-0.09
D31	-0.19
D32	-0.11
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.02
C13-06	-0.02
C13-05	-0.02

C13-04	-0.02
C13-03	0
C13-02	-0.02
C13-01	-0.05
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.15
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	0
U13-62	-0.02
U13-61	0
U13-60	-0.01
U13-59	0
U13-58	-0.01
U13-57	-0.01
U13-56	-0.01
U13-55	-0.05
U13-54	-0.10
U13-53	-0.03

U13-52	-0.15
U13-51	-0.02
U13-50	0
U13-49	-0.03
U13-48	-0.06
U13-47	-0.03
U13-46	0
U13-45	-0.02
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.01
U13-40	-0.01
U13-39	-0.01
U13-38	-0.01
U13-37	-0.01
U13-36	-0.15
U13-35	-0.15
U13-34	-0.15
U13-33	-0.06
U13-32	-0.05
U13-31	-0.03
U13-30	-0.03
U13-29	-0.03

U13-28	0.25
U13-27	Maintenance Needed
U13-26	0.25
U13-25	0.25
U13-24	0.25
U13-23	-0.02
U13-22	-0.10
U13-21	-0.05
U13-20	-0.05
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	0
U13-05	-0.10

U13-04	Maintenance Needed
U13-03	-0.10
U13-02	-0.10
U13-01	-0.25
L13-01	-0.04
L13-02	-0.11
L13-03	-0.01
L13-04	-0.25
L13-05	-0.25
L13-06	-0.20
L13-07	-0.05
L13-08	-0.20
L13-09	-0.25
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	0
L13-14	-0.03
L13-15	-0.25
L13-16	-0.05
L13-17	-0.10
L13-18	-0.10
L13-19	-0.10
L13-20	-0.08

L13-21	-0.10
L13-22	-0.05
L13-23	-0.05
L13-24	-0.10
L13-25	-0.20
L13-26	-0.05
L13-27	-0.20
L13-28	-0.20
L13-29	-0.10
L13-30	-0.25
L13-31	-0.20
L13-32	-0.05
L13-33	-0.06
L13-34	-0.05
L13-35	-0.03
L13-36	0.25
L13-37	-0.05
L13-38	-0.05
L13-39	0
L13-40	-0.01
L13-41	-0.01
L13-42	-0.05
L13-43	-0.04
L13-44	Maintenance Needed

L13-45	-0.03
L13-46	-0.03
L13-47	-0.03
L13-48	-0.03
L13-49	-0.03
L13-50	-0.03
L13-51	0
L13-52	0
L13-53	-0.03
L13-54	-0.15
L13-55	-0.15
L13-56	-0.25
L13-57	-0.01
L13-58	-0.15
L13-59	-0.15
L13-60	-0.20
L13-61	-0.17
L13-62	0
L13-63	-0.10
L13-64	-0.01
L13-65	-0.05
L13-66	0
L13-67	0
L13-68	-0.06

L13-69	-0.05
L13-70	-0.03
L13-71	Maintenance Needed
L13-72	-0.06
L13-73	-0.10
L13-74	-0.15
L13-75	-0.09
L13-76	-0.06
L13-77	0
L13-78	-0.05
L13-79	-0.05
L13-80	-0.10

Certification



John Boucher
5 Sep 2026 12:10 PM PDT

4050 - Daily Pressure Gauge Readings

John Boucher

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	Marked as ‘my site is not listed here’
Conducted on	6 Sep 2026 8:27 AM PDT
Prepared by	John Boucher

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	0
SW 06	0
SW 05	0
SW 04	0
SW 03	-0.05
SW 02	0
SW 01	0
44	0
111	-0.06
LCM 11	-0.09
LCM 12	-0.05
LCM 13	0
LCM 14	-0.10
LCM 15	0
LCM 6	0.05
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	0
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.12
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.04
D16	-0.20
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.20
D12	0
D11	-0.25
D10	-0.18
D9	-0.10
D8	Maintenance Needed
D7	0
D6	-0.13
D5	-0.15
D4	0
D3	-0.15
D18	Maintenance Needed

D19	-0.01
D20	-0.10
D21	Maintenance Needed
D22	0
D23	-0.10
D24	0
D25	-0.25
D26	-0.25
D27	0
D28	-0.15
D29	Maintenance Needed
D30	-0.10
D31	-0.20
D32	-0.10
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.01
C13-06	-0.01
C13-05	-0.01

C13-04	-0.01
C13-03	0
C13-02	-0.01
C13-01	-0.03
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.16
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	0
U13-62	-0.01
U13-61	0
U13-60	0
U13-59	0
U13-58	0
U13-57	0
U13-56	0
U13-55	-0.05
U13-54	-0.10
U13-53	-0.02

U13-52	-0.14
U13-51	-0.01
U13-50	0
U13-49	-0.02
U13-48	-0.05
U13-47	-0.02
U13-46	0
U13-45	-0.01
U13-44	0
U13-43	-0.01
U13-42	-0.01
U13-41	-0.01
U13-40	-0.01
U13-39	-0.01
U13-38	-0.01
U13-37	-0.01
U13-36	-0.15
U13-35	-0.15
U13-34	-0.15
U13-33	-0.05
U13-32	-0.05
U13-31	-0.04
U13-30	-0.04
U13-29	-0.03

U13-28	0.25
U13-27	Maintenance Needed
U13-26	0.25
U13-25	0.25
U13-24	0.25
U13-23	-0.01
U13-22	-0.10
U13-21	-0.05
U13-20	-0.05
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	0
U13-05	-0.10

U13-04	Maintenance Needed
U13-03	-0.10
U13-02	-0.10
U13-01	-0.25
L13-01	-0.05
L13-02	-0.10
L13-03	0
L13-04	-0.25
L13-05	-0.25
L13-06	-0.20
L13-07	-0.05
L13-08	-0.20
L13-09	-0.25
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	0
L13-14	-0.04
L13-15	-0.25
L13-16	-0.04
L13-17	-0.08
L13-18	-0.09
L13-19	-0.10
L13-20	-0.07

L13-21	-0.09
L13-22	-0.04
L13-23	-0.05
L13-24	-0.10
L13-25	-0.20
L13-26	-0.05
L13-27	-0.20
L13-28	-0.20
L13-29	-0.10
L13-30	-0.25
L13-31	-0.21
L13-32	-0.06
L13-33	-0.05
L13-34	-0.05
L13-35	-0.02
L13-36	0.25
L13-37	-0.04
L13-38	-0.04
L13-39	0
L13-40	0
L13-41	-0.01
L13-42	-0.05
L13-43	-0.05
L13-44	Maintenance Needed

L13-45	-0.04
L13-46	-0.03
L13-47	-0.04
L13-48	-0.04
L13-49	-0.03
L13-50	-0.03
L13-51	0
L13-52	0
L13-53	-0.02
L13-54	-0.15
L13-55	-0.15
L13-56	-0.25
L13-57	0
L13-58	-0.13
L13-59	-0.15
L13-60	-0.20
L13-61	-0.16
L13-62	0
L13-63	-0.10
L13-64	-0.02
L13-65	-0.05
L13-66	0
L13-67	0
L13-68	-0.05

L13-69	-0.05
L13-70	-0.04
L13-71	Maintenance Needed
L13-72	-0.05
L13-73	-0.10
L13-74	-0.15
L13-75	-0.10
L13-76	-0.05
L13-77	0
L13-78	-0.05
L13-79	-0.05
L13-80	-0.10

Certification



John Boucher
6 Sep 2026 12:00 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	7 Sep 2026 8:48 AM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	-0.02
SW 07	-0.04
SW 06	-0.02
SW 05	0.02
SW 04	-0.03
SW 03	-0.06
SW 02	-0.01
SW 01	-0.05
44	-0.01
111	0
LCM 11	-0.04
LCM 12	-0.01
LCM 13	-0.02
LCM 14	-0.05
LCM 15	-0.01
LCM 6	-0.02
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.06
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.05
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.04
D16	-0.03
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.05
D12	0.25
D11	-0.10
D10	-0.02
D9	-0.05
D8	Maintenance Needed
D7	0
D6	-0.05
D5	-0.02
D4	-0.05
D3	0.07
D18	Maintenance Needed

D19	0
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.02
D24	-0.02
D25	-0.07
D26	0
D27	0
D28	0
D29	Maintenance Needed
D30	-0.05
D31	-0.06
D32	-0.05
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	0
C13-06	-0.01
C13-05	-0.01

C13-04	0.02
C13-03	0
C13-02	0
C13-01	-0.02
C13-09	0.10
C13-10	0.25
C13-11	0.25
C13-12	0.05
C13-13	0.25
C13-14	0.25
C13-15	0.25
C13-16	0.25
T1/T2 190	0.25
U13-63	-0.01
U13-62	-0.01
U13-61	0
U13-60	0
U13-59	0
U13-58	0
U13-57	0
U13-56	0
U13-55	-0.03
U13-54	-0.20
U13-53	-0.05

U13-52	-0.15
U13-51	0
U13-50	0
U13-49	0
U13-48	-0.10
U13-47	-0.01
U13-46	0
U13-45	0
U13-44	0
U13-43	0
U13-42	-0.01
U13-41	-0.01
U13-40	-0.05
U13-39	0
U13-38	0
U13-37	-0.03
U13-36	-0.01
U13-35	-0.02
U13-34	-0.03
U13-33	-0.05
U13-32	-0.05
U13-31	-0.05
U13-30	-0.05
U13-29	-0.05

U13-28	-0.02
U13-27	-0.05
U13-26	Maintenance Needed
U13-25	0.25
U13-24	0.25
U13-23	-0.01
U13-22	-0.11
U13-21	-0.16
U13-20	-0.07
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.01
U13-05	-0.23

U13-04	Maintenance Needed
U13-03	-0.07
U13-02	-0.07
U13-01	-0.01
L13-01	0
L13-02	-0.25
L13-03	-0.02
L13-04	-0.12
L13-05	-0.15
L13-06	-0.25
L13-07	0
L13-08	-0.17
L13-09	-0.25
L13-10	0.01
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.01
L13-14	-0.01
L13-15	-0.25
L13-16	0.25
L13-17	-0.01
L13-18	-0.01
L13-19	0
L13-20	-0.01

L13-21	-0.01
L13-22	-0.01
L13-23	0
L13-24	-0.01
L13-25	-0.20
L13-26	0
L13-27	-0.20
L13-28	-0.25
L13-29	-0.01
L13-30	-0.04
L13-31	-0.02
L13-32	-0.01
L13-33	-0.02
L13-34	-0.02
L13-35	-0.01
L13-36	-0.03
L13-37	-0.06
L13-38	-0.01
L13-39	-0.01
L13-40	0
L13-41	-0.01
L13-42	-0.01
L13-43	-0.03
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.01
L13-47	-0.02
L13-48	-0.02
L13-49	-0.02
L13-50	-0.01
L13-51	-0.01
L13-52	0.01
L13-53	-0.01
L13-54	-0.20
L13-55	-0.20
L13-56	-0.15
L13-57	-0.02
L13-58	-0.20
L13-59	-0.20
L13-60	-0.25
L13-61	-0.20
L13-62	0
L13-63	-0.20
L13-64	-0.01
L13-65	-0.05
L13-66	-0.01
L13-67	-0.01
L13-68	0

L13-69	0.01
L13-70	0
L13-71	Maintenance Needed
L13-72	-0.03
L13-73	-0.17
L13-74	-0.17
L13-75	-0.02
L13-76	0.01
L13-77	0
L13-78	-0.12
L13-79	-0.10
L13-80	-0.03

Certification



Nancy Bahena Hernandez
7 Sep 2026 2:53 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	8 Sep 2026 10:02 AM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.02
SW 06	-0.01
SW 05	0.02
SW 04	-0.01
SW 03	-0.07
SW 02	0
SW 01	-0.07
44	0
111	-0.01
LCM 11	-0.09
LCM 12	-0.05
LCM 13	-0.02
LCM 14	-0.12
LCM 15	0
LCM 6	0.04
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.12
LCM 10	-0.05
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.11
CD3	Tank Not In Use/In Staging Area
CD4	Tank Not In Use/In Staging Area
D17	-0.03
D16	-0.12
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.12
D12	-0.07
D11	-0.20
D10	-0.10
D9	-0.07
D8	Maintenance Needed
D7	0.01
D6	-0.07
D5	-0.08
D4	-0.01
D3	-0.09
D18	Maintenance Needed

D19	0.01
D20	-0.10
D21	Maintenance Needed
D22	0
D23	-0.25
D24	0.25
D25	-0.17
D26	-0.16
D27	-0.01
D28	-0.10
D29	Maintenance Needed
D30	-0.13
D31	-0.15
D32	-0.17
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	Tank Not In Use/In Staging Area
C13-07	Tank Not In Use/In Staging Area
C13-06	Tank Not In Use/In Staging Area
C13-05	Tank Not In Use/In Staging Area

C13-04	Tank Not In Use/In Staging Area
C13-03	Tank Not In Use/In Staging Area
C13-02	Tank Not In Use/In Staging Area
C13-01	Tank Not In Use/In Staging Area
C13-09	-0.25
C13-10	-0.19
C13-11	-0.20
C13-12	-0.09
C13-13	-0.19
C13-14	-0.23
C13-15	-0.20
C13-16	-0.20
T1/T2 190	-0.22
U13-63	-0.02
U13-62	-0.02
U13-61	-0.02
U13-60	Tank Not In Use/In Staging Area
U13-59	Tank Not In Use/In Staging Area
U13-58	0
U13-57	Tank Not In Use/In Staging Area
U13-56	Tank Not In Use/In Staging Area
U13-55	Tank Not In Use/In Staging Area
U13-54	0.06
U13-53	-0.02

U13-52	-0.15
U13-51	-0.03
U13-50	-0.02
U13-49	Tank Not In Use/In Staging Area
U13-48	Tank Not In Use/In Staging Area
U13-47	Tank Not In Use/In Staging Area
U13-46	-0.02
U13-45	-0.02
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.03
U13-40	0
U13-39	-0.01
U13-38	-0.02
U13-37	-0.02
U13-36	-0.03
U13-35	-0.07
U13-34	-0.06
U13-33	-0.05
U13-32	-0.05
U13-31	-0.13
U13-30	-0.18
U13-29	-0.18

U13-28	-0.16
U13-27	-0.18
U13-26	Maintenance Needed
U13-25	-0.21
U13-24	-0.19
U13-23	-0.20
U13-22	-0.22
U13-21	-0.22
U13-20	-0.17
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	-0.04
U13-16	-0.05
U13-15	-0.13
U13-14	-0.11
U13-13	-0.10
U13-12	-0.09
U13-11	-0.07
U13-10	-0.08
U13-09	-0.04
U13-08	-0.02
U13-07	-0.02
U13-06	-0.01
U13-05	-0.17

U13-04	Maintenance Needed
U13-03	-0.09
U13-02	-0.06
U13-01	-0.19
L13-01	-0.02
L13-02	-0.09
L13-03	-0.02
L13-04	0
L13-05	-0.10
L13-06	-0.16
L13-07	-0.03
L13-08	-0.09
L13-09	-0.15
L13-10	0.05
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.01
L13-15	-0.24
L13-16	-0.06
L13-17	-0.04
L13-18	-0.05
L13-19	-0.03
L13-20	-0.02

L13-21	-0.05
L13-22	-0.03
L13-23	-0.03
L13-24	-0.02
L13-25	-0.09
L13-26	0.02
L13-27	-0.05
L13-28	-0.11
L13-29	-0.02
L13-30	0
L13-31	-0.06
L13-32	-0.03
L13-33	-0.03
L13-34	-0.02
L13-35	-0.02
L13-36	-0.05
L13-37	-0.05
L13-38	-0.01
L13-39	-0.02
L13-40	-0.01
L13-41	-0.04
L13-42	-0.10
L13-43	-0.06
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.03
L13-47	-0.02
L13-48	-0.02
L13-49	-0.02
L13-50	-0.01
L13-51	0
L13-52	0
L13-53	-0.02
L13-54	-0.05
L13-55	-0.08
L13-56	-0.01
L13-57	-0.02
L13-58	-0.06
L13-59	-0.08
L13-60	-0.13
L13-61	-0.11
L13-62	0.02
L13-63	-0.06
L13-64	0
L13-65	-0.03
L13-66	-0.02
L13-67	0
L13-68	-0.02

L13-69	-0.03
L13-70	-0.02
L13-71	Maintenance Needed
L13-72	-0.04
L13-73	-0.04
L13-74	-0.03
L13-75	-0.04
L13-76	-0.02
L13-77	-0.01
L13-78	-0.04
L13-79	0
L13-80	-0.05

Certification



Tom Roe
8 Sep 2026 3:20 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	9 Sep 2026 9:46 AM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.02
SW 06	-0.02
SW 05	0.03
SW 04	-0.02
SW 03	-0.05
SW 02	-0.01
SW 01	-0.05
44	0
111	0
LCM 11	-0.10
LCM 12	-0.04
LCM 13	-0.02
LCM 14	-0.15
LCM 15	0
LCM 6	0.04
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.16
LCM 10	-0.15
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.12
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.04
D16	-0.15
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.14
D12	0.10
D11	-0.20
D10	-0.09
D9	-0.11
D8	-0.02
D7	0
D6	-0.10
D5	-0.10
D4	0.10
D3	0.02
D18	Maintenance Needed

D19	0
D20	-0.10
D21	Maintenance Needed
D22	0.15
D23	-0.05
D24	-0.02
D25	-0.12
D26	-0.02
D27	0
D28	-0.10
D29	Maintenance Needed
D30	-0.11
D31	-0.16
D32	-0.15
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.04
C13-07	-0.05
C13-06	-0.02
C13-05	-0.05

C13-04	0.01
C13-03	0
C13-02	0.02
C13-01	0.01
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.10
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	0
U13-62	-0.01
U13-61	0
U13-60	0
U13-59	0
U13-58	0
U13-57	-0.01
U13-56	-0.01
U13-55	-0.04
U13-54	-0.05
U13-53	0

U13-52	-0.15
U13-51	0
U13-50	-0.01
U13-49	0
U13-48	-0.07
U13-47	-0.01
U13-46	0
U13-45	0
U13-44	0.05
U13-43	-0.01
U13-42	-0.01
U13-41	-0.01
U13-40	0
U13-39	0.01
U13-38	-0.01
U13-37	0
U13-36	-0.05
U13-35	0
U13-34	-0.03
U13-33	-0.03
U13-32	-0.02
U13-31	-0.11
U13-30	-0.25
U13-29	-0.24

U13-28	-0.20
U13-27	-0.23
U13-26	Maintenance Needed
U13-25	-0.25
U13-24	-0.21
U13-23	-0.20
U13-22	-0.25
U13-21	-0.25
U13-20	-0.25
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	0
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	-0.11
U13-02	-0.05
U13-01	-0.25
L13-01	0
L13-02	-0.11
L13-03	-0.01
L13-04	-0.15
L13-05	-0.25
L13-06	-0.22
L13-07	-0.02
L13-08	-0.15
L13-09	-0.16
L13-10	0.01
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	0
L13-14	0
L13-15	-0.25
L13-16	-0.02
L13-17	0.05
L13-18	0.05
L13-19	0.05
L13-20	0.24

L13-21	0.10
L13-22	0.05
L13-23	0
L13-24	-0.02
L13-25	-0.15
L13-26	0
L13-27	-0.15
L13-28	-0.15
L13-29	-0.02
L13-30	-0.03
L13-31	0.04
L13-32	-0.02
L13-33	0
L13-34	-0.01
L13-35	0
L13-36	0.10
L13-37	-0.05
L13-38	0
L13-39	0
L13-40	0.10
L13-41	0
L13-42	-0.04
L13-43	-0.06
L13-44	Maintenance Needed

L13-45	0
L13-46	0
L13-47	0
L13-48	0
L13-49	0
L13-50	0
L13-51	0
L13-52	0.01
L13-53	-0.01
L13-54	-0.12
L13-55	-0.15
L13-56	-0.06
L13-57	-0.01
L13-58	-0.15
L13-59	-0.15
L13-60	-0.20
L13-61	-0.17
L13-62	0.01
L13-63	-0.13
L13-64	-0.01
L13-65	-0.06
L13-66	-0.01
L13-67	0
L13-68	-0.01

L13-69	-0.01
L13-70	0
L13-71	Maintenance Needed
L13-72	-0.01
L13-73	-0.15
L13-74	-0.15
L13-75	-0.02
L13-76	0
L13-77	-0.03
L13-78	-0.20
L13-79	-0.17
L13-80	0

Certification



Nancy Bahena Hernandez
9 Sep 2026 2:13 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	10 Sep 2026 10:19 AM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.01
SW 06	-0.01
SW 05	0.05
SW 04	-0.02
SW 03	-0.05
SW 02	0
SW 01	-0.05
44	0
111	0
LCM 11	-0.10
LCM 12	-0.05
LCM 13	-0.02
LCM 14	-0.12
LCM 15	-0.01
LCM 6	0.02
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.10
LCM 10	-0.12
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.03
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.02
D6	-0.25
D5	-0.25
D4	-0.01
D3	-0.25
D18	Maintenance Needed

D19	0.05
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.22
D24	0
D25	-0.25
D26	-0.25
D27	0
D28	0.01
D29	Maintenance Needed
D30	-0.10
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	Tank Not In Use/In Staging Area
C13-07	Tank Not In Use/In Staging Area
C13-06	Tank Not In Use/In Staging Area
C13-05	Tank Not In Use/In Staging Area

C13-04	Tank Not In Use/In Staging Area
C13-03	Tank Not In Use/In Staging Area
C13-02	Tank Not In Use/In Staging Area
C13-01	Tank Not In Use/In Staging Area
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.10
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	0
U13-62	-0.01
U13-61	0
U13-60	0
U13-59	0.01
U13-58	0.01
U13-57	0
U13-56	0
U13-55	-0.01
U13-54	0.01
U13-53	0

U13-52	-0.15
U13-51	0
U13-50	-0.01
U13-49	0
U13-48	-0.05
U13-47	-0.01
U13-46	0
U13-45	0
U13-44	0
U13-43	0.01
U13-42	0
U13-41	0
U13-40	0
U13-39	0
U13-38	-0.01
U13-37	-0.02
U13-36	-0.07
U13-35	-0.05
U13-34	-0.07
U13-33	-0.10
U13-32	-0.05
U13-31	-0.25
U13-30	-0.25
U13-29	-0.25

U13-28	-0.25
U13-27	-0.25
U13-26	Maintenance Needed
U13-25	-0.25
U13-24	Maintenance Needed
U13-23	0.25
U13-22	Maintenance Needed
U13-21	0.25
U13-20	-0.25
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.04
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	-0.01
U13-02	-0.10
U13-01	-0.25
L13-01	0
L13-02	-0.15
L13-03	0
L13-04	-0.05
L13-05	-0.24
L13-06	-0.25
L13-07	-0.02
L13-08	-0.20
L13-09	-0.25
L13-10	0.02
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.01
L13-14	-0.01
L13-15	-0.25
L13-16	-0.05
L13-17	-0.05
L13-18	-0.03
L13-19	-0.02
L13-20	0

L13-21	-0.05
L13-22	-0.02
L13-23	-0.02
L13-24	-0.05
L13-25	-0.22
L13-26	0
L13-27	-0.20
L13-28	-0.22
L13-29	-0.02
L13-30	-0.03
L13-31	-0.03
L13-32	-0.02
L13-33	-0.02
L13-34	-0.02
L13-35	-0.02
L13-36	-0.03
L13-37	-0.03
L13-38	-0.02
L13-39	0.02
L13-40	0.02
L13-41	0
L13-42	0
L13-43	-0.02
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.01
L13-47	-0.01
L13-48	-0.02
L13-49	-0.02
L13-50	-0.02
L13-51	-0.02
L13-52	0.01
L13-53	0
L13-54	-0.20
L13-55	-0.20
L13-56	-0.10
L13-57	-0.01
L13-58	-0.15
L13-59	-0.20
L13-60	-0.20
L13-61	-0.25
L13-62	0
L13-63	-0.25
L13-64	-0.01
L13-65	-0.07
L13-66	-0.01
L13-67	-0.01
L13-68	-0.02

L13-69	0.01
L13-70	-0.01
L13-71	Maintenance Needed
L13-72	-0.03
L13-73	-0.20
L13-74	-0.15
L13-75	-0.05
L13-76	0
L13-77	-0.02
L13-78	-0.15
L13-79	-0.13
L13-80	-0.02

Certification



Nancy Bahena Hernandez
10 Sep 2026 3:47 PM PDT

4050 - Daily Pressure Gauge Readings

John Boucher

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	Marked as ‘my site is not listed here’
Conducted on	11 Sep 2026 7:18 AM PDT
Prepared by	John Boucher

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	0
SW 06	0
SW 05	0.04
SW 04	-0.01
SW 03	-0.04
SW 02	-0.01
SW 01	-0.04
44	-0.01
111	-0.01
LCM 11	-0.09
LCM 12	-0.04
LCM 13	-0.01
LCM 14	-0.10
LCM 15	-0.01
LCM 6	-0.01
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.08
LCM 10	-0.10
LCM 1	Maintenance Needed
LCM 2	-0.24

LCM 3	-0.24
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.02
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.01
D6	-0.25
D5	-0.25
D4	-0.02
D3	-0.25
D18	Maintenance Needed

D19	0.04
D20	-0.09
D21	Maintenance Needed
D22	0.25
D23	-0.20
D24	0
D25	-0.25
D26	-0.25
D27	0
D28	0
D29	Maintenance Needed
D30	-0.09
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	Tank Not In Use/In Staging Area
C13-07	Tank Not In Use/In Staging Area
C13-06	Tank Not In Use/In Staging Area
C13-05	Tank Not In Use/In Staging Area

C13-04	Tank Not In Use/In Staging Area
C13-03	Tank Not In Use/In Staging Area
C13-02	Tank Not In Use/In Staging Area
C13-01	Tank Not In Use/In Staging Area
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.10
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	0
U13-62	0
U13-61	0
U13-60	0
U13-59	-0.01
U13-58	-0.01
U13-57	0
U13-56	0
U13-55	-0.02
U13-54	-0.01
U13-53	0

U13-52	-0.15
U13-51	0
U13-50	0
U13-49	0
U13-48	-0.04
U13-47	-0.01
U13-46	0
U13-45	0
U13-44	0
U13-43	0
U13-42	0
U13-41	0
U13-40	0
U13-39	0
U13-38	0
U13-37	-0.01
U13-36	-0.05
U13-35	-0.05
U13-34	-0.05
U13-33	-0.09
U13-32	-0.05
U13-31	-0.25
U13-30	-0.25
U13-29	-0.25

U13-28	-0.25
U13-27	-0.25
U13-26	Maintenance Needed
U13-25	-0.25
U13-24	Maintenance Needed
U13-23	0.25
U13-22	Maintenance Needed
U13-21	0.25
U13-20	-0.25
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.05
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	-0.01
U13-02	-0.08
U13-01	-0.25
L13-01	0
L13-02	-0.15
L13-03	0
L13-04	-0.05
L13-05	-0.25
L13-06	-0.25
L13-07	-0.03
L13-08	-0.20
L13-09	-0.25
L13-10	0.01
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.01
L13-14	-0.01
L13-15	-0.25
L13-16	-0.05
L13-17	-0.05
L13-18	-0.02
L13-19	-0.02
L13-20	0

L13-21	-0.05
L13-22	-0.02
L13-23	-0.02
L13-24	-0.04
L13-25	-0.22
L13-26	0
L13-27	-0.20
L13-28	-0.20
L13-29	-0.02
L13-30	-0.02
L13-31	-0.02
L13-32	-0.02
L13-33	-0.02
L13-34	-0.02
L13-35	-0.02
L13-36	-0.02
L13-37	-0.02
L13-38	-0.02
L13-39	0.02
L13-40	0.01
L13-41	-0.01
L13-42	0
L13-43	-0.03
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.01
L13-47	-0.01
L13-48	-0.02
L13-49	-0.02
L13-50	-0.02
L13-51	-0.02
L13-52	0
L13-53	0
L13-54	-0.20
L13-55	-0.20
L13-56	-0.10
L13-57	-0.01
L13-58	-0.15
L13-59	-0.20
L13-60	-0.20
L13-61	-0.25
L13-62	-0.01
L13-63	-0.25
L13-64	-0.01
L13-65	-0.06
L13-66	-0.01
L13-67	-0.01
L13-68	-0.01

L13-69	0
L13-70	-0.01
L13-71	Maintenance Needed
L13-72	-0.02
L13-73	-0.20
L13-74	-0.15
L13-75	-0.05
L13-76	0
L13-77	-0.03
L13-78	-0.14
L13-79	-0.13
L13-80	-0.02

Certification



John Boucher
11 Sep 2026 12:44 PM PDT

4050 - Daily Pressure Gauge Readings

John Boucher

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	Marked as ‘my site is not listed here’
Conducted on	12 Sep 2026 7:15 AM PDT
Prepared by	John Boucher

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	0.01
SW 06	0
SW 05	0.05
SW 04	-0.01
SW 03	-0.05
SW 02	-0.01
SW 01	-0.05
44	-0.01
111	-0.01
LCM 11	-0.10
LCM 12	-0.05
LCM 13	-0.01
LCM 14	-0.10
LCM 15	-0.01
LCM 6	-0.01
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.10
LCM 10	-0.10
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.03
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.24
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	-0.03
D3	-0.25
D18	Maintenance Needed

D19	0.05
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.20
D24	0
D25	-0.25
D26	-0.25
D27	0
D28	0
D29	Maintenance Needed
D30	-0.10
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	Tank Not In Use/In Staging Area
C13-07	Tank Not In Use/In Staging Area
C13-06	Tank Not In Use/In Staging Area
C13-05	Tank Not In Use/In Staging Area

C13-04	Tank Not In Use/In Staging Area
C13-03	Tank Not In Use/In Staging Area
C13-02	Tank Not In Use/In Staging Area
C13-01	Tank Not In Use/In Staging Area
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.10
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	0
U13-62	0
U13-61	0
U13-60	0
U13-59	0
U13-58	0
U13-57	0
U13-56	0
U13-55	-0.01
U13-54	-0.01
U13-53	0

U13-52	-0.15
U13-51	0
U13-50	0
U13-49	0
U13-48	-0.04
U13-47	-0.01
U13-46	0
U13-45	0
U13-44	0
U13-43	0
U13-42	0
U13-41	0
U13-40	0
U13-39	0
U13-38	0
U13-37	0
U13-36	-0.05
U13-35	-0.06
U13-34	-0.06
U13-33	-0.10
U13-32	-0.05
U13-31	-0.25
U13-30	-0.25
U13-29	-0.25

U13-28	-0.25
U13-27	-0.25
U13-26	Maintenance Needed
U13-25	-0.25
U13-24	Maintenance Needed
U13-23	0.25
U13-22	Maintenance Needed
U13-21	0.25
U13-20	-0.25
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.05
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	-0.02
U13-02	-0.10
U13-01	-0.25
L13-01	0
L13-02	-0.15
L13-03	0
L13-04	-0.05
L13-05	-0.25
L13-06	-0.25
L13-07	-0.05
L13-08	-0.20
L13-09	-0.25
L13-10	0
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	0
L13-14	-0.01
L13-15	-0.25
L13-16	-0.05
L13-17	-0.05
L13-18	-0.04
L13-19	-0.04
L13-20	0

L13-21	-0.05
L13-22	-0.03
L13-23	-0.03
L13-24	-0.05
L13-25	-0.22
L13-26	0
L13-27	-0.20
L13-28	-0.20
L13-29	-0.03
L13-30	-0.03
L13-31	-0.03
L13-32	-0.01
L13-33	-0.02
L13-34	-0.03
L13-35	-0.03
L13-36	-0.01
L13-37	-0.02
L13-38	-0.01
L13-39	0.01
L13-40	0.01
L13-41	-0.01
L13-42	0
L13-43	-0.02
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.01
L13-47	-0.01
L13-48	-0.01
L13-49	-0.01
L13-50	-0.01
L13-51	-0.01
L13-52	0
L13-53	0
L13-54	-0.20
L13-55	-0.20
L13-56	-0.10
L13-57	-0.01
L13-58	-0.15
L13-59	-0.20
L13-60	-0.20
L13-61	-0.25
L13-62	-0.01
L13-63	-0.25
L13-64	-0.01
L13-65	-0.05
L13-66	-0.01
L13-67	-0.01
L13-68	-0.01

L13-69	-0.01
L13-70	-0.01
L13-71	Maintenance Needed
L13-72	-0.01
L13-73	-0.20
L13-74	-0.15
L13-75	-0.05
L13-76	0
L13-77	-0.02
L13-78	-0.15
L13-79	-0.15
L13-80	-0.01

Certification



John Boucher
12 Sep 2026 11:27 AM PDT

4050 - Daily Pressure Gauge Readings

Tom Roe

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	13 Sep 2026 8:10 AM PDT
Prepared by	Tom Roe

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	-0.02
SW 07	-0.03
SW 06	-0.01
SW 05	0.04
SW 04	-0.03
SW 03	-0.05
SW 02	0
SW 01	-0.05
44	0
111	0
LCM 11	-0.06
LCM 12	-0.03
LCM 13	-0.02
LCM 14	-0.08
LCM 15	-0.01
LCM 6	0.05
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.09
LCM 10	-0.07
LCM 1	0.11
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Tank Not In Use/In Staging Area
CD4	Tank Not In Use/In Staging Area
D17	-0.04
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.01
D6	-0.24
D5	-0.25
D4	-0.02
D3	-0.25
D18	Maintenance Needed

D19	0.01
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.25
D24	-0.02
D25	-0.25
D26	-0.25
D27	-0.03
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	Tank Not In Use/In Staging Area
C13-07	Tank Not In Use/In Staging Area
C13-06	Tank Not In Use/In Staging Area
C13-05	Tank Not In Use/In Staging Area

C13-04	Tank Not In Use/In Staging Area
C13-03	Tank Not In Use/In Staging Area
C13-02	Tank Not In Use/In Staging Area
C13-01	Tank Not In Use/In Staging Area
C13-09	-0.25
C13-10	-0.08
C13-11	-0.05
C13-12	-0.05
C13-13	-0.05
C13-14	-0.10
C13-15	-0.10
C13-16	-0.12
T1/T2 190	-0.13
U13-63	-0.02
U13-62	-0.02
U13-61	-0.01
U13-60	Tank Not In Use/In Staging Area
U13-59	Tank Not In Use/In Staging Area
U13-58	0
U13-57	Tank Not In Use/In Staging Area
U13-56	Tank Not In Use/In Staging Area
U13-55	Tank Not In Use/In Staging Area
U13-54	0.01
U13-53	-0.02

U13-52	-0.15
U13-51	-0.02
U13-50	-0.01
U13-49	Tank Not In Use/In Staging Area
U13-48	-0.04
U13-47	Tank Not In Use/In Staging Area
U13-46	-0.01
U13-45	0
U13-44	0
U13-43	0.02
U13-42	-0.03
U13-41	-0.02
U13-40	0.01
U13-39	-0.01
U13-38	-0.03
U13-37	-0.03
U13-36	-0.21
U13-35	-0.15
U13-34	-0.16
U13-33	-0.04
U13-32	-0.08
U13-31	-0.02
U13-30	-0.01
U13-29	-0.02

U13-28	0.02
U13-27	0
U13-26	-0.03
U13-25	-0.02
U13-24	-0.01
U13-23	0
U13-22	-0.01
U13-21	-0.02
U13-20	-0.01
U13-19	Maintenance Needed
U13-18	-0.05
U13-17	-0.06
U13-16	-0.07
U13-15	-0.11
U13-14	-0.14
U13-13	-0.11
U13-12	-0.12
U13-11	0.01
U13-10	-0.12
U13-09	-0.01
U13-08	-0.06
U13-07	-0.07
U13-06	-0.07
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.15
U13-01	-0.25
L13-01	-0.02
L13-02	0.03
L13-03	-0.03
L13-04	0.15
L13-05	-0.15
L13-06	-0.06
L13-07	-0.03
L13-08	-0.12
L13-09	-0.06
L13-10	0.04
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.02
L13-15	-0.21
L13-16	-0.09
L13-17	-0.11
L13-18	-0.08
L13-19	-0.08
L13-20	-0.07

L13-21	-0.09
L13-22	-0.04
L13-23	-0.06
L13-24	-0.09
L13-25	-0.05
L13-26	-0.05
L13-27	-0.08
L13-28	-0.09
L13-29	-0.09
L13-30	-0.11
L13-31	-0.04
L13-32	-0.05
L13-33	-0.06
L13-34	-0.03
L13-35	-0.02
L13-36	-0.08
L13-37	-0.07
L13-38	-0.04
L13-39	-0.03
L13-40	-0.03
L13-41	-0.02
L13-42	-0.03
L13-43	-0.03
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.03
L13-47	-0.03
L13-48	-0.03
L13-49	-0.03
L13-50	-0.04
L13-51	-0.01
L13-52	-0.02
L13-53	-0.03
L13-54	0.05
L13-55	-0.03
L13-56	0.11
L13-57	-0.03
L13-58	-0.03
L13-59	-0.04
L13-60	-0.05
L13-61	-0.10
L13-62	0.01
L13-63	0
L13-64	0
L13-65	-0.08
L13-66	-0.04
L13-67	-0.01
L13-68	-0.03

L13-69	-0.05
L13-70	-0.03
L13-71	Maintenance Needed
L13-72	-0.07
L13-73	0.03
L13-74	-0.08
L13-75	-0.09
L13-76	-0.04
L13-77	-0.03
L13-78	-0.08
L13-79	-0.06
L13-80	-0.02

Certification



Tom Roe
13 Sep 2026 12:12 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	14 Sep 2026 9:49 AM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.02
SW 06	0
SW 05	0.05
SW 04	-0.02
SW 03	-0.05
SW 02	0
SW 01	-0.17
44	0
111	0
LCM 11	-0.10
LCM 12	-0.05
LCM 13	-0.02
LCM 14	-0.11
LCM 15	-0.01
LCM 6	0.03
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.13
LCM 10	-0.10
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.01
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	-0.01
D3	-0.25
D18	Maintenance Needed

D19	0.01
D20	-0.11
D21	Maintenance Needed
D22	0.03
D23	-0.25
D24	-0.01
D25	-0.25
D26	-0.25
D27	0
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.08
C13-06	-0.07
C13-05	-0.10

C13-04	0.02
C13-03	0.01
C13-02	0.02
C13-01	-0.02
C13-09	-0.25
C13-10	-0.02
C13-11	-0.03
C13-12	-0.05
C13-13	-0.04
C13-14	-0.06
C13-15	-0.05
C13-16	-0.05
T1/T2 190	-0.10
U13-63	-0.01
U13-62	-0.02
U13-61	0
U13-60	-0.01
U13-59	0
U13-58	0
U13-57	-0.01
U13-56	0
U13-55	-0.05
U13-54	0
U13-53	-0.04

U13-52	-0.16
U13-51	0
U13-50	-0.01
U13-49	-0.01
U13-48	-0.05
U13-47	-0.02
U13-46	-0.02
U13-45	-0.02
U13-44	-0.02
U13-43	0
U13-42	-0.02
U13-41	-0.05
U13-40	-0.01
U13-39	0
U13-38	-0.01
U13-37	-0.01
U13-36	-0.12
U13-35	-0.08
U13-34	-0.09
U13-33	-0.05
U13-32	-0.04
U13-31	0
U13-30	0.25
U13-29	0.25

U13-28	Maintenance Needed
U13-27	0.25
U13-26	0.25
U13-25	-0.03
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.05
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.10
U13-01	-0.25
L13-01	0
L13-02	-0.25
L13-03	-0.01
L13-04	0.13
L13-05	-0.01
L13-06	-0.20
L13-07	-0.05
L13-08	-0.20
L13-09	-0.20
L13-10	0.05
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.25
L13-14	-0.02
L13-15	-0.25
L13-16	-0.07
L13-17	-0.06
L13-18	-0.05
L13-19	-0.05
L13-20	-0.03

L13-21	-0.05
L13-22	-0.01
L13-23	-0.04
L13-24	-0.04
L13-25	-0.17
L13-26	-0.01
L13-27	-0.20
L13-28	-0.22
L13-29	-0.05
L13-30	-0.12
L13-31	-0.03
L13-32	-0.02
L13-33	-0.02
L13-34	-0.02
L13-35	-0.02
L13-36	-0.05
L13-37	-0.07
L13-38	-0.02
L13-39	-0.02
L13-40	-0.02
L13-41	-0.02
L13-42	-0.03
L13-43	-0.04
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.02
L13-47	-0.02
L13-48	-0.01
L13-49	-0.02
L13-50	-0.01
L13-51	-0.01
L13-52	0
L13-53	-0.01
L13-54	-0.15
L13-55	-0.10
L13-56	-0.03
L13-57	-0.03
L13-58	-0.12
L13-59	-0.15
L13-60	-0.17
L13-61	-0.24
L13-62	0
L13-63	-0.16
L13-64	-0.01
L13-65	-0.07
L13-66	-0.02
L13-67	-0.01
L13-68	-0.02

L13-69	-0.01
L13-70	0
L13-71	Maintenance Needed
L13-72	0.01
L13-73	-0.15
L13-74	-0.12
L13-75	-0.02
L13-76	-0.01
L13-77	-0.01
L13-78	-0.10
L13-79	-0.08
L13-80	-0.02

Certification



Nancy Bahena Hernandez
14 Sep 2026 3:42 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	15 Sep 2026 1:41 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.01
SW 06	0
SW 05	0.03
SW 04	-0.01
SW 03	-0.05
SW 02	0
SW 01	-0.04
44	0
111	0
LCM 11	-0.07
LCM 12	-0.04
LCM 13	-0.02
LCM 14	-0.07
LCM 15	-0.01
LCM 6	0.01
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.02
LCM 10	0
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.04
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	-0.02
D3	-0.25
D18	Maintenance Needed

D19	0.01
D20	-0.10
D21	Maintenance Needed
D22	-0.25
D23	-0.25
D24	-0.02
D25	-0.25
D26	-0.25
D27	-0.01
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.01
C13-07	-0.03
C13-06	0
C13-05	-0.01

C13-04	-0.05
C13-03	0
C13-02	0
C13-01	-0.02
C13-09	-0.25
C13-10	-0.07
C13-11	-0.10
C13-12	-0.07
C13-13	-0.07
C13-14	-0.13
C13-15	-0.08
C13-16	-0.10
T1/T2 190	-0.10
U13-63	-0.01
U13-62	-0.02
U13-61	0
U13-60	-0.01
U13-59	-0.01
U13-58	0
U13-57	-0.01
U13-56	0
U13-55	-0.05
U13-54	0
U13-53	-0.05

U13-52	-0.15
U13-51	-0.02
U13-50	-0.01
U13-49	0
U13-48	-0.05
U13-47	-0.05
U13-46	0
U13-45	0
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.02
U13-40	0
U13-39	0
U13-38	0
U13-37	-0.05
U13-36	-0.15
U13-35	-0.15
U13-34	-0.20
U13-33	-0.06
U13-32	-0.07
U13-31	-0.02
U13-30	-0.25
U13-29	-0.25

U13-28	Maintenance Needed
U13-27	-0.10
U13-26	-0.25
U13-25	-0.02
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.05
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.10
U13-01	-0.25
L13-01	-0.02
L13-02	-0.20
L13-03	-0.01
L13-04	0.15
L13-05	-0.05
L13-06	-0.17
L13-07	-0.05
L13-08	-0.07
L13-09	-0.07
L13-10	0.05
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.02
L13-15	-0.25
L13-16	-0.10
L13-17	-0.10
L13-18	-0.07
L13-19	-0.06
L13-20	-0.05

L13-21	-0.10
L13-22	-0.03
L13-23	-0.05
L13-24	-0.10
L13-25	-0.17
L13-26	-0.02
L13-27	-0.20
L13-28	-0.25
L13-29	-0.05
L13-30	-0.07
L13-31	-0.05
L13-32	0.08
L13-33	0
L13-34	-0.03
L13-35	-0.02
L13-36	-0.07
L13-37	-0.07
L13-38	-0.02
L13-39	-0.02
L13-40	-0.02
L13-41	-0.02
L13-42	-0.05
L13-43	-0.05
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.02
L13-47	-0.01
L13-48	-0.01
L13-49	-0.01
L13-50	-0.01
L13-51	-0.01
L13-52	0
L13-53	-0.01
L13-54	-0.15
L13-55	-0.06
L13-56	-0.01
L13-57	-0.02
L13-58	-0.13
L13-59	-0.12
L13-60	-0.15
L13-61	-0.20
L13-62	0
L13-63	-0.08
L13-64	-0.02
L13-65	-0.07
L13-66	-0.03
L13-67	-0.01
L13-68	-0.05

L13-69	-0.05
L13-70	-0.04
L13-71	Maintenance Needed
L13-72	-0.07
L13-73	-0.13
L13-74	-0.15
L13-75	-0.07
L13-76	-0.05
L13-77	-0.02
L13-78	-0.05
L13-79	-0.05
L13-80	-0.06

Certification



Nancy Bahena Hernandez
15 Sep 2026 3:43 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	16 Sep 2026 2:01 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.02
SW 06	0
SW 05	0.04
SW 04	0
SW 03	-0.05
SW 02	0
SW 01	0
44	0
111	0
LCM 11	-0.07
LCM 12	-0.03
LCM 13	0
LCM 14	-0.10
LCM 15	0
LCM 6	0.03
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.04
LCM 10	-0.03
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.02
D6	-0.25
D5	-0.25
D4	-0.03
D3	-0.25
D18	Maintenance Needed

D19	0.01
D20	-0.11
D21	Maintenance Needed
D22	0.25
D23	-0.25
D24	0.02
D25	-0.25
D26	-0.25
D27	-0.02
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.02
C13-07	-0.04
C13-06	0
C13-05	-0.06

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.02
C13-09	-0.25
C13-10	-0.07
C13-11	-0.10
C13-12	-0.05
C13-13	-0.07
C13-14	-0.10
C13-15	-0.07
C13-16	-0.07
T1/T2 190	-0.06
U13-63	-0.02
U13-62	-0.01
U13-61	0
U13-60	-0.01
U13-59	0
U13-58	-0.01
U13-57	-0.01
U13-56	-0.01
U13-55	-0.03
U13-54	0
U13-53	-0.02

U13-52	-0.17
U13-51	-0.02
U13-50	-0.01
U13-49	0
U13-48	-0.05
U13-47	-0.02
U13-46	-0.01
U13-45	-0.01
U13-44	-0.01
U13-43	0
U13-42	-0.01
U13-41	-0.02
U13-40	-0.03
U13-39	0
U13-38	-0.01
U13-37	-0.02
U13-36	-0.22
U13-35	-0.15
U13-34	-0.18
U13-33	-0.07
U13-32	-0.07
U13-31	-0.02
U13-30	0.25
U13-29	-0.25

U13-28	Maintenance Needed
U13-27	-0.25
U13-26	-0.20
U13-25	-0.02
U13-24	0.25
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.07
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.15
U13-01	-0.25
L13-01	-0.01
L13-02	-0.10
L13-03	-0.01
L13-04	0.17
L13-05	-0.10
L13-06	-0.16
L13-07	-0.06
L13-08	-0.21
L13-09	-0.22
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.03
L13-15	-0.25
L13-16	-0.12
L13-17	-0.12
L13-18	-0.10
L13-19	-0.07
L13-20	-0.07

L13-21	-0.10
L13-22	-0.05
L13-23	-0.06
L13-24	-0.10
L13-25	-0.15
L13-26	-0.06
L13-27	-0.20
L13-28	-0.25
L13-29	-0.10
L13-30	0
L13-31	0.05
L13-32	-0.05
L13-33	-0.02
L13-34	-0.02
L13-35	-0.02
L13-36	0.25
L13-37	-0.07
L13-38	-0.05
L13-39	-0.01
L13-40	-0.01
L13-41	-0.06
L13-42	-0.09
L13-43	-0.03
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.05
L13-47	-0.02
L13-48	-0.02
L13-49	-0.04
L13-50	-0.03
L13-51	-0.01
L13-52	0
L13-53	-0.02
L13-54	-0.10
L13-55	-0.05
L13-56	0.01
L13-57	-0.02
L13-58	-0.11
L13-59	-0.12
L13-60	-0.12
L13-61	-0.18
L13-62	0
L13-63	-0.13
L13-64	0
L13-65	-0.10
L13-66	-0.05
L13-67	-0.01
L13-68	-0.05

L13-69	-0.05
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.12
L13-73	-0.10
L13-74	-0.15
L13-75	-0.12
L13-76	-0.07
L13-77	-0.01
L13-78	-0.06
L13-79	-0.05
L13-80	-0.03

Certification



Nancy Bahena Hernandez
16 Sep 2026 3:50 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	17 Sep 2026 1:31 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.01
SW 07	-0.02
SW 06	0
SW 05	0.03
SW 04	0
SW 03	-0.05
SW 02	0
SW 01	-0.03
44	0
111	-0.01
LCM 11	-0.07
LCM 12	-0.05
LCM 13	-0.02
LCM 14	-0.08
LCM 15	-0.01
LCM 6	0.02
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.03
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	-0.03
D3	-0.25
D18	Maintenance Needed

D19	0.02
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.25
D24	0
D25	-0.25
D26	-0.25
D27	-0.03
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.02
C13-06	-0.01
C13-05	-0.05

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.05
C13-09	-0.25
C13-10	-0.25
C13-11	-0.05
C13-12	-0.07
C13-13	-0.10
C13-14	-0.15
C13-15	-0.10
C13-16	-0.10
T1/T2 190	-0.15
U13-63	-0.02
U13-62	-0.03
U13-61	0
U13-60	-0.01
U13-59	-0.02
U13-58	-0.02
U13-57	-0.01
U13-56	-0.01
U13-55	-0.05
U13-54	0
U13-53	0

U13-52	-0.15
U13-51	0
U13-50	0
U13-49	0
U13-48	-0.06
U13-47	-0.02
U13-46	-0.02
U13-45	0
U13-44	0
U13-43	-0.01
U13-42	-0.02
U13-41	-0.02
U13-40	-0.02
U13-39	0
U13-38	-0.02
U13-37	-0.02
U13-36	-0.22
U13-35	-0.20
U13-34	-0.21
U13-33	-0.05
U13-32	-0.07
U13-31	-0.25
U13-30	0.15
U13-29	-0.25

U13-28	Maintenance Needed
U13-27	0.25
U13-26	0.25
U13-25	-0.02
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	-0.23
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.10
U13-05	-0.25


U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.25
U13-01	-0.25
L13-01	-0.01
L13-02	-0.10
L13-03	-0.01
L13-04	0.25
L13-05	-0.15
L13-06	-0.16
L13-07	-0.10
L13-08	-0.20
L13-09	-0.15
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.03
L13-15	-0.25
L13-16	-0.01
L13-17	-0.12
L13-18	-0.10
L13-19	-0.11
L13-20	-0.08

L13-21	-0.12
L13-22	-0.05
L13-23	-0.08
L13-24	-0.12
L13-25	-0.16
L13-26	-0.07
L13-27	-0.16
L13-28	-0.18
L13-29	-0.10
L13-30	-0.10
L13-31	-0.07
L13-32	-0.06
L13-33	-0.08
L13-34	-0.03
L13-35	-0.03
L13-36	-0.13
L13-37	-0.10
L13-38	-0.07
L13-39	-0.04
L13-40	-0.03
L13-41	-0.03
L13-42	-0.06
L13-43	-0.05
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.03
L13-47	-0.02
L13-48	-0.02
L13-49	-0.04
L13-50	-0.03
L13-51	-0.02
L13-52	0
L13-53	-0.02
L13-54	-0.10
L13-55	-0.05
L13-56	0.02
L13-57	-0.05
L13-58	-0.12
L13-59	-0.12
L13-60	-0.15
L13-61	-0.17
L13-62	0
L13-63	-0.12
L13-64	0
L13-65	-0.07
L13-66	-0.02
L13-67	-0.02
L13-68	-0.03

L13-69	-0.02
L13-70	-0.03
L13-71	Maintenance Needed
L13-72	-0.07
L13-73	-0.10
L13-74	-0.15
L13-75	-0.13
L13-76	-0.10
L13-77	-0.01
L13-78	-0.05
L13-79	-0.05
L13-80	-0.05

Certification



Nancy Bahena Hernandez
17 Sep 2026 3:22 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	18 Sep 2026 1:46 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.04
SW 06	-0.08
SW 05	0.04
SW 04	-0.01
SW 03	-0.05
SW 02	0
SW 01	-0.03
44	0
111	-0.01
LCM 11	-0.10
LCM 12	-0.05
LCM 13	-0.04
LCM 14	-0.10
LCM 15	0
LCM 6	0.05
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.02
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	-0.02
D3	-0.25
D18	Maintenance Needed

D19	0.01
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.25
D24	0
D25	-0.25
D26	0.10
D27	0
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.01
C13-07	-0.05
C13-06	-0.03
C13-05	-0.10

C13-04	0
C13-03	0
C13-02	-0.01
C13-01	-0.06
C13-09	-0.25
C13-10	-0.25
C13-11	-0.24
C13-12	-0.10
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.03
U13-62	-0.02
U13-61	0
U13-60	0
U13-59	-0.01
U13-58	-0.01
U13-57	-0.02
U13-56	-0.01
U13-55	-0.05
U13-54	0
U13-53	-0.03

U13-52	-0.16
U13-51	-0.02
U13-50	-0.03
U13-49	-0.05
U13-48	-0.07
U13-47	-0.05
U13-46	-0.02
U13-45	-0.02
U13-44	-0.02
U13-43	-0.01
U13-42	-0.07
U13-41	-0.01
U13-40	0
U13-39	-0.01
U13-38	-0.05
U13-37	-0.02
U13-36	-0.25
U13-35	-0.24
U13-34	-0.25
U13-33	-0.06
U13-32	-0.09
U13-31	0.25
U13-30	0.13
U13-29	-0.25

U13-28	-0.25
U13-27	0.25
U13-26	-0.25
U13-25	-0.02
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.10
U13-05	-0.25


U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.25
U13-01	-0.25
L13-01	-0.01
L13-02	-0.12
L13-03	0
L13-04	0.14
L13-05	-0.25
L13-06	-0.20
L13-07	-0.11
L13-08	-0.20
L13-09	-0.20
L13-10	0.15
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.02
L13-15	-0.25
L13-16	-0.15
L13-17	-0.12
L13-18	-0.10
L13-19	-0.10
L13-20	-0.10

L13-21	-0.12
L13-22	-0.06
L13-23	-0.11
L13-24	-0.12
L13-25	-0.15
L13-26	-0.07
L13-27	-0.17
L13-28	-0.25
L13-29	-0.12
L13-30	-0.10
L13-31	-0.06
L13-32	-0.07
L13-33	-0.07
L13-34	-0.02
L13-35	-0.02
L13-36	-0.12
L13-37	-0.20
L13-38	-0.02
L13-39	-0.01
L13-40	-0.01
L13-41	-0.01
L13-42	0
L13-43	-0.01
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.03
L13-47	-0.05
L13-48	-0.05
L13-49	-0.03
L13-50	-0.05
L13-51	-0.01
L13-52	-0.01
L13-53	-0.01
L13-54	-0.11
L13-55	-0.10
L13-56	-0.01
L13-57	-0.05
L13-58	-0.15
L13-59	-0.12
L13-60	-0.15
L13-61	-0.20
L13-62	0
L13-63	-0.12
L13-64	-0.05
L13-65	-0.10
L13-66	-0.05
L13-67	-0.02
L13-68	-0.05

L13-69	-0.05
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.05
L13-73	-0.11
L13-74	-0.10
L13-75	-0.07
L13-76	-0.06
L13-77	-0.02
L13-78	-0.06
L13-79	-0.05
L13-80	-0.05

Certification



Nancy Bahena Hernandez
18 Sep 2026 3:48 PM PDT

4050 - Daily Pressure Gauge Readings

John Boucher

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	Marked as ‘my site is not listed here’
Conducted on	19 Sep 2026 7:16 AM PDT
Prepared by	John Boucher

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.05
SW 06	-0.09
SW 05	0.05
SW 04	0
SW 03	-0.05
SW 02	0
SW 01	-0.04
44	0
111	0
LCM 11	-0.10
LCM 12	-0.05
LCM 13	-0.05
LCM 14	-0.10
LCM 15	0
LCM 6	0.05
LCM 7	-0.02
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.03
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	0
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	-0.03
D3	-0.25
D18	Maintenance Needed

D19	0
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.25
D24	0
D25	-0.25
D26	0.10
D27	0
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0
C13-07	-0.04
C13-06	-0.04
C13-05	-0.10

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.05
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.10
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.02
U13-62	-0.02
U13-61	-0.01
U13-60	-0.01
U13-59	-0.01
U13-58	-0.01
U13-57	-0.01
U13-56	-0.01
U13-55	-0.05
U13-54	0
U13-53	-0.02

U13-52	-0.15
U13-51	-0.02
U13-50	-0.02
U13-49	-0.05
U13-48	-0.05
U13-47	-0.05
U13-46	-0.03
U13-45	-0.02
U13-44	-0.02
U13-43	-0.02
U13-42	-0.05
U13-41	0
U13-40	0
U13-39	0
U13-38	-0.05
U13-37	-0.03
U13-36	-0.25
U13-35	-0.25
U13-34	-0.25
U13-33	-0.05
U13-32	-0.10
U13-31	0.25
U13-30	0.12
U13-29	-0.25

U13-28	-0.25
U13-27	0.25
U13-26	-0.25
U13-25	-0.02
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.08
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.25
U13-01	-0.25
L13-01	0
L13-02	-0.10
L13-03	0
L13-04	0.15
L13-05	-0.25
L13-06	-0.20
L13-07	-0.10
L13-08	-0.20
L13-09	-0.20
L13-10	0.15
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.02
L13-15	-0.25
L13-16	-0.15
L13-17	-0.11
L13-18	-0.10
L13-19	-0.10
L13-20	-0.10

L13-21	-0.10
L13-22	-0.05
L13-23	-0.10
L13-24	-0.10
L13-25	-0.15
L13-26	-0.06
L13-27	-0.15
L13-28	-0.25
L13-29	-0.10
L13-30	-0.10
L13-31	-0.05
L13-32	-0.05
L13-33	-0.05
L13-34	0
L13-35	-0.01
L13-36	-0.10
L13-37	-0.20
L13-38	-0.02
L13-39	-0.02
L13-40	-0.02
L13-41	-0.01
L13-42	0
L13-43	-0.02
L13-44	Maintenance Needed

L13-45	-0.03
L13-46	-0.03
L13-47	-0.05
L13-48	-0.05
L13-49	-0.05
L13-50	-0.05
L13-51	-0.02
L13-52	-0.01
L13-53	-0.02
L13-54	-0.10
L13-55	-0.10
L13-56	0
L13-57	-0.05
L13-58	-0.15
L13-59	-0.10
L13-60	-0.15
L13-61	-0.20
L13-62	0
L13-63	-0.10
L13-64	-0.05
L13-65	-0.10
L13-66	-0.05
L13-67	-0.01
L13-68	-0.05

L13-69	-0.05
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.05
L13-73	-0.10
L13-74	-0.10
L13-75	-0.06
L13-76	-0.05
L13-77	-0.02
L13-78	-0.05
L13-79	-0.05
L13-80	-0.05

Certification



John Boucher
19 Sep 2026 11:39 AM PDT

4050 - Daily Pressure Gauge Readings

Tom Roe

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	20 Sep 2026 7:36 AM PDT
Prepared by	Tom Roe

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.02
SW 07	Tank Not In Use/In Staging Area
SW 06	Tank Not In Use/In Staging Area
SW 05	0.03
SW 04	-0.03
SW 03	-0.06
SW 02	0
SW 01	-0.03
44	-0.02
111	-0.02
LCM 11	0
LCM 12	-0.04
LCM 13	-0.03
LCM 14	0
LCM 15	-0.02
LCM 6	0.05
LCM 7	-0.02
LCM 8	Maintenance Needed
LCM 9	0
LCM 10	-0.01
LCM 1	0.12
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.01
D2	-0.25
CD3	Tank Not In Use/In Staging Area
CD4	Tank Not In Use/In Staging Area
D17	-0.05
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.02
D6	-0.25
D5	-0.25
D4	0.25
D3	0.25
D18	Maintenance Needed

D19	0.01
D20	-0.10
D21	Maintenance Needed
D22	0.25
D23	-0.25
D24	-0.02
D25	-0.25
D26	-0.25
D27	-0.03
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	Tank Not In Use/In Staging Area
C13-07	Tank Not In Use/In Staging Area
C13-06	Tank Not In Use/In Staging Area
C13-05	Tank Not In Use/In Staging Area

C13-04	Tank Not In Use/In Staging Area
C13-03	Tank Not In Use/In Staging Area
C13-02	Tank Not In Use/In Staging Area
C13-01	Tank Not In Use/In Staging Area
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.14
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.02
U13-62	-0.02
U13-61	-0.01
U13-60	Tank Not In Use/In Staging Area
U13-59	Tank Not In Use/In Staging Area
U13-58	0
U13-57	Tank Not In Use/In Staging Area
U13-56	Tank Not In Use/In Staging Area
U13-55	Tank Not In Use/In Staging Area
U13-54	0.01
U13-53	-0.02

U13-52	-0.15
U13-51	-0.02
U13-50	-0.01
U13-49	Tank Not In Use/In Staging Area
U13-48	-0.03
U13-47	Tank Not In Use/In Staging Area
U13-46	0.25
U13-45	-0.01
U13-44	0
U13-43	0
U13-42	-0.03
U13-41	-0.02
U13-40	0
U13-39	-0.02
U13-38	-0.02
U13-37	-0.03
U13-36	-0.07
U13-35	-0.06
U13-34	-0.07
U13-33	-0.04
U13-32	-0.04
U13-31	0.25
U13-30	-0.25
U13-29	-0.25

U13-28	-0.25
U13-27	0.25
U13-26	-0.25
U13-25	0.25
U13-24	Maintenance Needed
U13-23	-0.25
U13-22	-0.02
U13-21	0
U13-20	0
U13-19	-0.01
U13-18	-0.10
U13-17	-0.09
U13-16	-0.08
U13-15	-0.14
U13-14	-0.12
U13-13	-0.10
U13-12	-0.10
U13-11	-0.07
U13-10	-0.11
U13-09	-0.09
U13-08	-0.04
U13-07	-0.10
U13-06	-0.03
U13-05	-0.22

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.06
U13-01	-0.25
L13-01	0.25
L13-02	0.02
L13-03	-0.02
L13-04	0.25
L13-05	-0.07
L13-06	-0.05
L13-07	-0.01
L13-08	0.02
L13-09	-0.06
L13-10	0.03
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.01
L13-15	-0.10
L13-16	-0.05
L13-17	-0.06
L13-18	-0.05
L13-19	-0.04
L13-20	-0.03

L13-21	-0.05
L13-22	-0.03
L13-23	-0.03
L13-24	-0.05
L13-25	-0.03
L13-26	-0.03
L13-27	-0.04
L13-28	-0.07
L13-29	-0.05
L13-30	-0.12
L13-31	-0.25
L13-32	-0.25
L13-33	-0.04
L13-34	-0.03
L13-35	-0.02
L13-36	-0.06
L13-37	-0.07
L13-38	-0.04
L13-39	-0.03
L13-40	-0.02
L13-41	-0.02
L13-42	-0.02
L13-43	-0.03
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.03
L13-47	-0.02
L13-48	-0.02
L13-49	-0.02
L13-50	-0.02
L13-51	-0.02
L13-52	-0.01
L13-53	-0.02
L13-54	0.12
L13-55	0.05
L13-56	0.15
L13-57	-0.04
L13-58	-0.01
L13-59	0.02
L13-60	-0.02
L13-61	-0.05
L13-62	0.01
L13-63	0.04
L13-64	0.02
L13-65	-0.08
L13-66	-0.03
L13-67	-0.02
L13-68	-0.03

L13-69	-0.04
L13-70	-0.02
L13-71	Maintenance Needed
L13-72	-0.05
L13-73	0.08
L13-74	-0.03
L13-75	-0.05
L13-76	-0.03
L13-77	-0.03
L13-78	0.05
L13-79	0.06
L13-80	-0.03

Certification



Tom Roe
20 Sep 2026 9:17 AM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	21 Sep 2026 1:44 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.01
SW 07	-0.03
SW 06	0.02
SW 05	0.04
SW 04	-0.02
SW 03	-0.05
SW 02	0
SW 01	-0.02
44	0
111	-0.02
LCM 11	-0.07
LCM 12	-0.05
LCM 13	-0.01
LCM 14	-0.07
LCM 15	-0.01
LCM 6	0.05
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.02
LCM 1	Maintenance Needed
LCM 2	-0.02

LCM 3	-0.07
LCM 4	-0.15
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.15
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	-0.25
D14	Maintenance Needed
D13	-0.25
D12	-0.02
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.01
D6	-0.25
D5	-0.25
D4	-0.01
D3	-0.25
D18	-0.25

D19	0.02
D20	-0.11
D21	Maintenance Needed
D22	0.02
D23	-0.25
D24	0
D25	-0.25
D26	-0.25
D27	-0.01
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.02
C13-07	-0.01
C13-06	0
C13-05	-0.03

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.02
C13-09	-0.25
C13-10	-0.20
C13-11	-0.18
C13-12	-0.08
C13-13	-0.20
C13-14	-0.24
C13-15	-0.23
C13-16	-0.22
T1/T2 190	-0.25
U13-63	-0.02
U13-62	-0.04
U13-61	0
U13-60	-0.02
U13-59	-0.01
U13-58	0
U13-57	-0.01
U13-56	-0.01
U13-55	-0.03
U13-54	-0.25
U13-53	-0.03

U13-52	-0.15
U13-51	-0.01
U13-50	-0.01
U13-49	0
U13-48	-0.10
U13-47	-0.02
U13-46	-0.01
U13-45	0
U13-44	-0.01
U13-43	0
U13-42	-0.02
U13-41	-0.02
U13-40	-0.02
U13-39	0
U13-38	-0.01
U13-37	-0.05
U13-36	-0.20
U13-35	-0.15
U13-34	-0.16
U13-33	-0.06
U13-32	-0.07
U13-31	0.25
U13-30	-0.25
U13-29	-0.25

U13-28	Maintenance Needed
U13-27	0.05
U13-26	-0.25
U13-25	-0.25
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.06
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.15
U13-01	-0.25
L13-01	0
L13-02	-0.25
L13-03	0
L13-04	0.06
L13-05	-0.10
L13-06	-0.20
L13-07	-0.02
L13-08	-0.18
L13-09	-0.22
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.05
L13-14	-0.25
L13-15	-0.25
L13-16	-0.25
L13-17	-0.11
L13-18	-0.10
L13-19	-0.10
L13-20	-0.09

L13-21	-0.11
L13-22	-0.04
L13-23	-0.07
L13-24	-0.10
L13-25	-0.16
L13-26	-0.05
L13-27	-0.17
L13-28	-0.22
L13-29	-0.07
L13-30	0.25
L13-31	-0.07
L13-32	-0.07
L13-33	-0.07
L13-34	-0.02
L13-35	-0.03
L13-36	-0.25
L13-37	-0.05
L13-38	-0.03
L13-39	-0.05
L13-40	-0.05
L13-41	-0.06
L13-42	-0.05
L13-43	-0.05
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.02
L13-47	-0.02
L13-48	-0.02
L13-49	-0.03
L13-50	-0.03
L13-51	0
L13-52	-0.01
L13-53	-0.02
L13-54	-0.15
L13-55	-0.10
L13-56	-0.01
L13-57	-0.05
L13-58	-0.15
L13-59	-0.15
L13-60	-0.18
L13-61	-0.22
L13-62	0.01
L13-63	-0.15
L13-64	0
L13-65	-0.08
L13-66	-0.05
L13-67	-0.01
L13-68	-0.05

L13-69	-0.05
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.10
L13-73	-0.11
L13-74	-0.15
L13-75	-0.10
L13-76	-0.05
L13-77	0
L13-78	-0.07
L13-79	-0.05
L13-80	-0.04

Certification



Nancy Bahena Hernandez
21 Sep 2026 3:35 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	22 Sep 2026 2:15 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.02
SW 07	-0.03
SW 06	-0.02
SW 05	0.05
SW 04	-0.02
SW 03	-0.06
SW 02	0
SW 01	-0.02
44	0
111	0
LCM 11	-0.10
LCM 12	-0.05
LCM 13	-0.02
LCM 14	-0.10
LCM 15	0
LCM 6	0.02
LCM 7	-0.01
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.03
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.22
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.12
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	0.01
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.01
D6	-0.25
D5	-0.25
D4	-0.03
D3	-0.25
D18	-0.25

D19	0.01
D20	-0.10
D21	Maintenance Needed
D22	-0.06
D23	-0.23
D24	0
D25	-0.25
D26	-0.25
D27	-0.02
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.05
C13-06	-0.01
C13-05	-0.02

C13-04	0
C13-03	0
C13-02	-0.02
C13-01	-0.02
C13-09	-0.24
C13-10	-0.10
C13-11	-0.12
C13-12	-0.04
C13-13	-0.10
C13-14	-0.12
C13-15	-0.05
C13-16	-0.05
T1/T2 190	0.25
U13-63	-0.05
U13-62	-0.05
U13-61	0
U13-60	-0.02
U13-59	-0.01
U13-58	0
U13-57	-0.01
U13-56	-0.05
U13-55	-0.05
U13-54	0
U13-53	-0.05

U13-52	-0.15
U13-51	-0.02
U13-50	-0.02
U13-49	0
U13-48	-0.06
U13-47	-0.05
U13-46	-0.02
U13-45	-0.01
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.03
U13-40	-0.01
U13-39	0
U13-38	0
U13-37	-0.02
U13-36	-0.08
U13-35	-0.07
U13-34	-0.07
U13-33	-0.05
U13-32	-0.06
U13-31	-0.01
U13-30	-0.01
U13-29	-0.05

U13-28	-0.01
U13-27	0.01
U13-26	-0.02
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.02
U13-05	-0.17

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.12
U13-01	-0.25
L13-01	0
L13-02	-0.25
L13-03	-0.01
L13-04	0
L13-05	-0.15
L13-06	-0.25
L13-07	-0.05
L13-08	-0.25
L13-09	-0.25
L13-10	0.03
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.02
L13-15	-0.25
L13-16	0.25
L13-17	-0.07
L13-18	-0.07
L13-19	-0.05
L13-20	-0.04

L13-21	-0.05
L13-22	-0.03
L13-23	-0.02
L13-24	-0.05
L13-25	-0.20
L13-26	-0.01
L13-27	-0.20
L13-28	-0.25
L13-29	-0.05
L13-30	-0.07
L13-31	-0.05
L13-32	-0.05
L13-33	-0.02
L13-34	-0.02
L13-35	-0.02
L13-36	-0.05
L13-37	-0.07
L13-38	-0.05
L13-39	-0.07
L13-40	-0.25
L13-41	-0.25
L13-42	-0.25
L13-43	-0.21
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.02
L13-47	-0.02
L13-48	-0.01
L13-49	-0.01
L13-50	-0.02
L13-51	0
L13-52	0
L13-53	-0.01
L13-54	-0.15
L13-55	-0.13
L13-56	-0.02
L13-57	-0.03
L13-58	-0.15
L13-59	-0.17
L13-60	-0.20
L13-61	-0.25
L13-62	-0.02
L13-63	-0.17
L13-64	-0.02
L13-65	-0.07
L13-66	-0.02
L13-67	-0.01
L13-68	-0.01

L13-69	-0.02
L13-70	-0.01
L13-71	Maintenance Needed
L13-72	-0.05
L13-73	-0.14
L13-74	-0.15
L13-75	-0.04
L13-76	0
L13-77	-0.02
L13-78	-0.10
L13-79	-0.10
L13-80	-0.05

Certification



Nancy Bahena Hernandez
22 Sep 2026 3:48 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	23 Sep 2026 1:56 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.05
SW 07	-0.05
SW 06	-0.02
SW 05	0.05
SW 04	-0.05
SW 03	-0.05
SW 02	0
SW 01	-0.05
44	0
111	-0.01
LCM 11	-0.12
LCM 12	-0.05
LCM 13	-0.02
LCM 14	-0.12
LCM 15	-0.04
LCM 6	0.02
LCM 7	0
LCM 8	-0.03
LCM 9	-0.06
LCM 10	-0.04
LCM 1	Maintenance Needed
LCM 2	-0.10

LCM 3	-0.15
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.20
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.04
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	-0.02
D3	-0.25
D18	-0.25

D19	0.01
D20	-0.10
D21	Maintenance Needed
D22	0.12
D23	-0.25
D24	-0.01
D25	-0.25
D26	-0.25
D27	0.01
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.01
C13-06	0
C13-05	-0.02

C13-04	0
C13-03	0
C13-02	0.01
C13-01	-0.01
C13-09	-0.25
C13-10	0.25
C13-11	-0.25
C13-12	0.15
C13-13	-0.20
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.01
U13-62	-0.02
U13-61	0
U13-60	-0.01
U13-59	-0.01
U13-58	0.01
U13-57	-0.01
U13-56	-0.01
U13-55	-0.05
U13-54	-0.01
U13-53	-0.03

U13-52	-0.15
U13-51	0
U13-50	0
U13-49	0
U13-48	-0.10
U13-47	-0.02
U13-46	0
U13-45	0
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.02
U13-40	-0.03
U13-39	0.01
U13-38	0
U13-37	0
U13-36	-0.13
U13-35	-0.11
U13-34	-0.12
U13-33	-0.05
U13-32	-0.07
U13-31	Maintenance Needed
U13-30	Maintenance Needed
U13-29	Maintenance Needed

U13-28	Maintenance Needed
U13-27	Maintenance Needed
U13-26	Maintenance Needed
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.10
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.15
U13-01	-0.25
L13-01	0
L13-02	-0.25
L13-03	-0.01
L13-04	-0.18
L13-05	-0.25
L13-06	-0.25
L13-07	-0.07
L13-08	-0.25
L13-09	-0.25
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.03
L13-14	-0.01
L13-15	-0.25
L13-16	-0.11
L13-17	-0.10
L13-18	-0.10
L13-19	-0.10
L13-20	-0.10

L13-21	-0.12
L13-22	-0.06
L13-23	-0.09
L13-24	-0.10
L13-25	-0.25
L13-26	-0.10
L13-27	-0.25
L13-28	-0.25
L13-29	-0.10
L13-30	-0.07
L13-31	-0.07
L13-32	-0.07
L13-33	-0.07
L13-34	-0.02
L13-35	-0.02
L13-36	-0.12
L13-37	-0.06
L13-38	0
L13-39	-0.02
L13-40	0
L13-41	-0.03
L13-42	-0.01
L13-43	-0.02
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.02
L13-47	-0.02
L13-48	-0.05
L13-49	-0.05
L13-50	-0.05
L13-51	-0.01
L13-52	0
L13-53	-0.01
L13-54	-0.25
L13-55	-0.20
L13-56	-0.11
L13-57	-0.01
L13-58	-0.20
L13-59	-0.25
L13-60	-0.25
L13-61	-0.25
L13-62	0
L13-63	-0.25
L13-64	-0.01
L13-65	-0.06
L13-66	-0.05
L13-67	-0.01
L13-68	-0.05

L13-69	-0.05
L13-70	-0.04
L13-71	Maintenance Needed
L13-72	-0.10
L13-73	-0.23
L13-74	-0.12
L13-75	-0.11
L13-76	-0.10
L13-77	-0.01
L13-78	-0.15
L13-79	-0.15
L13-80	-0.05

Certification



Nancy Bahena Hernandez
23 Sep 2026 4:05 PM PDT

4050 - Daily Pressure Gauge Readings

John Boucher

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	Marked as ‘my site is not listed here’
Conducted on	24 Sep 2026 7:06 AM PDT
Prepared by	John Boucher

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.04
SW 07	-0.05
SW 06	-0.03
SW 05	0.05
SW 04	-0.05
SW 03	-0.05
SW 02	0
SW 01	-0.05
44	0
111	-0.02
LCM 11	-0.10
LCM 12	-0.06
LCM 13	-0.03
LCM 14	-0.10
LCM 15	-0.05
LCM 6	0.01
LCM 7	0
LCM 8	-0.02
LCM 9	-0.05
LCM 10	-0.05
LCM 1	Maintenance Needed
LCM 2	-0.10

LCM 3	-0.15
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.20
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.24
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.25
D5	-0.25
D4	0
D3	-0.25
D18	-0.25

D19	0
D20	-0.09
D21	Maintenance Needed
D22	0.10
D23	-0.25
D24	0
D25	-0.25
D26	-0.25
D27	0
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	0
C13-06	-0.01
C13-05	-0.01

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.01
C13-09	-0.25
C13-10	0.25
C13-11	-0.25
C13-12	0.14
C13-13	-0.19
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	0
U13-62	-0.01
U13-61	0
U13-60	0
U13-59	0
U13-58	0
U13-57	0
U13-56	-0.01
U13-55	-0.04
U13-54	-0.02
U13-53	-0.02

U13-52	-0.14
U13-51	0
U13-50	0
U13-49	0
U13-48	-0.08
U13-47	-0.03
U13-46	0
U13-45	0
U13-44	-0.01
U13-43	0
U13-42	-0.01
U13-41	-0.01
U13-40	-0.02
U13-39	0
U13-38	0
U13-37	0
U13-36	-0.12
U13-35	-0.10
U13-34	-0.11
U13-33	-0.05
U13-32	-0.06
U13-31	Maintenance Needed
U13-30	Maintenance Needed
U13-29	Maintenance Needed

U13-28	Maintenance Needed
U13-27	Maintenance Needed
U13-26	Maintenance Needed
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.09
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.15
U13-01	-0.25
L13-01	0
L13-02	-0.25
L13-03	0
L13-04	-0.20
L13-05	-0.25
L13-06	-0.25
L13-07	-0.05
L13-08	-0.25
L13-09	-0.25
L13-10	0.09
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	0
L13-15	-0.25
L13-16	-0.10
L13-17	-0.10
L13-18	-0.10
L13-19	-0.10
L13-20	-0.10

L13-21	-0.10
L13-22	-0.07
L13-23	-0.08
L13-24	-0.10
L13-25	-0.25
L13-26	-0.09
L13-27	-0.25
L13-28	-0.25
L13-29	-0.09
L13-30	-0.07
L13-31	-0.06
L13-32	-0.06
L13-33	-0.06
L13-34	-0.01
L13-35	-0.01
L13-36	-0.10
L13-37	-0.05
L13-38	0
L13-39	-0.01
L13-40	-0.01
L13-41	-0.02
L13-42	-0.01
L13-43	-0.01
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.02
L13-47	-0.01
L13-48	-0.05
L13-49	-0.04
L13-50	-0.05
L13-51	0
L13-52	0
L13-53	-0.01
L13-54	-0.25
L13-55	-0.20
L13-56	-0.10
L13-57	-0.01
L13-58	-0.20
L13-59	-0.25
L13-60	-0.25
L13-61	-0.25
L13-62	0
L13-63	-0.25
L13-64	0
L13-65	-0.05
L13-66	-0.05
L13-67	0
L13-68	-0.05

L13-69	-0.05
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.10
L13-73	-0.22
L13-74	-0.11
L13-75	-0.10
L13-76	-0.10
L13-77	0
L13-78	-0.15
L13-79	-0.15
L13-80	-0.05

Certification



John Boucher
24 Sep 2026 10:16 AM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	25 Sep 2026 7:45 AM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	-0.20
SW 07	-0.02
SW 06	0.25
SW 05	0.02
SW 04	-0.02
SW 03	-0.05
SW 02	0
SW 01	-0.05
44	0
111	-0.01
LCM 11	-0.05
LCM 12	-0.02
LCM 13	-0.01
LCM 14	-0.10
LCM 15	0
LCM 6	0.05
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.10
LCM 10	-0.07
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.05
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0.01
D6	-0.02
D5	0
D4	-0.01
D3	0.25
D18	-0.20

D19	0
D20	-0.11
D21	Maintenance Needed
D22	0.10
D23	-0.08
D24	-0.02
D25	-0.25
D26	0.25
D27	0
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.04
C13-07	-0.04
C13-06	-0.03
C13-05	-0.07

C13-04	0
C13-03	-0.01
C13-02	0
C13-01	-0.02
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.18
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.02
U13-62	-0.02
U13-61	0
U13-60	-0.01
U13-59	-0.01
U13-58	0
U13-57	-0.01
U13-56	-0.01
U13-55	-0.05
U13-54	0
U13-53	-0.01

U13-52	-0.15
U13-51	-0.02
U13-50	-0.02
U13-49	-0.01
U13-48	-0.02
U13-47	-0.02
U13-46	0
U13-45	-0.02
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.01
U13-40	-0.01
U13-39	0
U13-38	-0.02
U13-37	-0.02
U13-36	-0.20
U13-35	-0.15
U13-34	-0.17
U13-33	-0.05
U13-32	-0.06
U13-31	Maintenance Needed
U13-30	Maintenance Needed
U13-29	Maintenance Needed

U13-28	Maintenance Needed
U13-27	Maintenance Needed
U13-26	Maintenance Needed
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.10
U13-05	-0.25


U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.20
U13-01	-0.25
L13-01	-0.01
L13-02	0.10
L13-03	-0.02
L13-04	-0.17
L13-05	-0.10
L13-06	-0.02
L13-07	-0.06
L13-08	-0.01
L13-09	-0.04
L13-10	0.07
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.02
L13-15	-0.07
L13-16	-0.10
L13-17	-0.10
L13-18	-0.07
L13-19	-0.07
L13-20	-0.06

L13-21	-0.10
L13-22	-0.05
L13-23	-0.05
L13-24	-0.02
L13-25	0
L13-26	0.25
L13-27	-0.06
L13-28	-0.05
L13-29	-0.02
L13-30	-0.07
L13-31	-0.05
L13-32	-0.05
L13-33	-0.05
L13-34	-0.02
L13-35	-0.02
L13-36	-0.07
L13-37	-0.06
L13-38	-0.02
L13-39	-0.02
L13-40	-0.03
L13-41	-0.02
L13-42	-0.04
L13-43	-0.03
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.04
L13-47	-0.03
L13-48	-0.04
L13-49	-0.03
L13-50	-0.03
L13-51	-0.01
L13-52	-0.01
L13-53	-0.01
L13-54	0.15
L13-55	0.05
L13-56	0.20
L13-57	-0.05
L13-58	0.03
L13-59	0.02
L13-60	0.01
L13-61	-0.04
L13-62	0
L13-63	0.07
L13-64	0
L13-65	-0.10
L13-66	-0.05
L13-67	-0.01
L13-68	-0.05

L13-69	-0.06
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.07
L13-73	0.10
L13-74	-0.02
L13-75	-0.10
L13-76	-0.05
L13-77	-0.03
L13-78	0
L13-79	0.01
L13-80	-0.03

Certification



Nancy Bahena Hernandez
25 Sep 2026 3:12 PM PDT

4050 - Daily Pressure Gauge Readings

John Boucher

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	Marked as ‘my site is not listed here’
Conducted on	26 Sep 2026 7:12 AM PDT
Prepared by	John Boucher

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	-0.19
SW 07	-0.01
SW 06	-0.24
SW 05	0.01
SW 04	-0.01
SW 03	-0.04
SW 02	-0.01
SW 01	-0.04
44	0
111	0
LCM 11	-0.04
LCM 12	-0.01
LCM 13	-0.01
LCM 14	-0.08
LCM 15	0
LCM 6	0.03
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.09
LCM 10	-0.05
LCM 1	Maintenance Needed
LCM 2	-0.23

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.04
D2	-0.24
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.03
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	0
D6	-0.01
D5	0
D4	0
D3	0.25
D18	-0.21

D19	0
D20	-0.10
D21	Maintenance Needed
D22	0.08
D23	-0.06
D24	-0.01
D25	-0.25
D26	0.25
D27	0
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.03
C13-07	-0.05
C13-06	-0.04
C13-05	-0.08

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.01
C13-09	-0.25
C13-10	-0.25
C13-11	-0.25
C13-12	-0.20
C13-13	-0.25
C13-14	-0.25
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.01
U13-62	-0.01
U13-61	0
U13-60	0
U13-59	0
U13-58	0
U13-57	0
U13-56	0
U13-55	-0.04
U13-54	0
U13-53	0

U13-52	-0.15
U13-51	-0.01
U13-50	-0.01
U13-49	-0.01
U13-48	-0.01
U13-47	-0.01
U13-46	0
U13-45	-0.01
U13-44	0
U13-43	0
U13-42	-0.01
U13-41	-0.01
U13-40	-0.01
U13-39	-0.01
U13-38	-0.01
U13-37	-0.01
U13-36	-0.20
U13-35	-0.15
U13-34	-0.15
U13-33	-0.05
U13-32	-0.05
U13-31	Maintenance Needed
U13-30	Maintenance Needed
U13-29	Maintenance Needed

U13-28	Maintenance Needed
U13-27	Maintenance Needed
U13-26	Maintenance Needed
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.08
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.19
U13-01	-0.25
L13-01	0
L13-02	0.09
L13-03	-0.01
L13-04	-0.15
L13-05	-0.10
L13-06	-0.01
L13-07	-0.05
L13-08	-0.01
L13-09	-0.05
L13-10	0.05
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.01
L13-14	-0.01
L13-15	-0.06
L13-16	-0.10
L13-17	-0.10
L13-18	-0.06
L13-19	-0.06
L13-20	-0.05

L13-21	-0.10
L13-22	-0.05
L13-23	-0.05
L13-24	-0.03
L13-25	0
L13-26	0.25
L13-27	-0.05
L13-28	-0.05
L13-29	-0.01
L13-30	-0.05
L13-31	-0.05
L13-32	-0.05
L13-33	-0.05
L13-34	-0.01
L13-35	-0.01
L13-36	-0.06
L13-37	-0.05
L13-38	-0.01
L13-39	-0.01
L13-40	-0.02
L13-41	-0.02
L13-42	-0.05
L13-43	-0.04
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.05
L13-47	-0.04
L13-48	-0.05
L13-49	-0.04
L13-50	-0.05
L13-51	-0.02
L13-52	-0.02
L13-53	-0.02
L13-54	0.15
L13-55	0.05
L13-56	0.20
L13-57	-0.03
L13-58	0.03
L13-59	0.01
L13-60	0.01
L13-61	-0.05
L13-62	0
L13-63	0.06
L13-64	0
L13-65	-0.10
L13-66	-0.06
L13-67	0
L13-68	-0.06

L13-69	-0.05
L13-70	-0.05
L13-71	Maintenance Needed
L13-72	-0.07
L13-73	0.10
L13-74	-0.01
L13-75	-0.10
L13-76	-0.06
L13-77	-0.04
L13-78	-0.01
L13-79	0
L13-80	-0.01

Certification



John Boucher
26 Sep 2026 11:42 AM PDT

4050 - Daily Pressure Gauge Readings

Tom Roe

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	27 Sep 2026 7:40 AM PDT
Prepared by	Tom Roe

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.05
SW 06	0.01
SW 05	0.04
SW 04	-0.03
SW 03	-0.06
SW 02	0
SW 01	-0.03
44	0
111	-0.01
LCM 11	0
LCM 12	-0.04
LCM 13	-0.03
LCM 14	-0.01
LCM 15	-0.02
LCM 6	0.05
LCM 7	-0.02
LCM 8	Maintenance Needed
LCM 9	0
LCM 10	-0.02
LCM 1	0.11
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.17
D2	-0.25
CD3	Tank Not In Use/In Staging Area
CD4	Tank Not In Use/In Staging Area
D17	-0.05
D16	-0.25
D15	Maintenance Needed
D14	Maintenance Needed
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	Maintenance Needed
D7	-0.02
D6	-0.25
D5	-0.02
D4	-0.03
D3	-0.25
D18	-0.25

D19	0.02
D20	-0.11
D21	Maintenance Needed
D22	0.03
D23	-0.25
D24	-0.03
D25	-0.25
D26	-0.25
D27	-0.02
D28	-0.25
D29	Maintenance Needed
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	Tank Not In Use/In Staging Area
C13-07	Tank Not In Use/In Staging Area
C13-06	Tank Not In Use/In Staging Area
C13-05	Tank Not In Use/In Staging Area

C13-04	Tank Not In Use/In Staging Area
C13-03	Tank Not In Use/In Staging Area
C13-02	Tank Not In Use/In Staging Area
C13-01	Tank Not In Use/In Staging Area
C13-09	-0.25
C13-10	-0.25
C13-11	0.25
C13-12	-0.15
C13-13	-0.25
C13-14	-0.25
C13-15	0.25
C13-16	0.25
T1/T2 190	-0.12
U13-63	-0.02
U13-62	-0.02
U13-61	-0.01
U13-60	-0.01
U13-59	-0.01
U13-58	0
U13-57	Tank Not In Use/In Staging Area
U13-56	Tank Not In Use/In Staging Area
U13-55	Tank Not In Use/In Staging Area
U13-54	0.01
U13-53	-0.01

U13-52	-0.14
U13-51	-0.02
U13-50	-0.01
U13-49	Tank Not In Use/In Staging Area
U13-48	-0.05
U13-47	-0.02
U13-46	-0.02
U13-45	0
U13-44	0.01
U13-43	0.02
U13-42	-0.02
U13-41	-0.02
U13-40	0.01
U13-39	0
U13-38	-0.02
U13-37	-0.03
U13-36	-0.20
U13-35	-0.12
U13-34	-0.17
U13-33	-0.04
U13-32	-0.07
U13-31	-0.12
U13-30	-0.11
U13-29	-0.05

U13-28	-0.11
U13-27	-0.07
U13-26	-0.06
U13-25	-0.11
U13-24	-0.10
U13-23	-0.12
U13-22	-0.08
U13-21	-0.04
U13-20	-0.01
U13-19	-0.08
U13-18	0.25
U13-17	0.25
U13-16	0.25
U13-15	0.25
U13-14	0.25
U13-13	0.25
U13-12	0.25
U13-11	0.25
U13-10	0.25
U13-09	0.25
U13-08	0.25
U13-07	0.25
U13-06	-0.07
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.14
U13-01	-0.25
L13-01	0.08
L13-02	-0.25
L13-03	0.05
L13-04	-0.15
L13-05	-0.13
L13-06	-0.10
L13-07	-0.07
L13-08	-0.11
L13-09	-0.09
L13-10	0.11
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.02
L13-14	-0.01
L13-15	-0.17
L13-16	-0.12
L13-17	-0.11
L13-18	-0.10
L13-19	-0.09
L13-20	-0.09

L13-21	-0.12
L13-22	-0.04
L13-23	-0.08
L13-24	-0.10
L13-25	-0.07
L13-26	-0.07
L13-27	-0.08
L13-28	-0.12
L13-29	-0.10
L13-30	-0.09
L13-31	-0.04
L13-32	-0.06
L13-33	-0.06
L13-34	-0.02
L13-35	-0.02
L13-36	-0.10
L13-37	-0.04
L13-38	-0.02
L13-39	-0.03
L13-40	-0.16
L13-41	-0.25
L13-42	-0.25
L13-43	-0.15
L13-44	Maintenance Needed

L13-45	-0.02
L13-46	-0.03
L13-47	-0.04
L13-48	-0.04
L13-49	-0.04
L13-50	-0.03
L13-51	-0.02
L13-52	-0.02
L13-53	-0.03
L13-54	-0.01
L13-55	-0.03
L13-56	0.04
L13-57	-0.03
L13-58	-0.05
L13-59	-0.07
L13-60	-0.09
L13-61	-0.14
L13-62	0.01
L13-63	-0.03
L13-64	0
L13-65	-0.08
L13-66	-0.04
L13-67	-0.02
L13-68	-0.03

L13-69	-0.05
L13-70	-0.04
L13-71	Maintenance Needed
L13-72	-0.09
L13-73	-0.02
L13-74	-0.07
L13-75	-0.09
L13-76	-0.07
L13-77	-0.04
L13-78	-0.12
L13-79	-0.11
L13-80	-0.02

Certification



Tom Roe
27 Sep 2026 10:06 AM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	28 Sep 2026 1:53 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0
SW 07	-0.02
SW 06	-0.06
SW 05	-0.02
SW 04	-0.01
SW 03	-0.06
SW 02	0
SW 01	-0.02
44	0
111	0
LCM 11	-0.10
LCM 12	-0.03
LCM 13	-0.02
LCM 14	-0.07
LCM 15	-0.01
LCM 6	0.03
LCM 7	0
LCM 8	-0.02
LCM 9	-0.05
LCM 10	-0.01
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.10
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.04
D16	-0.25
D15	-0.25
D14	-0.25
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	-0.25
D7	-0.02
D6	-0.07
D5	-0.25
D4	-0.02
D3	-0.25
D18	-0.25

D19	0.07
D20	-0.10
D21	-0.05
D22	0.01
D23	-0.25
D24	-0.02
D25	-0.25
D26	-0.25
D27	-0.05
D28	-0.25
D29	0.25
D30	-0.07
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.04
C13-07	-0.03
C13-06	-0.03
C13-05	-0.05

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.01
C13-09	-0.20
C13-10	0.25
C13-11	-0.12
C13-12	0.25
C13-13	-0.25
C13-14	-0.17
C13-15	-0.25
C13-16	-0.25
T1/T2 190	-0.25
U13-63	-0.02
U13-62	-0.02
U13-61	0
U13-60	-0.01
U13-59	-0.01
U13-58	0
U13-57	-0.01
U13-56	-0.01
U13-55	-0.05
U13-54	0
U13-53	-0.02

U13-52	-0.15
U13-51	-0.02
U13-50	0
U13-49	0
U13-48	-0.07
U13-47	-0.01
U13-46	-0.02
U13-45	0
U13-44	0
U13-43	0
U13-42	-0.02
U13-41	-0.03
U13-40	0
U13-39	-0.02
U13-38	0
U13-37	-0.02
U13-36	-0.25
U13-35	-0.20
U13-34	-0.20
U13-33	-0.07
U13-32	-0.10
U13-31	Maintenance Needed
U13-30	Maintenance Needed
U13-29	Maintenance Needed

U13-28	Maintenance Needed
U13-27	Maintenance Needed
U13-26	Maintenance Needed
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.05
U13-05	-0.25

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.25
U13-01	-0.25
L13-01	0
L13-02	-0.20
L13-03	0
L13-04	-0.10
L13-05	0
L13-06	-0.17
L13-07	-0.10
L13-08	-0.17
L13-09	-0.20
L13-10	0.15
L13-11	Maintenance Needed
L13-12	-0.12
L13-13	-0.03
L13-14	-0.03
L13-15	-0.25
L13-16	-0.10
L13-17	-0.12
L13-18	-0.10
L13-19	-0.08
L13-20	-0.07

L13-21	-0.10
L13-22	-0.05
L13-23	-0.10
L13-24	-0.10
L13-25	-0.15
L13-26	-0.06
L13-27	-0.15
L13-28	-0.20
L13-29	-0.11
L13-30	-0.03
L13-31	-0.06
L13-32	-0.06
L13-33	-0.10
L13-34	-0.02
L13-35	-0.02
L13-36	-0.13
L13-37	-0.10
L13-38	-0.03
L13-39	-0.01
L13-40	-0.05
L13-41	0
L13-42	0.03
L13-43	-0.01
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.05
L13-47	-0.05
L13-48	-0.05
L13-49	-0.05
L13-50	-0.05
L13-51	-0.01
L13-52	-0.01
L13-53	-0.02
L13-54	-0.15
L13-55	-0.11
L13-56	-0.05
L13-57	-0.05
L13-58	-0.11
L13-59	-0.15
L13-60	-0.15
L13-61	-0.20
L13-62	-0.03
L13-63	-0.12
L13-64	-0.01
L13-65	-0.07
L13-66	-0.05
L13-67	-0.01
L13-68	-0.05

L13-69	-0.06
L13-70	-0.06
L13-71	Maintenance Needed
L13-72	-0.10
L13-73	-0.12
L13-74	-0.10
L13-75	-0.10
L13-76	-0.06
L13-77	-0.02
L13-78	-0.10
L13-79	-0.08
L13-80	-0.02

Certification



Nancy Bahena Hernandez
28 Sep 2026 3:32 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	Flagged items	0	Actions	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	29 Sep 2026 1:50 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.01
SW 07	-0.01
SW 06	0.10
SW 05	0.05
SW 04	-0.01
SW 03	-0.05
SW 02	0
SW 01	-0.03
44	0
111	-0.01
LCM 11	-0.10
LCM 12	-0.05
LCM 13	-0.01
LCM 14	-0.10
LCM 15	0
LCM 6	0.05
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	0
LCM 1	Maintenance Needed
LCM 2	-0.25

LCM 3	-0.25
LCM 4	-0.25
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.20
D2	-0.25
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.03
D16	-0.25
D15	-0.25
D14	-0.25
D13	-0.25
D12	-0.25
D11	-0.25
D10	-0.25
D9	-0.25
D8	-0.25
D7	-0.01
D6	-0.25
D5	-0.25
D4	0
D3	0.10
D18	-0.25

D19	0.02
D20	-0.10
D21	-0.05
D22	0.01
D23	-0.25
D24	0
D25	-0.25
D26	-0.25
D27	0
D28	-0.25
D29	0.25
D30	-0.25
D31	-0.25
D32	-0.25
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	0
C13-06	0
C13-05	-0.01

C13-04	0
C13-03	0
C13-02	0
C13-01	0
C13-09	-0.25
C13-10	0.25
C13-11	0
C13-12	-0.05
C13-13	-0.05
C13-14	-0.05
C13-15	-0.02
C13-16	-0.05
T1/T2 190	0
U13-63	-0.01
U13-62	-0.02
U13-61	0
U13-60	-0.02
U13-59	-0.05
U13-58	-0.02
U13-57	-0.02
U13-56	0
U13-55	-0.05
U13-54	0
U13-53	-0.02

U13-52	-0.15
U13-51	0
U13-50	-0.02
U13-49	-0.01
U13-48	-0.06
U13-47	-0.02
U13-46	-0.01
U13-45	0
U13-44	0
U13-43	0
U13-42	-0.01
U13-41	-0.02
U13-40	0
U13-39	0
U13-38	-0.01
U13-37	0
U13-36	-0.07
U13-35	-0.05
U13-34	-0.07
U13-33	-0.05
U13-32	-0.03
U13-31	Maintenance Needed
U13-30	Maintenance Needed
U13-29	Maintenance Needed

U13-28	Maintenance Needed
U13-27	Maintenance Needed
U13-26	Maintenance Needed
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.06
U13-05	-0.24

U13-04	Maintenance Needed
U13-03	0
U13-02	-0.05
U13-01	-0.25
L13-01	-0.01
L13-02	-0.20
L13-03	0
L13-04	-0.20
L13-05	-0.15
L13-06	-0.25
L13-07	-0.05
L13-08	-0.24
L13-09	-0.25
L13-10	0.03
L13-11	Maintenance Needed
L13-12	-0.22
L13-13	-0.02
L13-14	-0.02
L13-15	-0.25
L13-16	-0.05
L13-17	-0.05
L13-18	-0.05
L13-19	-0.05
L13-20	-0.25

L13-21	-0.25
L13-22	-0.02
L13-23	0.01
L13-24	-0.05
L13-25	-0.21
L13-26	-0.02
L13-27	-0.23
L13-28	-0.25
L13-29	-0.05
L13-30	-0.05
L13-31	-0.01
L13-32	-0.02
L13-33	-0.02
L13-34	-0.02
L13-35	-0.02
L13-36	-0.10
L13-37	-0.06
L13-38	-0.02
L13-39	-0.02
L13-40	0
L13-41	-0.05
L13-42	-0.05
L13-43	-0.10
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.05
L13-47	-0.04
L13-48	-0.05
L13-49	-0.05
L13-50	-0.05
L13-51	-0.02
L13-52	0
L13-53	-0.02
L13-54	-0.25
L13-55	-0.20
L13-56	-0.15
L13-57	-0.02
L13-58	-0.20
L13-59	-0.22
L13-60	-0.25
L13-61	-0.25
L13-62	0
L13-63	-0.25
L13-64	-0.01
L13-65	-0.06
L13-66	0
L13-67	-0.01
L13-68	-0.02

L13-69	-0.02
L13-70	-0.02
L13-71	-0.02
L13-72	-0.05
L13-73	-0.20
L13-74	-0.15
L13-75	-0.07
L13-76	-0.02
L13-77	0
L13-78	-0.17
L13-79	-0.15
L13-80	-0.02

Certification



Nancy Bahena Hernandez
29 Sep 2026 3:25 PM PDT

4050 - Daily Pressure Gauge Readings

Nancy Bahena Hernandez

Complete

Score	224 / 224 (100%)	**Flagged items**	0	**Actions**	0

Site conducted	4050 - Chiquita Canyon Landfill -, Corporate (Overall), Western, Western/SO CA L/F
Conducted on	30 Sep 2026 1:39 PM PDT
Prepared by	Nancy Bahena Hernandez

Pressure Gauge Readings	224 / 224 (100%)
#7 Tank Farm	25 / 25 (100%)
SW 08	0.01
SW 07	-0.02
SW 06	0
SW 05	0.02
SW 04	-0.01
SW 03	-0.06
SW 02	0
SW 01	-0.03
44	0
111	0
LCM 11	-0.11
LCM 12	-0.05
LCM 13	-0.01
LCM 14	-0.10
LCM 15	0.01
LCM 6	0.03
LCM 7	0
LCM 8	Maintenance Needed
LCM 9	-0.05
LCM 10	-0.03
LCM 1	Maintenance Needed
LCM 2	-0.12

LCM 3	-0.12
LCM 4	-0.16
LCM 5	-0.25
#10 Tank Farm Canyon D	39 / 39 (100%)
D1	-0.02
D2	-0.12
CD3	Maintenance Needed
CD4	Maintenance Needed
D17	-0.05
D16	-0.20
D15	-0.12
D14	-0.20
D13	-0.24
D12	0.01
D11	-0.23
D10	-0.21
D9	-0.20
D8	-0.16
D7	-0.01
D6	-0.20
D5	-0.21
D4	-0.05
D3	-0.23
D18	-0.16

D19	0.01
D20	-0.10
D21	0.02
D22	0.02
D23	-0.12
D24	-0.01
D25	-0.25
D26	-0.25
D27	0.01
D28	-0.12
D29	0.25
D30	-0.12
D31	-0.08
D32	-0.07
D/SW-01	Maintenance Needed
D/SW-02	Maintenance Needed
D/SW-03	Maintenance Needed
D/SW-04	Maintenance Needed
D/SW-05	Maintenance Needed
#13 Tank Farm	160 / 160 (100%)
C13-08	0.05
C13-07	-0.01
C13-06	0
C13-05	-0.01

C13-04	0
C13-03	0
C13-02	0
C13-01	-0.05
C13-09	Maintenance Needed
C13-10	0.25
C13-11	0.25
C13-12	0.25
C13-13	0.25
C13-14	0.25
C13-15	0.25
C13-16	0.25
T1/T2 190	0.25
U13-63	-0.01
U13-62	-0.02
U13-61	0
U13-60	-0.02
U13-59	-0.01
U13-58	0
U13-57	-0.02
U13-56	0
U13-55	-0.05
U13-54	0
U13-53	-0.05

U13-52	-0.15
U13-51	-0.01
U13-50	-0.01
U13-49	0
U13-48	-0.06
U13-47	-0.05
U13-46	0
U13-45	0
U13-44	-0.01
U13-43	0
U13-42	-0.02
U13-41	-0.02
U13-40	0
U13-39	0
U13-38	-0.01
U13-37	0
U13-36	-0.02
U13-35	-0.02
U13-34	-0.03
U13-33	-0.05
U13-32	-0.05
U13-31	Maintenance Needed
U13-30	Maintenance Needed
U13-29	Maintenance Needed

U13-28	Maintenance Needed
U13-27	Maintenance Needed
U13-26	Maintenance Needed
U13-25	Maintenance Needed
U13-24	Maintenance Needed
U13-23	Maintenance Needed
U13-22	Maintenance Needed
U13-21	Maintenance Needed
U13-20	Maintenance Needed
U13-19	Maintenance Needed
U13-18	Maintenance Needed
U13-17	Maintenance Needed
U13-16	Maintenance Needed
U13-15	Maintenance Needed
U13-14	Maintenance Needed
U13-13	Maintenance Needed
U13-12	Maintenance Needed
U13-11	Maintenance Needed
U13-10	Maintenance Needed
U13-09	Maintenance Needed
U13-08	Maintenance Needed
U13-07	Maintenance Needed
U13-06	-0.05
U13-05	-0.07

U13-04	Maintenance Needed
U13-03	Maintenance Needed
U13-02	-0.06
U13-01	-0.10
L13-01	-0.01
L13-02	-0.16
L13-03	0
L13-04	-0.15
L13-05	-0.12
L13-06	-0.25
L13-07	-0.07
L13-08	-0.25
L13-09	-0.25
L13-10	0.10
L13-11	Maintenance Needed
L13-12	Maintenance Needed
L13-13	-0.03
L13-14	-0.02
L13-15	-0.25
L13-16	-0.10
L13-17	-0.06
L13-18	-0.06
L13-19	-0.06
L13-20	-0.05

L13-21	-0.06
L13-22	-0.05
L13-23	-0.02
L13-24	-0.07
L13-25	-0.20
L13-26	-0.05
L13-27	-0.20
L13-28	-0.25
L13-29	-0.06
L13-30	-0.05
L13-31	-0.07
L13-32	-0.06
L13-33	-0.06
L13-34	-0.04
L13-35	-0.03
L13-36	-0.10
L13-37	-0.10
L13-38	-0.02
L13-39	-0.02
L13-40	-0.02
L13-41	-0.02
L13-42	-0.05
L13-43	-0.05
L13-44	Maintenance Needed

L13-45	-0.01
L13-46	-0.02
L13-47	-0.01
L13-48	-0.03
L13-49	-0.05
L13-50	-0.04
L13-51	-0.01
L13-52	0
L13-53	-0.02
L13-54	-0.25
L13-55	-0.17
L13-56	-0.12
L13-57	-0.02
L13-58	-0.15
L13-59	-0.20
L13-60	-0.22
L13-61	-0.25
L13-62	0
L13-63	-0.20
L13-64	-0.01
L13-65	-0.07
L13-66	-0.05
L13-67	-0.02
L13-68	-0.05

L13-69	-0.05
L13-70	-0.04
L13-71	Maintenance Needed
L13-72	-0.09
L13-73	-0.21
L13-74	-0.15
L13-75	-0.10
L13-76	-0.02
L13-77	-0.01
L13-78	-0.15
L13-79	-0.11
L13-80	-0.01

Certification



Nancy Bahena Hernandez
30 Sep 2026 3:13 PM PDT

Attachment N

Various Location Equipment/PERP Log

Permit, VIN or Registration # of Equipment	Application #	Location of Equipment	Date In	Date Out	Date Moved	Moved From	Comments
Reg# 164437 (Rent-A-Bin)	N/A	Primary Canyon	1/3/2025	Still Onsite	May 2026	Pick Up Area	Eagle Crusher (third-party consultant)
Reg# 198839 & 198840 (United # 11456733)	N/A	3 TOx	1/28/2025	Still Onsite	January 2026	Flares	Standby Generator for TOx if lose power
Reg# 149175 (Rent-A-Bin)	N/A	Primary Canyon	6/1/2025	Still Onsite	May 2026	Pick Up Area	McCloskey Screen (third-party consultant)
Reg# 184642 (United # 10966686)	N/A	TF13	6/13/2025	Still Onsite	May 2026	Top Deck	Waiting for new mini TOx station
Reg# 199845 (United # 11442219)	N/A	North Perimeter	7/25/2025	Still Onsite	July 2026	Top Deck	Standby Generator for Hero TOx
Reg# 221126 (United # 12283682)	N/A	Top Deck East	8/17/2026	Still Onsite	N/A	N/A	Standby Generator for Parnel TOx

Attachment O

Geosynthetic Cover Weekly Inspections

4050 - Weekly Geosynthetic Cover Inspection-Condition 97

27 Aug 2026 / Nancy Bahena Hernandez / Tom Roe

Complete

Score	0 / 0 (0%)	**Flagged items**	0	**Actions**	0

Conducted on	27 Aug 2026 9:09 AM PDT
Prepared by	Nancy Bahena Hernandez / Tom Roe

Identification of Issues	
Identified Issue	
Identified Issue 1	
Are there any issues with the geosynthetic cover?	No



Photo 1

Media summary



Photo 1

4050 - Weekly Geosynthetic Cover Inspection-Condition 97

3 Sep 2026 / John Boucher/Tom Roe

Complete

Score	0 / 0 (0%)	**Flagged items**	0	**Actions**	0

Conducted on	3 Sep 2026 6:54 AM PDT
Prepared by	John Boucher/Tom Roe

Identification of Issues	
Identified Issue	
Identified Issue 1	
Are there any issues with the geosynthetic cover?	Yes
Date/Time Issue Found	8 Sep 2026 12:24 PM PDT

Take photo of identified issues



Photo 1

Notate what the issue is and what needs to be repaired	Tear at boot on well needs to be patched/extrusion welded.

Grid Location



Take photo of repair



Photo 2



Photo 3

Description of repair work	Tear taped upon discovery and later boot was replaced.
Date and time of repair	8 Sep 2026 12:34 PM PDT
Are further permanent repairs required?	No

Media summary



Photo 1



Photo 2



Photo 3

4050 - Weekly Geosynthetic Cover Inspection-Condition 97

10 Sep 2026 / John Boucher/Tom Roe

Complete

Score	0 / 0 (0%)	Flagged items	0	Actions	0

Conducted on	10 Sep 2026 12:48 PM PDT
Prepared by	John Boucher/Tom Roe

Identification of Issues	
Identified Issue	
Identified Issue 1	
Are there any issues with the geosynthetic cover?	No



Photo 1

Media summary



Photo 1

4050 - Weekly Geosynthetic Cover Inspection-Condition 97

17 Sep 2026 / John Boucher/Tom Roe

Complete

Score	0 / 0 (0%)	Flagged items	0	Actions	0

Conducted on	17 Sep 2026 2:40 PM PDT
Prepared by	John Boucher/Tom Roe

Identification of Issues	
Identified Issue	
Identified Issue 1	
Are there any issues with the geosynthetic cover?	Yes
Date/Time Issue Found	22 Sep 2026 10:27 AM PDT

Take photo of identified issues



Photo 1

Notate what the issue is and what needs to be repaired	Tear at weld on boot needs to be patched/extrusion welded.

Grid Location



Take photo of repair



Photo 2



Photo 3

Description of repair work	Tear taped upon discovery and later extrusion welded
Date and time of repair	22 Sep 2026 10:31 AM PDT
Are further permanent repairs required?	No

Permanent repairs completed on 9/30

Media summary



Photo 1



Photo 2



Photo 3

4050 - Weekly Geosynthetic Cover Inspection-Condition 97

24 Sep 2026 / John Boucher/Tom Roe

Complete

Score	0 / 0 (0%)	Flagged items	0	Actions	0

Conducted on	24 Sep 2026 7:05 AM PDT
Prepared by	John Boucher/Tom Roe

Identification of Issues	
Identified Issue	
Identified Issue 1	
Are there any issues with the geosynthetic cover?	Yes
Date/Time Issue Found	28 Sep 2026 10:05 AM PDT

Take photo of identified issues



Photo 1

Notate what the issue is and what needs to be repaired	Tear at weld in boot needs to be patched/extrusion welded.

Grid Location



Take photo of repair



Photo 2



Photo 3

Description of repair work	Tear taped upon discovery and later extrusion welded.
Date and time of repair	28 Sep 2026 10:11 AM PDT
Are further permanent repairs required?	No

Permanent repair completed on 9/30/26

Media summary



Photo 1



Photo 2



Photo 3

Attachment P

Leachate Tank Farm As-Built

DRAWINGS FOR THE

EXISTING LEACHATE TANK FARM SITE-MAPS


AT THE

CHIQUITA CANYON LANDFILL

CASTAIC, CALIFORNIA


PREPARED FOR

WASTE CONNECTIONS

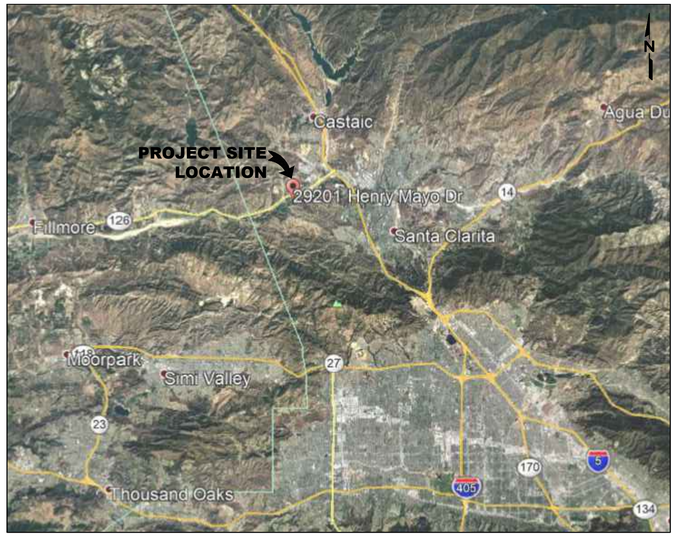

VICINITY MAP
N.T.S.

DRAWING NO.	DRAWING TITLE
1	TITLE SHEET
2	TANK FARM LOCATION MAP
3	TANK FARM 7
4	TANK FARM 10
5A	TANK FARM 13 - PRE-TREATMENT
5B	TANK FARM 13 - POST-TREATMENT
6	LCRS FRAC TANKS

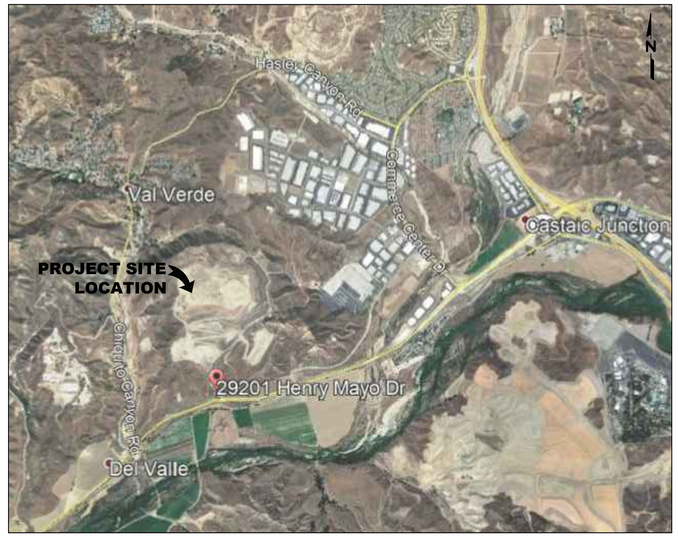

LOCATION MAP
N.T.S.

NO.	REVISION	DATE

SHEET TITLE: TITLE SHEET

PROJECT TITLE: EXISTING LEACHATE TANK FARM SITE-MAPS
CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544


PROJ. NO. 01204123.45 | DSN. BY: - | DWN. BY: CNW | CHK. BY: RNH | ACAD FILE: F:\ENGINEERS | APP. BY: RNH

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 1

\\bc-fs01\Data\CAD\ASBUILT - MASTERS\CHIQUITA\Leachate Tank Schematic\DWG\2026-10-20_CCLF Tank Farm Site Map(s) As-Built_v1.dwg Oct 20, 2026 - 11:44am By: raulramirez

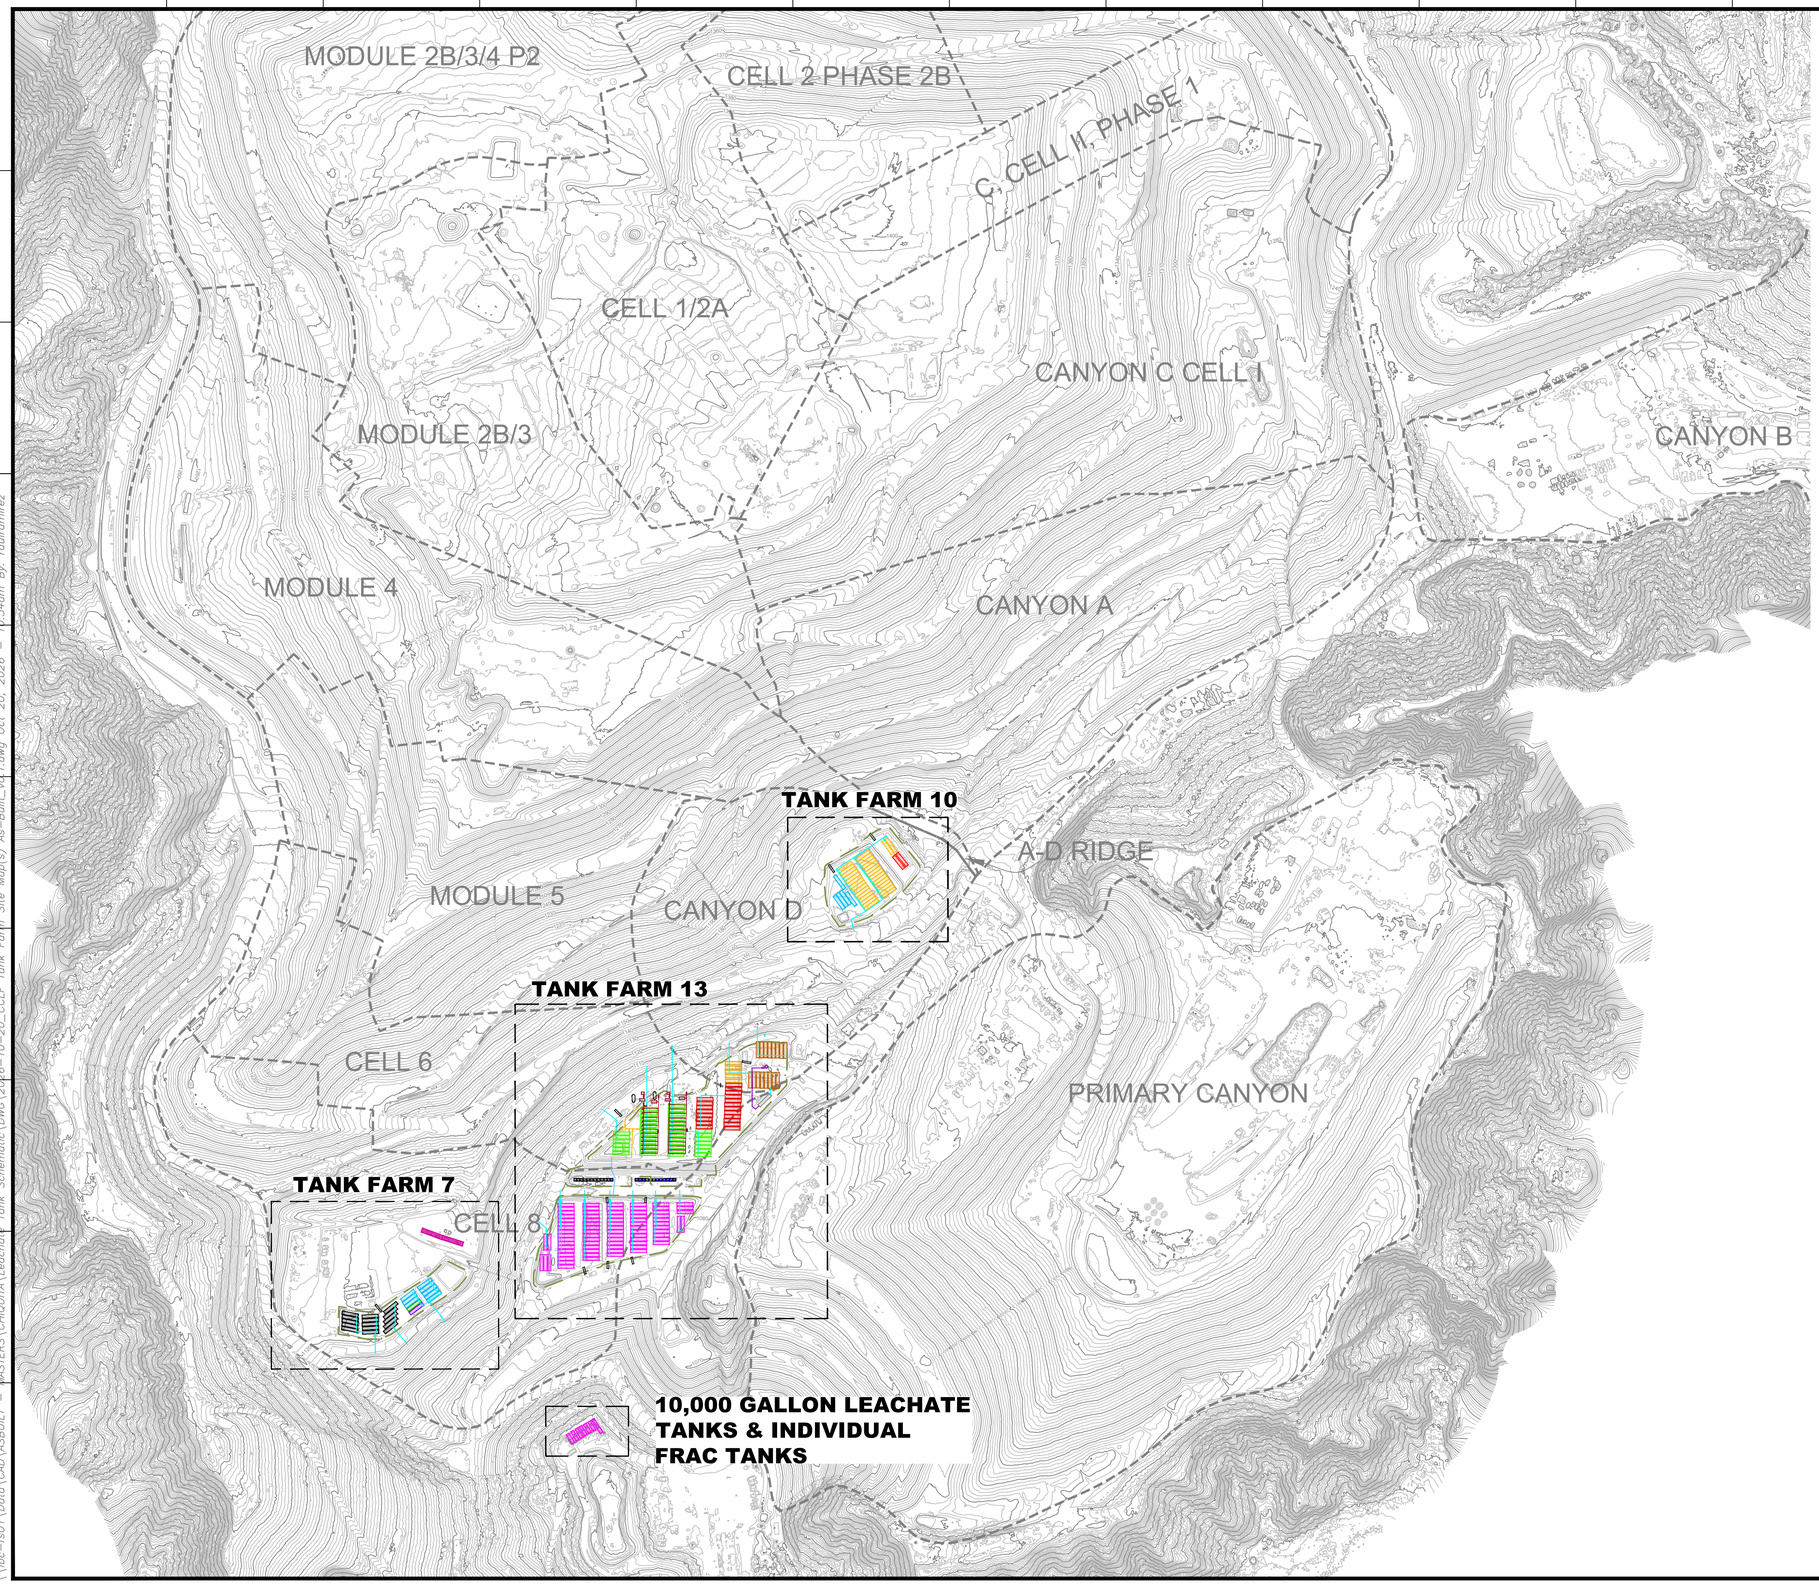

N

GRAPHIC SCALE

200 100 0 200 400 600

SCALE: 1"=200'

LEGEND

- EXISTING CELL LIMITS (APPROXIMATE)
- EXISTING FRAK TANK (COLOR BASED ON TANK TYPE)
- SP — SAMPLE POINT

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER AERIAL PHOTOGRAPHY DATED OCTOBER 14, 2026.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM LOCATION MAP

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3187 RED HILL AVENUE, SUITE 300
COSTA MESA, CALIFORNIA 92626
LONG BEACH, CA 90806
PH: (562) 426-9544

PROJ. NO. 01204123.45 | DSN. BY: RNH | DWN. BY: RR / CNW | CHK. BY: RNH | ACAD FILE: F:/ENGINEERS | APP. BY: RNH

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 2

\\lbc-fs01\Data\CAD\ASBUILT - MASTERS\CHIQUITA\Leachate Tank Schematic\DWG\2026-10-20_CCLF Tank Farm Site Map(s) As-Built_v01.dwg Oct 20, 2026 - 10:54am By: raulramirez

SOUTHERN
TOx STATION

INLET FORCEMAIN LINE

LOADOUT RACK
PUMP

LOADOUT RACK
PUMP

DESIGNATED LOCATION
FOR RECORDING LEACHATE
TEMPERATURE AT TANK FARM 7

STAIRS

LCM-05
LCM-04
LCM-03
LCM-02
LCM-01
LCM-06
LCM-07
LCM-08
LCM-09
LCM-10
LCM-15
LCM-14
LCM-13
LCM-12
LCM-11
SW-03
SW-02
SW-01
44
111
SW-04
SW-05
SW-06
SW-07
SW-08

ARV

TIES INTO EXISTING
VACUUM LINES

TIES INTO EXISTING
VACUUM LINES

TIES INTO EXISTING
VACUUM LINES

TF7 SAMPLE
POINT

TO TANK
FARM 13

1130
1120
1110
1100

N

GRAPHIC SCALE
30 15 0 30 60 90
SCALE: 1"= 30'

LEGEND

- 1150 — TOPOGRAPHIC CONTOUR
- 24" — EXISTING LFG COLLECTION HEADER PIPE
- 12" — EXISTING LFG COLLECTION HEADER PIPE
- 3" & 6" — EXISTING DUAL FORCEMAIN PIPES
- 6" — EXISTING FOREMAIN PIPE
- 4"/6" — EXISTING LFG COLLECTION LATERAL PIPE
- BELOW-GRADE LFG PIPES
- 4" — EXISTING LOADOUT PULL PIPE
- 4" — EXISTING VACUUM PIPE
- EXISTING FRAC TANK - CONDENSATE
- EXISTING FRAC TANK - B SUMP
- EXISTING FRAC TANK - STORM WATER
- EXISTING FRAC TANK - LCM
- EXISTING PUMP / TRUCK LOADOUT
- EXISTING POLYVALVE (COLOR BASED ON PIPE TYPE)
- SP — SAMPLE POINT

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER AERIAL PHOTOGRAPHY DATED OCTOBER 14, 2026.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM 7

PROJECT TITLE: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544


PROJ. NO. 01204123.45 | DSN. BY: RNH | DWN. BY: RR / CNW | CHK. BY: RNH | ACAD FILE: F:/ENGINEERS | APP. BY: RNH

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 3

\\bc-fs01\Data\CAD\ASBUILT - MASTERS\CHIQUITA\Leachate Tank Schematic\DWG\2026-10-20_CCLF Tank Farm Site Map(s) As-Built_v1.dwg Oct 20, 2026 - 11:00am By: raulramirez

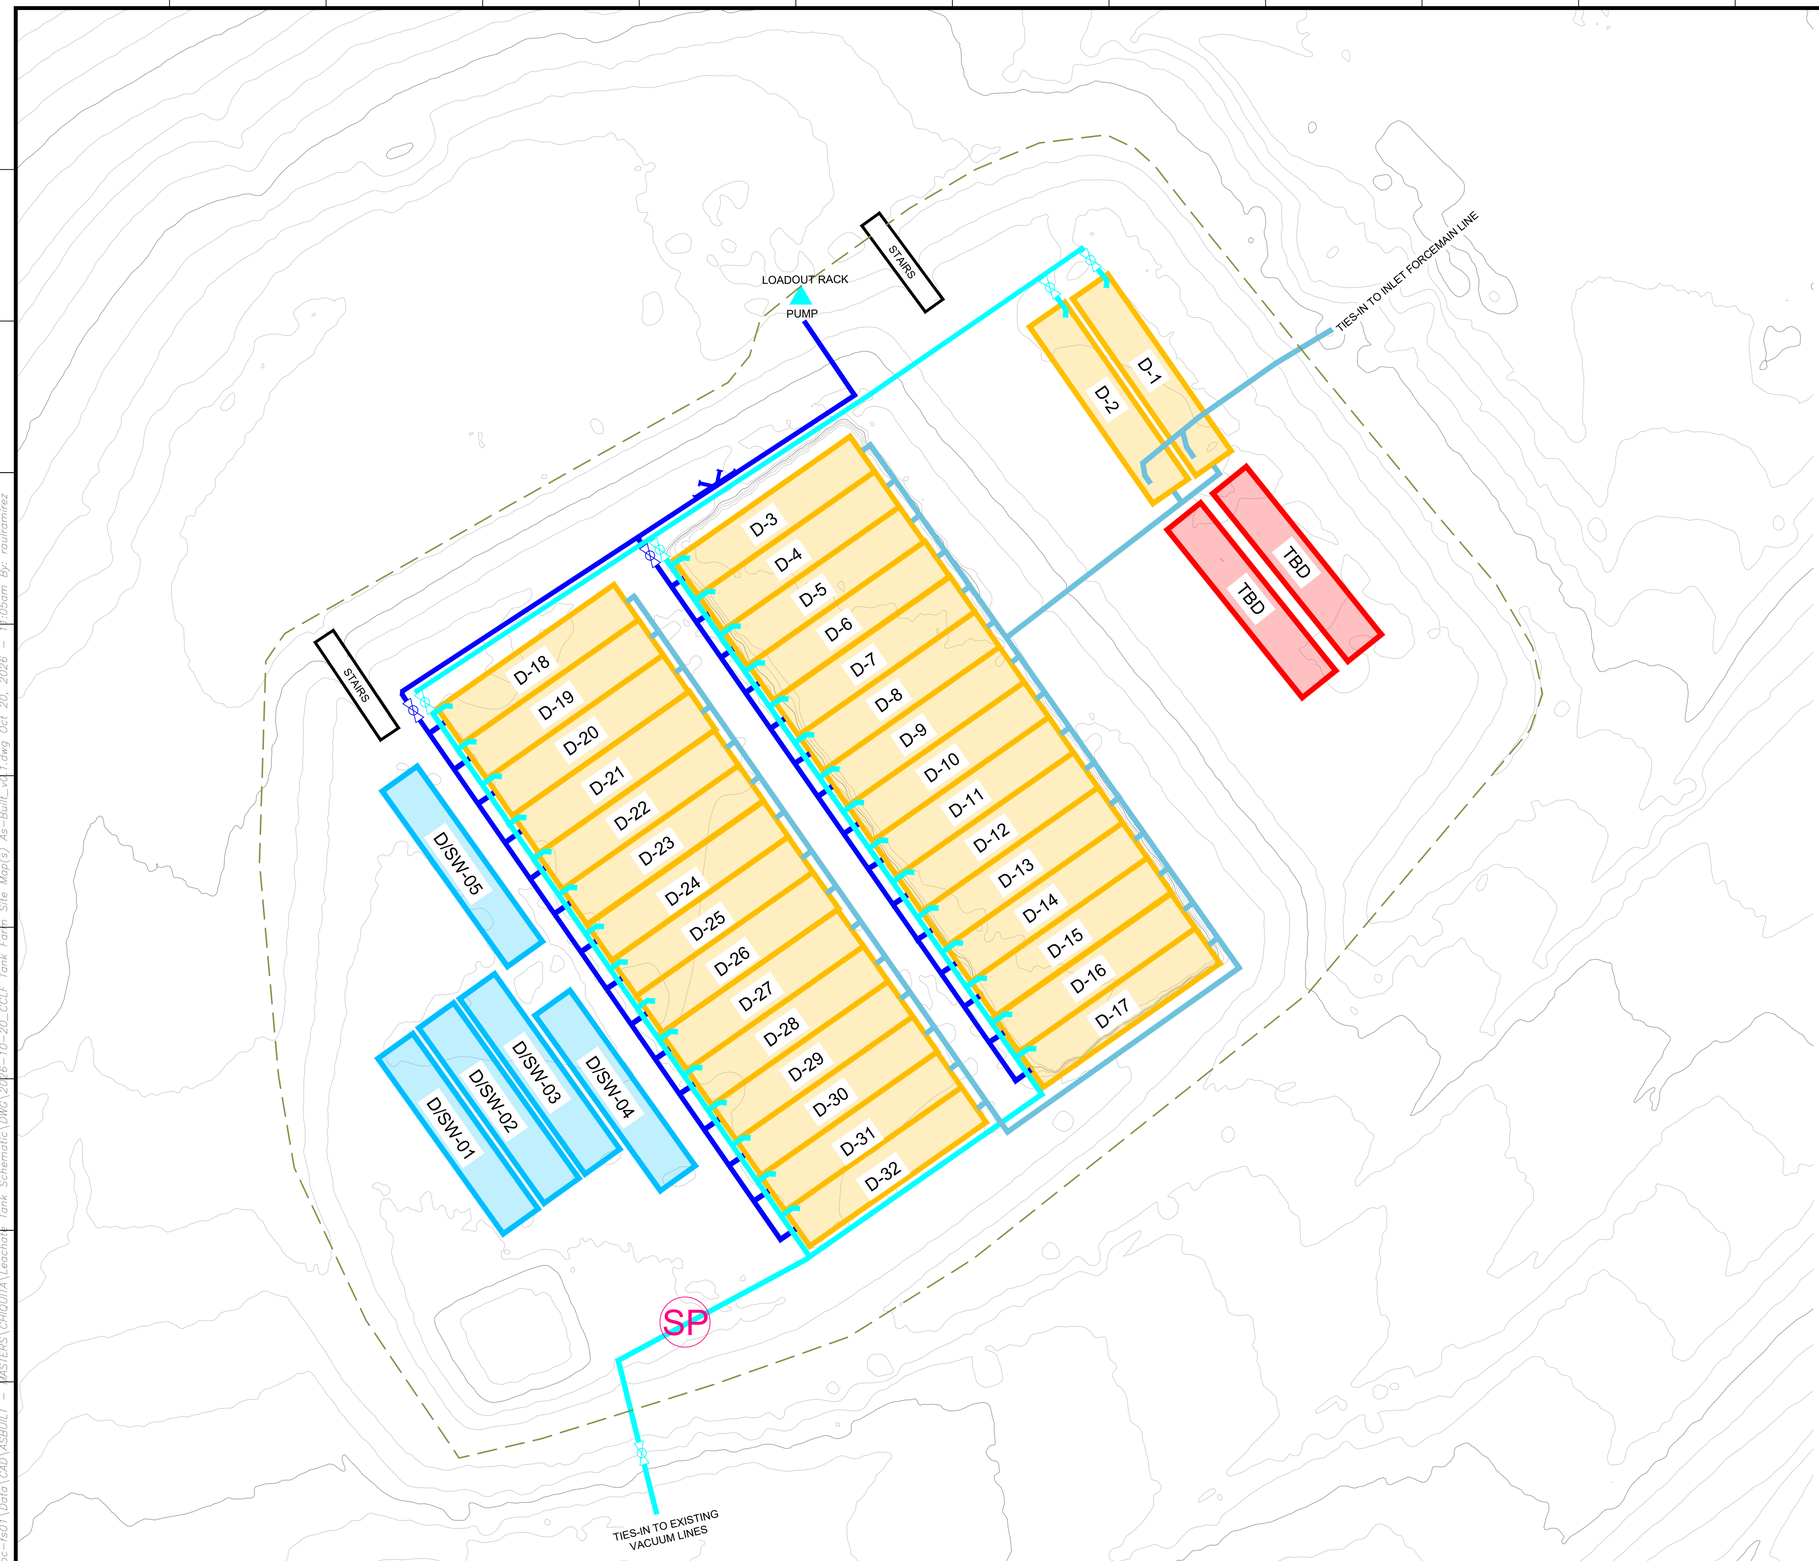

N

GRAPHIC SCALE

15 7.5 0 15 30 45

SCALE: 1"=15'

LEGEND

- 1150 — TOPOGRAPHIC CONTOUR
- 6" — EXISTING INLET FORCEMAIN PIPE
- 4" — EXISTING LOADOUT PULL PIPE
- 4" — EXISTING VACUUM PIPE
- EXISTING FRAC TANK - IN SERVICE
- EXISTING FRAC TANK - NOT IN SERVICE
- EXISTING FRAC TANK - STORM WATER
- EXISTING PUMP / TRUCK LOADOUT
- EXISTING CLEANOUT
- EXISTING POLYVALVE (COLOR BASED ON PIPE TYPE)
- SP — SAMPLE POINT

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER AERIAL PHOTOGRAPHY DATED OCTOBER 14, 2026.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

DATE | REVISION | NO.

SHEET TITLE: TANK FARM 10

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544


PROJ. NO. 01204123.45 | DSN. BY: RNH | DWN. BY: RR / CNW | CHK. BY: RNH | ACAD FILE: F:/ENGINEERS | APP. BY: RNH

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 4

J:\Ubc-fs01\Data\CAD\ASBUILT - MASTERS\CHIQUITA\Leachate Tank Schematic\DWG\2026-10-20_CCLF Tank Farm Site Map(s) As-Built_v1.dwg Oct 20, 2026 - 11:05am By: raulramirez

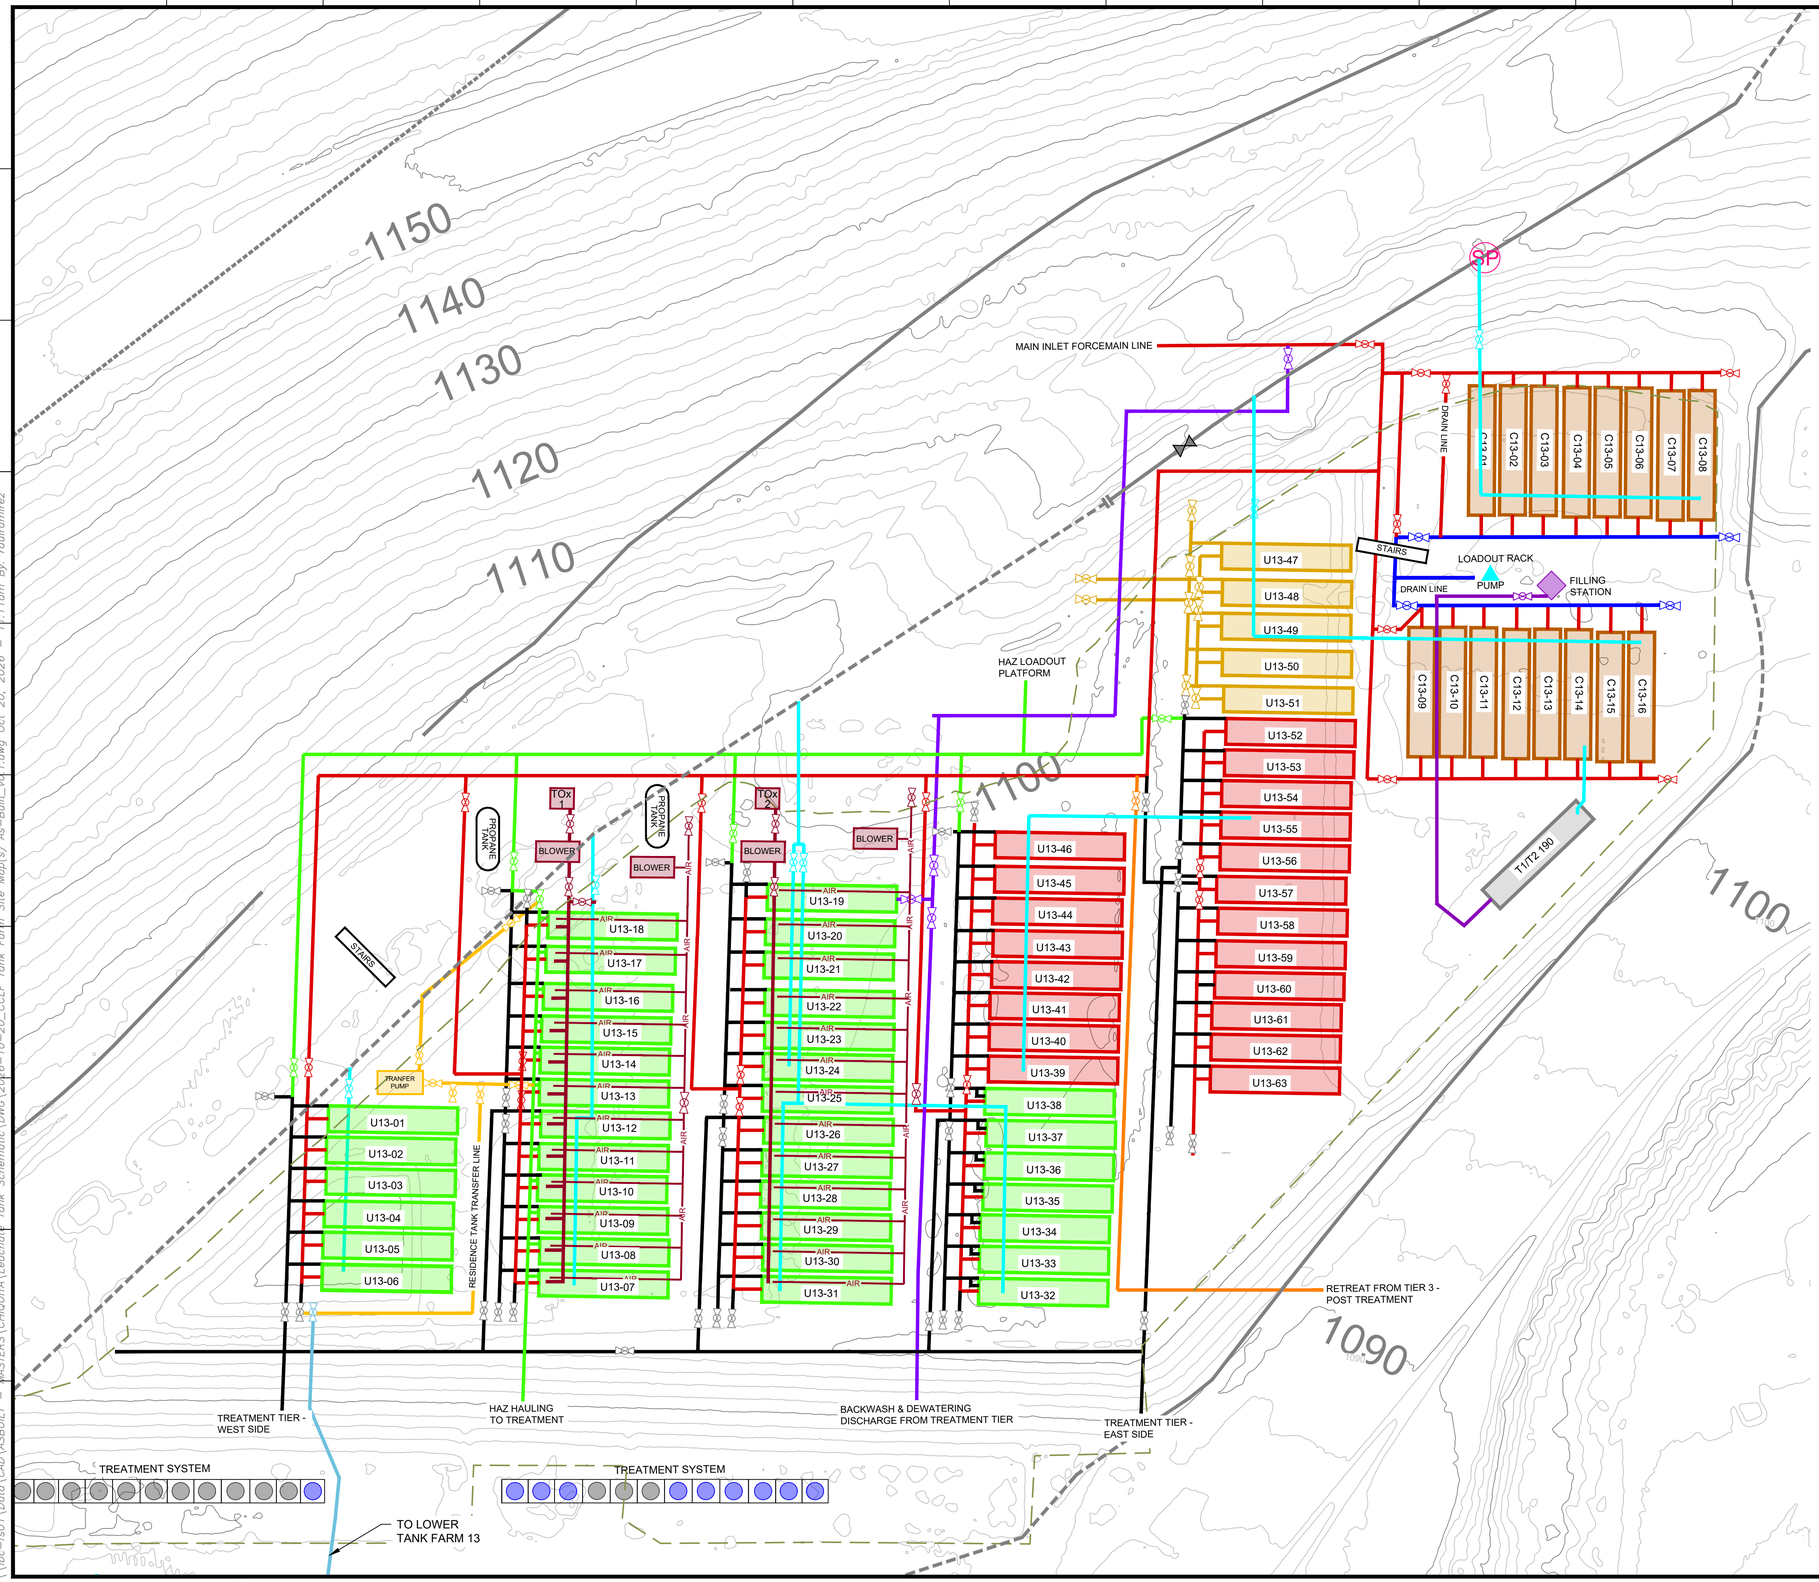

N

GRAPHIC SCALE

25 12.5 0 25 50 75

SCALE: 1"= 25'

LEGEND

- 1150 — TOPOGRAPHIC CONTOUR
- 8" — EXISTING INLET FORCEMAIN PIPE
- 6" — EXISTING INLET FORCEMAIN PIPE
- AIR 3"/ 6" AIR — EXISTING AIR RECIRC PIPE
- 4" — EXISTING MINI TOX VACUUM PIPE
- 4" — EXISTING TREATMENT PIPE
- 4" — EXISTING T HAZ LOADOUT PIPE
- 4" — EXISTING RETREAT PIPE
- 4" — EXISTING BACKWASH & DEWATERING PIPE
- 4" — EXISTING SLUDGE TANKS FILL/PULL PIPE
- 4" — EXISTING TRANSFER LINE
- 4" — EXISTING VACUUM PIPE
- 4" — EXISTING LOADOUT PULL PIPE
- 4" — EXISTING LOADOUT FILLING STATION PIPE
- EXISTING FRAC TANK - CLARIFIER
- EXISTING FRAC TANK - RESERVE INFLUENT
- EXISTING FRAC TANK - SLUDGE
- EXISTING FRAC TANK - H2S CONDENSATE
- EXISTING FRAC TANK - INFLUENT
- EXISTING PUMP / TRUCK LOADOUT
- EXISTING POLYVALVE (COLOR BASED ON PIPE TYPE)
- EXISTING FILLING STATION
- SP — SAMPLE POINT

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER AERIAL PHOTOGRAPHY DATED OCTOBER 14, 2026.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM 13 PRE-TREATMENT

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
SCS WORLD HEADQUARTERS
3900 KILROY AIRPORT WAY, BOEING I, SUITE 300
LONG BEACH, CA 90806
PH: (562) 426-9544


PROJ. NO. 01204123.45 | DSN. BY: RNH | DWN. BY: RR / CNW | CHK. BY: RNH | ACAD FILE: F:\ENGINEERS | APP. BY: RNH

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 5A

\\lbc-fs01\Data\CAD\ASBUILT - MASTERS\CHIQUITA\Leachate Tank Schematic\DWG\2026-10-20_CCLF Tank Farm Site Map(s) As-Built_v1.dwg Oct 20, 2026 - 11:11am By: raulramirez

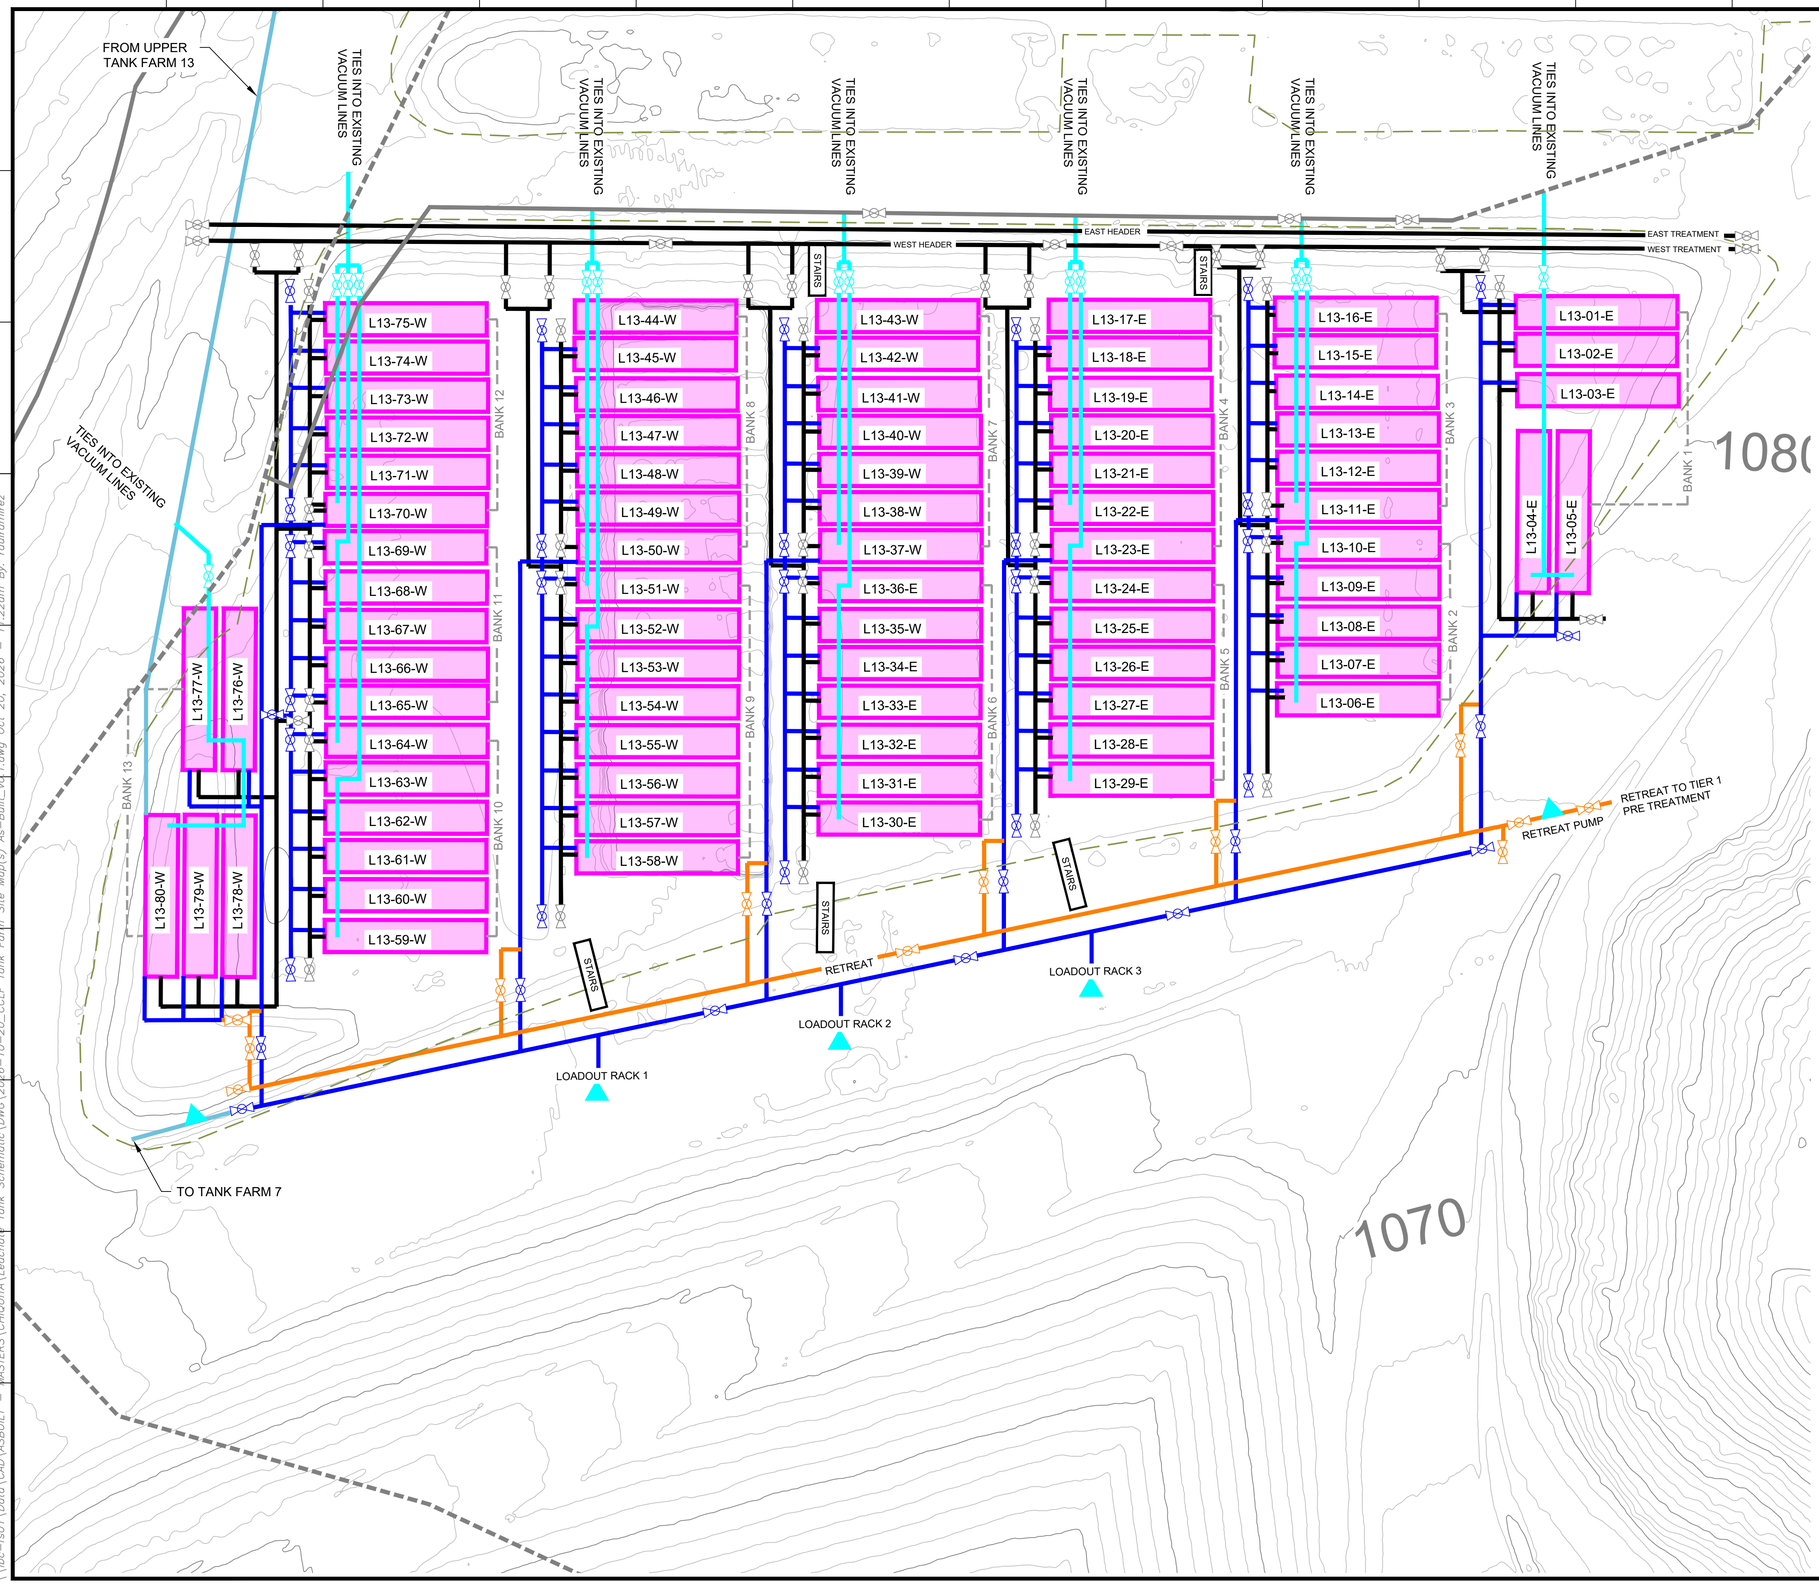

N

GRAPHIC SCALE

20 10 0 20 40 60

SCALE: 1"= 20'

LEGEND

- 1150 — TOPOGRAPHIC CONTOUR
- 6" — EXISTING FORCEMAIN INLET PIPE
- 4" — EXISTING TREATMENT FILL PIPE
- 4" — EXISTING LOADOUT PULL PIPE
- 4" — EXISTING VACUUM PIPE
- 4" — EXISTING RETREAT PIPE
- EXISTING FRAC TANK - POST TREATMENT
- EXISTING PUMP / TRUCK LOADOUT
- EXISTING POLYVALVE (COLOR BASED ON PIPE TYPE)

WEST TREATMENT
BANK#7
BANK#8
BANK#9
BANK#10
BANK#11
BANK#12
BANK#13

EAST TREATMENT
BANK#1
BANK#2
BANK#3
BANK#4
BANK#5
BANK#6

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLER AERIAL PHOTOGRAPHY DATED OCTOBER 14, 2026.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO.	REVISION	DATE

SHEET TITLE: TANK FARM 13 POST-TREATMENT

PROJECT TITLE: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3900 KILROY AIRPORT WAY, SUITE 100
LONG BEACH, CA 90806
PH: (562) 426-9544


PROJ. NO.	DSN. BY:	DWN. BY:	CHK. BY:	ACAD FILE:	APP. BY:
012041123.45	RNH	RR / CNW	RNH	F:/ENGINEERS	RNH

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 5B

\\lac-fs01\Data\CAD\ASBUILT - MASTERS\CHIQUITA\Leachate Tank Schematic\DWG\2026-10-20_CCLF Tank Farm Site Map(s) As-Built_v1.dwg Oct 20, 2026 - 11:22am By: raulramirez

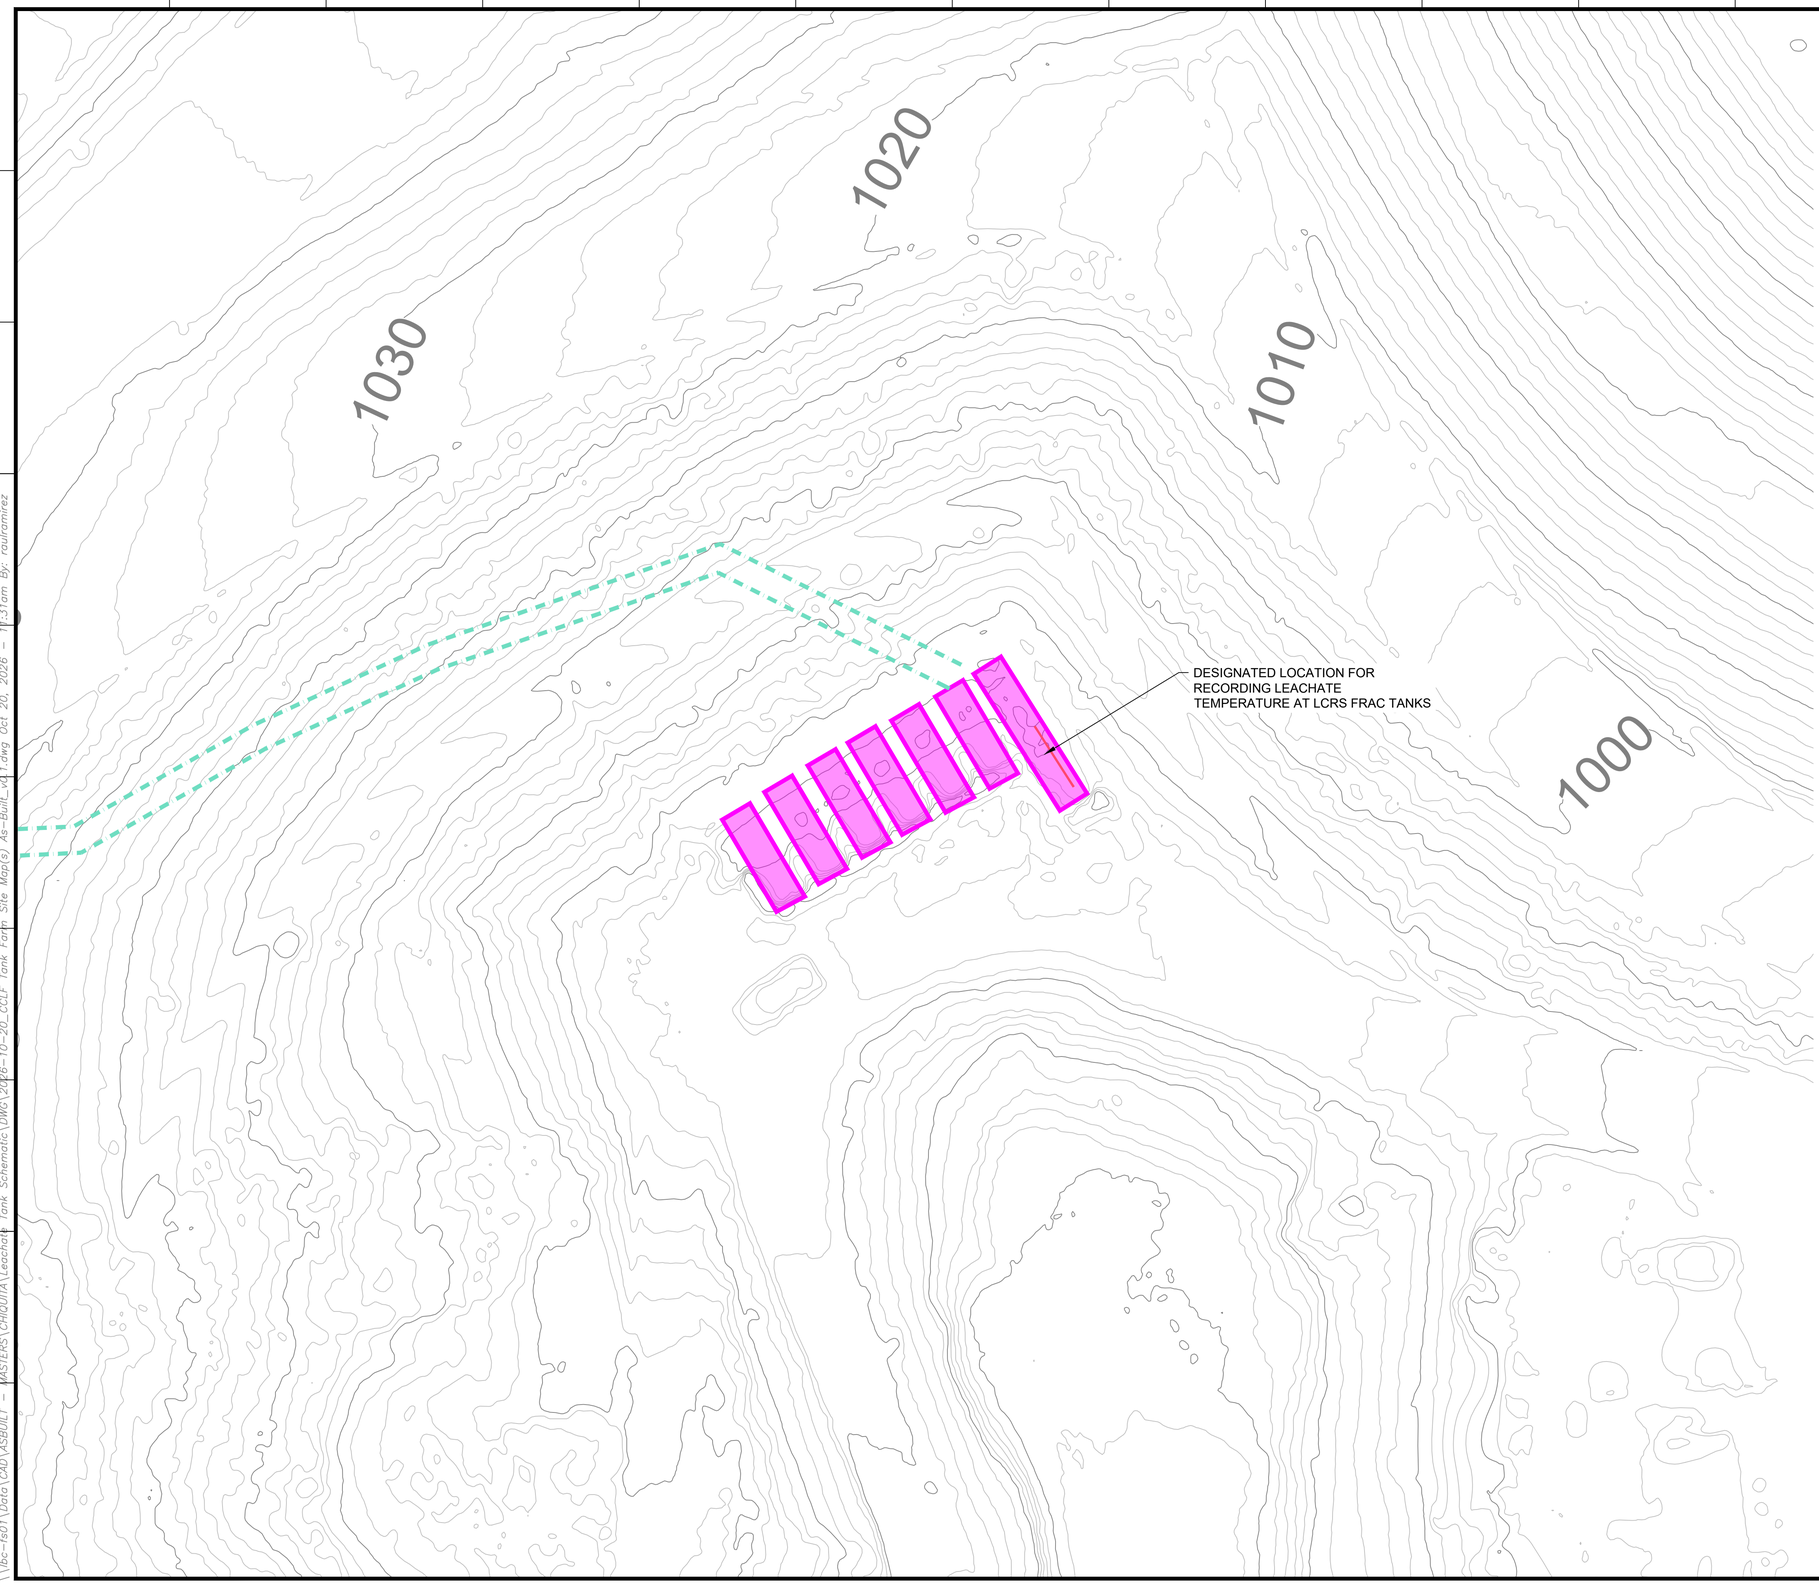

N

GRAPHIC SCALE

20 10 0 20 40 60

SCALE: 1"= 20'

LEGEND

1150 — TOPOGRAPHIC CONTOUR

EXISTING FORCEMAIN PIPE

EXISTING FRAC TANK

GENERAL DRAWING NOTES:

1. EXISTING TOPOGRAPHIC SURVEY INFORMATION SHOWN WAS PROVIDED BY PROPELLOR. AERIAL PHOTOGRAPHY DATED OCTOBER 14, 2026.
2. NORTH ARROW SHOWN HERE IS REFERENCE TO THE CALIFORNIA STATE PLANE ZONE V COORDINATE SYSTEM, NAD 83.

NO. | REVISION | DATE

SHEET TITLE: LCRS FRAC TANKS

PROJECT TITLE: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

CLIENT: CHIQUITA CANYON LANDFILL
CASTAIC, CALIFORNIA

SCS ENGINEERS
ENVIRONMENTAL CONSULTANTS
3211 W. MACARTHUR BLVD., SUITE 300
SANTA ANA, CALIFORNIA 92704
LONG BEACH, CA 90808
PH: (562) 426-9544

PROJ. NO. 01204123.45 | DWN. BY: SRM | ACAD FILE: F:/ENGINEERS
DSN. BY: - | CHK. BY: - | APP. BY: -

DATE: 10/20/2026

SCALE: AS SHOWN

SHEET: 6

\\lbc-fs01\Data\CAD\ASBUILT - MASTERS\CHIQUITA\Leachate Tank Schematic\DWG\2026-10-20_CCLF Tank Farm Site Map(s) As-Built_v1.dwg Oct 20, 2026 - 11:31am By: raulramirez

Attachment Q

Condition 42 Monitoring Results

West Slope Toe Improvement Condition 42 Sampling | **CCL081926EX01**
3-in From Exposed Waste - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles

Sample Type: Summa Canister
Sample Date: 8/19/2026 1:48 PM
Location: 3-inches from exposed waste layer
Location Category: Site Characterization
GPS: 34.432128, -118.651456


Sample Start Time: 8/19/2026 2:17:00 PM
Sample Stop Time: 8/19/2026 2:21:34 PM
Sample Duration: 4.57 mins
Start Pressure: -29
Stop Pressure: -5
Sample Volume: 6 L
Pump: C70393 **Regulator:** A30421

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC:0.0
LEL: 0







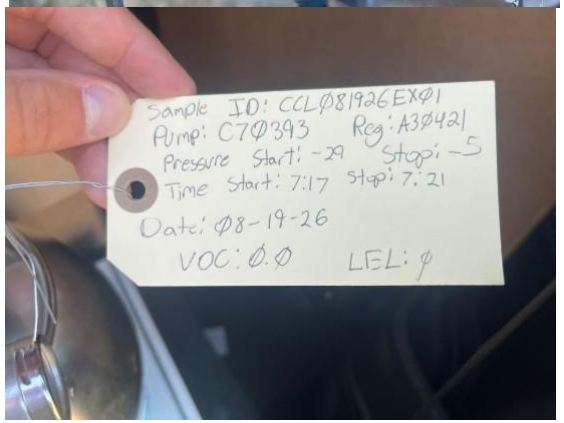

Onterris

West Slope Toe Improvement Condition 42 Sampling | **CCL081926DW02**

Immediately Downwind - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles

Sample Type: Summa Canister
Sample Date: 8/19/2026 1:59 PM
Location: Immediately downwind of excavation.
Location Category: Site Characterization
GPS: 34.432287, -118.651714


Sample Start Time: 8/19/2026 2:34:00 PM
Sample Stop Time: 8/19/2026 2:42:42 PM
Sample Duration: 8.7 mins
Start Pressure: -21
Stop Pressure: -4
Sample Volume: 6 L
Pump: C70162 **Regulator:** A30404

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC: 0.0
LEL: 0







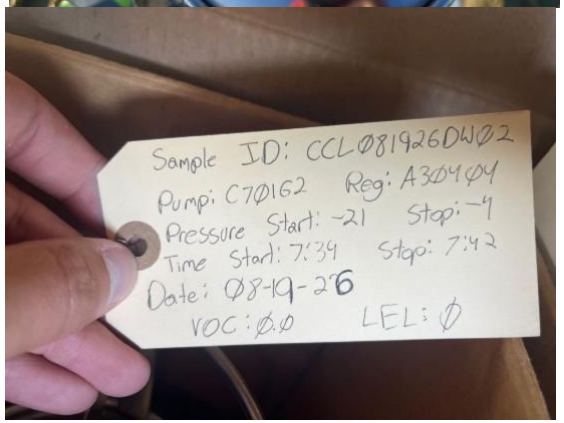

Onterris

West Slope Toe Improvement Condition 42 Sampling | **CCL081926UW03**

Immediately Upwind - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles

Sample Type: Summa Canister
Sample Date: 8/19/2026 2:01 PM
Location: Immediately upwind of excavation.
Location Category: Site Characterization
GPS: 34.431892, -118.650925


Sample Start Time: 8/19/2026 2:07:00 PM
Sample Stop Time: 8/19/2026 2:14:35 PM
Sample Duration: 7.58 mins
Start Pressure: -15
Stop Pressure: -4
Sample Volume: 6 L
Pump: C70689 **Regulator:** A30437

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC: 0.0
LEL: 0







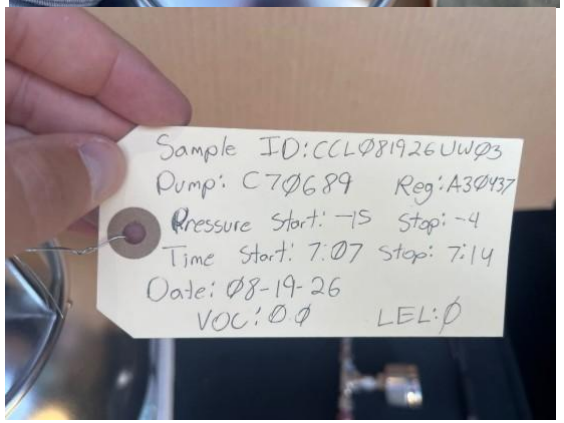

Onterris

West Slope Toe Improvement Condition 42 Sampling | **CCL081926PL04**

Downwind Property Line - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles

Sample Type: Summa Canister
Sample Date: 8/19/2026 2:02 PM
Location: Downwind as close to the property line that can be accessed by road or path.
Location Category: Site Characterization
GPS: 34.432668, -118.652201

Sample Start Time: 8/19/2026 2:47:00 PM
Sample Stop Time: 8/19/2026 3:09:56 PM
Sample Duration: 22.93 mins
Start Pressure: -26


Stop Pressure: -5
Sample Volume: 6 L
Pump: C70907 **Regulator:** A30422

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC: 0.0
LEL: 0







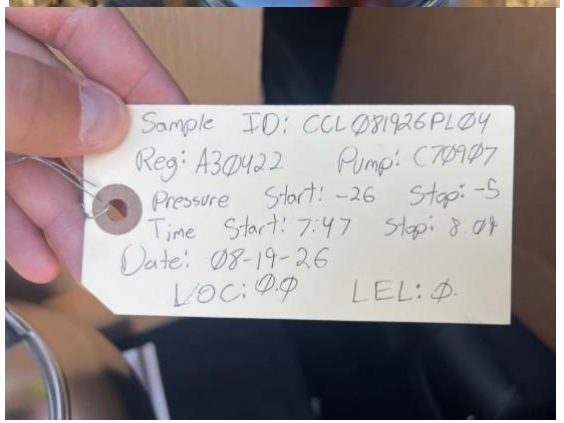

West Slope Toe Improvement Condition 42 Sampling | **CCL081926EX05**
3-in From Exposed Waste - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles

Sample Type: Summa Canister
Sample Date: 8/19/2026 8:15 PM
Location: 3-inches from exposed waste layer
Location Category: Site Characterization
GPS: 34.432025, -118.651177


Sample Start Time: 8/19/2026 9:11:00 PM
Sample Stop Time: 8/19/2026 9:14:14 PM
Sample Duration: 3.23 mins
Start Pressure: -30
Stop Pressure: -5
Sample Volume: 6 L
Pump: C70858 **Regulator:** A30449

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC: 0.0
LEL: 0







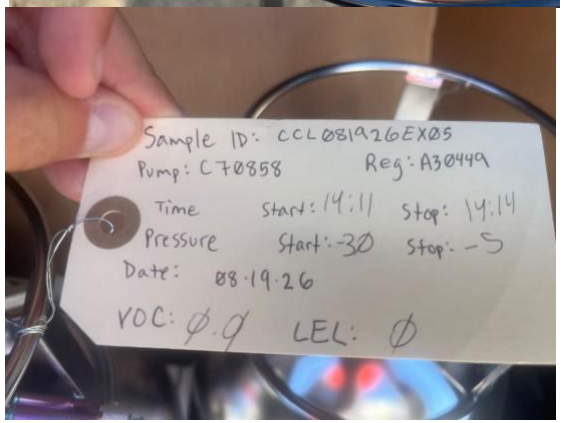

West Slope Toe Improvement Condition 42 Sampling | **CCL081926DW06**
Immediately Downwind - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles

Sample Type: Summa Canister
Sample Date: 8/19/2026 8:18 PM
Location: Immediately downwind of excavation.
Location Category: Site Characterization
GPS: 34.43222, -118.651697


Sample Start Time: 8/19/2026 9:25:00 PM
Sample Stop Time: 8/19/2026 9:33:47 PM
Sample Duration: 8.78 mins
Start Pressure: -20
Stop Pressure: -4
Sample Volume: 6 L
Pump: C70831 **Regulator:** A30406

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC: 0.0
LEL: 0







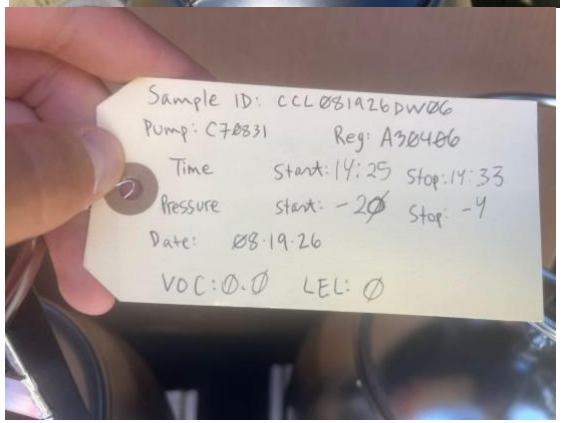

West Slope Toe Improvement Condition 42 Sampling | **CCL081926UW07**
Immediately Upwind - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles


Sample Type: Summa Canister
Sample Date: 8/19/2026 8:19 PM
Location: Immediately upwind of excavation.
Location Category: Site Characterization
GPS: 34.431821, -118.650914


Sample Start Time: 8/19/2026 9:00:00 PM
Sample Stop Time: 8/19/2026 9:08:16 PM
Sample Duration: 8.27 mins
Start Pressure: -22
Stop Pressure: -4
Sample Volume: 6 L
Pump: C71127 **Regulator:** A30393

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC: 0.0
LEL: 0





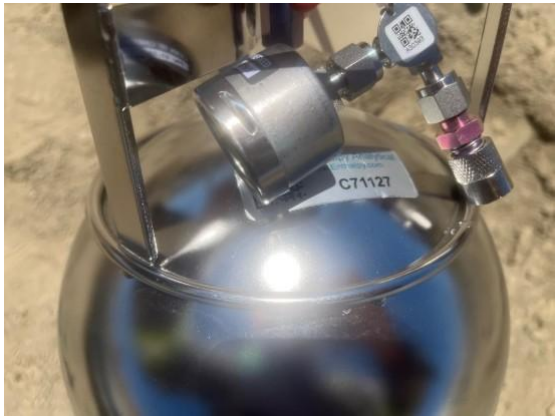

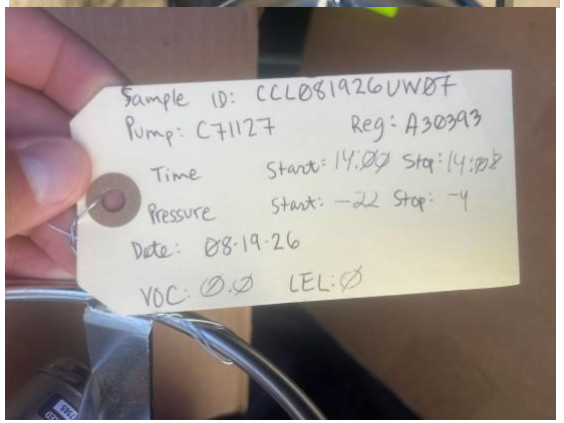

Onterris

West Slope Toe Improvement Condition 42 Sampling | **CCL081926PL08**

Downwind Property Line - Sample-Pickup

Project No.	070361
Sample Date	8/19/2026
City	Castaic, CA
County	Los Angeles

Sample Type: Summa Canister
Sample Date: 8/19/2026 8:20 PM
Location: Downwind as close to the property line that can be accessed by road or path.
Location Category: Site Characterization
GPS: 34.432666, -118.652204

Sample Start Time: 8/19/2026 9:38:00 PM
Sample Stop Time: 8/19/2026 9:58:35 PM
Sample Duration: 20.58 mins
Start Pressure: -23


Stop Pressure: -5
Sample Volume: 6 L
Pump: C70646 **Regulator:** A30432

Comments: Prevailing winds from the N
Ground winds from the S to the N
Used MR M01EA17450 for readings.
VOC: 0.0
LEL: 0







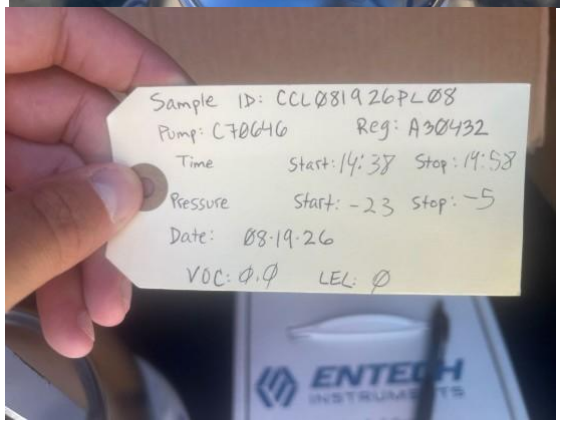

Onterris
931 West Barkley Ave
Orange, CA 92868
(714) 771-6900

onterris.com

Lab Job Number	:	566281
Report Level	:	II
Report Date	:	08/25/2026

Analytical Report *prepared for:*

Jason Callahan
Chiquita Canyon Landfill
Onterris Response and Recovery
5120 Northshore Drive
North Little Rock, AR 72118

Project: PROJ-070361 - Condition 42 - Soil Excavation

Authorized for release by:



David Tripp, Senior Project Manager
david.tripp@onterris.com

This data package has been reviewed for technical correctness and completeness. Release of this data has been authorized by the Laboratory Manager or the Manager's designee, as verified by the above signature which applies to this PDF file as well as any associated electronic data deliverable files. The results contained in this report meet all requirements of NELAP and pertain only to those samples which were submitted for analysis. This report may be reproduced only in its entirety.

CA ELAP# 1338, CA ELAP #1338-S1, NELAP# 4038, SCAQMD LAP# 18LA0518, LACSD ID# 10105, ORELAP# 4197

Onterris™

Sample Summary

Jason Callahan Chiquita Canyon Landfill Onterris Response and Recovery 5120 Northshore Drive North Little Rock, AR 72118	Lab Job #: Project No: Location: Date Received:	566281 PROJ-070361 Condition 42 - Soil Excavation 08/20/26

Sample ID	Lab ID	Collected	Matrix
CCL081926EX01	566281-001	08/19/26 07:21	Air
CCL081926DW02	566281-002	08/19/26 07:42	Air
CCL081926UW03	566281-003	08/19/26 07:14	Air
CCL081926PL04	566281-004	08/19/26 08:09	Air
CCL081926EX05	566281-005	08/19/26 14:14	Air
CCL081926DW06	566281-006	08/19/26 14:33	Air
CCL081926UW07	566281-007	08/19/26 14:08	Air
CCL081926PL08	566281-008	08/19/26 14:58	Air

Case Narrative

Chiquita Canyon Landfill Onterris Response and Recovery 5120 Northshore Drive North Little Rock, AR 72118 Jason Callahan	Lab Job Number: 566281 Project No: PROJ-070361 Location: Condition 42 - Soil Excavation Date Received: 08/20/26

- This data package contains sample and QC results for eight air samples, requested for the above referenced project on 08/20/26. The samples were received in good condition.
- Analyses were performed at 2532 E Cerritos Ave., Anaheim, CA, 92806.

Volatile Organics in Air by MS (EPA TO-15):
No analytical problems were encountered.

Volatile Organics in Air GC - TO3 (EPA TO-3M):
No analytical problems were encountered.

Detection Summary

Jason Callahan
Chiquita Canyon Landfill
Onterris Response and Recovery
5120 Northshore Drive
North Little Rock, AR 72118

Lab Job #: 566281
Project No: PROJ-070361
Location: Condition 42 - Soil Excavation
Date Received: 08/20/26

Sample ID: CCL081926EX01 **Lab ID: 566281-001** **Collected: 08/19/26 07:21**
Matrix: Air

566281-001 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.46**		ppbv	0.36
Freon 12	**2.3**		ug/m3	1.8
Chloromethane	**0.57**		ppbv	0.36
Chloromethane	**1.2**		ug/m3	0.75
Acetone	**27**		ppbv	3.6
Acetone	**64**		ug/m3	8.6
Carbon Disulfide	**0.72**		ppbv	0.36
Carbon Disulfide	**2.2**		ug/m3	1.1
Isopropanol (IPA)	**7.8**		ppbv	1.8
Isopropanol (IPA)	**19**		ug/m3	4.4
n-Hexane	**0.46**		ppbv	0.36
n-Hexane	**1.6**		ug/m3	1.3
2-Butanone	**5.9**		ppbv	1.8
2-Butanone	**17**		ug/m3	5.3
Benzene	**3.8**		ppbv	0.36
Benzene	**12**		ug/m3	1.2
Toluene	**3.0**		ppbv	0.36
Toluene	**11**		ug/m3	1.4
Ethylbenzene	**1.7**		ppbv	0.36
Ethylbenzene	**7.3**		ug/m3	1.6
m,p-Xylenes	**2.3**		ppbv	0.72
m,p-Xylenes	**9.9**		ug/m3	3.1
o-Xylene	**1.1**		ppbv	0.36
o-Xylene	**4.6**		ug/m3	1.6
1,2,4-Trimethylbenzene	**0.61**		ppbv	0.36
1,2,4-Trimethylbenzene	**3.0**		ug/m3	1.8
Xylene (total)	**3.3**		ppbv	0.36
Xylene (total)	**14**		ug/m3	1.6
Method: EPA TO-3M				
TVOC as Hexane	**0.24**		ppmv	0.090
TVOC as Hexane	**830**		ug/m3	320

Onterris

Detection Summary

Sample ID: CCL081926DW02	Lab ID: 566281-002	Collected: 08/19/26 07:42
	Matrix: Air	

566281-002 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.47**		ppbv	0.36
Freon 12	**2.3**		ug/m3	1.8
Chloromethane	**0.58**		ppbv	0.36
Chloromethane	**1.2**		ug/m3	0.75
Acetone	**16**		ppbv	3.6
Acetone	**38**		ug/m3	8.6
Benzene	**2.8**		ppbv	0.36
Benzene	**8.8**		ug/m3	1.2
Toluene	**0.51**		ppbv	0.36
Toluene	**1.9**		ug/m3	1.4
Styrene	**0.45**		ppbv	0.36
Styrene	**1.9**		ug/m3	1.5

Sample ID: CCL081926UW03	Lab ID: 566281-003	Collected: 08/19/26 07:14
	Matrix: Air	

566281-003 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.48**		ppbv	0.44
Freon 12	**2.4**		ug/m3	2.2
Chloromethane	**0.63**		ppbv	0.44
Chloromethane	**1.3**		ug/m3	0.90
Acetone	**13**		ppbv	4.4
Acetone	**31**		ug/m3	10
Isopropanol (IPA)	**2.2**		ppbv	2.2
Isopropanol (IPA)	**5.4**		ug/m3	5.4
Toluene	**0.54**		ppbv	0.44
Toluene	**2.0**		ug/m3	1.6

Onterris

Detection Summary

Sample ID: CCL081926PL04	Lab ID: 566281-004	Collected: 08/19/26 08:09
	Matrix: Air	

566281-004 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.45**		ppbv	0.38
Freon 12	**2.2**		ug/m3	1.9
Chloromethane	**0.60**		ppbv	0.38
Chloromethane	**1.2**		ug/m3	0.78
Acetone	**18**		ppbv	3.8
Acetone	**42**		ug/m3	9.0
Isopropanol (IPA)	**2.7**		ppbv	1.9
Isopropanol (IPA)	**6.6**		ug/m3	4.7
Benzene	**2.3**		ppbv	0.38
Benzene	**7.3**		ug/m3	1.2
Toluene	**0.50**		ppbv	0.38
Toluene	**1.9**		ug/m3	1.4

Sample ID: CCL081926EX05	Lab ID: 566281-005	Collected: 08/19/26 14:14
	Matrix: Air	

566281-005 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.46**		ppbv	0.39
Freon 12	**2.3**		ug/m3	1.9
Chloromethane	**0.53**		ppbv	0.39
Chloromethane	**1.1**		ug/m3	0.80
Acetone	**15**		ppbv	3.9
Acetone	**36**		ug/m3	9.2
Carbon Disulfide	**0.43**		ppbv	0.39
Carbon Disulfide	**1.4**		ug/m3	1.2
n-Hexane	**0.40**		ppbv	0.39
n-Hexane	**1.4**		ug/m3	1.4
Benzene	**3.2**		ppbv	0.39
Benzene	**10**		ug/m3	1.2
Toluene	**2.2**		ppbv	0.39
Toluene	**8.3**		ug/m3	1.5
Ethylbenzene	**1.0**		ppbv	0.39
Ethylbenzene	**4.4**		ug/m3	1.7
m,p-Xylenes	**1.2**		ppbv	0.77
m,p-Xylenes	**5.3**		ug/m3	3.4
o-Xylene	**0.52**		ppbv	0.39
o-Xylene	**2.2**		ug/m3	1.7
Xylene (total)	**1.7**		ppbv	0.39
Xylene (total)	**7.6**		ug/m3	1.7
Method: EPA TO-3M				
TVOC as Hexane	**0.13**		ppmv	0.097
TVOC as Hexane	**450**		ug/m3	340

Onterris

Detection Summary

Sample ID: CCL081926DW06	Lab ID: 566281-006	Collected: 08/19/26 14:33
	Matrix: Air	

566281-006 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.48**		ppbv	0.37
Freon 12	**2.4**		ug/m3	1.8
Chloromethane	**0.56**		ppbv	0.37
Chloromethane	**1.2**		ug/m3	0.77
Acetone	**11**		ppbv	3.7
Acetone	**27**		ug/m3	8.8
Benzene	**1.7**		ppbv	0.37
Benzene	**5.6**		ug/m3	1.2

Sample ID: CCL081926UW07	Lab ID: 566281-007	Collected: 08/19/26 14:08
	Matrix: Air	

566281-007 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.46**		ppbv	0.37
Freon 12	**2.3**		ug/m3	1.8
Chloromethane	**0.55**		ppbv	0.37
Chloromethane	**1.1**		ug/m3	0.77
Acetone	**12**		ppbv	3.7
Acetone	**29**		ug/m3	8.9

Sample ID: CCL081926PL08	Lab ID: 566281-008	Collected: 08/19/26 14:58
	Matrix: Air	

566281-008 Analyte	Result	Qual	Units	RL
Method: EPA TO-15 Prep Method: METHOD				
Freon 12	**0.48**		ppbv	0.43
Freon 12	**2.4**		ug/m3	2.1
Chloromethane	**0.57**		ppbv	0.43
Chloromethane	**1.2**		ug/m3	0.89
Acetone	**14**		ppbv	4.3
Acetone	**33**		ug/m3	10

COC instructions can be found under the instructions tab

Onterris

Air Media Chain of Custody

Select Testing Laboratory

LAB-COR-GF001-00 | Page 1 of 1

Client:	GCL
Address:	29201 HENRY MMO DR.
City/State/ZIP:	CASTAIC, CA 91 384
Phone|Email:	501 366 8044 | JCALLAHAN@GEOSCAN
Collected By:	Gage Taylor, Devan Zaziac
Project Manager:	JASON CALLAHAN
Project Name|Number:	Condition 42 Sampling | PROJ-070361
Site Address:	29201 HENRY MMO DR. CASTAIC, CA 91384
Invoice Info|PO#|Quote#:	PROJ-070361

Analysis Requested

	Sample Identification	Matrix	Sample Type	Media Type	Media ID	Flow Controller ID	Sample Start/Stop Date (mm/dd/yyyy)		Sample Start/Stop Time (24hr clock)		Initial/Final Pressure (in Hg)		Initial/Final Canister Temp (°F)		Final Volume (m^3,mL,L)	TO-15	TO-3			
1	CCL081926EX01	A	G	C	C70393	A3042	08-19-26	08-19-26	07:17	07:21	-29	-5				X	X			
2	CCL081926DW02				C70162	A3040			07:34	07:42	-21	-4				X	X			
3	CCL081926UW03				C70689	A3043			07:07	07:14	-15	-4				X	X			
4	CCL081926PL04				C70407	A3042			07:47	08:09	-26	-5				X	X			GT
5	CCL081926EX05				C70858	A3044			14:11	14:14	-30	-5				X	X			
6	CCL081926DW06				C70831	A3040			14:25	14:33	-20	-4				X	X			
7	CCL081926UW07				C71127	A3039			14:00	14:08	-22	-4				X	X			
8	CCL081926PL08				C70646	A3043			14:38	14:58	-23	-5				X	X			
9																				
10																				

GT

↓ Relinquished By ↓	↓ Date ↓ (mm/dd/yyyy)	↓ Time ↓ (24hr clock)	↓ Received By ↓	↓ Date ↓ (mm/dd/yyyy)	↓ Time ↓ (24hr clock)
Gage Taylor	08/19/2026	15:30	Guillermo Alvarenga	08/19/2026	15:30
G. Alvarenga	8/20/26	00:00	FEDEX	8/20/26	07:00

Standard ☐ 1 Day ☐ 2 Day ☐ 3 Day ☒ 5 Day ☐

All TATs Subject to Approval by Onterris Laboratories, LLC

Comments

	VOC	LEL		VOC	LEL
EX01	0.0	0	EX05	0.0	0
DW02	0.0	0	DW06	0.0	0
UW03	0.0	0	UW07	0.0	0
PL04	0.0	0	PL08	0.0	0

Workorder #

Login 566281

Matrix: A=Ambient|H=Headspace|I=Indoor|LV=Landfill/Vent Gas|PM=Particulate Matter|S=Source|V=Vapor/Soil Vapor|W=Worker exposure|X=Other

Sample Type: B=Blank|C=Composite|Co=Co-located|D=Duplicate|G=Grab|S=Spike|X=Other

Media Type: B=Bag|Bd=Badge|C=Canister|F=Filter|L=Liquid|P=PUF|S=Sampling bomb|T=Tube|TD=Thermal Desorption|X=Other

Unless otherwise agreed in writing, these services are provided pursuant to the terms and conditions as set forth at onterris.com/ter this order is **expressly limited** to these terms and conditions

Onterris

SAMPLE RECEIPT CHECKLIST

Section 1: General Info
Date Received: 8/20/26 Job#: 566281 Client: Onterris Response and Recovery

Section 2: Shipping / Custody **Are custody seals present?** ☐ Yes ☒ No
Custody seals intact on arrival? ☒ N/A ☐ Yes ☐ No ☐ On cooler / box ☐ On samples
☐ Courier ☒ Walk-In ☐ Field Sampling ☐ Shipping Info: _____

Section 3a: Condition / Packaging ☐ **Outside 0.0 - 6.0°C (0.0 - 10.0°C for microbiology) (PM notified)**
Date Opened 08/20/26 By (initials) FPD Type of ice used: ☐ Wet ☐ Blue/Gel ☒ None
☐ Samples received on ice directly from the field; cooling process had begun. (if checked, skip temperatures)
☒ Sample matrix doesn't require cooling (e.g. air, bulk PCB). (if checked, skip temperatures)
If no cooler: Observed/Corrected Temp (°C): _____ / _____ Thermometer/IR Gun ID:_____CF:_____
Cooler Temp (obs/corr) (°C) #1:_____ /_____ #2:_____ /_____ #3:_____ /_____ #4:_____ /_____ #5:_____ /_____ #6:_____ /_____

Section 3b: Microbiology Samples ☒ **No microbiology samples submitted (skip 3b)**
☐ Within temp range 0.0 - 10.0°C or received on ice directly from field.
☐ Adequate headspace for microbiology analysis.

Section 3c: Air Samples ☐ **No air samples submitted (skip 3c)**
☐ 1.4L Canisters ☒ 6L Canisters ☐ Tedlar Bags ☐ MCE Cassettes ☐ Sorbent Tubes ☐ Other_____
Tedlar Bags received protected from light (ASTM D5504 Sulfur only)? ☐ N/A ☐ Yes ☐ No

Section 4: Containers / Labels / Samples	YES	NO	N/A
1) Were custody papers present, filled properly, and legible?	✔		
2) Is the sampler's name present on the CoC?	✔		
3) Were containers received in good condition (unbroken / unopened / uncompromised)?	✔		
4) Were the samples bagged? (required for microbiology samples; recommended for soil samples)			✔
5) Were all of, and only, the correct samples received?	✔		
6) Are sample labels present, legible, and in agreement with the CoC?	✔		
7) Does the container count match the CoC?	✔		
8) Was sufficient sample volume / mass received for the analyses requested?	✔		
9) Were samples received in proper containers for the analyses requested?	✔		
10) Were samples received with > 1/2 holding time remaining?	✔		
11) Are samples properly preserved as indicated by CoC / labels?	✔		
12) Unpreserved VOAs received - If necessary, was the hold time changed in LIMS?			✔
13) Are VOA vials free from headspace/bubbles > 6mm?			✔

Section 5: Explanations / Comments
(If no comments are made, then no discrepancies noted.)

☐ **No additional discrepancies**

Form Completed By (print): FPD **(sign):** _____

Date Labeled: 08/20/26 **By (print):** FPD **(sign):** _____

Analysis Results for 566281

Jason Callahan
Chiquita Canyon Landfill
Onterris Response and Recovery
5120 Northshore Drive
North Little Rock, AR 72118

Lab Job #: 566281
Project No: PROJ-070361
Location: Condition 42 - Soil Excavation
Date Received: 08/20/26

Method: EPA TO-3M, TVOC as Hexane - Results are defined as Total Volatile Organic Compounds measured from approximately C4-C12 as detectable by GC-FID

Sample ID: CCL081926EX01 **Lab ID: 566281-001** **Collected: 08/19/26 07:21**
Matrix: Air

566281-001 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Acrolein	ND		ug/m3	0.83	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1-Difluoroethane	ND		ppbv	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1-Difluoroethane	ND		ug/m3	4.9	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Freon 12	**0.46**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Freon 12	**2.3**		ug/m3	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Freon 114	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Freon 114	ND		ug/m3	2.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chloromethane	**0.57**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chloromethane	**1.2**		ug/m3	0.75	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Vinyl Chloride	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Vinyl Chloride	ND		ug/m3	0.92	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Bromomethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Bromomethane	ND		ug/m3	1.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chloroethane	ND		ug/m3	0.95	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Trichlorofluoromethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Trichlorofluoromethane	ND		ug/m3	2.0	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1-Dichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1-Dichloroethene	ND		ug/m3	1.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Freon 113	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Freon 113	ND		ug/m3	2.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Acetone	**27**		ppbv	3.6	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Acetone	**64**		ug/m3	8.6	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Carbon Disulfide	**0.72**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Carbon Disulfide	**2.2**		ug/m3	1.1	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Isopropanol (IPA)	**7.8**		ppbv	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Isopropanol (IPA)	**19**		ug/m3	4.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Methylene Chloride	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Methylene Chloride	ND		ug/m3	1.3	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
MTBE	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
MTBE	ND		ug/m3	1.3	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
n-Hexane	**0.46**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
n-Hexane	**1.6**		ug/m3	1.3	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1-Dichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-001 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,1-Dichloroethane	ND		ug/m3	1.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Vinyl Acetate	ND		ppbv	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Vinyl Acetate	ND		ug/m3	6.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
2-Butanone	**5.9**		ppbv	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
2-Butanone	**17**		ug/m3	5.3	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chloroform	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chloroform	ND		ug/m3	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,1-Trichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.0	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Carbon Tetrachloride	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Carbon Tetrachloride	ND		ug/m3	2.3	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Benzene	**3.8**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Benzene	**12**		ug/m3	1.2	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dichloroethane	ND		ug/m3	1.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Trichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Trichloroethene	ND		ug/m3	1.9	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dichloropropane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dichloropropane	ND		ug/m3	1.7	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Bromodichloromethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Bromodichloromethane	ND		ug/m3	2.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
cis-1,3-Dichloropropene	ND		ug/m3	1.6	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Toluene	**3.0**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Toluene	**11**		ug/m3	1.4	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
trans-1,3-Dichloropropene	ND		ug/m3	1.6	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,2-Trichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.0	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Tetrachloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Tetrachloroethene	ND		ug/m3	2.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
2-Hexanone	ND		ppbv	0.90	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
2-Hexanone	ND		ug/m3	3.7	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Dibromochloromethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Dibromochloromethane	ND		ug/m3	3.1	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dibromoethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dibromoethane	ND		ug/m3	2.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Chlorobenzene	ND		ug/m3	1.7	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Ethylbenzene	**1.7**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Ethylbenzene	**7.3**		ug/m3	1.6	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
m,p-Xylenes	**2.3**		ppbv	0.72	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
m,p-Xylenes	**9.9**		ug/m3	3.1	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
o-Xylene	**1.1**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
o-Xylene	**4.6**		ug/m3	1.6	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Styrene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Styrene	ND		ug/m3	1.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Bromoform	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-001 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Bromoform	ND		ug/m3	3.7	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	2.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	2.5	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
4-Ethyltoluene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
4-Ethyltoluene	ND		ug/m3	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,3,5-Trimethylbenzene	ND		ug/m3	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2,4-Trimethylbenzene	**0.61**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2,4-Trimethylbenzene	**3.0**		ug/m3	1.8	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,3-Dichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.2	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,4-Dichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.2	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Benzyl chloride	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Benzyl chloride	ND		ug/m3	1.9	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.2	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	2.7	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Hexachlorobutadiene	ND		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Hexachlorobutadiene	ND		ug/m3	3.9	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Xylene (total)	**3.3**		ppbv	0.36	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Xylene (total)	**14**		ug/m3	1.6	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Surrogates				**Limits**					
Bromofluorobenzene	98%		%REC	60-140	1.8	413612	08/21/26 14:32	08/21/26 14:32	OHD
Method: EPA TO-3M									
TVOC as Hexane	**0.24**		ppmv	0.090	1.8	413653	08/21/26 19:59	08/21/26 19:59	RXD
TVOC as Hexane	**830**		ug/m3	320	1.8	413653	08/21/26 19:59	08/21/26 19:59	RXD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

Sample ID: CCL081926DW02	Lab ID: 566281-002	Collected: 08/19/26 07:42
	Matrix: Air	

566281-002 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Acrolein	ND		ug/m3	0.83	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1-Difluoroethane	ND		ppbv	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1-Difluoroethane	ND		ug/m3	4.9	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Freon 12	**0.47**		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Freon 12	**2.3**		ug/m3	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Freon 114	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Freon 114	ND		ug/m3	2.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Chloromethane	**0.58**		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Chloromethane	**1.2**		ug/m3	0.75	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Vinyl Chloride	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Vinyl Chloride	ND		ug/m3	0.93	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Bromomethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Bromomethane	ND		ug/m3	1.4	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Chloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Chloroethane	ND		ug/m3	0.96	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Trichlorofluoromethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Trichlorofluoromethane	ND		ug/m3	2.0	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1-Dichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1-Dichloroethene	ND		ug/m3	1.4	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Freon 113	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Freon 113	ND		ug/m3	2.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Acetone	**16**		ppbv	3.6	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Acetone	**38**		ug/m3	8.6	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Carbon Disulfide	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Carbon Disulfide	ND		ug/m3	1.1	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Isopropanol (IPA)	ND		ppbv	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Isopropanol (IPA)	ND		ug/m3	4.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Methylene Chloride	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Methylene Chloride	ND		ug/m3	1.3	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.4	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
MTBE	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
MTBE	ND		ug/m3	1.3	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
n-Hexane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
n-Hexane	ND		ug/m3	1.3	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1-Dichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1-Dichloroethane	ND		ug/m3	1.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Vinyl Acetate	ND		ppbv	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Vinyl Acetate	ND		ug/m3	6.4	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.4	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
2-Butanone	ND		ppbv	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
2-Butanone	ND		ug/m3	5.3	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Chloroform	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-002 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Chloroform	ND		ug/m3	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,1-Trichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.0	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Carbon Tetrachloride	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Carbon Tetrachloride	ND		ug/m3	2.3	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Benzene	**2.8**		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Benzene	**8.8**		ug/m3	1.2	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dichloroethane	ND		ug/m3	1.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Trichloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Trichloroethene	ND		ug/m3	1.9	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dichloropropane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dichloropropane	ND		ug/m3	1.7	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Bromodichloromethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Bromodichloromethane	ND		ug/m3	2.4	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
cis-1,3-Dichloropropene	ND		ug/m3	1.6	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Toluene	**0.51**		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Toluene	**1.9**		ug/m3	1.4	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
trans-1,3-Dichloropropene	ND		ug/m3	1.6	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,2-Trichloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.0	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Tetrachloroethene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Tetrachloroethene	ND		ug/m3	2.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
2-Hexanone	ND		ppbv	0.91	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
2-Hexanone	ND		ug/m3	3.7	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Dibromochloromethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Dibromochloromethane	ND		ug/m3	3.1	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dibromoethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dibromoethane	ND		ug/m3	2.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Chlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Chlorobenzene	ND		ug/m3	1.7	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Ethylbenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Ethylbenzene	ND		ug/m3	1.6	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
m,p-Xylenes	ND		ppbv	0.72	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
m,p-Xylenes	ND		ug/m3	3.1	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
o-Xylene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
o-Xylene	ND		ug/m3	1.6	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Styrene	**0.45**		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Styrene	**1.9**		ug/m3	1.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Bromoform	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Bromoform	ND		ug/m3	3.7	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	2.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	2.5	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
4-Ethyltoluene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
4-Ethyltoluene	ND		ug/m3	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-002 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,3,5-Trimethylbenzene	ND		ug/m3	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2,4-Trimethylbenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2,4-Trimethylbenzene	ND		ug/m3	1.8	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,3-Dichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.2	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,4-Dichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.2	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Benzyl chloride	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Benzyl chloride	ND		ug/m3	1.9	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.2	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	2.7	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Hexachlorobutadiene	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Hexachlorobutadiene	ND		ug/m3	3.9	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Xylene (total)	ND		ppbv	0.36	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Xylene (total)	ND		ug/m3	1.6	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Surrogates				**Limits**					
Bromofluorobenzene	97%		%REC	60-140	1.8	413612	08/21/26 15:05	08/21/26 15:05	OHD
Method: EPA TO-3M									
TVOC as Hexane	ND		ppmv	0.091	1.8	413653	08/21/26 20:28	08/21/26 20:28	RXD
TVOC as Hexane	ND		ug/m3	320	1.8	413653	08/21/26 20:28	08/21/26 20:28	RXD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

Sample ID: CCL081926UW03	Lab ID: 566281-003	Collected: 08/19/26 07:14
	Matrix: Air	

566281-003 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Acrolein	ND		ug/m3	1.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1-Difluoroethane	ND		ppbv	2.2	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1-Difluoroethane	ND		ug/m3	5.9	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Freon 12	**0.48**		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Freon 12	**2.4**		ug/m3	2.2	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Freon 114	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Freon 114	ND		ug/m3	3.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Chloromethane	**0.63**		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Chloromethane	**1.3**		ug/m3	0.90	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Vinyl Chloride	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Vinyl Chloride	ND		ug/m3	1.1	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Bromomethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Bromomethane	ND		ug/m3	1.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Chloroethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Chloroethane	ND		ug/m3	1.2	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Trichlorofluoromethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Trichlorofluoromethane	ND		ug/m3	2.5	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1-Dichloroethene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1-Dichloroethene	ND		ug/m3	1.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Freon 113	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Freon 113	ND		ug/m3	3.3	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Acetone	**13**		ppbv	4.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Acetone	**31**		ug/m3	10	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Carbon Disulfide	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Carbon Disulfide	ND		ug/m3	1.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Isopropanol (IPA)	**2.2**		ppbv	2.2	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Isopropanol (IPA)	**5.4**		ug/m3	5.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Methylene Chloride	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Methylene Chloride	ND		ug/m3	1.5	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
MTBE	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
MTBE	ND		ug/m3	1.6	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
n-Hexane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
n-Hexane	ND		ug/m3	1.5	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1-Dichloroethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1-Dichloroethane	ND		ug/m3	1.8	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Vinyl Acetate	ND		ppbv	2.2	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Vinyl Acetate	ND		ug/m3	7.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
2-Butanone	ND		ppbv	2.2	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
2-Butanone	ND		ug/m3	6.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Chloroform	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-003 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Chloroform	ND		ug/m3	2.1	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,1-Trichloroethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Carbon Tetrachloride	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Carbon Tetrachloride	ND		ug/m3	2.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Benzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Benzene	ND		ug/m3	1.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dichloroethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dichloroethane	ND		ug/m3	1.8	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Trichloroethene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Trichloroethene	ND		ug/m3	2.3	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dichloropropane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dichloropropane	ND		ug/m3	2.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Bromodichloromethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Bromodichloromethane	ND		ug/m3	2.9	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
cis-1,3-Dichloropropene	ND		ug/m3	2.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.8	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Toluene	**0.54**		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Toluene	**2.0**		ug/m3	1.6	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
trans-1,3-Dichloropropene	ND		ug/m3	2.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,2-Trichloroethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Tetrachloroethene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Tetrachloroethene	ND		ug/m3	3.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
2-Hexanone	ND		ppbv	1.1	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
2-Hexanone	ND		ug/m3	4.5	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Dibromochloromethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Dibromochloromethane	ND		ug/m3	3.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dibromoethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dibromoethane	ND		ug/m3	3.4	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Chlorobenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Chlorobenzene	ND		ug/m3	2.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Ethylbenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Ethylbenzene	ND		ug/m3	1.9	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
m,p-Xylenes	ND		ppbv	0.87	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
m,p-Xylenes	ND		ug/m3	3.8	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
o-Xylene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
o-Xylene	ND		ug/m3	1.9	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Styrene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Styrene	ND		ug/m3	1.9	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Bromoform	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Bromoform	ND		ug/m3	4.5	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	3.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	3.0	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
4-Ethyltoluene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
4-Ethyltoluene	ND		ug/m3	2.1	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-003 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,3,5-Trimethylbenzene	ND		ug/m3	2.1	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2,4-Trimethylbenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2,4-Trimethylbenzene	ND		ug/m3	2.1	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,3-Dichlorobenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.6	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,4-Dichlorobenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.6	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Benzyl chloride	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Benzyl chloride	ND		ug/m3	2.3	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dichlorobenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.6	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	3.2	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Hexachlorobutadiene	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Hexachlorobutadiene	ND		ug/m3	4.7	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Xylene (total)	ND		ppbv	0.44	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Xylene (total)	ND		ug/m3	1.9	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Surrogates				**Limits**					
Bromofluorobenzene	98%		%REC	60-140	2.2	413612	08/21/26 15:38	08/21/26 15:38	OHD
Method: EPA TO-3M									
TVOC as Hexane	ND		ppmv	0.11	2.2	413653	08/21/26 20:58	08/21/26 20:58	RXD
TVOC as Hexane	ND		ug/m3	380	2.2	413653	08/21/26 20:58	08/21/26 20:58	RXD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

Sample ID: CCL081926PL04	Lab ID: 566281-004	Collected: 08/19/26 08:09
	Matrix: Air	

566281-004 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Acrolein	ND		ug/m3	0.87	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1-Difluoroethane	ND		ppbv	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1-Difluoroethane	ND		ug/m3	5.1	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Freon 12	**0.45**		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Freon 12	**2.2**		ug/m3	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Freon 114	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Freon 114	ND		ug/m3	2.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Chloromethane	**0.60**		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Chloromethane	**1.2**		ug/m3	0.78	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Vinyl Chloride	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Vinyl Chloride	ND		ug/m3	0.97	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Bromomethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Bromomethane	ND		ug/m3	1.5	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Chloroethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Chloroethane	ND		ug/m3	1.0	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Trichlorofluoromethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Trichlorofluoromethane	ND		ug/m3	2.1	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1-Dichloroethene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Freon 113	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Freon 113	ND		ug/m3	2.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Acetone	**18**		ppbv	3.8	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Acetone	**42**		ug/m3	9.0	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Carbon Disulfide	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Carbon Disulfide	ND		ug/m3	1.2	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Isopropanol (IPA)	**2.7**		ppbv	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Isopropanol (IPA)	**6.6**		ug/m3	4.7	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Methylene Chloride	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Methylene Chloride	ND		ug/m3	1.3	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
MTBE	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
MTBE	ND		ug/m3	1.4	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
n-Hexane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
n-Hexane	ND		ug/m3	1.3	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1-Dichloroethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1-Dichloroethane	ND		ug/m3	1.5	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Vinyl Acetate	ND		ppbv	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Vinyl Acetate	ND		ug/m3	6.7	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
2-Butanone	ND		ppbv	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
2-Butanone	ND		ug/m3	5.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Chloroform	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-004 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Chloroform	ND		ug/m3	1.8	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,1-Trichloroethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.1	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Carbon Tetrachloride	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Carbon Tetrachloride	ND		ug/m3	2.4	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Benzene	**2.3**		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Benzene	**7.3**		ug/m3	1.2	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dichloroethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dichloroethane	ND		ug/m3	1.5	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Trichloroethene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Trichloroethene	ND		ug/m3	2.0	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dichloropropane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dichloropropane	ND		ug/m3	1.8	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Bromodichloromethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Bromodichloromethane	ND		ug/m3	2.5	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
cis-1,3-Dichloropropene	ND		ug/m3	1.7	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Toluene	**0.50**		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Toluene	**1.9**		ug/m3	1.4	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
trans-1,3-Dichloropropene	ND		ug/m3	1.7	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,2-Trichloroethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.1	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Tetrachloroethene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Tetrachloroethene	ND		ug/m3	2.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
2-Hexanone	ND		ppbv	0.95	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
2-Hexanone	ND		ug/m3	3.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Dibromochloromethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Dibromochloromethane	ND		ug/m3	3.2	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dibromoethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dibromoethane	ND		ug/m3	2.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Chlorobenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Chlorobenzene	ND		ug/m3	1.7	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Ethylbenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Ethylbenzene	ND		ug/m3	1.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
m,p-Xylenes	ND		ppbv	0.76	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
m,p-Xylenes	ND		ug/m3	3.3	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
o-Xylene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
o-Xylene	ND		ug/m3	1.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Styrene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Styrene	ND		ug/m3	1.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Bromoform	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Bromoform	ND		ug/m3	3.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	2.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	2.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
4-Ethyltoluene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
4-Ethyltoluene	ND		ug/m3	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-004 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,3,5-Trimethylbenzene	ND		ug/m3	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2,4-Trimethylbenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2,4-Trimethylbenzene	ND		ug/m3	1.9	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,3-Dichlorobenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.3	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,4-Dichlorobenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.3	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Benzyl chloride	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Benzyl chloride	ND		ug/m3	2.0	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dichlorobenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.3	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	2.8	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Hexachlorobutadiene	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Hexachlorobutadiene	ND		ug/m3	4.0	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Xylene (total)	ND		ppbv	0.38	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Xylene (total)	ND		ug/m3	1.6	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Surrogates				**Limits**					
Bromofluorobenzene	98%		%REC	60-140	1.9	413612	08/21/26 16:11	08/21/26 16:11	OHD
Method: EPA TO-3M									
TVOC as Hexane	ND		ppmv	0.095	1.9	413653	08/21/26 21:27	08/21/26 21:27	RXD
TVOC as Hexane	ND		ug/m3	330	1.9	413653	08/21/26 21:27	08/21/26 21:27	RXD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

Sample ID: CCL081926EX05	Lab ID: 566281-005	Collected: 08/19/26 14:14
	Matrix: Air	

566281-005 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Acrolein	ND		ug/m3	0.89	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1-Difluoroethane	ND		ppbv	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1-Difluoroethane	ND		ug/m3	5.2	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Freon 12	**0.46**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Freon 12	**2.3**		ug/m3	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Freon 114	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Freon 114	ND		ug/m3	2.7	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Chloromethane	**0.53**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Chloromethane	**1.1**		ug/m3	0.80	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Vinyl Chloride	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Vinyl Chloride	ND		ug/m3	0.99	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Bromomethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Bromomethane	ND		ug/m3	1.5	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Chloroethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Chloroethane	ND		ug/m3	1.0	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Trichlorofluoromethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Trichlorofluoromethane	ND		ug/m3	2.2	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1-Dichloroethene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Freon 113	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Freon 113	ND		ug/m3	3.0	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Acetone	**15**		ppbv	3.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Acetone	**36**		ug/m3	9.2	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Carbon Disulfide	**0.43**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Carbon Disulfide	**1.4**		ug/m3	1.2	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Isopropanol (IPA)	ND		ppbv	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Isopropanol (IPA)	ND		ug/m3	4.8	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Methylene Chloride	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Methylene Chloride	ND		ug/m3	1.3	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
MTBE	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
MTBE	ND		ug/m3	1.4	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
n-Hexane	**0.40**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
n-Hexane	**1.4**		ug/m3	1.4	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1-Dichloroethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1-Dichloroethane	ND		ug/m3	1.6	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Vinyl Acetate	ND		ppbv	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Vinyl Acetate	ND		ug/m3	6.8	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
2-Butanone	ND		ppbv	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
2-Butanone	ND		ug/m3	5.7	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Chloroform	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-005 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Chloroform	ND		ug/m3	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,1-Trichloroethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.1	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Carbon Tetrachloride	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Carbon Tetrachloride	ND		ug/m3	2.4	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Benzene	**3.2**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Benzene	**10**		ug/m3	1.2	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dichloroethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dichloroethane	ND		ug/m3	1.6	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Trichloroethene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Trichloroethene	ND		ug/m3	2.1	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dichloropropane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dichloropropane	ND		ug/m3	1.8	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Bromodichloromethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Bromodichloromethane	ND		ug/m3	2.6	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
cis-1,3-Dichloropropene	ND		ug/m3	1.8	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.6	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Toluene	**2.2**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Toluene	**8.3**		ug/m3	1.5	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
trans-1,3-Dichloropropene	ND		ug/m3	1.8	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,2-Trichloroethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.1	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Tetrachloroethene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Tetrachloroethene	ND		ug/m3	2.6	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
2-Hexanone	ND		ppbv	0.97	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
2-Hexanone	ND		ug/m3	4.0	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Dibromochloromethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Dibromochloromethane	ND		ug/m3	3.3	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dibromoethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dibromoethane	ND		ug/m3	3.0	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Chlorobenzene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Chlorobenzene	ND		ug/m3	1.8	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Ethylbenzene	**1.0**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Ethylbenzene	**4.4**		ug/m3	1.7	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
m,p-Xylenes	**1.2**		ppbv	0.77	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
m,p-Xylenes	**5.3**		ug/m3	3.4	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
o-Xylene	**0.52**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
o-Xylene	**2.2**		ug/m3	1.7	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Styrene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Styrene	ND		ug/m3	1.6	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Bromoform	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Bromoform	ND		ug/m3	4.0	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	2.7	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	2.7	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
4-Ethyltoluene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
4-Ethyltoluene	ND		ug/m3	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-005 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,3,5-Trimethylbenzene	ND		ug/m3	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2,4-Trimethylbenzene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2,4-Trimethylbenzene	ND		ug/m3	1.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,3-Dichlorobenzene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.3	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,4-Dichlorobenzene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.3	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Benzyl chloride	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Benzyl chloride	ND		ug/m3	2.0	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dichlorobenzene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.3	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	2.9	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Hexachlorobutadiene	ND		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Hexachlorobutadiene	ND		ug/m3	4.1	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Xylene (total)	**1.7**		ppbv	0.39	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Xylene (total)	**7.6**		ug/m3	1.7	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Surrogates				**Limits**					
Bromofluorobenzene	98%		%REC	60-140	1.9	413612	08/21/26 16:44	08/21/26 16:44	OHD
Method: EPA TO-3M									
TVOC as Hexane	**0.13**		ppmv	0.097	1.9	413653	08/21/26 21:57	08/21/26 21:57	RXD
TVOC as Hexane	**450**		ug/m3	340	1.9	413653	08/21/26 21:57	08/21/26 21:57	RXD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

Sample ID: CCL081926DW06	Lab ID: 566281-006	Collected: 08/19/26 14:33
	Matrix: Air	

566281-006 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Acrolein	ND		ug/m3	0.85	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1-Difluoroethane	ND		ppbv	1.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1-Difluoroethane	ND		ug/m3	5.0	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Freon 12	**0.48**		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Freon 12	**2.4**		ug/m3	1.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Freon 114	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Freon 114	ND		ug/m3	2.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Chloromethane	**0.56**		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Chloromethane	**1.2**		ug/m3	0.77	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Vinyl Chloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Vinyl Chloride	ND		ug/m3	0.95	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Bromomethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Bromomethane	ND		ug/m3	1.4	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Chloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Chloroethane	ND		ug/m3	0.98	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Trichlorofluoromethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Trichlorofluoromethane	ND		ug/m3	2.1	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1-Dichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Freon 113	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Freon 113	ND		ug/m3	2.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Acetone	**11**		ppbv	3.7	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Acetone	**27**		ug/m3	8.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Carbon Disulfide	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Carbon Disulfide	ND		ug/m3	1.2	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Isopropanol (IPA)	ND		ppbv	1.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Isopropanol (IPA)	ND		ug/m3	4.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Methylene Chloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Methylene Chloride	ND		ug/m3	1.3	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
MTBE	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
MTBE	ND		ug/m3	1.3	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
n-Hexane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
n-Hexane	ND		ug/m3	1.3	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1-Dichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1-Dichloroethane	ND		ug/m3	1.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Vinyl Acetate	ND		ppbv	1.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Vinyl Acetate	ND		ug/m3	6.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
2-Butanone	ND		ppbv	1.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
2-Butanone	ND		ug/m3	5.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Chloroform	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-006 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Chloroform	ND		ug/m3	1.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,1-Trichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.0	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Carbon Tetrachloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Carbon Tetrachloride	ND		ug/m3	2.3	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Benzene	**1.7**		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Benzene	**5.6**		ug/m3	1.2	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dichloroethane	ND		ug/m3	1.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Trichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Trichloroethene	ND		ug/m3	2.0	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dichloropropane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dichloropropane	ND		ug/m3	1.7	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Bromodichloromethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Bromodichloromethane	ND		ug/m3	2.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
cis-1,3-Dichloropropene	ND		ug/m3	1.7	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Toluene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Toluene	ND		ug/m3	1.4	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
trans-1,3-Dichloropropene	ND		ug/m3	1.7	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,2-Trichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.0	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Tetrachloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Tetrachloroethene	ND		ug/m3	2.5	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
2-Hexanone	ND		ppbv	0.93	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
2-Hexanone	ND		ug/m3	3.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Dibromochloromethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Dibromochloromethane	ND		ug/m3	3.2	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dibromoethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dibromoethane	ND		ug/m3	2.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Chlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Chlorobenzene	ND		ug/m3	1.7	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Ethylbenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Ethylbenzene	ND		ug/m3	1.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
m,p-Xylenes	ND		ppbv	0.74	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
m,p-Xylenes	ND		ug/m3	3.2	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
o-Xylene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
o-Xylene	ND		ug/m3	1.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Styrene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Styrene	ND		ug/m3	1.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Bromoform	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Bromoform	ND		ug/m3	3.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	2.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	2.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
4-Ethyltoluene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
4-Ethyltoluene	ND		ug/m3	1.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD

Results for any subcontracted analyses are not included in this section.

Analysis Results for 566281

566281-006 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,3,5-Trimethylbenzene	ND		ug/m3	1.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2,4-Trimethylbenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2,4-Trimethylbenzene	ND		ug/m3	1.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,3-Dichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.2	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,4-Dichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.2	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Benzyl chloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Benzyl chloride	ND		ug/m3	1.9	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.2	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	2.8	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Hexachlorobutadiene	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Hexachlorobutadiene	ND		ug/m3	4.0	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Xylene (total)	ND		ppbv	0.37	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Xylene (total)	ND		ug/m3	1.6	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Surrogates				**Limits**					
Bromofluorobenzene	97%		%REC	60-140	1.9	413612	08/21/26 17:16	08/21/26 17:16	OHD
Method: EPA TO-3M									
TVOC as Hexane	ND		ppmv	0.093	1.9	413653	08/21/26 22:26	08/21/26 22:26	RXD
TVOC as Hexane	ND		ug/m3	330	1.9	413653	08/21/26 22:26	08/21/26 22:26	RXD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

Sample ID: CCL081926UW07	Lab ID: 566281-007	Collected: 08/19/26 14:08
	Matrix: Air	

566281-007 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Acrolein	ND		ug/m3	0.86	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1-Difluoroethane	ND		ppbv	1.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1-Difluoroethane	ND		ug/m3	5.0	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Freon 12	**0.46**		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Freon 12	**2.3**		ug/m3	1.8	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Freon 114	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Freon 114	ND		ug/m3	2.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Chloromethane	**0.55**		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Chloromethane	**1.1**		ug/m3	0.77	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Vinyl Chloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Vinyl Chloride	ND		ug/m3	0.95	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Bromomethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Bromomethane	ND		ug/m3	1.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Chloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Chloroethane	ND		ug/m3	0.99	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Trichlorofluoromethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Trichlorofluoromethane	ND		ug/m3	2.1	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1-Dichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Freon 113	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Freon 113	ND		ug/m3	2.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Acetone	**12**		ppbv	3.7	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Acetone	**29**		ug/m3	8.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Carbon Disulfide	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Carbon Disulfide	ND		ug/m3	1.2	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Isopropanol (IPA)	ND		ppbv	1.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Isopropanol (IPA)	ND		ug/m3	4.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Methylene Chloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Methylene Chloride	ND		ug/m3	1.3	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
MTBE	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
MTBE	ND		ug/m3	1.3	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
n-Hexane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
n-Hexane	ND		ug/m3	1.3	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1-Dichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1-Dichloroethane	ND		ug/m3	1.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Vinyl Acetate	ND		ppbv	1.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Vinyl Acetate	ND		ug/m3	6.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
2-Butanone	ND		ppbv	1.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
2-Butanone	ND		ug/m3	5.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Chloroform	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-007 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Chloroform	ND		ug/m3	1.8	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,1-Trichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.0	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Carbon Tetrachloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Carbon Tetrachloride	ND		ug/m3	2.4	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Benzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Benzene	ND		ug/m3	1.2	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dichloroethane	ND		ug/m3	1.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Trichloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Trichloroethene	ND		ug/m3	2.0	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dichloropropane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dichloropropane	ND		ug/m3	1.7	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Bromodichloromethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Bromodichloromethane	ND		ug/m3	2.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
cis-1,3-Dichloropropene	ND		ug/m3	1.7	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Toluene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Toluene	ND		ug/m3	1.4	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
trans-1,3-Dichloropropene	ND		ug/m3	1.7	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,2-Trichloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.0	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Tetrachloroethene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Tetrachloroethene	ND		ug/m3	2.5	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
2-Hexanone	ND		ppbv	0.93	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
2-Hexanone	ND		ug/m3	3.8	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Dibromochloromethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Dibromochloromethane	ND		ug/m3	3.2	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dibromoethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dibromoethane	ND		ug/m3	2.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Chlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Chlorobenzene	ND		ug/m3	1.7	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Ethylbenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Ethylbenzene	ND		ug/m3	1.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
m,p-Xylenes	ND		ppbv	0.75	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
m,p-Xylenes	ND		ug/m3	3.2	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
o-Xylene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
o-Xylene	ND		ug/m3	1.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Styrene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Styrene	ND		ug/m3	1.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Bromoform	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Bromoform	ND		ug/m3	3.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	2.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	2.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
4-Ethyltoluene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
4-Ethyltoluene	ND		ug/m3	1.8	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-007 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,3,5-Trimethylbenzene	ND		ug/m3	1.8	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2,4-Trimethylbenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2,4-Trimethylbenzene	ND		ug/m3	1.8	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,3-Dichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.2	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,4-Dichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.2	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Benzyl chloride	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Benzyl chloride	ND		ug/m3	1.9	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.2	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	2.8	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Hexachlorobutadiene	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Hexachlorobutadiene	ND		ug/m3	4.0	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Xylene (total)	ND		ppbv	0.37	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Xylene (total)	ND		ug/m3	1.6	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Surrogates				**Limits**					
Bromofluorobenzene	98%		%REC	60-140	1.9	413612	08/21/26 17:49	08/21/26 17:49	OHD
Method: EPA TO-3M									
TVOC as Hexane	ND		ppmv	0.093	1.9	413653	08/21/26 22:55	08/21/26 22:55	RXD
TVOC as Hexane	ND		ug/m3	330	1.9	413653	08/21/26 22:55	08/21/26 22:55	RXD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

Sample ID: CCL081926PL08	Lab ID: 566281-008	Collected: 08/19/26 14:58
	Matrix: Air	

566281-008 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Method: EPA TO-15 Prep Method: METHOD									
Acrolein	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Acrolein	ND		ug/m3	0.99	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1-Difluoroethane	ND		ppbv	2.2	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1-Difluoroethane	ND		ug/m3	5.8	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Freon 12	**0.48**		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Freon 12	**2.4**		ug/m3	2.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Freon 114	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Freon 114	ND		ug/m3	3.0	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Chloromethane	**0.57**		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Chloromethane	**1.2**		ug/m3	0.89	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Vinyl Chloride	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Vinyl Chloride	ND		ug/m3	1.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Bromomethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Bromomethane	ND		ug/m3	1.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Chloroethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Chloroethane	ND		ug/m3	1.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Trichlorofluoromethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Trichlorofluoromethane	ND		ug/m3	2.4	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1-Dichloroethene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1-Dichloroethene	ND		ug/m3	1.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Freon 113	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Freon 113	ND		ug/m3	3.3	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Acetone	**14**		ppbv	4.3	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Acetone	**33**		ug/m3	10	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Carbon Disulfide	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Carbon Disulfide	ND		ug/m3	1.3	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Isopropanol (IPA)	ND		ppbv	2.2	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Isopropanol (IPA)	ND		ug/m3	5.3	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Methylene Chloride	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Methylene Chloride	ND		ug/m3	1.5	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
trans-1,2-Dichloroethene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
trans-1,2-Dichloroethene	ND		ug/m3	1.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
MTBE	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
MTBE	ND		ug/m3	1.6	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
n-Hexane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
n-Hexane	ND		ug/m3	1.5	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1-Dichloroethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1-Dichloroethane	ND		ug/m3	1.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Vinyl Acetate	ND		ppbv	2.2	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Vinyl Acetate	ND		ug/m3	7.6	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
cis-1,2-Dichloroethene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
cis-1,2-Dichloroethene	ND		ug/m3	1.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
2-Butanone	ND		ppbv	2.2	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
2-Butanone	ND		ug/m3	6.4	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Chloroform	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD

Results for any subcontracted analyses are not included in this section.

Onterris

Analysis Results for 566281

566281-008 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
Chloroform	ND		ug/m3	2.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,1-Trichloroethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,1-Trichloroethane	ND		ug/m3	2.4	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Carbon Tetrachloride	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Carbon Tetrachloride	ND		ug/m3	2.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Benzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Benzene	ND		ug/m3	1.4	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dichloroethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dichloroethane	ND		ug/m3	1.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Trichloroethene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Trichloroethene	ND		ug/m3	2.3	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dichloropropane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dichloropropane	ND		ug/m3	2.0	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Bromodichloromethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Bromodichloromethane	ND		ug/m3	2.9	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
cis-1,3-Dichloropropene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
cis-1,3-Dichloropropene	ND		ug/m3	2.0	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
4-Methyl-2-Pentanone	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
4-Methyl-2-Pentanone	ND		ug/m3	1.8	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Toluene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Toluene	ND		ug/m3	1.6	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
trans-1,3-Dichloropropene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
trans-1,3-Dichloropropene	ND		ug/m3	2.0	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,2-Trichloroethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,2-Trichloroethane	ND		ug/m3	2.4	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Tetrachloroethene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Tetrachloroethene	ND		ug/m3	2.9	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
2-Hexanone	ND		ppbv	1.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
2-Hexanone	ND		ug/m3	4.4	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Dibromochloromethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Dibromochloromethane	ND		ug/m3	3.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dibromoethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dibromoethane	ND		ug/m3	3.3	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Chlorobenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Chlorobenzene	ND		ug/m3	2.0	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Ethylbenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Ethylbenzene	ND		ug/m3	1.9	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
m,p-Xylenes	ND		ppbv	0.86	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
m,p-Xylenes	ND		ug/m3	3.7	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
o-Xylene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
o-Xylene	ND		ug/m3	1.9	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Styrene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Styrene	ND		ug/m3	1.8	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Bromoform	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Bromoform	ND		ug/m3	4.5	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,2,2-Tetrachloroethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,2,2-Tetrachloroethane	ND		ug/m3	3.0	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,1,2-Tetrachloroethane	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,1,1,2-Tetrachloroethane	ND		ug/m3	3.0	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
4-Ethyltoluene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
4-Ethyltoluene	ND		ug/m3	2.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,3,5-Trimethylbenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD

Results for any subcontracted analyses are not included in this section.

Analysis Results for 566281

566281-008 Analyte	Result	Qual	Units	RL	DF	Batch	Prepared	Analyzed	Chemist
1,3,5-Trimethylbenzene	ND		ug/m3	2.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2,4-Trimethylbenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2,4-Trimethylbenzene	ND		ug/m3	2.1	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,3-Dichlorobenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,3-Dichlorobenzene	ND		ug/m3	2.6	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,4-Dichlorobenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,4-Dichlorobenzene	ND		ug/m3	2.6	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Benzyl chloride	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Benzyl chloride	ND		ug/m3	2.2	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dichlorobenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2-Dichlorobenzene	ND		ug/m3	2.6	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2,4-Trichlorobenzene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
1,2,4-Trichlorobenzene	ND		ug/m3	3.2	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Hexachlorobutadiene	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Hexachlorobutadiene	ND		ug/m3	4.6	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Xylene (total)	ND		ppbv	0.43	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Xylene (total)	ND		ug/m3	1.9	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Surrogates				**Limits**					
Bromofluorobenzene	98%		%REC	60-140	2.2	413612	08/21/26 18:21	08/21/26 18:21	OHD
Method: EPA TO-3M									
TVOC as Hexane	ND		ppmv	0.11	2.2	413653	08/21/26 23:24	08/21/26 23:24	RXD
TVOC as Hexane	ND		ug/m3	380	2.2	413653	08/21/26 23:24	08/21/26 23:24	RXD

ND Not Detected

Results for any subcontracted analyses are not included in this section.

Onterris

Batch QC

Type:	**Lab Control Sample**	**Lab ID:**	**QC1406819**	**Batch:**	**413612**
Matrix:	**Air**	**Method:**	**EPA TO-15**	**Prep Method:**	**METHOD**

QC1406819 Analyte	Result	Spiked	Units	Recovery	Qual	Limits
Acrolein	9.536	10.00	ppbv	95%		70-130
1,1-Difluoroethane	9.566	10.00	ppbv	96%		70-130
Freon 12	10.40	10.00	ppbv	104%		70-130
Freon 114	9.891	10.00	ppbv	99%		70-130
Chloromethane	10.01	10.00	ppbv	100%		70-130
Vinyl Chloride	10.02	10.00	ppbv	100%		70-130
Bromomethane	9.808	10.00	ppbv	98%		70-130
Chloroethane	9.909	10.00	ppbv	99%		70-130
Trichlorofluoromethane	10.42	10.00	ppbv	104%		70-130
1,1-Dichloroethene	10.21	10.00	ppbv	102%		70-130
Freon 113	9.998	10.00	ppbv	100%		70-130
Acetone	10.34	10.00	ppbv	103%		70-130
Carbon Disulfide	9.978	10.00	ppbv	100%		70-130
Isopropanol (IPA)	10.91	10.00	ppbv	109%		70-130
Methylene Chloride	10.26	10.00	ppbv	103%		70-130
trans-1,2-Dichloroethene	9.755	10.00	ppbv	98%		70-130
MTBE	10.31	10.00	ppbv	103%		70-130
n-Hexane	10.10	10.00	ppbv	101%		70-130
1,1-Dichloroethane	9.889	10.00	ppbv	99%		70-130
Vinyl Acetate	9.753	10.00	ppbv	98%		70-130
cis-1,2-Dichloroethene	10.04	10.00	ppbv	100%		70-130
2-Butanone	10.39	10.00	ppbv	104%		70-130
Chloroform	10.23	10.00	ppbv	102%		70-130
1,1,1-Trichloroethane	10.34	10.00	ppbv	103%		70-130
Carbon Tetrachloride	10.37	10.00	ppbv	104%		70-130
Benzene	9.788	10.00	ppbv	98%		70-130
1,2-Dichloroethane	10.25	10.00	ppbv	102%		70-130
Trichloroethene	9.859	10.00	ppbv	99%		70-130
1,2-Dichloropropane	9.608	10.00	ppbv	96%		70-130
Bromodichloromethane	10.41	10.00	ppbv	104%		70-130
cis-1,3-Dichloropropene	10.17	10.00	ppbv	102%		70-130
4-Methyl-2-Pentanone	10.63	10.00	ppbv	106%		70-130
Toluene	10.26	10.00	ppbv	103%		70-130
trans-1,3-Dichloropropene	10.41	10.00	ppbv	104%		70-130
1,1,2-Trichloroethane	10.32	10.00	ppbv	103%		70-130
Tetrachloroethene	11.18	10.00	ppbv	112%		70-130
2-Hexanone	10.85	10.00	ppbv	109%		70-130
Dibromochloromethane	10.23	10.00	ppbv	102%		70-130
1,2-Dibromoethane	10.29	10.00	ppbv	103%		70-130
Chlorobenzene	10.17	10.00	ppbv	102%		70-130
Ethylbenzene	10.60	10.00	ppbv	106%		70-130
m,p-Xylenes	22.19	20.00	ppbv	111%		70-130
o-Xylene	11.19	10.00	ppbv	112%		70-130
Styrene	11.10	10.00	ppbv	111%		70-130
Bromoform	9.681	10.00	ppbv	97%		70-130
1,1,2,2-Tetrachloroethane	10.38	10.00	ppbv	104%		70-130
1,1,1,2-Tetrachloroethane	10.36	10.00	ppbv	104%		70-130

Onterris™

Batch QC

QC1406819 Analyte	Result	Spiked	Units	Recovery	Qual	Limits
4-Ethyltoluene	10.88	10.00	ppbv	109%		70-130
1,3,5-Trimethylbenzene	11.25	10.00	ppbv	112%		70-130
1,2,4-Trimethylbenzene	11.71	10.00	ppbv	117%		70-130
1,3-Dichlorobenzene	11.02	10.00	ppbv	110%		70-130
1,4-Dichlorobenzene	11.37	10.00	ppbv	114%		70-130
Benzyl chloride	11.49	10.00	ppbv	115%		70-130
1,2-Dichlorobenzene	10.92	10.00	ppbv	109%		70-130
1,2,4-Trichlorobenzene	10.96	10.00	ppbv	110%		70-130
Hexachlorobutadiene	11.06	10.00	ppbv	111%		70-130
Surrogates						
Bromofluorobenzene	10.47	10.00	ppbv	105%		60-140

Onterris

Batch QC

Type:	**Lab Control Sample Duplicate**	**Lab ID:**	**QC1406820**	**Batch:**	**413612**
Matrix:	**Air**	**Method:**	**EPA TO-15**	**Prep Method:**	**METHOD**

QC1406820 Analyte	Result	Spiked	Units	Recovery	Qual	Limits	RPD	RPD Lim
Acrolein	9.869	10.00	ppbv	99%		70-130	3	25
1,1-Difluoroethane	9.647	10.00	ppbv	96%		70-130	1	25
Freon 12	10.53	10.00	ppbv	105%		70-130	1	25
Freon 114	10.14	10.00	ppbv	101%		70-130	2	25
Chloromethane	10.25	10.00	ppbv	102%		70-130	2	25
Vinyl Chloride	10.34	10.00	ppbv	103%		70-130	3	25
Bromomethane	9.913	10.00	ppbv	99%		70-130	1	25
Chloroethane	10.03	10.00	ppbv	100%		70-130	1	25
Trichlorofluoromethane	10.29	10.00	ppbv	103%		70-130	1	25
1,1-Dichloroethene	10.13	10.00	ppbv	101%		70-130	1	25
Freon 113	9.806	10.00	ppbv	98%		70-130	2	25
Acetone	10.40	10.00	ppbv	104%		70-130	1	25
Carbon Disulfide	9.804	10.00	ppbv	98%		70-130	2	25
Isopropanol (IPA)	11.16	10.00	ppbv	112%		70-130	2	25
Methylene Chloride	10.06	10.00	ppbv	101%		70-130	2	25
trans-1,2-Dichloroethene	9.709	10.00	ppbv	97%		70-130	0	25
MTBE	10.32	10.00	ppbv	103%		70-130	0	25
n-Hexane	9.990	10.00	ppbv	100%		70-130	1	25
1,1-Dichloroethane	9.786	10.00	ppbv	98%		70-130	1	25
Vinyl Acetate	9.743	10.00	ppbv	97%		70-130	0	25
cis-1,2-Dichloroethene	9.919	10.00	ppbv	99%		70-130	1	25
2-Butanone	9.636	10.00	ppbv	96%		70-130	8	25
Chloroform	10.10	10.00	ppbv	101%		70-130	1	25
1,1,1-Trichloroethane	10.21	10.00	ppbv	102%		70-130	1	25
Carbon Tetrachloride	10.11	10.00	ppbv	101%		70-130	3	25
Benzene	9.669	10.00	ppbv	97%		70-130	1	25
1,2-Dichloroethane	10.15	10.00	ppbv	102%		70-130	1	25
Trichloroethene	9.752	10.00	ppbv	98%		70-130	1	25
1,2-Dichloropropane	9.621	10.00	ppbv	96%		70-130	0	25
Bromodichloromethane	10.14	10.00	ppbv	101%		70-130	3	25
cis-1,3-Dichloropropene	10.13	10.00	ppbv	101%		70-130	0	25
4-Methyl-2-Pentanone	10.59	10.00	ppbv	106%		70-130	0	25
Toluene	10.15	10.00	ppbv	101%		70-130	1	25
trans-1,3-Dichloropropene	10.26	10.00	ppbv	103%		70-130	1	25
1,1,2-Trichloroethane	9.968	10.00	ppbv	100%		70-130	3	25
Tetrachloroethene	10.99	10.00	ppbv	110%		70-130	2	25
2-Hexanone	10.88	10.00	ppbv	109%		70-130	0	25
Dibromochloromethane	10.12	10.00	ppbv	101%		70-130	1	25
1,2-Dibromoethane	10.08	10.00	ppbv	101%		70-130	2	25
Chlorobenzene	10.00	10.00	ppbv	100%		70-130	2	25
Ethylbenzene	10.55	10.00	ppbv	106%		70-130	0	25
m,p-Xylenes	21.93	20.00	ppbv	110%		70-130	1	25
o-Xylene	11.07	10.00	ppbv	111%		70-130	1	25
Styrene	11.08	10.00	ppbv	111%		70-130	0	25
Bromoform	9.493	10.00	ppbv	95%		70-130	2	25
1,1,2,2-Tetrachloroethane	10.28	10.00	ppbv	103%		70-130	1	25

Onterris™

Batch QC

QC1406820 Analyte	Result	Spiked	Units	Recovery	Qual	Limits	RPD	RPD Lim
1,1,1,2-Tetrachloroethane	10.35	10.00	ppbv	103%		70-130	0	25
4-Ethyltoluene	10.78	10.00	ppbv	108%		70-130	1	25
1,3,5-Trimethylbenzene	11.08	10.00	ppbv	111%		70-130	2	25
1,2,4-Trimethylbenzene	11.58	10.00	ppbv	116%		70-130	1	25
1,3-Dichlorobenzene	10.93	10.00	ppbv	109%		70-130	1	25
1,4-Dichlorobenzene	11.23	10.00	ppbv	112%		70-130	1	25
Benzyl chloride	11.19	10.00	ppbv	112%		70-130	3	25
1,2-Dichlorobenzene	10.73	10.00	ppbv	107%		70-130	2	25
1,2,4-Trichlorobenzene	10.94	10.00	ppbv	109%		70-130	0	25
Hexachlorobutadiene	10.86	10.00	ppbv	109%		70-130	2	25
Surrogates								
Bromofluorobenzene	10.41	10.00	ppbv	104%		60-140		

Onterris

Batch QC

Type:	**Blank**	**Lab ID:**	**QC1406821**	**Batch:**	**413612**
Matrix:	**Air**	**Method:**	**EPA TO-15**	**Prep Method:**	**METHOD**

QC1406821 Analyte	Result	Qual	Units	RL	Prepared	Analyzed
Acrolein	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,1-Difluoroethane	ND		ppbv	1.0	08/21/26 10:32	08/21/26 10:32
Freon 12	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Freon 114	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Chloromethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Vinyl Chloride	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Bromomethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Chloroethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Trichlorofluoromethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,1-Dichloroethene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Freon 113	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Acetone	ND		ppbv	2.0	08/21/26 10:32	08/21/26 10:32
Carbon Disulfide	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Isopropanol (IPA)	ND		ppbv	1.0	08/21/26 10:32	08/21/26 10:32
Methylene Chloride	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
trans-1,2-Dichloroethene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
MTBE	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
n-Hexane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,1-Dichloroethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Vinyl Acetate	ND		ppbv	1.0	08/21/26 10:32	08/21/26 10:32
cis-1,2-Dichloroethene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
2-Butanone	ND		ppbv	1.0	08/21/26 10:32	08/21/26 10:32
Chloroform	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,1,1-Trichloroethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Carbon Tetrachloride	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Benzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,2-Dichloroethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Trichloroethene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,2-Dichloropropane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Bromodichloromethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
cis-1,3-Dichloropropene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
4-Methyl-2-Pentanone	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Toluene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
trans-1,3-Dichloropropene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,1,2-Trichloroethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Tetrachloroethene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
2-Hexanone	ND		ppbv	0.50	08/21/26 10:32	08/21/26 10:32
Dibromochloromethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,2-Dibromoethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Chlorobenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Ethylbenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
m,p-Xylenes	ND		ppbv	0.40	08/21/26 10:32	08/21/26 10:32
o-Xylene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Styrene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Bromoform	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,1,2,2-Tetrachloroethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,1,1,2-Tetrachloroethane	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32

Batch QC

QC1406821 Analyte	Result	Qual	Units	RL	Prepared	Analyzed
4-Ethyltoluene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,3,5-Trimethylbenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,2,4-Trimethylbenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,3-Dichlorobenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,4-Dichlorobenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Benzyl chloride	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,2-Dichlorobenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
1,2,4-Trichlorobenzene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Hexachlorobutadiene	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Xylene (total)	ND		ppbv	0.20	08/21/26 10:32	08/21/26 10:32
Surrogates				**Limits**		
Bromofluorobenzene	98%		%REC	60-140	08/21/26 10:32	08/21/26 10:32

Type: Lab Control Sample **Lab ID: QC1406972** **Batch: 413653**
Matrix: Air **Method: EPA TO-3M**

QC1406972 Analyte	Result	Spiked	Units	Recovery	Qual	Limits
n-Hexane	0.09207	0.09615	ppmv	96%		70-130

Type: Lab Control Sample Duplicate **Lab ID: QC1406973** **Batch: 413653**
Matrix: Air **Method: EPA TO-3M**

QC1406973 Analyte	Result	Spiked	Units	Recovery	Qual	Limits	RPD	RPD Lim
n-Hexane	0.09180	0.09615	ppmv	95%		70-130	0	25

Type: Blank **Lab ID: QC1406974** **Batch: 413653**
Matrix: Air **Method: EPA TO-3M**

QC1406974 Analyte	Result	Qual	Units	RL	Prepared	Analyzed
TVOC as Hexane	ND		ppmv	0.050	08/21/26 14:02	08/21/26 14:02

ND Not Detected
