
## **Update on Coyote Creek Flood Projects**



#### Background


- 9-Miles Long
- 2017 Flood
- FERC\* Order
  Compliance
  Project (FOCP)
- Two Parts:
  - 40% CCFMMP
  - 60% CCFPP

<sup>\*</sup> Federal Energy Regulatory Commission (FERC)'s FOCP for Anderson Dam Tunnel

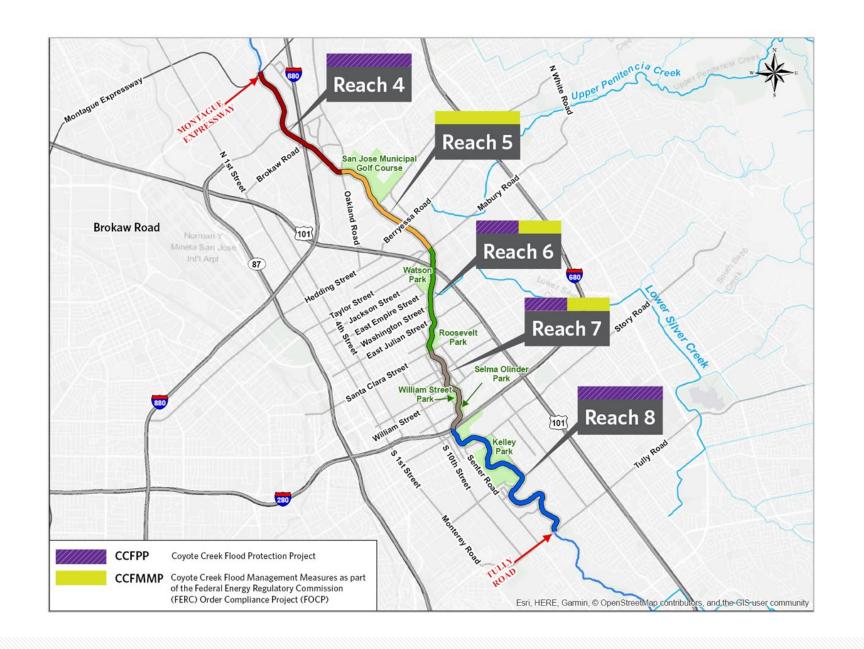




#### **Project Design**

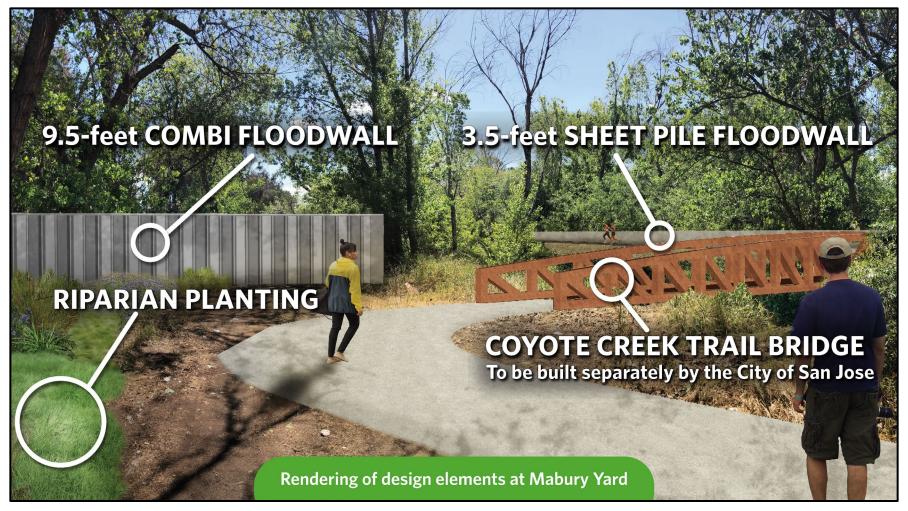



#### **Project Progress**




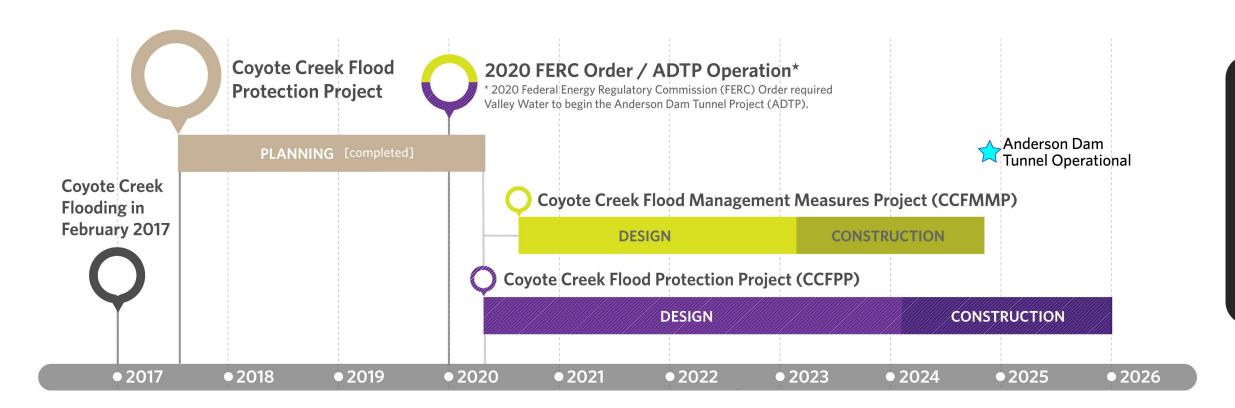



#### Right-of-Way (ROW) Needs

- 31 Properties for CCFMMP
- 51 Properties for CCFPP
- Relocation Plan Adopted
  by the Board (2/22/22)

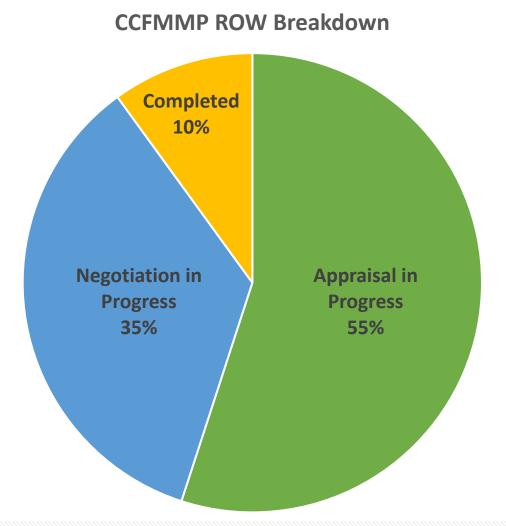



#### **Unhoused Abatement**








Document Name: Coyote Projects



#### **Unhoused Abatement – Timeline**

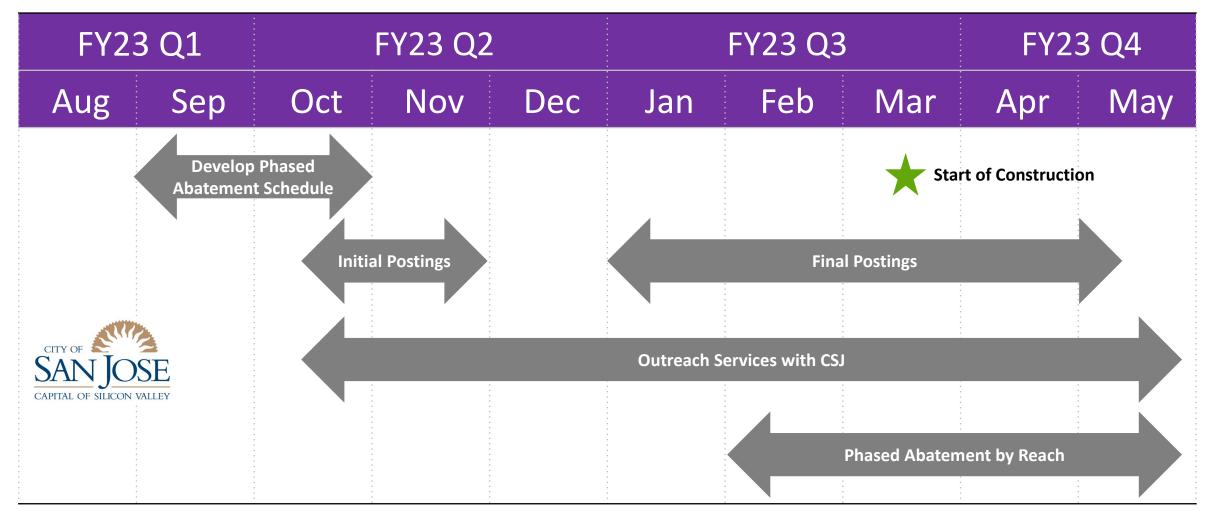




#### **Public Outreach and Stakeholder Engagement**

- 27 Meetings Since 2017
- Mailers to 7,200 addresses
- Nextdoor.com Notifications
- Email Updates
- Social Media Boosting
- ValleyWater.org/Coyote-Creek







#### **Public Input Opportunities**



July 2018: Ongoing evaluation of conceptual solutions

October 2017: Coyote Creek Flood Risk Reduction Ad Hoc Committee at Roosevelt Community Center, public n

October 2017: Joint City of San Jose and Valley Water Winter Preparedness and Emergency Action Plan Fair

September 2017: Rocksprings Pre-Construction on Flood Barrier and Berm Installation, public meeting

August 2017: Coyote Creek Flood Risk Reduction Ad Hoc Committee, two public meetings

April 2017: Response to February 2017 Flood, three public meetings





#### **Environmental Planning**

10

- CCFMMP
  - CEQA Exempt FOCP
  - Lake & Streambed
    Alteration Agreement
    (LSAA)
  - State and Regional Water Boards 401 Cert.
  - Valley Habitat Plan (VHP)




CCFPP - CEQA Review



#### **Financial Impacts**

- Prelim. CIP FY 2024 28 Five-Year Plan
  - Inflation
  - COVID
  - Supply Chain
  - Design Elements
  - Field Conditions
- WIFIA Loan Package
- Notice of Interest (NOI) for FEMA BRIC

Grant

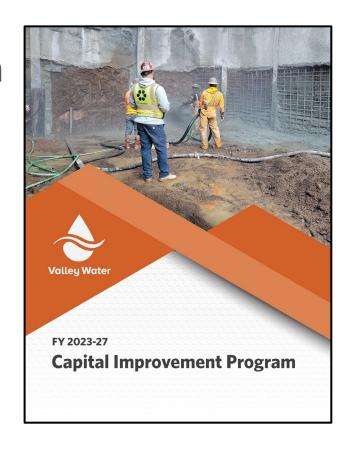

- \* Water Infrastructure Finance and Innovation Act WIFIA
- \* Building Resilient Infrastructure and Communities BRIC



#### **Implementation Challenges**

- 18-Month Construction
- Local Agency Coordination
- Bird Nesting Season
- Noise and Vibration
- Site Security
- Supply Chain









## **Upcoming Board Engagement**

13

- Oct 2022 to Feb 2023 Real Estate Transactions
- Oct 2022 WIFIA Loan
- Nov 2022 Significant Capital Project Plan Updates (CIP Committee\*)
- Dec 2022 Prelim. FY 24 28 CIP Five-Year Plan (CIP Committee\*)
- Dec 2022 Award CM Services Contract
- Dec 2022 Advertise Construction Contract for CCFMMP
- Jan 2023 Prelim. CIP FY 2024 28 Five-Year Plan
- Feb 2023 Award Construction Contract for CCFMMP

\* The CIP Committee is a Board Committee that provides feedback and recommendations to the full-board for board decisions.



# QUESTIONS





# Valley Water

Clean Water • Healthy Environment • Flood Protection
